EXHIBIT 10

PRELIMINARY BASELINE SCHEDULE

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
Total			1626	01-Apr-09	24-Jun-15	0
PROJECT WIDE ACTIVITIES			1626	01-Apr-09	24-Jun-15	0
ADMINISTRATION			1626	01-Apr-09	24-Jun-15	0
1.1.1	NTP1	NOTICE TO PROCEED 1	0	01-Apr-09		0
1.1.1	900OM01	Obtain and Prepare TxDOT & IE Office	30	01-Apr-09	30-Apr-09	246
1.1.1	PMP	Prepare & Submit PMP, Baseline Schedule ...	120	01-Apr-09	29-Jul-09	156
1.1.1	900R01	Prepare ROW Parcel Identification Packages	120	14-Apr-09	29-Sep-09	68
1.1.1	900OM02	Transition of O&M from TxDOT to Concessio...	60	03-Aug-...	02-Oct-09	92
1.1.1	900OM04	Prepare & Submit Maintenance Management...	60	03-Nov-...	01-Jan-10	0
1.1.1	900OM05	Prepare & Submit Operations Management ...	60	03-Nov-...	01-Jan-10	0
1.1.1	900OM03	Train O&M Personnel	30	03-Dec-...	01-Jan-10	0
1.1.1	NTP2	NOTICE TO PROCEED 2	0		01-Jan-10	0
1.1.1	900OM06	Prepare & Submit Operations Management ...	30	27-Mar-15	25-Apr-15	0
1.1.1	SCD	SERVICE COMMENCEMENT DEADLINE	0		24-Jun-15	0
OPERATIONS			1428	02-Jan-10	24-Jun-15	0
1.6	900O600	Developer Assumes Operational Duties	0	02-Jan-10		0
1.6.2	900O602	Facility Patrols and Inspections	2000	02-Jan-10	24-Jun-15	0
1.6.3	900O603	Traffic Control and Incident Management	2000	02-Jan-10	24-Jun-15	0
1.6.4	900O604	Operations Policies	2000	02-Jan-10	24-Jun-15	0
1.6.5	900O605	Operations Power Costs	2000	02-Jan-10	24-Jun-15	0
MAINTENANCE			1428	02-Jan-10	24-Jun-15	0
1.7	900M700	Developer Assumes Maintenance Duties	0	02-Jan-10		0
1.7.1	900M701	Maintenance of Roadway	2000	02-Jan-10	24-Jun-15	0
1.7.2	900M702	Maintenance of Drainage	2000	02-Jan-10	24-Jun-15	0
1.7.3	900M703	Maintenance of Structures	2000	02-Jan-10	24-Jun-15	0
1.7.4	900M704	Maintenance of Pvmt Marking, Object Marke...	2000	02-Jan-10	24-Jun-15	0
1.7.5	900M705	Maintenance of Guard Rail, Safety Barrier, I...	2000	02-Jan-10	24-Jun-15	0
1.7.6	900M706	Maintenance of Signs	2000	02-Jan-10	24-Jun-15	0
1.7.7	900M707	Maintenance of Traffic Signal Systems	2000	02-Jan-10	24-Jun-15	0
1.7.8	900M708	Maintenance of Lighting	2000	02-Jan-10	24-Jun-15	0
1.7.9	900M709	Maintenance of Fences and Noise Walls	2000	02-Jan-10	24-Jun-15	0
1.7.10	900M710	Maintenance of Roadside Management	2000	02-Jan-10	24-Jun-15	0
1.7.11	900M711	Maintenance of ITS and ETCS	2000	02-Jan-10	24-Jun-15	0
1.7.12	900M712	Maintenance of Buildings	2000	02-Jan-10	24-Jun-15	0
1.7.13	900M713	Snow and Ice Removal	2000	02-Jan-10	24-Jun-15	0
1.7.14	900M714	Incident Response	2000	02-Jan-10	24-Jun-15	0
1.7.15	900M715	Customer Response	2000	02-Jan-10	24-Jun-15	0
1.7.16	900M716	Sweeping and Cleaning	2000	02-Jan-10	24-Jun-15	0
1.7.17	900M717	Maintenance Fleet & Equipment	2000	02-Jan-10	24-Jun-15	0
DESIGN			422	01-Apr-09	11-Nov-10	204
1.2	900D103	CONDUCT DESIGN SURVEY	100	01-Apr-09	18-Aug-09	249
1.2	900D105	CONDUCT GEOTECHNICAL INVESTIGATION	100	01-Apr-09	18-Aug-09	526
1.2.11	900D12111	MILESTONE 1 QA/QC OF DESIGN PACKAGE	10	11-Nov-...	25-Nov-09	440
1.2.12	900D12121	MILESTONE 1 INDEPENDENT ENGINEER ...	15	25-Nov-...	16-Dec-09	440
1.2	900D106	MILESTONE 1 DESIGN SUBMITTAL	0		16-Dec-09	440
1.2.11	900D12112	MILESTONE 2 QA/QC OF DESIGN PACKAGE	10	05-May...	19-May-10	315
1.2.12	900D12122	MILESTONE 2 INDEPENDENT ENGINEER ...	15	19-May...	09-Jun-10	315
1.2	900D107	MILESTONE 2 DESIGN SUBMITTAL	0		09-Jun-10	315
1.2.11	900D12113	MILESTONE 3 QA/QC OF DESIGN PACKAGE	10	14-Jul-10	28-Jul-10	265
1.2.12	900D12123	MILESTONE 3 INDEPENDENT ENGINEER ...	15	28-Jul-10	18-Aug-10	265
1.2	900D108	MILESTONE 3 DESIGN SUBMITTAL	0		18-Aug-10	265
1.2.11	900D12114	MILESTONE 4 QA/QC OF DESIGN PACKAGE	10	07-Oct-10	21-Oct-10	204
1.2.12	900D12124	MILESTONE 4 INDEPENDENT ENGINEER ...	15	21-Oct-10	11-Nov-10	204
1.2	900D109	MILESTONE 4 DESIGN SUBMITTAL	0		11-Nov-10	204
1.2	900D110	FORMAL DESIGN PACKAGE COMPLETION	0		11-Nov-10	204
ROW ACQUISITION			120	01-Jan-10	18-Jun-10	198
1.3	90R0P000B010	Submit ROW Block 1 Packages to TxDOT	0		01-Jan-10	105
1.3	90R0P000B020	Submit ROW Block 2 Packages to TxDOT	0		15-Jan-10	105
1.3	90R0P000B030	Submit ROW Block 3 Packages to TxDOT	0		29-Jan-10	105
1.3	90R0P000B040	Submit ROW Block 4 Packages to TxDOT	0		12-Feb-10	105
1.3	90R0P000B050	Submit ROW Block 5 Packages to TxDOT	0		26-Feb-10	105
1.3	90R0P000B060	Submit ROW Block 6 Packages to TxDOT	0		12-Mar-10	105
1.3	90R0P000B070	Submit ROW Block 7 Packages to TxDOT	0		26-Mar-10	105
1.3	90R0P000B080	Submit ROW Block 8 Packages to TxDOT	0		09-Apr-10	105
1.3	90R0P000B090	Submit ROW Block 9 Packages to TxDOT	0		23-Apr-10	105
1.3	90R0P000B100	Submit ROW Block 10 Packages to TxDOT	0		07-May-10	136
1.3	90R0P000B110	Submit ROW Block 11 Packages to TxDOT	0		21-May-10	149
1.3	90R0P000B120	Submit ROW Block 12 Packages to TxDOT	0		04-Jun-10	168
1.3	90R0P000B130	Submit ROW Block 13 Packages to TxDOT	0		18-Jun-10	198
UTILITY RELOCATIONS			245	10-Apr-09	19-Mar-10	188
1.4	900U100	Initial Meetings with Utility Owners	20	10-Apr-09	08-May-09	333
1.4	900U200	Perform Level B SUE Work	120	10-Apr-09	25-Sep-09	188
1.4	900U300	Prepare Utility Strip Map and Tracking Report	30	28-Aug-...	09-Oct-09	188
1.4	900U400	Develop Utility Adjustment Concept Plan	35	09-Oct-09	27-Nov-09	188
1.4	900U500	Negotiate MUAAs with Utility Owners	80	27-Nov-...	19-Mar-10	188
CONSTRUCTION MILESTONES			1179	11-Nov-...	20-May-15	25
1.5	00001	START CONSTRUCTION	0	11-Nov-...		204
1.5	99999	FINISH CONSTRUCTION	0		20-May-15	25
CONSTRUCTION PHASE 1			592	11-Nov-...	18-Feb-13	612
1.5	0010	PHASE 1 CONSTRUCTION	592	11-Nov-...	18-Feb-13	612
CONSTRUCTION PHASE 2			481	22-Nov-...	25-Sep-13	247
1.5	0020	PHASE 2 CONSTRUCTION	481	22-Nov-...	25-Sep-13	247
CONSTRUCTION PHASE 3			471	02-Jan-13	23-Oct-14	174
1.5	0030	PHASE 3 CONSTRUCTION	471	02-Jan-13	23-Oct-14	174
CONSTRUCTION PHASE 4			475	24-Jul-13	20-May-15	25

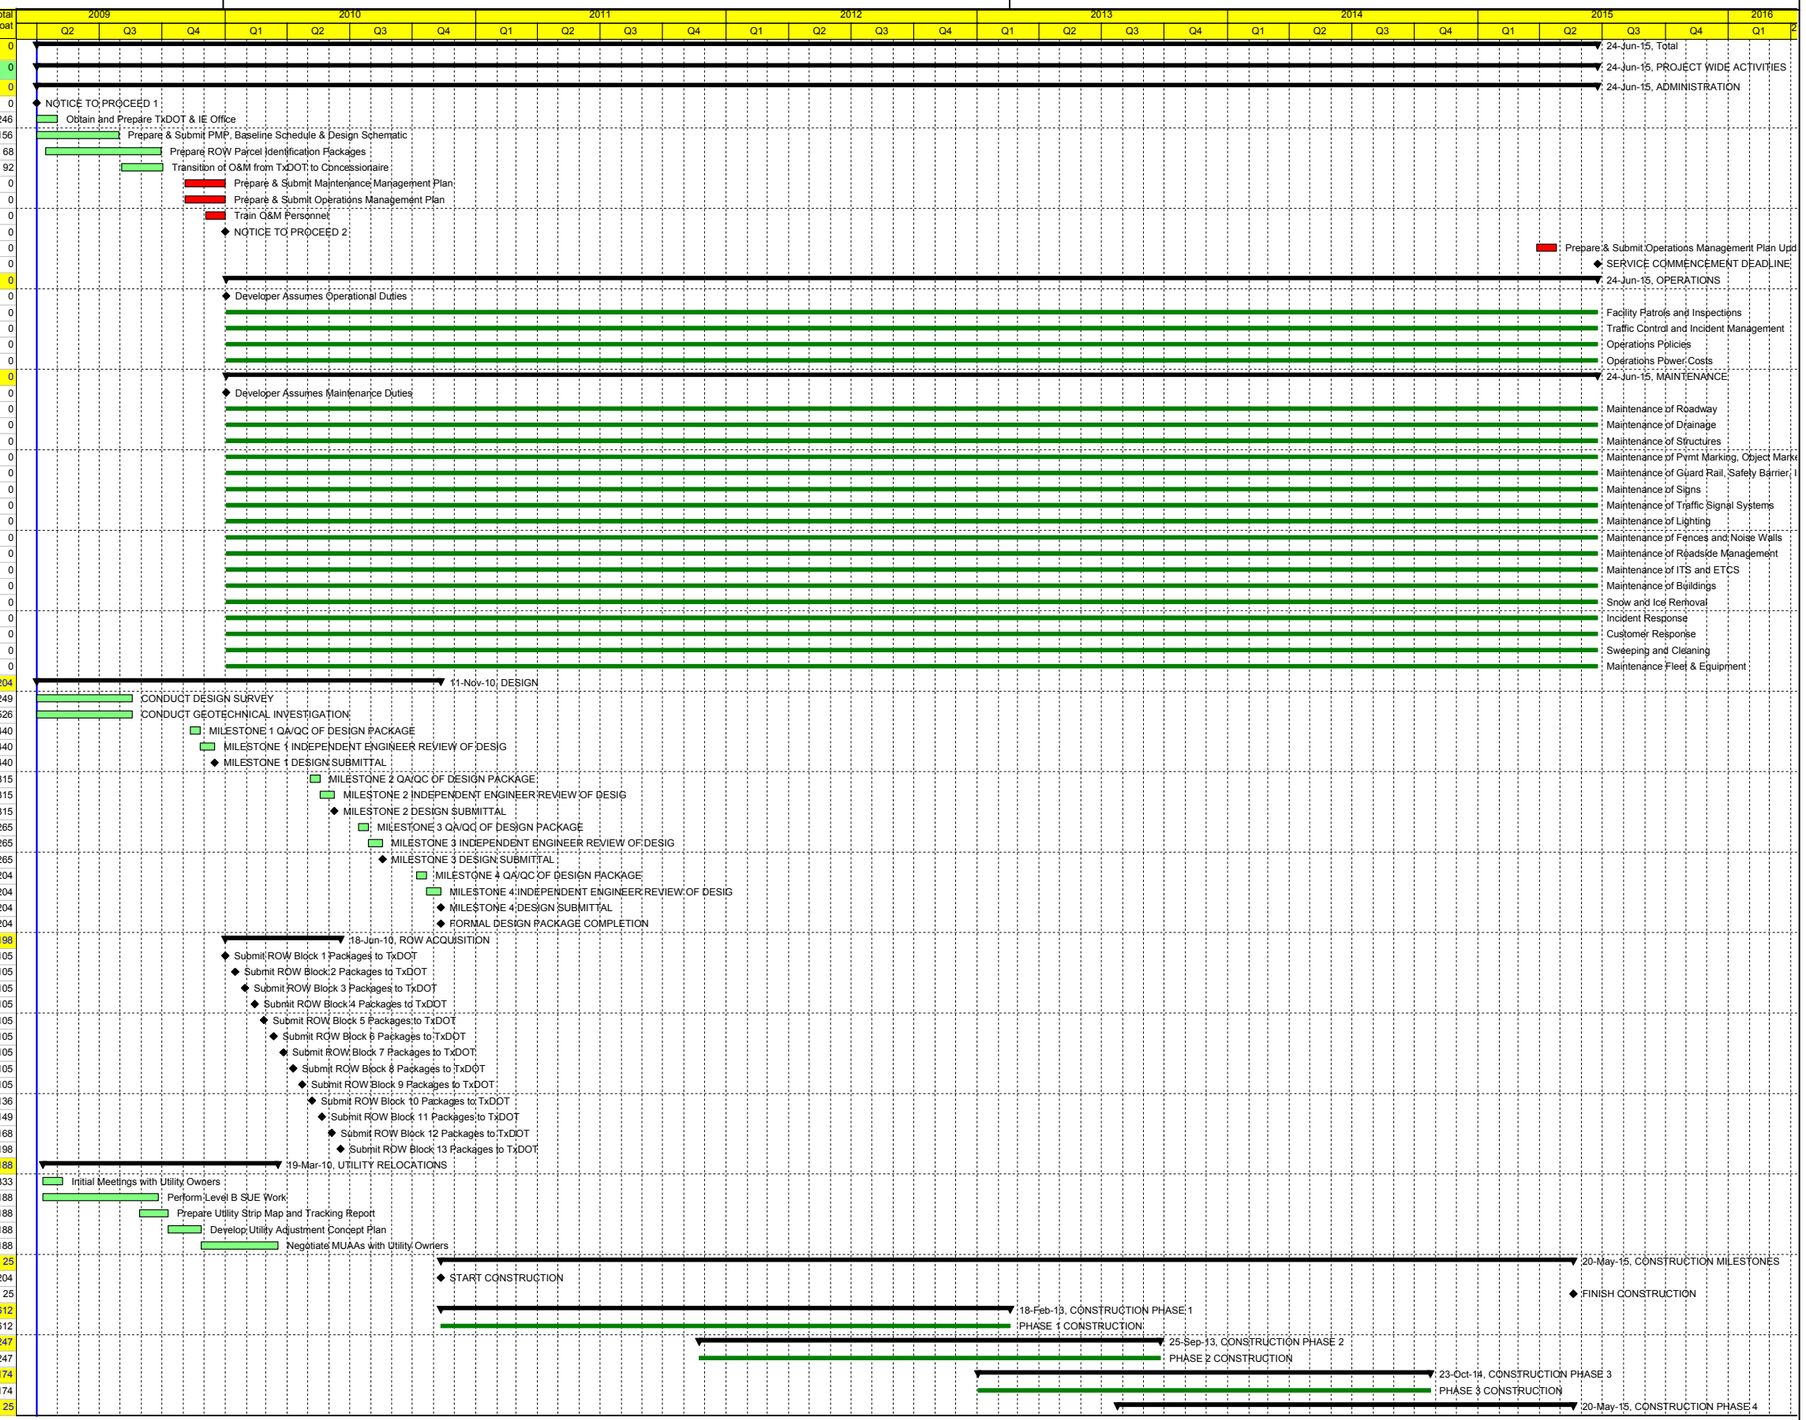

Remaining Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.5	0040	PHASE 4 CONSTRUCTION	475	24-Jul-13	20-May-15	25
Segment 1A - IH 35W / IH 820 Interchange			1120	29-Jul-09	13-Nov-13	420
DESIGN			303	29-Jul-09	27-Sep-10	212
1.2.1.2	1A0D1201	DEVELOP SEGMENT 1A ENVIRONMENTA...	150	29-Jul-09	24-Feb-10	316
1.2.2.2	1A0D1202	DEVELOP SEGMENT 1A ROADWAY DESIG...	275	29-Jul-09	18-Aug-10	212
1.2.4.2	1A0D1241	DEVELOP SEGMENT 1A STRUCTURES DE...	300	29-Jul-09	22-Sep-10	215
1.2.3.2	1A0D1203	DEVELOP SEGMENT 1A DRAINAGE DESI...	288	19-Aug-...	27-Sep-10	212
1.2.4.2	1A0D1242	DEVELOP SEGMENT 1A STRUCTURES DE...	200	17-Sep-...	24-Jun-10	204
1.2.9.2	1A0D1209	DEVELOP SEGMENT 1A TRAFFIC MGMT &...	198	28-Oct-09	02-Aug-10	250
1.2.8.2	1A0D1208	DEVELOP SEGMENT 1A ITS DESIGN (OPTI...	14	28-Dec-...	14-Jan-10	258
1.2.7.2	1A0D1271	DEVELOP SEGMENT 1A TRAFFIC DESIGN...	79	28-Dec-...	15-Apr-10	258
1.2.7.2	1A0D1272	DEVELOP SEGMENT 1A TRAFFIC DESIGN...	79	28-Dec-...	15-Apr-10	258
1.2.7.2	1A0D1273	DEVELOP SEGMENT 1A TRAFFIC DESIG...	79	28-Dec-...	15-Apr-10	258
1.2.6.2	1A0D1206	DEVELOP SEGMENT 1A LANDSCAPE & A...	63	15-Feb-10	12-May-10	273
1.2.10.0	1B0D1210	DEVELOP SEGMENT 1B TOLLING DESIGN	100	15-Feb-10	02-Jul-10	273
ROW ACQUISITION			320	01-Jan-10	25-Mar-11	1108
1.3.2	1AR0P1610R00	Parcel 161, Initiate Aquisition	0	01-Jan-10		1148
1.3.2	1AR0P1660R00	Parcel 166, Initiate Aquisition	0	01-Jan-10		1148
1.3.2	1AR0P1670R00	Parcel 167, Initiate Aquisition	0	01-Jan-10		1148
1.3.2	1AR0P1680R00	Parcel 168, Initiate Aquisition	0	01-Jan-10		1148
1.3.2	1AR0P1710R00	Parcel 171, Initiate Aquisition	0	01-Jan-10		208
1.3.2	1AR0P1720R00	Parcel 172, Initiate Aquisition	0	01-Jan-10		208
1.3.2	1AR0P1810R00	Parcel 181, Initiate Aquisition	0	01-Jan-10		468
1.3.2	1AR0P1820R00	Parcel 182, Initiate Aquisition	0	01-Jan-10		251
1.3.2	1AR0P1830R00	Parcel 183, Initiate Aquisition	0	01-Jan-10		251
1.3.2	1AR0P1700R00	Parcel 170, Initiate Aquisition	0	01-Jan-10		428
1.3.2	1AR0P1610R10	Parcel 161, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	1148
1.3.2	1AR0P1660R10	Parcel 166, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	1148
1.3.2	1AR0P1670R10	Parcel 167, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	1148
1.3.2	1AR0P1680R10	Parcel 168, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	1148
1.3.2	1AR0P1710R10	Parcel 171, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	208
1.3.2	1AR0P1720R10	Parcel 172, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	208
1.3.2	1AR0P1810R10	Parcel 181, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	468
1.3.2	1AR0P1820R10	Parcel 182, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	251
1.3.2	1AR0P1830R10	Parcel 183, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	251
1.3.2	1AR0P1700R10	Parcel 170, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	428
1.3.2	1AR0P1610R20	Parcel 161, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	1148
1.3.2	1AR0P1660R20	Parcel 166, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	1148
1.3.2	1AR0P1670R20	Parcel 167, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	1148
1.3.2	1AR0P1680R20	Parcel 168, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	1148
1.3.2	1AR0P1710R20	Parcel 171, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	208
1.3.2	1AR0P1720R20	Parcel 172, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	208
1.3.2	1AR0P1810R20	Parcel 181, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	468
1.3.2	1AR0P1820R20	Parcel 182, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	251
1.3.2	1AR0P1830R20	Parcel 183, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	251
1.3.2	1AR0P1700R20	Parcel 170, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	428
1.3.2	1AR0P1610R30	Parcel 161, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	1148
1.3.2	1AR0P1660R30	Parcel 166, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	1148
1.3.2	1AR0P1670R30	Parcel 167, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	1148
1.3.2	1AR0P1680R30	Parcel 168, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	1148
1.3.2	1AR0P1710R30	Parcel 171, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	208
1.3.2	1AR0P1720R30	Parcel 172, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	208
1.3.2	1AR0P1810R30	Parcel 181, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	468
1.3.2	1AR0P1820R30	Parcel 182, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	251
1.3.2	1AR0P1830R30	Parcel 183, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	251
1.3.2	1AR0P1700R30	Parcel 170, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	428
1.3.2	1AR0P1610R40	Parcel 161, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	1148
1.3.2	1AR0P1660R40	Parcel 166, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	1148
1.3.2	1AR0P1670R40	Parcel 167, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	1148
1.3.2	1AR0P1680R40	Parcel 168, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	1148
1.3.2	1AR0P1710R40	Parcel 171, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	208
1.3.2	1AR0P1720R40	Parcel 172, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	208
1.3.2	1AR0P1810R40	Parcel 181, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	468
1.3.2	1AR0P1820R40	Parcel 182, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	251
1.3.2	1AR0P1830R40	Parcel 183, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	251
1.3.2	1AR0P1700R40	Parcel 170, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	428
1.3.2	1AR0P1700R50	Parcel 170, Prepare for Relocation	60	02-Jul-10	24-Sep-10	518
1.3.2	1AR0P1610R60	Parcel 161, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	1148
1.3.2	1AR0P1660R60	Parcel 166, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	1148
1.3.2	1AR0P1670R60	Parcel 167, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	1148
1.3.2	1AR0P1680R60	Parcel 168, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	1148
1.3.2	1AR0P1710R60	Parcel 171, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	208
1.3.2	1AR0P1720R60	Parcel 172, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	208
1.3.2	1AR0P1810R60	Parcel 181, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	468
1.3.2	1AR0P1820R60	Parcel 182, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	251
1.3.2	1AR0P1830R60	Parcel 183, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	251
1.3.2	1AR0P1700R60	Parcel 170, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	428
1.3.2	1AR0P1610R99	Parcel 161, Cleared for Construction	0		28-Jan-11	1148
1.3.2	1AR0P1660R99	Parcel 166, Cleared for Construction	0		28-Jan-11	1148
1.3.2	1AR0P1670R99	Parcel 167, Cleared for Construction	0		28-Jan-11	1148
1.3.2	1AR0P1680R99	Parcel 168, Cleared for Construction	0		28-Jan-11	1148
1.3.2	1AR0P1710R99	Parcel 171, Cleared for Construction	0		28-Jan-11	208
1.3.2	1AR0P1720R99	Parcel 172, Cleared for Construction	0		28-Jan-11	208
1.3.2	1AR0P1810R99	Parcel 181, Cleared for Construction	0		28-Jan-11	468
1.3.2	1AR0P1820R99	Parcel 182, Cleared for Construction	0		28-Jan-11	251

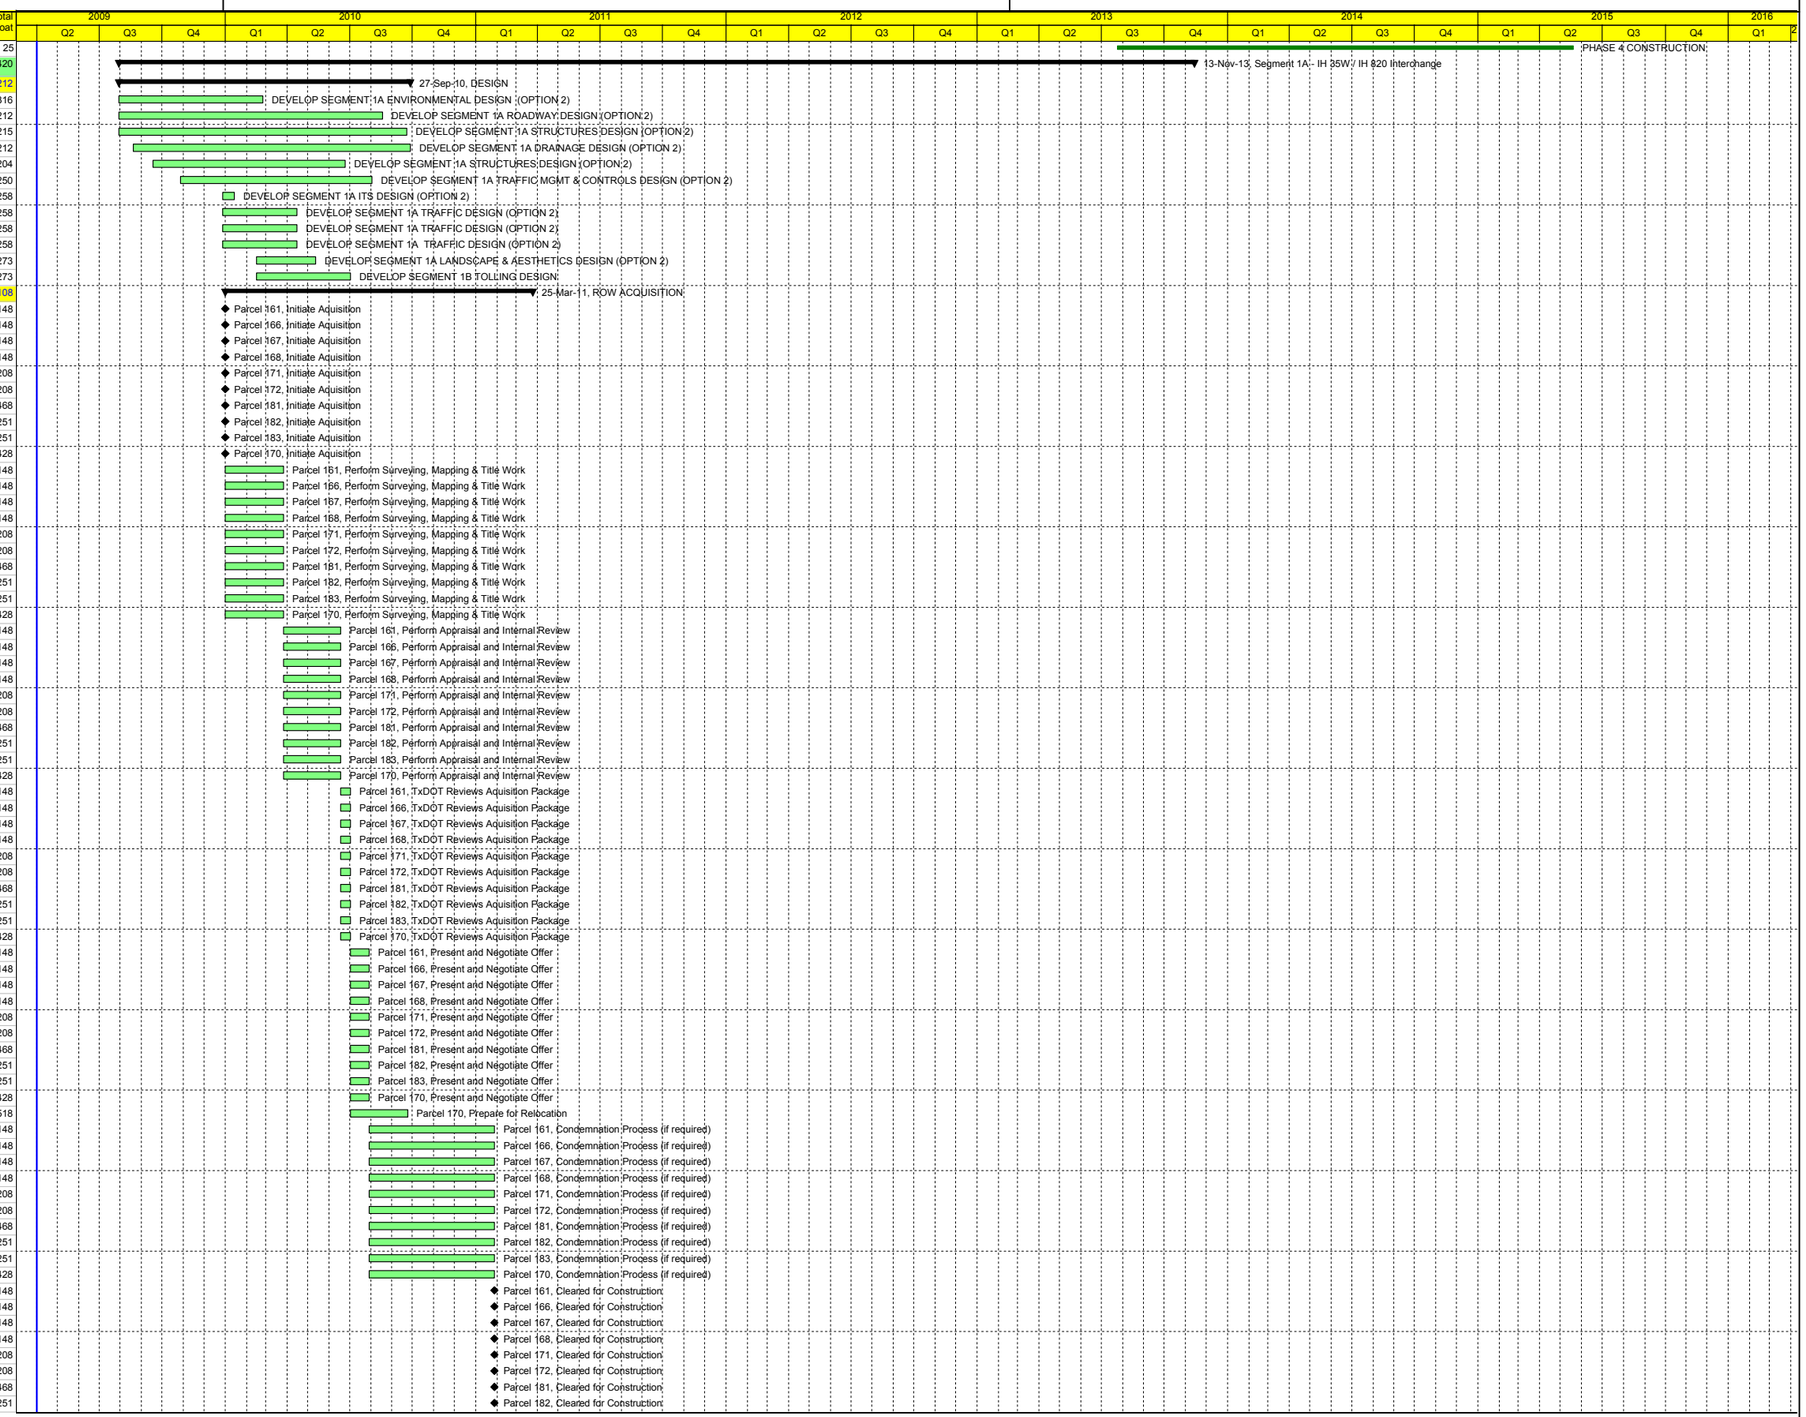

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.3.2	1AR0P1830R99	Parcel 183, Cleared for Construction	0		28-Jan-11	251
1.3.2	1AR0P1700R70	Parcel 170, Execute Relocation	20	28-Jan-11	25-Feb-11	428
1.3.2	1AR0P1700R80	Parcel 170, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	428
1.3.2	1AR0P1700R99	Parcel 170, Cleared for Construction	0		25-Mar-11	428
UTILITY RELOCATIONS			273	19-Mar-10	06-Apr-11	251
1.4.E2	1A2UE02UAA	Prep Assembly, Seg 1A Electric, Fort Worth (...	20	19-Mar-10	16-Apr-10	411
1.4.W2	1A2UW02UAA	Prep Assembly, Seg 1A Water , Fort Worth (...	20	19-Mar-10	16-Apr-10	403
1.4.G1	1A2UG01UAA	Prep Assembly, Seg 1A Gas/Petro, Citgo (Op...	20	19-Mar-10	16-Apr-10	446
1.4.E2	1A2UE02TX	TxDOT Review, Seg 1A Electric, Fort Worth (...	10	16-Apr-10	30-Apr-10	411
1.4.W2	1A2UW02TX	TxDOT Review, Seg 1A Water , Fort Worth (...	10	16-Apr-10	30-Apr-10	403
1.4.G1	1A2UG01TX	TxDOT Review, Seg 1A Gas/Petro, Citgo (Op...	10	16-Apr-10	30-Apr-10	446
1.4.E2	1A2UE02	Seg 1A, Relocate Electric, Fort Worth (Opt 2)	38	28-Jan-11	23-Mar-11	216
1.4.W2	1A2UW02	Seg 1A, Relocate Water , Fort Worth (Opt 2)	46	28-Jan-11	04-Apr-11	208
1.4.G1	1A2UG01	Seg 1A, Relocate Gas/Petro, Citgo (Opt 2)	48	28-Jan-11	06-Apr-11	251
CONSTRUCTION MILESTONES			784	11-Nov-...	13-Nov-13	420
1.5	1A00ML20000001	START Managed Lanes - IH 35W (Opt 2)	0	11-Nov-...		921
1.5	1A00SG20000001	START SB General Purpose Lanes - IH 35W...	0	11-Nov-...		623
1.5	1A00SG20099999	FINISH SB General Purpose Lanes - IH 35W...	0		10-Feb-11	1139
1.5	1A00EG30000001	START EB General Purpose Lanes - IH 35W...	0	04-Apr-11		1102
1.5	1A00NF30000001	START NB Frontage Roads - IH 35W Interch...	0	04-Apr-11		1102
1.5	1A00NF20000001	START NB Frontage Road - IH 35W (Opt 2)	0	06-Apr-11		420
1.5	1A00NG20000001	START NB General Purpose Lanes - IH 35W...	0	06-Apr-11		1012
1.5	1A00RP20000001	START Ramps - IH 35W (Opt 2)	0	06-Apr-11		540
1.5	1A00RP30000001	START Ramps - IH 35W Interchange	0	06-Apr-11		1100
1.5	1A00NM30000001	START NB/SB Managed Lanes - IH 35W Int...	0	06-Apr-11		1100
1.5	1A00SF30000001	START SB Frontage Roads - IH 35W Interch...	0	06-Apr-11		1100
1.5	1A00SG30000001	START SB General Purpose Lanes - IH 35W...	0	06-Apr-11		1100
1.5	1A00WG300000...	START WB General Purpose Lanes - IH 35...	0	24-May...		1066
1.5	1A00NF20099999	FINISH NB Frontage Road - IH 35W (Opt 2)	0		22-Nov-11	936
1.5	1A00EM30000001	START EB/WB Managed Lanes - IH 35W Int...	0	03-May...		819
1.5	1A00ML20099999	FINISH Managed Lanes - IH 35W (Opt 2)	0		09-May-13	554
1.5	1A00NG20099999	FINISH NB General Purpose Lanes - IH 35W...	0		29-May-13	540
1.5	1A00RP20099999	FINISH Ramps - IH 35W (Opt 2)	0		13-Nov-13	420
1.5	1A00	SUBSEGMENT 1A CONSTRUCTION	784	11-Nov-...	13-Nov-13	420
CONSTRUCTION PHASE 1			268	11-Nov-...	22-Nov-11	420
1.5	1A10SG20000001	Area SG2, PH 1, Start	0	11-Nov-...		623
1.5.2.2	1A10SG20050600	Area SG2, PH 1, Place Temp Erosion Control	3	11-Nov-...	16-Nov-10	623
1.5.2.2	1A10SG20010410	Area SG2, PH 1, Rem Conc Pavement	2	16-Nov-...	18-Nov-10	623
1.5.2.2	1A10SG20013210	Area SG2, PH 1, Place Embankment	6	18-Nov-...	26-Nov-10	641
1.5.2.2	1A10SG20011010	Area SG2, PH 1, Excavate Cut Areas	9	18-Nov-...	01-Dec-10	638
1.5.3.2	1A10SG20046230	Area SG2, PH 1, Install Large CBC	13	18-Nov-...	07-Dec-10	623
1.5.7.2	1A10SG20061320	Area SG2, PH 1, Install High Mast Illumination	9	01-Dec-...	14-Dec-10	659
1.5.2.2	1A10SG20026010	Area SG2, PH 1, Lime Treat Subgrade	15	01-Dec-...	22-Dec-10	639
1.5.3.2	1A10SG20046220	Area SG2, PH 1, Install Medium CBC	9	07-Dec-...	20-Dec-10	623
1.5.3.2	1A10SG20046210	Area SG2, PH 1, Install Small CBC	1	20-Dec-...	21-Dec-10	623
1.5.3.2	1A10SG20046420	Area SG2, PH 1, Install Medium RCP	1	21-Dec-...	22-Dec-10	623
1.5.8.2	1A10SG20061899	Area SG2, PH 1, Install ITS Duct Bank	2	22-Dec-...	24-Dec-10	640
1.5.3.2	1A10SG20046410	Area SG2, PH 1, Install Small RCP	10	22-Dec-...	05-Jan-11	623
1.5.8.2	1A10SG20041699	Area SG2, PH 1, Install ITS Structures & Equip	11	24-Dec-...	10-Jan-11	640
1.5.3.2	1A10SG20046510	Area SG2, PH 1, Install MHs and Inlets	6	05-Jan-11	13-Jan-11	623
1.5.2.2	1A10SG20024711	Area SG2, PH 1, Place Flexible Base	4	13-Jan-11	19-Jan-11	623
1.5.2.2	1A10SG20034012	Area SG2, PH 1, Place HMA Base	4	19-Jan-11	25-Jan-11	623
1.5.9.2	1A10SG20066200	Area SG2, PH 1, Place Temp Marking & Sig...	1	25-Jan-11	26-Jan-11	634
1.5.2.2	1A10SG20045010	Area SG2, PH 1, Place Conc Rail (Ret Wall)	2	25-Jan-11	27-Jan-11	632
1.5.7.2	1A10SG20065010	Area SG2, PH 1, Install OH Sign Structures	6	25-Jan-11	02-Feb-11	623
1.5.2.2	1A10SG20034610	Area SG2, PH 1, Place SMA Surface	5	02-Feb-11	09-Feb-11	623
1.5.7.2	1A10SG20066610	Area SG2, PH 1, Install Perm Markings	1	09-Feb-11	10-Feb-11	623
1.5	1A10SG20099999	Area SG2, PH 1, Finish	0		10-Feb-11	623
1.5	1A10NF20000001	Area NF2, PH 1, Start	0	06-Apr-11		420
1.5	1A10RP20000001	Area RP2, PH 1, Start	0	06-Apr-11		540
1.5.2.2	1A10NF20050600	Area NF2, PH 1, Place Temp Erosion Control	17	06-Apr-11	29-Apr-11	420
1.5.4.2	1A10RP20042310	Area RP2, PH 1, Install Fill Wall Complete	32	06-Apr-11	20-May-11	540
1.5.2.2	1A10NF20010410	Area NF2, PH 1, Rem Conc Pavement	9	29-Apr-11	12-May-11	420
1.5.3.2	1A10NF20046220	Area NF2, PH 1, Install Medium CBC	1	12-May...	13-May-11	455
1.5.2.2	1A10NF20013210	Area NF2, PH 1, Place Embankment	33	12-May...	28-Jun-11	440
1.5.2.2	1A10NF20011010	Area NF2, PH 1, Excavate Cut Areas	53	12-May...	26-Jul-11	420
1.5.3.2	1A10NF20046210	Area NF2, PH 1, Install Small CBC	3	13-May...	18-May-11	455
1.5.3.2	1A10NF20046420	Area NF2, PH 1, Install Medium RCP	14	18-May...	07-Jun-11	455
1.5.4.2	1A10RP20042315	Area RP2, PH 1, Install Moment Slabs	12	20-May...	07-Jun-11	540
1.5	1A10RP20099999	Area RP2, PH 1, Finish	0		07-Jun-11	540
1.5.8.2	1A10NF20061899	Area NF2, PH 1, Install ITS Duct Bank	12	26-Jul-11	11-Aug-11	466
1.5.2.2	1A10NF20026010	Area NF2, PH 1, Lime Treat Subgrade	16	26-Jul-11	17-Aug-11	446
1.5.3.2	1A10NF20046410	Area NF2, PH 1, Install Small RCP	26	26-Jul-11	31-Aug-11	420
1.5.3.2	1A10NF20046510	Area NF2, PH 1, Install MHs and Inlets	16	31-Aug-...	22-Sep-11	420
1.5.2.2	1A10NF20024711	Area NF2, PH 1, Place Flexible Base	7	22-Sep-...	03-Oct-11	420
1.5.2.2	1A10NF20034011	Area NF2, PH 1, Place HMA Base	9	03-Oct-11	14-Oct-11	420
1.5.9.2	1A10NF20066200	Area NF2, PH 1, Place Temp Marking & Sign...	1	14-Oct-11	17-Oct-11	446
1.5.2.2	1A10NF20045010	Area NF2, PH 1, Place Conc Rail (Ret Wall)	10	14-Oct-11	28-Oct-11	436
1.5.2.2	1A10NF20043210	Area NF2, PH 1, Place Conc RipRap	17	14-Oct-11	08-Nov-11	420
1.5.2.2	1A10NF20034610	Area NF2, PH 1, Place SMA Surface	9	08-Nov-...	21-Nov-11	420
1.5.7.2	1A10NF20066610	Area NF2, PH 1, Install Perm Markings	1	21-Nov-...	22-Nov-11	420
1.5	1A10NF20099999	Area NF2, PH 1, Finish	0		22-Nov-11	420
1.5	1A100000000001	START PHASE 1, SUBSEGMENT 1A	0	11-Nov-...		524
1.5	1A100000099999	FINISH PHASE 1, SUBSEGMENT 1A	0		22-Nov-11	420
CONSTRUCTION PHASE 2			308	22-Nov-...	25-Jan-13	420
1.5	1A20ML20000001	Area ML2, PH 2, Start	0	22-Nov-...		653

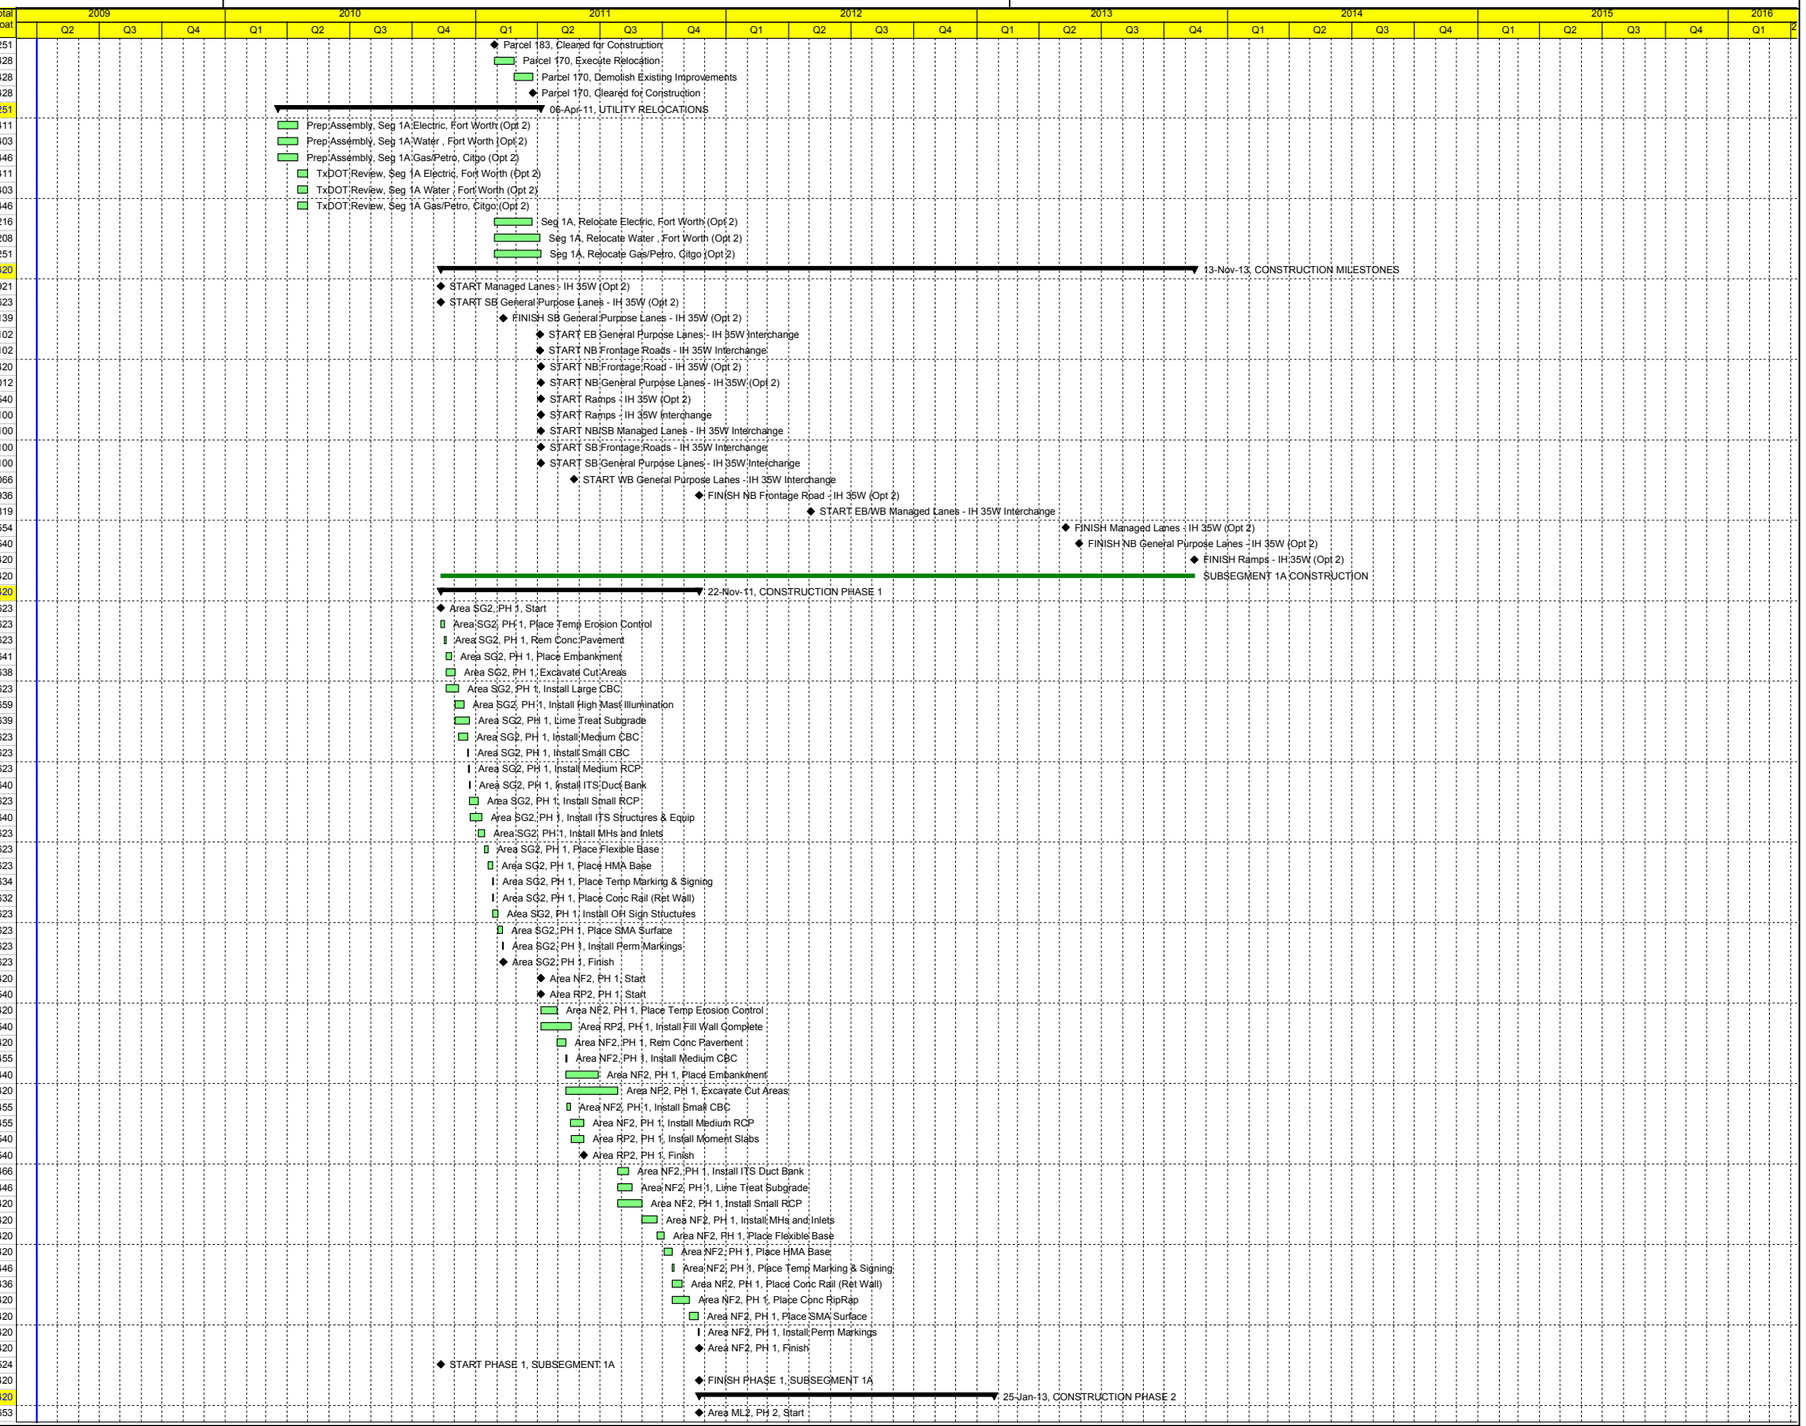

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.5	1A20RP20000001	Area RP2, PH 2, Start	0	22-Nov-...		420
1.5.3.2	1A20ML20046420	Area ML2, PH 2, Install Medium RCP	2	22-Nov-...	24-Nov-11	693
1.5.2.2	1A20RP20010410	Area RP2, PH 2, Rem Conc Pavement	4	22-Nov-...	28-Nov-11	654
1.5.2.2	1A20ML20013210	Area ML2, PH 2, Place Embankment	13	22-Nov-...	09-Dec-11	661
1.5.2.2	1A20ML20011010	Area ML2, PH 2, Excavate Cut Areas	21	22-Nov-...	21-Dec-11	653
1.5.2.2	1A20RP20013210	Area RP2, PH 2, Place Embankment	14	28-Nov-...	16-Dec-11	661
1.5.4.2	1A20RP20042310	Area RP2, PH 2, Install Fill Wall Complete	15	28-Nov-...	19-Dec-11	661
1.5.2.2	1A20RP20011010	Area RP2, PH 2, Excavate Cut Areas	22	28-Nov-...	28-Dec-11	654
1.5.3.2	1A20ML20046410	Area ML2, PH 2, Install Small RCP	3	21-Dec-...	26-Dec-11	674
1.5.2.2	1A20ML20026010	Area ML2, PH 2, Lime Treat Subgrade	27	21-Dec-...	27-Jan-12	653
1.5.3.2	1A20ML20046510	Area ML2, PH 2, Install MHs and Inlets	3	26-Dec-...	29-Dec-11	674
1.5.8.2	1A20RP20061899	Area RP2, PH 2, Install ITS Duct Bank	2	28-Dec-...	30-Dec-11	679
1.5.3.2	1A20RP20046510	Area RP2, PH 2, Install MHs and Inlets	5	28-Dec-...	04-Jan-12	667
1.5.2.2	1A20RP20026010	Area RP2, PH 2, Lime Treat Subgrade	13	28-Dec-...	16-Jan-12	654
1.5.2.2	1A20RP20024711	Area RP2, PH 2, Place Flexible Base	3	16-Jan-12	19-Jan-12	659
1.5.4.2	1A20RP20042315	Area RP2, PH 2, Install Moment Slabs	8	16-Jan-12	26-Jan-12	654
1.5.2.2	1A20RP20034012	Area RP2, PH 2, Place HMA Base	4	26-Jan-12	01-Feb-12	654
1.5.10.2	1A20RP20041698	Area RP2, PH 2, Install Tolling Systems	21	26-Jan-12	24-Feb-12	660
1.5.2.2	1A20ML20024710	Area ML2, PH 2, Place Flexible Base	5	27-Jan-12	03-Feb-12	653
1.5.2.2	1A20RP20045010	Area RP2, PH 2, Place Conc Rail (Ret Wall)	4	01-Feb-12	07-Feb-12	672
1.5.7.2	1A20RP20065010	Area RP2, PH 2, Install OH Sign Structures	11	01-Feb-12	16-Feb-12	654
1.5.2.2	1A20ML20034010	Area ML2, PH 2, Place HMA Base	7	03-Feb-12	14-Feb-12	653
1.5.2.2	1A20ML20045010	Area ML2, PH 2, Place Conc Rail (Ret Wall)	4	14-Feb-12	20-Feb-12	663
1.5.7.2	1A20ML20065010	Area ML2, PH 2, Install OH Sign Structures	6	14-Feb-12	22-Feb-12	653
1.5.2.2	1A20RP20043210	Area RP2, PH 2, Place Conc RipRap	7	16-Feb-12	27-Feb-12	654
1.5.2.2	1A20ML20034610	Area ML2, PH 2, Place SMA Surface	8	22-Feb-12	05-Mar-12	653
1.5.2.2	1A20RP20034610	Area RP2, PH 2, Place SMA Surface	4	27-Feb-12	02-Mar-12	654
1.5.7.2	1A20RP20066610	Area RP2, PH 2, Install Perm Markings	1	02-Mar-12	05-Mar-12	654
1.5.7.2	1A20ML20066610	Area ML2, PH 2, Install Perm Markings	1	05-Mar-12	06-Mar-12	653
1.5	1A20ML20099999	Area ML2, PH 2, Finish	0		06-Mar-12	653
1.5	1A20RP20099999	Area RP2, PH 2, Finish	0		25-Jan-13	420
1.5.4.2.1.19	1A20B019000001	BR 19, PH 2, Start	0	22-Nov-...		560
1.5.4.2.1.19	1A20B019041600	BR 19, PH 2, Install Drill Shafts	10	22-Nov-...	06-Dec-11	560
1.5.4.2.1.19	1A20B019042040	BR 19, PH 2, Install Abutments	2	06-Dec-...	08-Dec-11	639
1.5.4.2.1.19	1A20B019042010	BR 19, PH 2, Install Footings	34	06-Dec-...	23-Jan-12	560
1.5.4.2.1.19	1A20B019042020	BR 19, PH 2, Install Columns	51	26-Dec-...	06-Mar-12	560
1.5.4.2.1.19	1A20B019042030	BR 19, PH 2, Install Bent Caps	36	07-Feb-12	28-Mar-12	560
1.5.4.2.1.19	1A20B019042510	BR 19, PH 2, Install Conc Beams	7	28-Mar-12	06-Apr-12	560
1.5.4.2.1.19	1A20B019044210	BR 19, PH 2, Install Plate Girders	7	28-Mar-12	06-Apr-12	560
1.5.4.2.1.19	1A20B019045410	BR 19, PH 2, Install Exp Joints	3	06-Apr-12	11-Apr-12	560
1.5.4.2.1.19	1A20B019042210	BR 19, PH 2, Install Deck Slab	48	11-Apr-12	18-Jun-12	560
1.5.4.2.1.19	1A20B019042050	BR 19, PH 2, Install Apprch Slabs	5	18-Jun-12	25-Jun-12	565
1.5.4.2.1.19	1A20B019045020	BR 19, PH 2, Install Conc Rail	9	02-Jul-12	13-Jul-12	560
1.5.4.2.1.19	1A20B019099999	BR 19, PH 2, Finish	0		13-Jul-12	560
1.5.4.2.1.20	1A20B020000001	BR 20, PH 2, Start	0	22-Nov-...		420
1.5.4.2.1.20	1A20B020041600	BR 20, PH 2, Install Drill Shafts	10	22-Nov-...	06-Dec-11	420
1.5.4.2.1.20	1A20B020042040	BR 20, PH 2, Install Abutments	2	06-Dec-...	08-Dec-11	602
1.5.4.2.1.20	1A20B020042010	BR 20, PH 2, Install Footings	69	06-Dec-...	12-Mar-12	420
1.5.4.2.1.20	1A20B020042020	BR 20, PH 2, Install Columns	60	12-Mar-12	04-Jun-12	420
1.5.4.2.1.20	1A20B020042030	BR 20, PH 2, Install Bent Caps	55	04-Jun-12	20-Aug-12	420
1.5.4.2.1.20	1A20B020044210	BR 20, PH 2, Install Plate Girders	7	20-Aug-...	29-Aug-12	423
1.5.4.2.1.20	1A20B020042510	BR 20, PH 2, Install Conc Beams	10	20-Aug-...	03-Sep-12	420
1.5.4.2.1.20	1A20B020045410	BR 20, PH 2, Install Exp Joints	4	03-Sep-...	07-Sep-12	420
1.5.4.2.1.20	1A20B020042210	BR 20, PH 2, Install Deck Slab	74	07-Sep-...	20-Dec-12	420
1.5.4.2.1.20	1A20B020042050	BR 20, PH 2, Install Apprch Slabs	4	20-Dec-...	26-Dec-12	426
1.5.4.2.1.20	1A20B020045020	BR 20, PH 2, Install Conc Rail	16	03-Jan-13	25-Jan-13	420
1.5.4.2.1.20	1A20B020099999	BR 20, PH 2, Finish	0		25-Jan-13	420
1.5.4.2.1.32A	1A20B032A00001	BR 32A, PH 2, Start	0	22-Nov-...		667
1.5.4.2.1.32A	1A20B032A49610	BR 32A, PH 2, Demo Extg Bridge	3	22-Nov-...	25-Nov-11	667
1.5.4.2.1.32A	1A20B032A41600	BR 32A, PH 2, Install Drill Shafts	2	25-Nov-...	29-Nov-11	667
1.5.4.2.1.32A	1A20B032A42020	BR 32A, PH 2, Install Columns	2	29-Nov-...	01-Dec-11	669
1.5.4.2.1.32A	1A20B032A42040	BR 32A, PH 2, Install Abutments	7	29-Nov-...	08-Dec-11	667
1.5.4.2.1.32A	1A20B032A42030	BR 32A, PH 2, Install Bent Caps	3	01-Dec-...	06-Dec-11	669
1.5.4.2.1.32A	1A20B032A42510	BR 32A, PH 2, Install Conc Beams	1	08-Dec-...	09-Dec-11	667
1.5.4.2.1.32A	1A20B032A45410	BR 32A, PH 2, Install Exp Joints	2	09-Dec-...	13-Dec-11	667
1.5.4.2.1.32A	1A20B032A42210	BR 32A, PH 2, Install Deck Slab	10	13-Dec-...	27-Dec-11	667
1.5.4.2.1.32A	1A20B032A42050	BR 32A, PH 2, Install Apprch Slabs	35	27-Dec-...	14-Feb-12	667
1.5.4.2.1.32A	1A20B032A45020	BR 32A, PH 2, Install Conc Rail	1	14-Feb-12	15-Feb-12	667
1.5.4.2.1.32A	1A20B032A99999	BR 32A, PH 2, Finish	0		15-Feb-12	667
1.5	1A200000000001	START PHASE 2, SUBSEGMENT 1A	0	22-Nov-...		420
1.5	1A200000099999	FINISH PHASE 2, SUBSEGMENT 1A	0		25-Jan-13	420
CONSTRUCTION PHASE 3			208	25-Jan-13	13-Nov-13	420
1.5	1A30NG20000001	Area NG2, PH 3, Start	0	25-Jan-13		540
1.5	1A30ML20000001	Area ML2, PH 3, Start	0	25-Jan-13		554
1.5	1A30RP20000001	Area RP2, PH 3, Start	0	25-Jan-13		420
1.5.3.2	1A30ML20046420	Area ML2, PH 3, Install Medium RCP	2	25-Jan-13	29-Jan-13	590
1.5.2.2	1A30RP20010410	Area RP2, PH 3, Rem Conc Pavement	2	25-Jan-13	29-Jan-13	565
1.5.2.2	1A30NG20050600	Area NG2, PH 3, Place Temp Erosion Control	5	25-Jan-13	01-Feb-13	540
1.5.2.2	1A30ML20013210	Area ML2, PH 3, Place Embankment	12	25-Jan-13	12-Feb-13	561
1.5.2.2	1A30ML20011010	Area ML2, PH 3, Excavate Cut Areas	19	25-Jan-13	21-Feb-13	554
1.5.4.2	1A30RP20042320	Area RP2, PH 3, Install Cut Wall, Stage 1	12	29-Jan-13	14-Feb-13	565
1.5.2.2	1A30NG20010410	Area NG2, PH 3, Rem Conc Pavement	2	01-Feb-13	05-Feb-13	540
1.5.2.2	1A30NG20013210	Area NG2, PH 3, Place Embankment	8	05-Feb-13	15-Feb-13	567
1.5.2.2	1A30NG20011010	Area NG2, PH 3, Excavate Cut Areas	13	05-Feb-13	22-Feb-13	562
1.5.3.2	1A30NG20046230	Area NG2, PH 3, Install Large CBC	19	05-Feb-13	04-Mar-13	540
1.5.2.2	1A30RP20013210	Area RP2, PH 3, Place Embankment	9	14-Feb-13	27-Feb-13	578

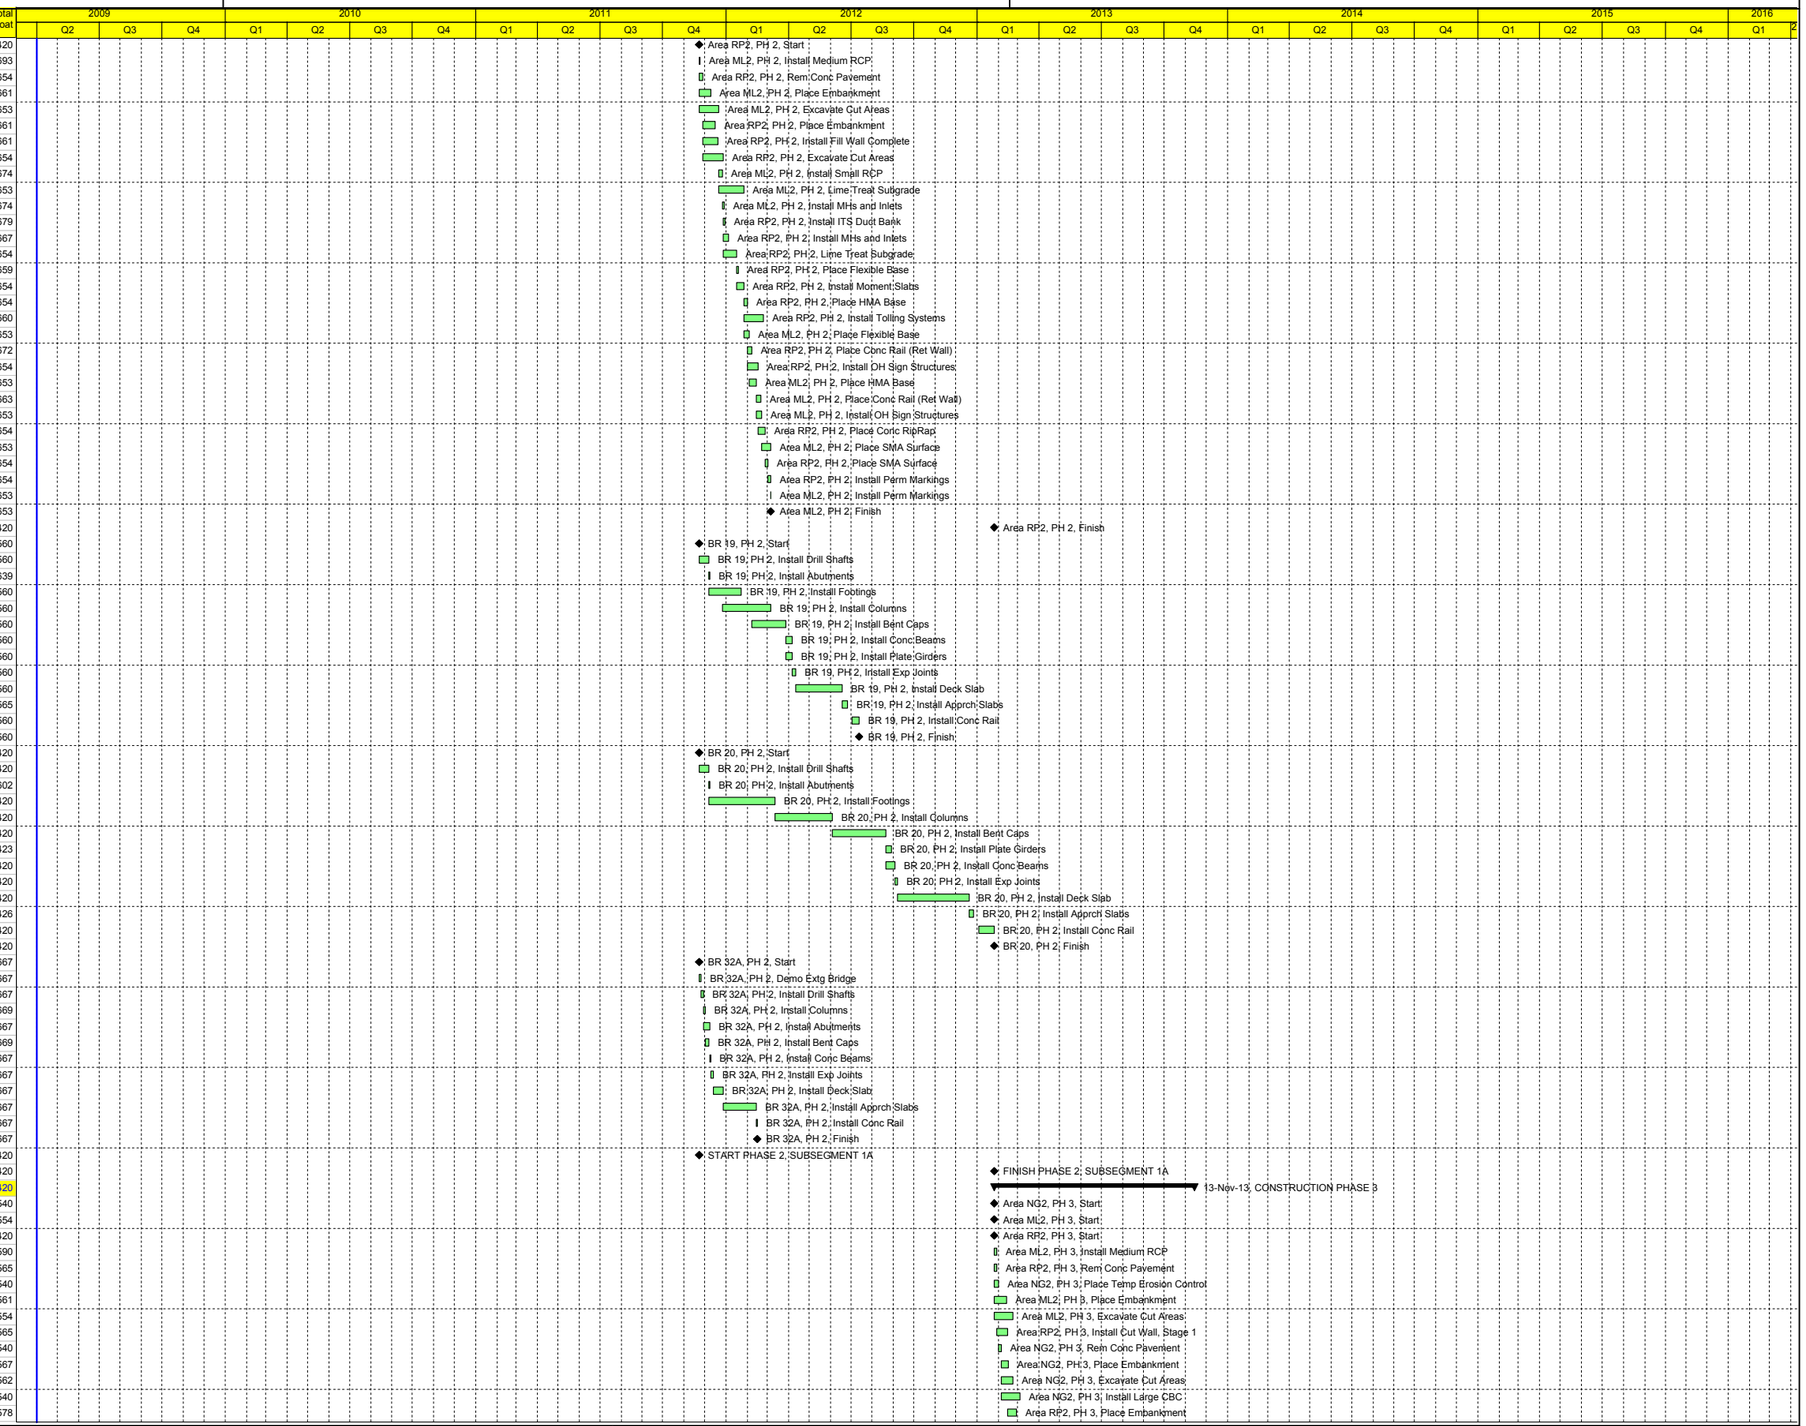

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.5.2.2	1A30RP20011010	Area RP2, PH 3, Excavate Cut Areas	14	14-Feb-13	06-Mar-13	565
1.5.3.2	1A30ML20046410	Area ML2, PH 3, Install Small RCP	3	21-Feb-13	26-Feb-13	573
1.5.2.2	1A30ML20026010	Area ML2, PH 3, Lime Treat Subgrade	25	21-Feb-13	28-Mar-13	554
1.5.7.2	1A30NG20061320	Area NG2, PH 3, Install High Mast Illumination	9	22-Feb-13	07-Mar-13	592
1.5.2.2	1A30NG20026010	Area NG2, PH 3, Lime Treat Subgrade	21	22-Feb-13	25-Mar-13	563
1.5.3.2	1A30ML20046510	Area ML2, PH 3, Install MHs and Inlets	3	26-Feb-13	01-Mar-13	573
1.5.3.2	1A30NG20046220	Area NG2, PH 3, Install Medium CBC	14	04-Mar-13	22-Mar-13	540
1.5.3.2	1A30RP20046510	Area RP2, PH 3, Install MHs and Inlets	3	06-Mar-13	11-Mar-13	578
1.5.2.2	1A30RP20026010	Area RP2, PH 3, Lime Treat Subgrade	8	06-Mar-13	18-Mar-13	573
1.5.4.2	1A30RP20042325	Area RP2, PH 3, Install Cut Wall, Stage 2	18	06-Mar-13	01-Apr-13	565
1.5.2.2	1A30RP20024711	Area RP2, PH 3, Place Flexible Base	2	18-Mar-13	20-Mar-13	573
1.5.3.2	1A30NG20046210	Area NG2, PH 3, Install Small CBC	1	22-Mar-13	25-Mar-13	540
1.5.3.2	1A30NG20046420	Area NG2, PH 3, Install Medium RCP	1	25-Mar-13	26-Mar-13	540
1.5.8.2	1A30NG20061899	Area NG2, PH 3, Install ITS Duct Bank	2	26-Mar-13	28-Mar-13	561
1.5.3.2	1A30NG20046410	Area NG2, PH 3, Install Small RCP	14	26-Mar-13	15-Apr-13	540
1.5.2.2	1A30ML20024710	Area ML2, PH 3, Place Flexible Base	5	28-Mar-13	04-Apr-13	554
1.5.8.2	1A30NG20041699	Area NG2, PH 3, Install ITS Structures & Equip	16	28-Mar-13	19-Apr-13	561
1.5.2.2	1A30RP20034012	Area RP2, PH 3, Place HMA Base	3	01-Apr-13	04-Apr-13	565
1.5.2.2	1A30RP20045010	Area RP2, PH 3, Place Conc Rail (Ret Wall)	3	04-Apr-13	09-Apr-13	575
1.5.2.2	1A30ML20034010	Area ML2, PH 3, Place HMA Base	6	04-Apr-13	12-Apr-13	554
1.5.7.2	1A30RP20065010	Area RP2, PH 3, Install OH Sign Structures	6	04-Apr-13	12-Apr-13	565
1.5.2.2	1A30ML20045010	Area ML2, PH 3, Place Conc Rail (Ret Wall)	4	12-Apr-13	18-Apr-13	568
1.5.2.2	1A30RP20043210	Area RP2, PH 3, Place Conc RipRap	4	12-Apr-13	18-Apr-13	565
1.5.7.2	1A30ML20065010	Area ML2, PH 3, Install OH Sign Structures	11	12-Apr-13	29-Apr-13	554
1.5.3.2	1A30NG20046510	Area NG2, PH 3, Install MHs and Inlets	8	15-Apr-13	25-Apr-13	540
1.5.2.2	1A30RP20034610	Area RP2, PH 3, Place SMA Surface	3	18-Apr-13	23-Apr-13	565
1.5.7.2	1A30RP20066610	Area RP2, PH 3, Install Perm Markings	1	23-Apr-13	24-Apr-13	565
1.5.2.2	1A30NG20024711	Area NG2, PH 3, Place Flexible Base	5	25-Apr-13	02-May-13	540
1.5.2.2	1A30ML20034610	Area ML2, PH 3, Place SMA Surface	7	29-Apr-13	08-May-13	554
1.5.2.2	1A30NG20034012	Area NG2, PH 3, Place HMA Base	6	02-May...	10-May-13	540
1.5.7.2	1A30ML20066610	Area ML2, PH 3, Install Perm Markings	1	08-May...	09-May-13	554
1.5	1A30ML20099999	Area ML2, PH 3, Finish	0		09-May-13	554
1.5.9.2	1A30NG20066200	Area NG2, PH 3, Place Temp Marking & Sig...	1	10-May...	13-May-13	552
1.5.2.2	1A30NG20045010	Area NG2, PH 3, Place Conc Rail (Ret Wall)	3	10-May...	15-May-13	549
1.5.7.2	1A30NG20065010	Area NG2, PH 3, Install OH Sign Structures	6	10-May...	20-May-13	540
1.5.2.2	1A30NG20034610	Area NG2, PH 3, Place SMA Surface	6	20-May...	28-May-13	540
1.5.7.2	1A30NG20066610	Area NG2, PH 3, Install Perm Markings	1	28-May...	29-May-13	540
1.5	1A30NG20099999	Area NG2, PH 3, Finish	0		29-May-13	540
1.5	1A30RP20099999	Area RP2, PH 3, Finish	0		13-Nov-13	420
1.5.4.2.1.19	1A30B019000001	BR 19, PH 3, Start	0	25-Jan-13		420
1.5.4.2.1.19	1A30B019041600	BR 19, PH 3, Install Drill Shafts	10	25-Jan-13	08-Feb-13	420
1.5.4.2.1.19	1A30B019042040	BR 19, PH 3, Install Abutments	2	08-Feb-13	12-Feb-13	539
1.5.4.2.1.19	1A30B019042010	BR 19, PH 3, Install Footings	34	08-Feb-13	28-Mar-13	420
1.5.4.2.1.19	1A30B019042020	BR 19, PH 3, Install Columns	51	28-Mar-13	07-Jun-13	420
1.5.4.2.1.19	1A30B019042030	BR 19, PH 3, Install Bent Caps	36	07-Jun-13	29-Jul-13	420
1.5.4.2.1.19	1A30B019042510	BR 19, PH 3, Install Conc Beams	7	29-Jul-13	07-Aug-13	420
1.5.4.2.1.19	1A30B019044210	BR 19, PH 3, Install Plate Girders	7	29-Jul-13	07-Aug-13	420
1.5.4.2.1.19	1A30B019045410	BR 19, PH 3, Install Exp Joints	3	07-Aug-...	12-Aug-13	420
1.5.4.2.1.19	1A30B019042210	BR 19, PH 3, Install Deck Slab	48	12-Aug-...	17-Oct-13	420
1.5.4.2.1.19	1A30B019042050	BR 19, PH 3, Install Apprch Slabs	5	17-Oct-13	24-Oct-13	425
1.5.4.2.1.19	1A30B019045020	BR 19, PH 3, Install Conc Rail	9	31-Oct-13	13-Nov-13	420
1.5.4.2.1.19	1A30B019099999	BR 19, PH 3, Finish	0		13-Nov-13	420
1.5	1A300000000001	START PHASE 3, SUBSEGMENT 1A	0	25-Jan-13		420
1.5	1A300000099999	FINISH PHASE 3, SUBSEGMENT 1A	0		13-Nov-13	420
CONSTRUCTION PHASE 4			0	13-Nov-...	13-Nov-13	420
1.5	1A400000000001	START PHASE 4, SUBSEGMENT 1A	0	13-Nov-...		420
1.5	1A400000099999	FINISH PHASE 4, SUBSEGMENT 1A	0		13-Nov-13	420
Segment 1B - IH 820 - IH 35W to Station 955			1601	01-Apr-09	20-May-15	25
DESIGN			354	19-May...	27-Sep-10	212
1.2.2.0	1B0D1202	DEVELOP SEGMENT 1B ROADWAY DESIGN	275	19-May...	08-Jun-10	266
1.2.1.0	1B0D1201	DEVELOP SEGMENT 1B ENVIRONMENTA...	151	29-Jul-09	25-Feb-10	364
1.2.3.0	1B0D1203	DEVELOP SEGMENT 1B DRAINAGE DESI...	275	07-Sep-...	27-Sep-10	212
1.2.9.0	1B0D1209	DEVELOP SEGMENT 1B TRAFFIC MGMT &...	200	28-Oct-09	04-Aug-10	250
1.2.4.0	1B0D1242	DEVELOP SEGMENT 1B STRUCTURES D...	153	23-Nov-...	24-Jun-10	279
1.2.5	1B0D1205	DEVELOP SEGMENT 1B RAILROAD DESIGN	150	16-Dec-...	14-Jul-10	265
1.2.4.0	1B0D1241	DEVELOP SEGMENT 1B STRUCTURES D...	200	16-Dec-...	22-Sep-10	215
1.2.8.0	1B0D1208	DEVELOP SEGMENT 1B ITS DESIGN	29	28-Dec-...	04-Feb-10	379
1.2.7.0	1B0D1271	DEVELOP SEGMENT 1B TRAFFIC DESIGN	129	28-Dec-...	24-Jun-10	258
1.2.7.0	1B0D1272	DEVELOP SEGMENT 1B TRAFFIC DESIGN	129	28-Dec-...	24-Jun-10	258
1.2.7.0	1B0D1273	DEVELOP SEGMENT 1B TRAFFIC DESIGN	129	28-Dec-...	24-Jun-10	258
1.2.10.2	1A0D1210	DEVELOP SEGMENT 1A TOLLING DESIGN...	100	15-Feb-10	02-Jul-10	273
1.2.6.0	1B0D1206	DEVELOP SEGMENT 1B LANDSCAPE & A...	55	25-Feb-10	12-May-10	310
ROW ACQUISITION			377	14-Oct-09	25-Mar-11	259
1.3.0	1BR0P1380R10	Parcel 138, Perform Surveying, Mapping & Ti...	60	14-Oct-09	06-Jan-10	82
1.3.0	1BR0P0260R10	Parcel 026, Perform Surveying, Mapping & Ti...	60	06-Nov-...	29-Jan-10	68
1.3.0	1BR0P0250R10	Parcel 025, Perform Surveying, Mapping & Ti...	60	16-Dec-...	10-Mar-10	118
1.3.0	1BR0P0030R00	Parcel 003, Initiate Aquisition	0	01-Jan-10		208
1.3.0	1BR0P0050R00	Parcel 005, Initiate Aquisition	0	01-Jan-10		106
1.3.0	1BR0P0060R00	Parcel 006, Initiate Aquisition	0	01-Jan-10		65
1.3.0	1BR0P0070R00	Parcel 007, Initiate Aquisition	0	01-Jan-10		65
1.3.0	1BR0P0080R00	Parcel 008, Initiate Aquisition	0	01-Jan-10		65
1.3.0	1BR0P0090R00	Parcel 009, Initiate Aquisition	0	01-Jan-10		65
1.3.0	1BR0P0130R00	Parcel 013, Initiate Aquisition	0	01-Jan-10		169
1.3.0	1BR0P0140R00	Parcel 014, Initiate Aquisition	0	01-Jan-10		169
1.3.0	1BR0P0160R00	Parcel 016, Initiate Aquisition	0	01-Jan-10		125

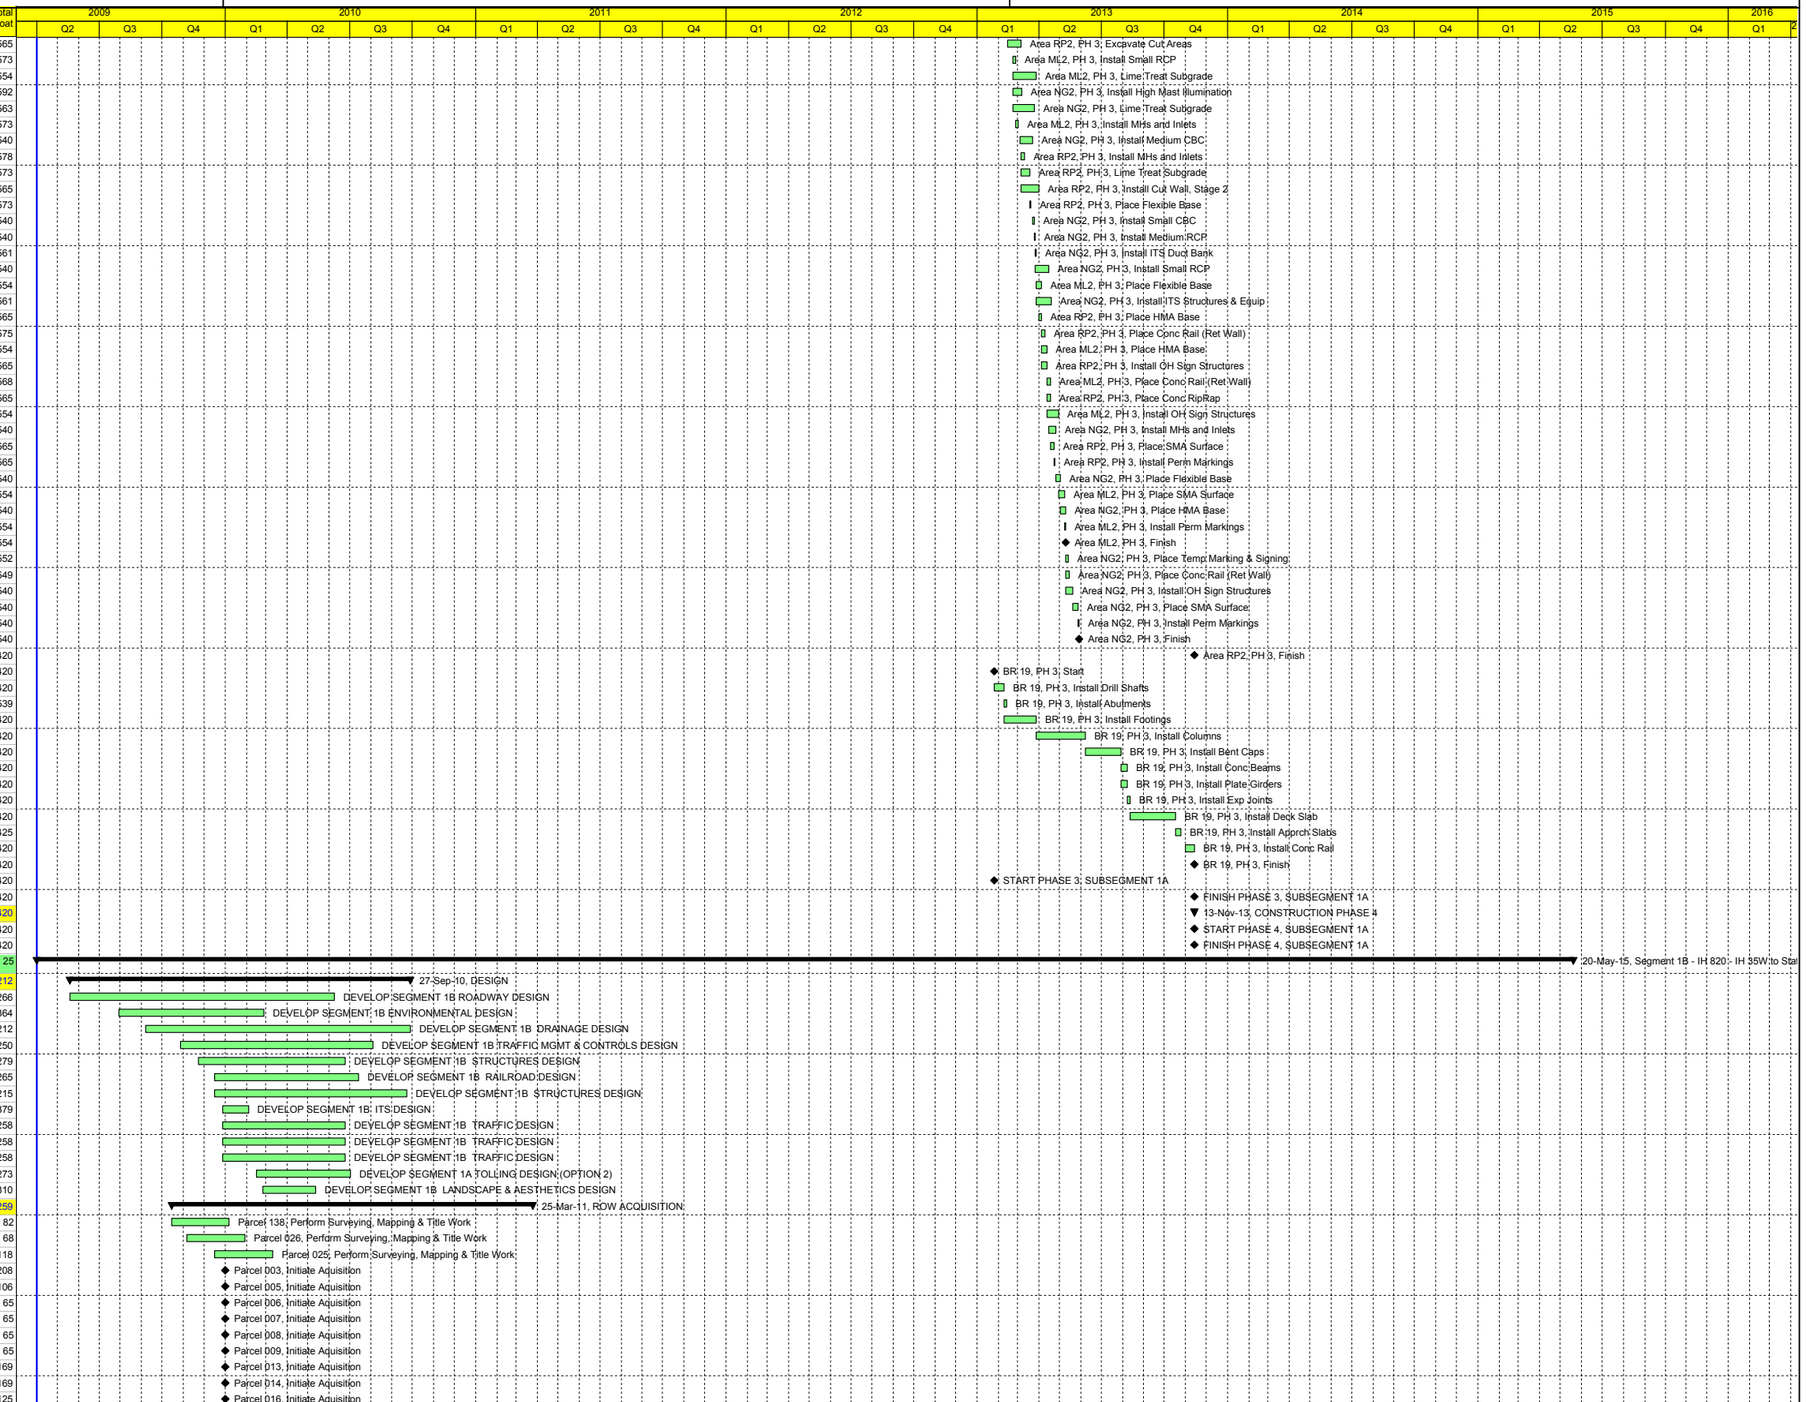

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.3.0	1BR0P0170R00	Parcel 017, Initiate Aquisition	0	01-Jan-10		106
1.3.0	1BR0P0190R00	Parcel 019, Initiate Aquisition	0	01-Jan-10		211
1.3.0	1BR0P0250R00	Parcel 025, Initiate Aquisition	0	01-Jan-10		118
1.3.0	1BR0P0280R00	Parcel 028, Initiate Aquisition	0	01-Jan-10		106
1.3.0	1BR0P0300R00	Parcel 030, Initiate Aquisition	0	01-Jan-10		106
1.3.0	1BR0P0310R00	Parcel 031, Initiate Aquisition	0	01-Jan-10		106
1.3.0	1BR0P0320R00	Parcel 032, Initiate Aquisition	0	01-Jan-10		106
1.3.0	1BR0P0330R00	Parcel 033, Initiate Aquisition	0	01-Jan-10		254
1.3.0	1BR0P0360R00	Parcel 036, Initiate Aquisition	0	01-Jan-10		254
1.3.0	1BR0P0390R00	Parcel 039, Initiate Aquisition	0	01-Jan-10		125
1.3.0	1BR0P0400R00	Parcel 040, Initiate Aquisition	0	01-Jan-10		254
1.3.0	1BR0P0510R00	Parcel 051, Initiate Aquisition	0	01-Jan-10		65
1.3.0	1BR0P0580R00	Parcel 058, Initiate Aquisition	0	01-Jan-10		65
1.3.0	1BR0P0590R00	Parcel 059, Initiate Aquisition	0	01-Jan-10		65
1.3.0	1BR0P0920R00	Parcel 092, Initiate Aquisition	0	01-Jan-10		174
1.3.0	1BR0P0940R00	Parcel 094, Initiate Aquisition	0	01-Jan-10		65
1.3.0	1BR0P0960R00	Parcel 096, Initiate Aquisition	0	01-Jan-10		174
1.3.0	1BR0P1000R00	Parcel 100, Initiate Aquisition	0	01-Jan-10		65
1.3.0	1BR0P1010R00	Parcel 101, Initiate Aquisition	0	01-Jan-10		65
1.3.0	1BR0P1030R00	Parcel 103, Initiate Aquisition	0	01-Jan-10		65
1.3.0	1BR0P1040R00	Parcel 104, Initiate Aquisition	0	01-Jan-10		65
1.3.0	1BR0P1050R00	Parcel 105, Initiate Aquisition	0	01-Jan-10		65
1.3.0	1BR0P1080R00	Parcel 108, Initiate Aquisition	0	01-Jan-10		112
1.3.0	1BR0P1100R00	Parcel 110, Initiate Aquisition	0	01-Jan-10		65
1.3.0	1BR0P1150R00	Parcel 115, Initiate Aquisition	0	01-Jan-10		65
1.3.0	1BR0P1160R00	Parcel 116, Initiate Aquisition	0	01-Jan-10		65
1.3.0	1BR0P1170R00	Parcel 117, Initiate Aquisition	0	01-Jan-10		106
1.3.0	1BR0P1180R00	Parcel 118, Initiate Aquisition	0	01-Jan-10		65
1.3.0	1BR0P1240R00	Parcel 124, Initiate Aquisition	0	01-Jan-10		65
1.3.0	1BR0P1250R00	Parcel 125, Initiate Aquisition	0	01-Jan-10		65
1.3.0	1BR0P1260R00	Parcel 126, Initiate Aquisition	0	01-Jan-10		65
1.3.0	1BR0P1270R00	Parcel 127, Initiate Aquisition	0	01-Jan-10		65
1.3.0	1BR0P1320R00	Parcel 132, Initiate Aquisition	0	01-Jan-10		65
1.3.0	1BR0P1340R00	Parcel 134, Initiate Aquisition	0	01-Jan-10		65
1.3.0	1BR0P1430R00	Parcel 143, Initiate Aquisition	0	01-Jan-10		174
1.3.0	1BR0P1500R00	Parcel 150, Initiate Aquisition	0	01-Jan-10		112
1.3.0	1BR0P1510R00	Parcel 151, Initiate Aquisition	0	01-Jan-10		299
1.3.0	1BR0P1520R00	Parcel 152, Initiate Aquisition	0	01-Jan-10		174
1.3.0	1BR0P1550R00	Parcel 155, Initiate Aquisition	0	01-Jan-10		254
1.3.0	1BR0P1560R00	Parcel 156, Initiate Aquisition	0	01-Jan-10		65
1.3.0	1BR0P1590R00	Parcel 159, Initiate Aquisition	0	01-Jan-10		65
1.3.0	1BR0P1600R00	Parcel 160, Initiate Aquisition	0	01-Jan-10		65
1.3.0	1BR0P1620R00	Parcel 162, Initiate Aquisition	0	01-Jan-10		169
1.3.0	1BR0P1640R00	Parcel 164, Initiate Aquisition	0	01-Jan-10		106
1.3.0	1BR0P1650R00	Parcel 165, Initiate Aquisition	0	01-Jan-10		65
1.3.0	1BR0P1730R00	Parcel 173, Initiate Aquisition	0	01-Jan-10		65
1.3.0	1BR0P1750R00	Parcel 175, Initiate Aquisition	0	01-Jan-10		106
1.3.0	1BR0P1760R00	Parcel 176, Initiate Aquisition	0	01-Jan-10		65
1.3.0	1BR0P1770R00	Parcel 177, Initiate Aquisition	0	01-Jan-10		65
1.3.0	1BR0P1780R00	Parcel 178, Initiate Aquisition	0	01-Jan-10		65
1.3.0	1BR0P1790R00	Parcel 179, Initiate Aquisition	0	01-Jan-10		65
1.3.0	1BR0P1800R00	Parcel 180, Initiate Aquisition	0	01-Jan-10		125
1.3.0	1BR0P0040R00	Parcel 004, Initiate Aquisition	0	01-Jan-10		66
1.3.0	1BR0P0120R00	Parcel 012, Initiate Aquisition	0	01-Jan-10		129
1.3.0	1BR0P0150R00	Parcel 015, Initiate Aquisition	0	01-Jan-10		85
1.3.0	1BR0P0180R00	Parcel 018, Initiate Aquisition	0	01-Jan-10		85
1.3.0	1BR0P0260R00	Parcel 026, Initiate Aquisition	0	01-Jan-10		68
1.3.0	1BR0P0270R00	Parcel 027, Initiate Aquisition	0	01-Jan-10		66
1.3.0	1BR0P0340R00	Parcel 034, Initiate Aquisition	0	01-Jan-10		66
1.3.0	1BR0P0350R00	Parcel 035, Initiate Aquisition	0	01-Jan-10		214
1.3.0	1BR0P0370R00	Parcel 037, Initiate Aquisition	0	01-Jan-10		66
1.3.0	1BR0P0380R00	Parcel 038, Initiate Aquisition	0	01-Jan-10		85
1.3.0	1BR0P0930R00	Parcel 093, Initiate Aquisition	0	01-Jan-10		134
1.3.0	1BR0P1070R00	Parcel 107, Initiate Aquisition	0	01-Jan-10		25
1.3.0	1BR0P1110R00	Parcel 111, Initiate Aquisition	0	01-Jan-10		25
1.3.0	1BR0P1120R00	Parcel 112, Initiate Aquisition	0	01-Jan-10		25
1.3.0	1BR0P1130R00	Parcel 113, Initiate Aquisition	0	01-Jan-10		25
1.3.0	1BR0P1140R00	Parcel 114, Initiate Aquisition	0	01-Jan-10		25
1.3.0	1BR0P1200R00	Parcel 120, Initiate Aquisition	0	01-Jan-10		25
1.3.0	1BR0P1210R00	Parcel 121, Initiate Aquisition	0	01-Jan-10		25
1.3.0	1BR0P1220R00	Parcel 122, Initiate Aquisition	0	01-Jan-10		25
1.3.0	1BR0P1230R00	Parcel 123, Initiate Aquisition	0	01-Jan-10		25
1.3.0	1BR0P1290R00	Parcel 129, Initiate Aquisition	0	01-Jan-10		25
1.3.0	1BR0P1300R00	Parcel 130, Initiate Aquisition	0	01-Jan-10		25
1.3.0	1BR0P1310R00	Parcel 131, Initiate Aquisition	0	01-Jan-10		25
1.3.0	1BR0P1330R00	Parcel 133, Initiate Aquisition	0	01-Jan-10		25
1.3.0	1BR0P1350R00	Parcel 135, Initiate Aquisition	0	01-Jan-10		25
1.3.0	1BR0P1360R00	Parcel 136, Initiate Aquisition	0	01-Jan-10		25
1.3.0	1BR0P1370R00	Parcel 137, Initiate Aquisition	0	01-Jan-10		25
1.3.0	1BR0P1380R00	Parcel 138, Initiate Aquisition	0	01-Jan-10		82
1.3.0	1BR0P1390R00	Parcel 139, Initiate Aquisition	0	01-Jan-10		25
1.3.0	1BR0P1400R00	Parcel 140, Initiate Aquisition	0	01-Jan-10		25
1.3.0	1BR0P1410R00	Parcel 141, Initiate Aquisition	0	01-Jan-10		25
1.3.0	1BR0P1420R00	Parcel 142, Initiate Aquisition	0	01-Jan-10		259
1.3.0	1BR0P1440R00	Parcel 144, Initiate Aquisition	0	01-Jan-10		25
1.3.0	1BR0P1450R00	Parcel 145, Initiate Aquisition	0	01-Jan-10		259

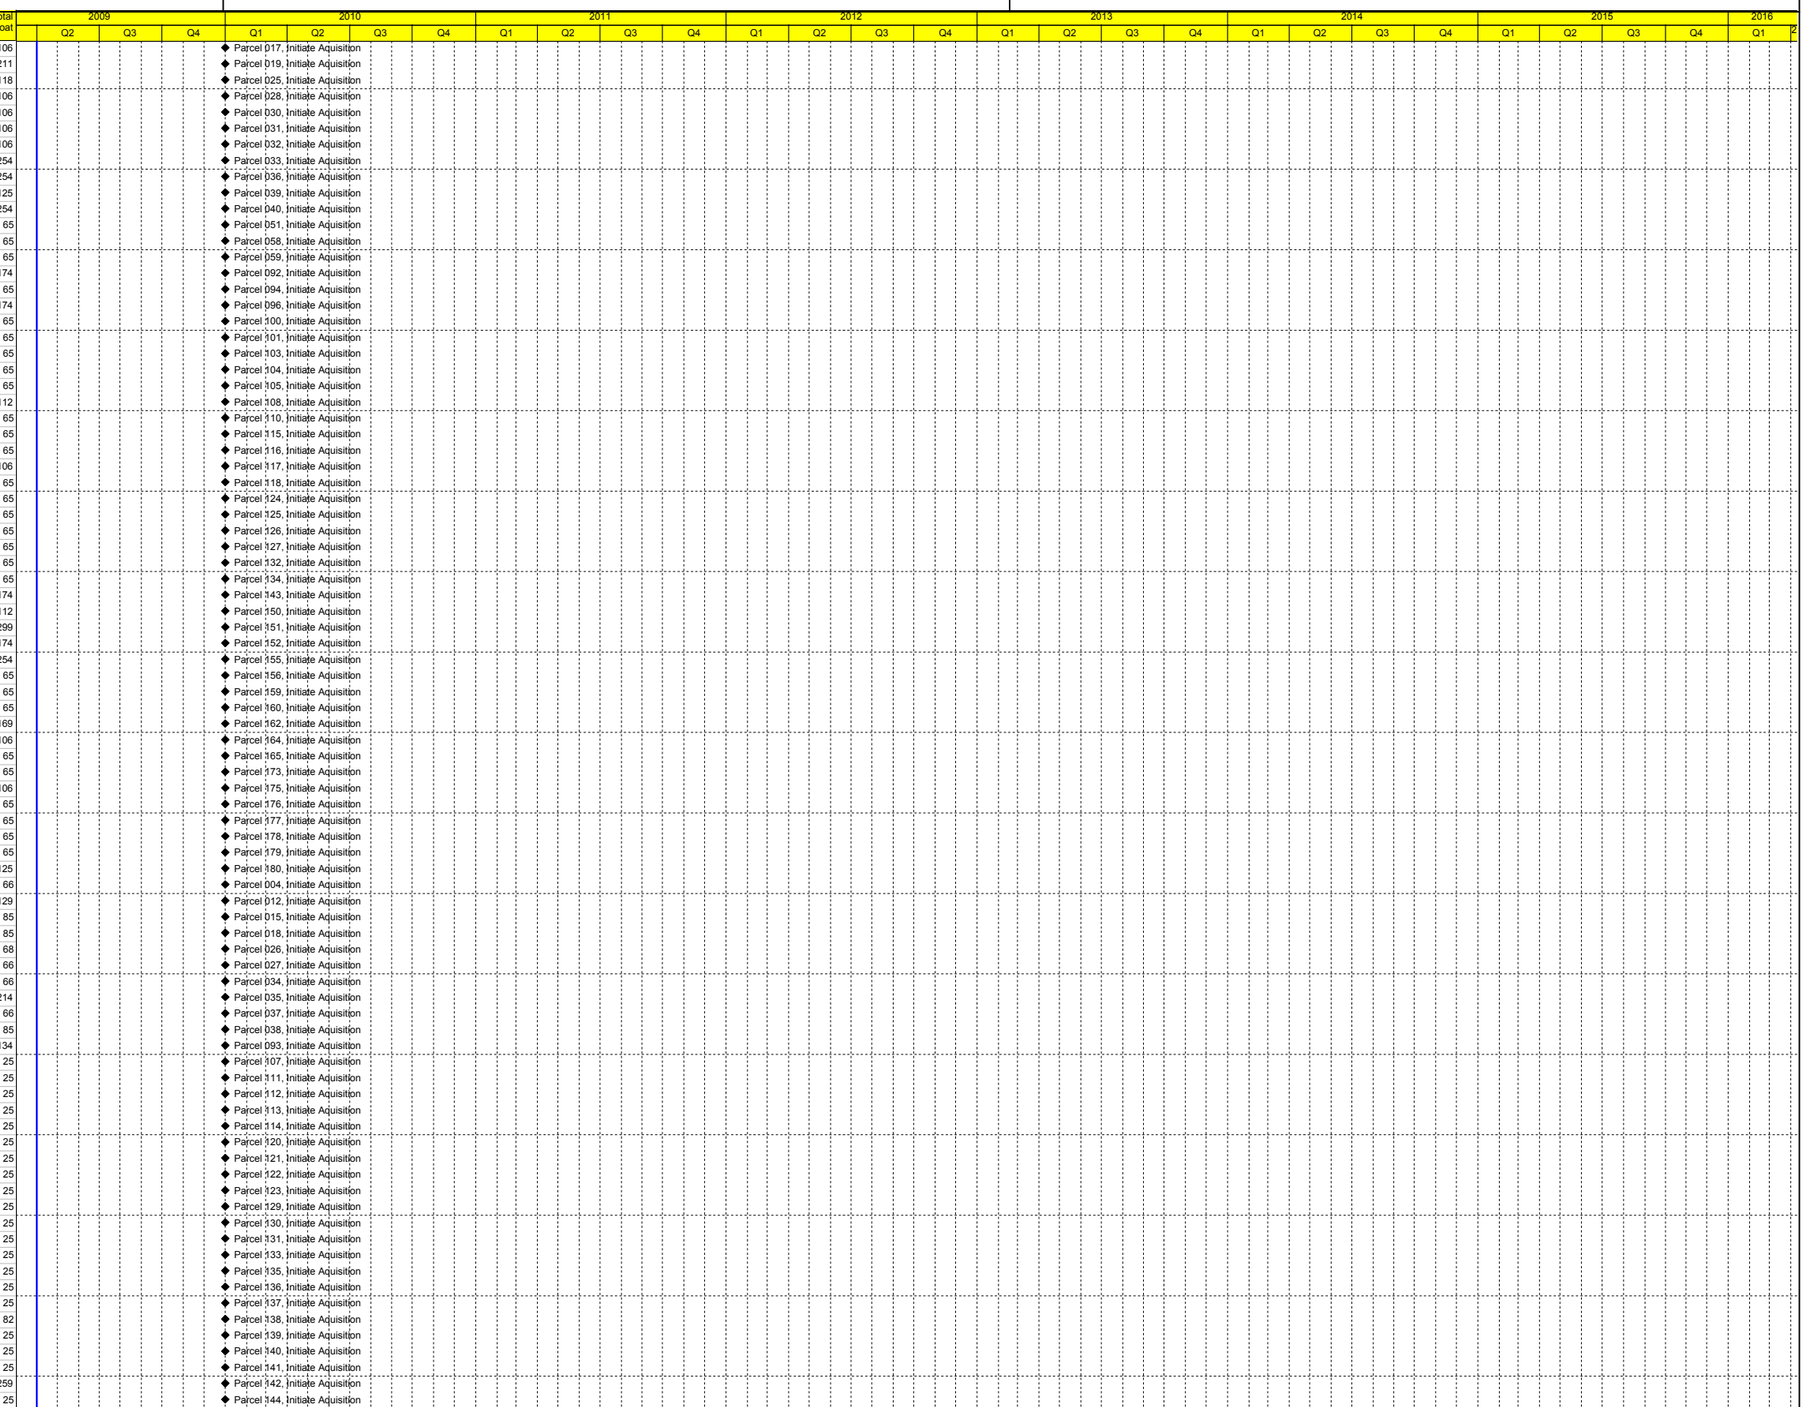

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.3.0	1BR0P1460R00	Parcel 146, Initiate Aquisition	0	01-Jan-10		259
1.3.0	1BR0P1470R00	Parcel 147, Initiate Aquisition	0	01-Jan-10		25
1.3.0	1BR0P1480R00	Parcel 148, Initiate Aquisition	0	01-Jan-10		25
1.3.0	1BR0P1530R00	Parcel 153, Initiate Aquisition	0	01-Jan-10		72
1.3.0	1BR0P1540R00	Parcel 154, Initiate Aquisition	0	01-Jan-10		25
1.3.0	1BR0P1570R00	Parcel 157, Initiate Aquisition	0	01-Jan-10		72
1.3.0	1BR0P1580R00	Parcel 158, Initiate Aquisition	0	01-Jan-10		72
1.3.0	1BR0P0030R10	Parcel 003, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	208
1.3.0	1BR0P0050R10	Parcel 005, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	106
1.3.0	1BR0P0060R10	Parcel 006, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	65
1.3.0	1BR0P0070R10	Parcel 007, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	65
1.3.0	1BR0P0080R10	Parcel 008, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	65
1.3.0	1BR0P0090R10	Parcel 009, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	65
1.3.0	1BR0P0130R10	Parcel 013, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	169
1.3.0	1BR0P0140R10	Parcel 014, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	169
1.3.0	1BR0P0160R10	Parcel 016, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	125
1.3.0	1BR0P0170R10	Parcel 017, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	106
1.3.0	1BR0P0190R10	Parcel 019, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	211
1.3.0	1BR0P0280R10	Parcel 028, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	106
1.3.0	1BR0P0300R10	Parcel 030, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	106
1.3.0	1BR0P0310R10	Parcel 031, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	106
1.3.0	1BR0P0320R10	Parcel 032, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	106
1.3.0	1BR0P0330R10	Parcel 033, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	254
1.3.0	1BR0P0360R10	Parcel 036, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	254
1.3.0	1BR0P0390R10	Parcel 039, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	125
1.3.0	1BR0P0400R10	Parcel 040, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	254
1.3.0	1BR0P0510R10	Parcel 051, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	65
1.3.0	1BR0P0580R10	Parcel 058, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	65
1.3.0	1BR0P0590R10	Parcel 059, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	65
1.3.0	1BR0P0920R10	Parcel 092, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	174
1.3.0	1BR0P0940R10	Parcel 094, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	65
1.3.0	1BR0P0960R10	Parcel 096, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	174
1.3.0	1BR0P1000R10	Parcel 100, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	65
1.3.0	1BR0P1010R10	Parcel 101, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	65
1.3.0	1BR0P1030R10	Parcel 103, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	65
1.3.0	1BR0P1040R10	Parcel 104, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	65
1.3.0	1BR0P1050R10	Parcel 105, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	65
1.3.0	1BR0P1080R10	Parcel 108, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	112
1.3.0	1BR0P1100R10	Parcel 110, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	65
1.3.0	1BR0P1150R10	Parcel 115, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	65
1.3.0	1BR0P1160R10	Parcel 116, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	65
1.3.0	1BR0P1170R10	Parcel 117, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	106
1.3.0	1BR0P1180R10	Parcel 118, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	65
1.3.0	1BR0P1240R10	Parcel 124, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	65
1.3.0	1BR0P1250R10	Parcel 125, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	65
1.3.0	1BR0P1260R10	Parcel 126, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	65
1.3.0	1BR0P1270R10	Parcel 127, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	65
1.3.0	1BR0P1320R10	Parcel 132, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	65
1.3.0	1BR0P1340R10	Parcel 134, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	65
1.3.0	1BR0P1430R10	Parcel 143, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	174
1.3.0	1BR0P1500R10	Parcel 150, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	112
1.3.0	1BR0P1510R10	Parcel 151, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	299
1.3.0	1BR0P1520R10	Parcel 152, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	174
1.3.0	1BR0P1550R10	Parcel 155, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	254
1.3.0	1BR0P1560R10	Parcel 156, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	65
1.3.0	1BR0P1590R10	Parcel 159, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	65
1.3.0	1BR0P1600R10	Parcel 160, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	65
1.3.0	1BR0P1620R10	Parcel 162, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	169
1.3.0	1BR0P1640R10	Parcel 164, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	106
1.3.0	1BR0P1650R10	Parcel 165, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	65
1.3.0	1BR0P1730R10	Parcel 173, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	65
1.3.0	1BR0P1750R10	Parcel 175, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	106
1.3.0	1BR0P1760R10	Parcel 176, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	65
1.3.0	1BR0P1770R10	Parcel 177, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	65
1.3.0	1BR0P1780R10	Parcel 178, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	65
1.3.0	1BR0P1790R10	Parcel 179, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	65
1.3.0	1BR0P1800R10	Parcel 180, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	125
1.3.0	1BR0P0040R10	Parcel 004, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	66
1.3.0	1BR0P0120R10	Parcel 012, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	129
1.3.0	1BR0P0150R10	Parcel 015, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	85
1.3.0	1BR0P0180R10	Parcel 018, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	85
1.3.0	1BR0P0270R10	Parcel 027, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	66
1.3.0	1BR0P0340R10	Parcel 034, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	66
1.3.0	1BR0P0350R10	Parcel 035, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	214
1.3.0	1BR0P0370R10	Parcel 037, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	66
1.3.0	1BR0P0380R10	Parcel 038, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	85
1.3.0	1BR0P0930R10	Parcel 093, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	134
1.3.0	1BR0P1070R10	Parcel 107, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	25
1.3.0	1BR0P1110R10	Parcel 111, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	25
1.3.0	1BR0P1120R10	Parcel 112, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	25
1.3.0	1BR0P1130R10	Parcel 113, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	25
1.3.0	1BR0P1140R10	Parcel 114, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	25
1.3.0	1BR0P1200R10	Parcel 120, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	25
1.3.0	1BR0P1210R10	Parcel 121, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	25
1.3.0	1BR0P1220R10	Parcel 122, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	25
1.3.0	1BR0P1230R10	Parcel 123, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	25

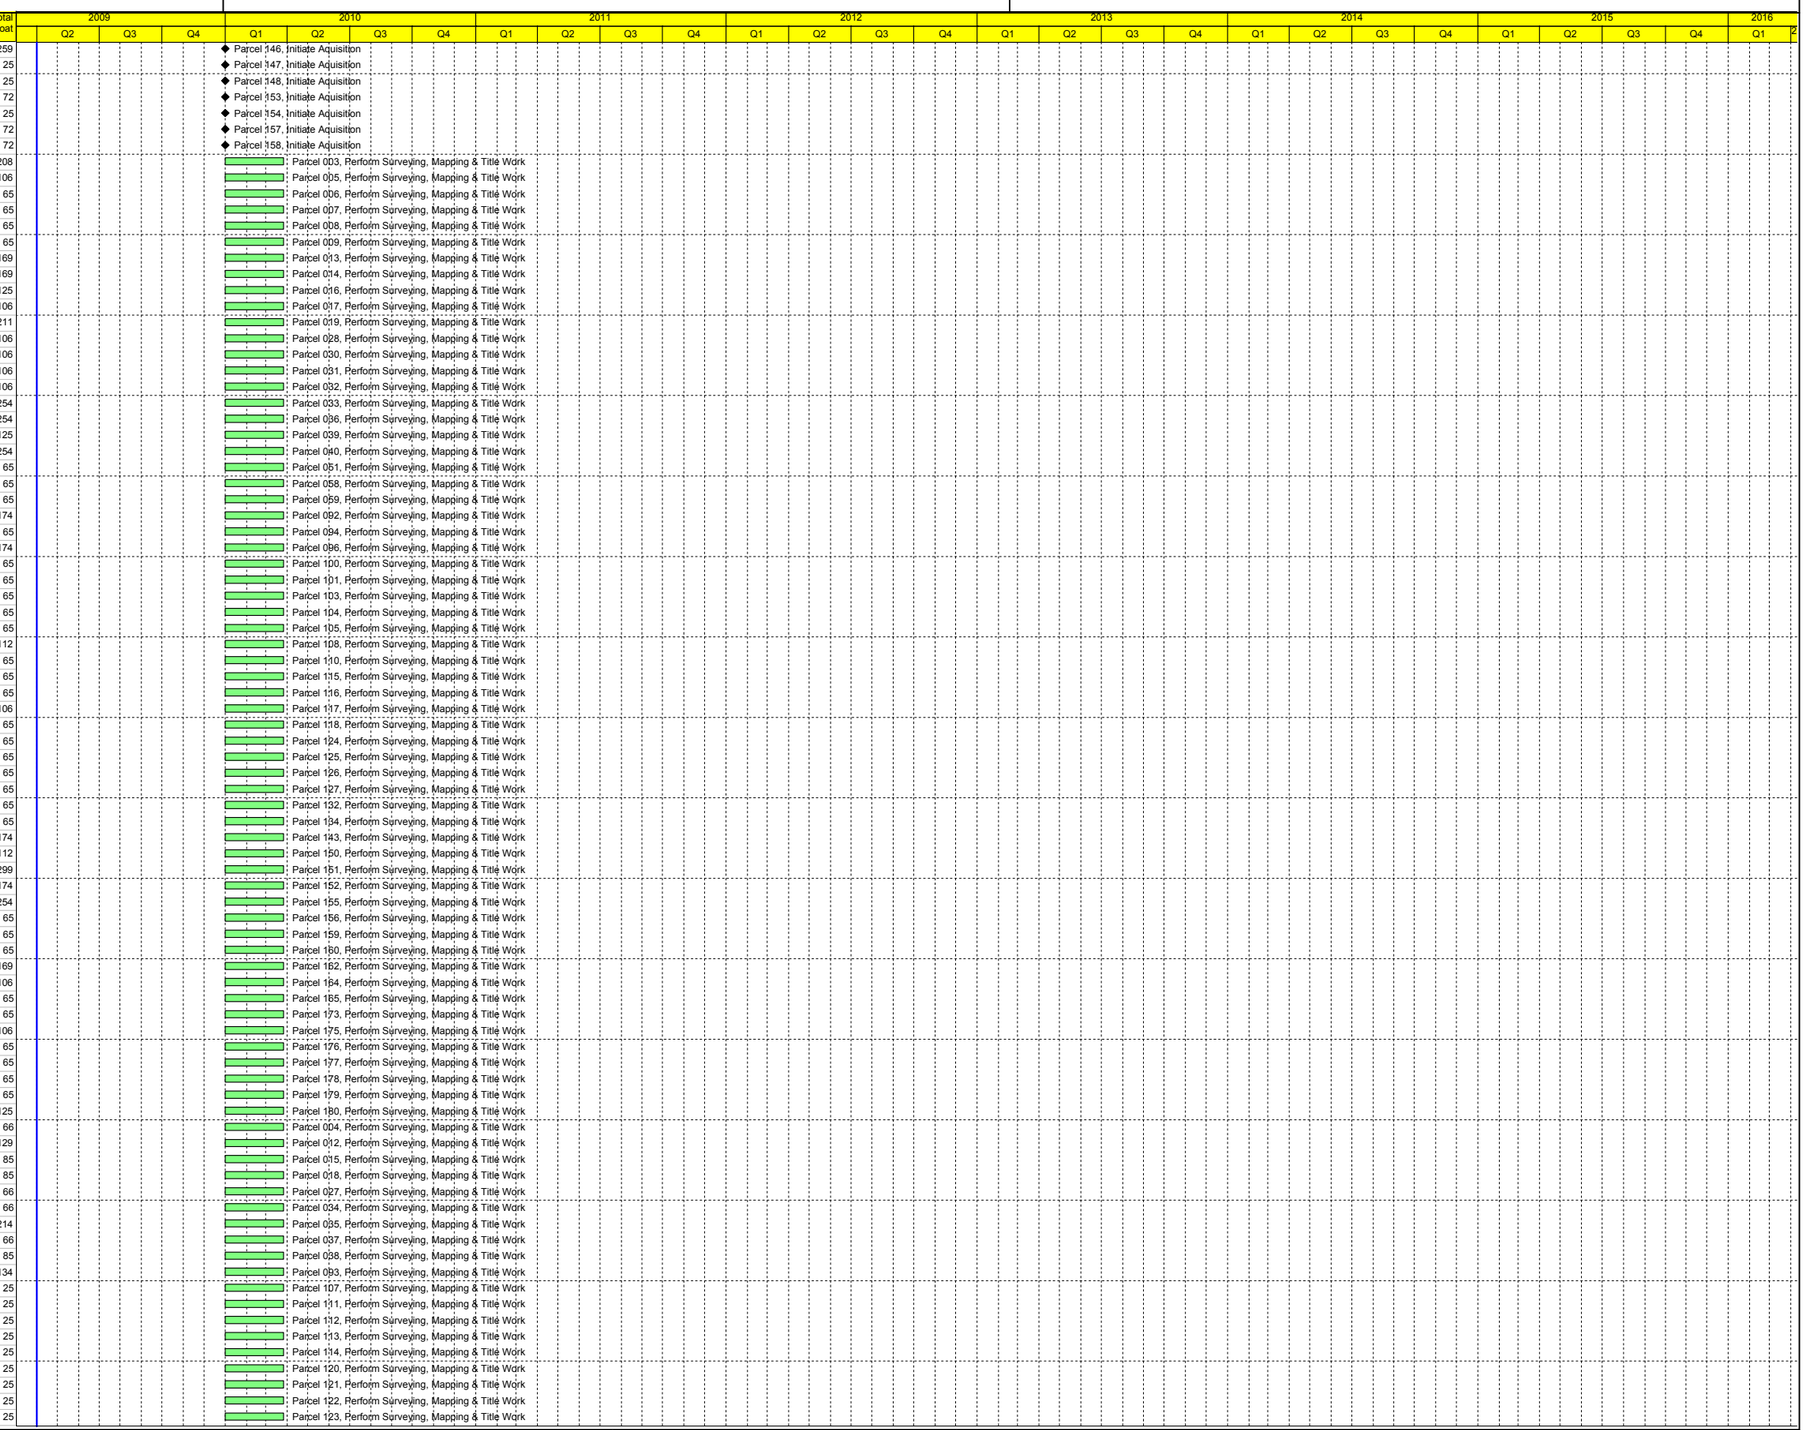

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.3.0	1BR0P1290R10	Parcel 129, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	25
1.3.0	1BR0P1300R10	Parcel 130, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	25
1.3.0	1BR0P1310R10	Parcel 131, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	25
1.3.0	1BR0P1330R10	Parcel 133, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	25
1.3.0	1BR0P1350R10	Parcel 135, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	25
1.3.0	1BR0P1360R10	Parcel 136, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	25
1.3.0	1BR0P1370R10	Parcel 137, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	25
1.3.0	1BR0P1390R10	Parcel 139, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	25
1.3.0	1BR0P1400R10	Parcel 140, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	25
1.3.0	1BR0P1410R10	Parcel 141, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	25
1.3.0	1BR0P1420R10	Parcel 142, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	259
1.3.0	1BR0P1440R10	Parcel 144, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	25
1.3.0	1BR0P1450R10	Parcel 145, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	259
1.3.0	1BR0P1460R10	Parcel 146, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	259
1.3.0	1BR0P1470R10	Parcel 147, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	25
1.3.0	1BR0P1480R10	Parcel 148, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	25
1.3.0	1BR0P1530R10	Parcel 153, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	72
1.3.0	1BR0P1540R10	Parcel 154, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	25
1.3.0	1BR0P1570R10	Parcel 157, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	72
1.3.0	1BR0P1580R10	Parcel 158, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	72
1.3.0	1BR0P1380R20	Parcel 138, Perform Appraisal and Internal R...	60	06-Jan-10	31-Mar-10	82
1.3.0	1BR0P0260R20	Parcel 026, Perform Appraisal and Internal R...	60	29-Jan-10	23-Apr-10	68
1.3.0	1BR0P0250R20	Parcel 025, Perform Appraisal and Internal R...	60	10-Mar-10	02-Jun-10	118
1.3.0	1BR0P0030R20	Parcel 003, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	208
1.3.0	1BR0P0050R20	Parcel 005, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	106
1.3.0	1BR0P0060R20	Parcel 006, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	65
1.3.0	1BR0P0070R20	Parcel 007, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	65
1.3.0	1BR0P0080R20	Parcel 008, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	65
1.3.0	1BR0P0090R20	Parcel 009, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	65
1.3.0	1BR0P0130R20	Parcel 013, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	169
1.3.0	1BR0P0140R20	Parcel 014, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	169
1.3.0	1BR0P0160R20	Parcel 016, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	125
1.3.0	1BR0P0170R20	Parcel 017, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	106
1.3.0	1BR0P0190R20	Parcel 019, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	211
1.3.0	1BR0P0280R20	Parcel 028, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	106
1.3.0	1BR0P0300R20	Parcel 030, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	106
1.3.0	1BR0P0310R20	Parcel 031, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	106
1.3.0	1BR0P0320R20	Parcel 032, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	106
1.3.0	1BR0P0330R20	Parcel 033, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	254
1.3.0	1BR0P0360R20	Parcel 036, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	254
1.3.0	1BR0P0390R20	Parcel 039, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	125
1.3.0	1BR0P0400R20	Parcel 040, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	254
1.3.0	1BR0P0510R20	Parcel 051, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	65
1.3.0	1BR0P0580R20	Parcel 058, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	65
1.3.0	1BR0P0590R20	Parcel 059, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	65
1.3.0	1BR0P0920R20	Parcel 092, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	174
1.3.0	1BR0P0940R20	Parcel 094, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	65
1.3.0	1BR0P0960R20	Parcel 096, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	174
1.3.0	1BR0P1000R20	Parcel 100, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	65
1.3.0	1BR0P1010R20	Parcel 101, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	65
1.3.0	1BR0P1030R20	Parcel 103, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	65
1.3.0	1BR0P1040R20	Parcel 104, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	65
1.3.0	1BR0P1050R20	Parcel 105, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	65
1.3.0	1BR0P1080R20	Parcel 108, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	112
1.3.0	1BR0P1100R20	Parcel 110, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	65
1.3.0	1BR0P1150R20	Parcel 115, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	65
1.3.0	1BR0P1160R20	Parcel 116, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	65
1.3.0	1BR0P1170R20	Parcel 117, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	106
1.3.0	1BR0P1180R20	Parcel 118, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	65
1.3.0	1BR0P1240R20	Parcel 124, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	65
1.3.0	1BR0P1250R20	Parcel 125, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	65
1.3.0	1BR0P1260R20	Parcel 126, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	65
1.3.0	1BR0P1270R20	Parcel 127, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	65
1.3.0	1BR0P1320R20	Parcel 132, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	65
1.3.0	1BR0P1340R20	Parcel 134, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	65
1.3.0	1BR0P1430R20	Parcel 143, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	174
1.3.0	1BR0P1500R20	Parcel 150, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	112
1.3.0	1BR0P1510R20	Parcel 151, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	299
1.3.0	1BR0P1520R20	Parcel 152, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	174
1.3.0	1BR0P1550R20	Parcel 155, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	254
1.3.0	1BR0P1560R20	Parcel 156, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	65
1.3.0	1BR0P1590R20	Parcel 159, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	65
1.3.0	1BR0P1600R20	Parcel 160, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	65
1.3.0	1BR0P1620R20	Parcel 162, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	169
1.3.0	1BR0P1640R20	Parcel 164, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	106
1.3.0	1BR0P1650R20	Parcel 165, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	65
1.3.0	1BR0P1730R20	Parcel 173, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	65
1.3.0	1BR0P1750R20	Parcel 175, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	106
1.3.0	1BR0P1760R20	Parcel 176, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	65
1.3.0	1BR0P1770R20	Parcel 177, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	65
1.3.0	1BR0P1780R20	Parcel 178, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	65
1.3.0	1BR0P1790R20	Parcel 179, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	65
1.3.0	1BR0P1800R20	Parcel 180, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	125
1.3.0	1BR0P0040R20	Parcel 004, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	66
1.3.0	1BR0P0120R20	Parcel 012, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	129
1.3.0	1BR0P0150R20	Parcel 015, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	85

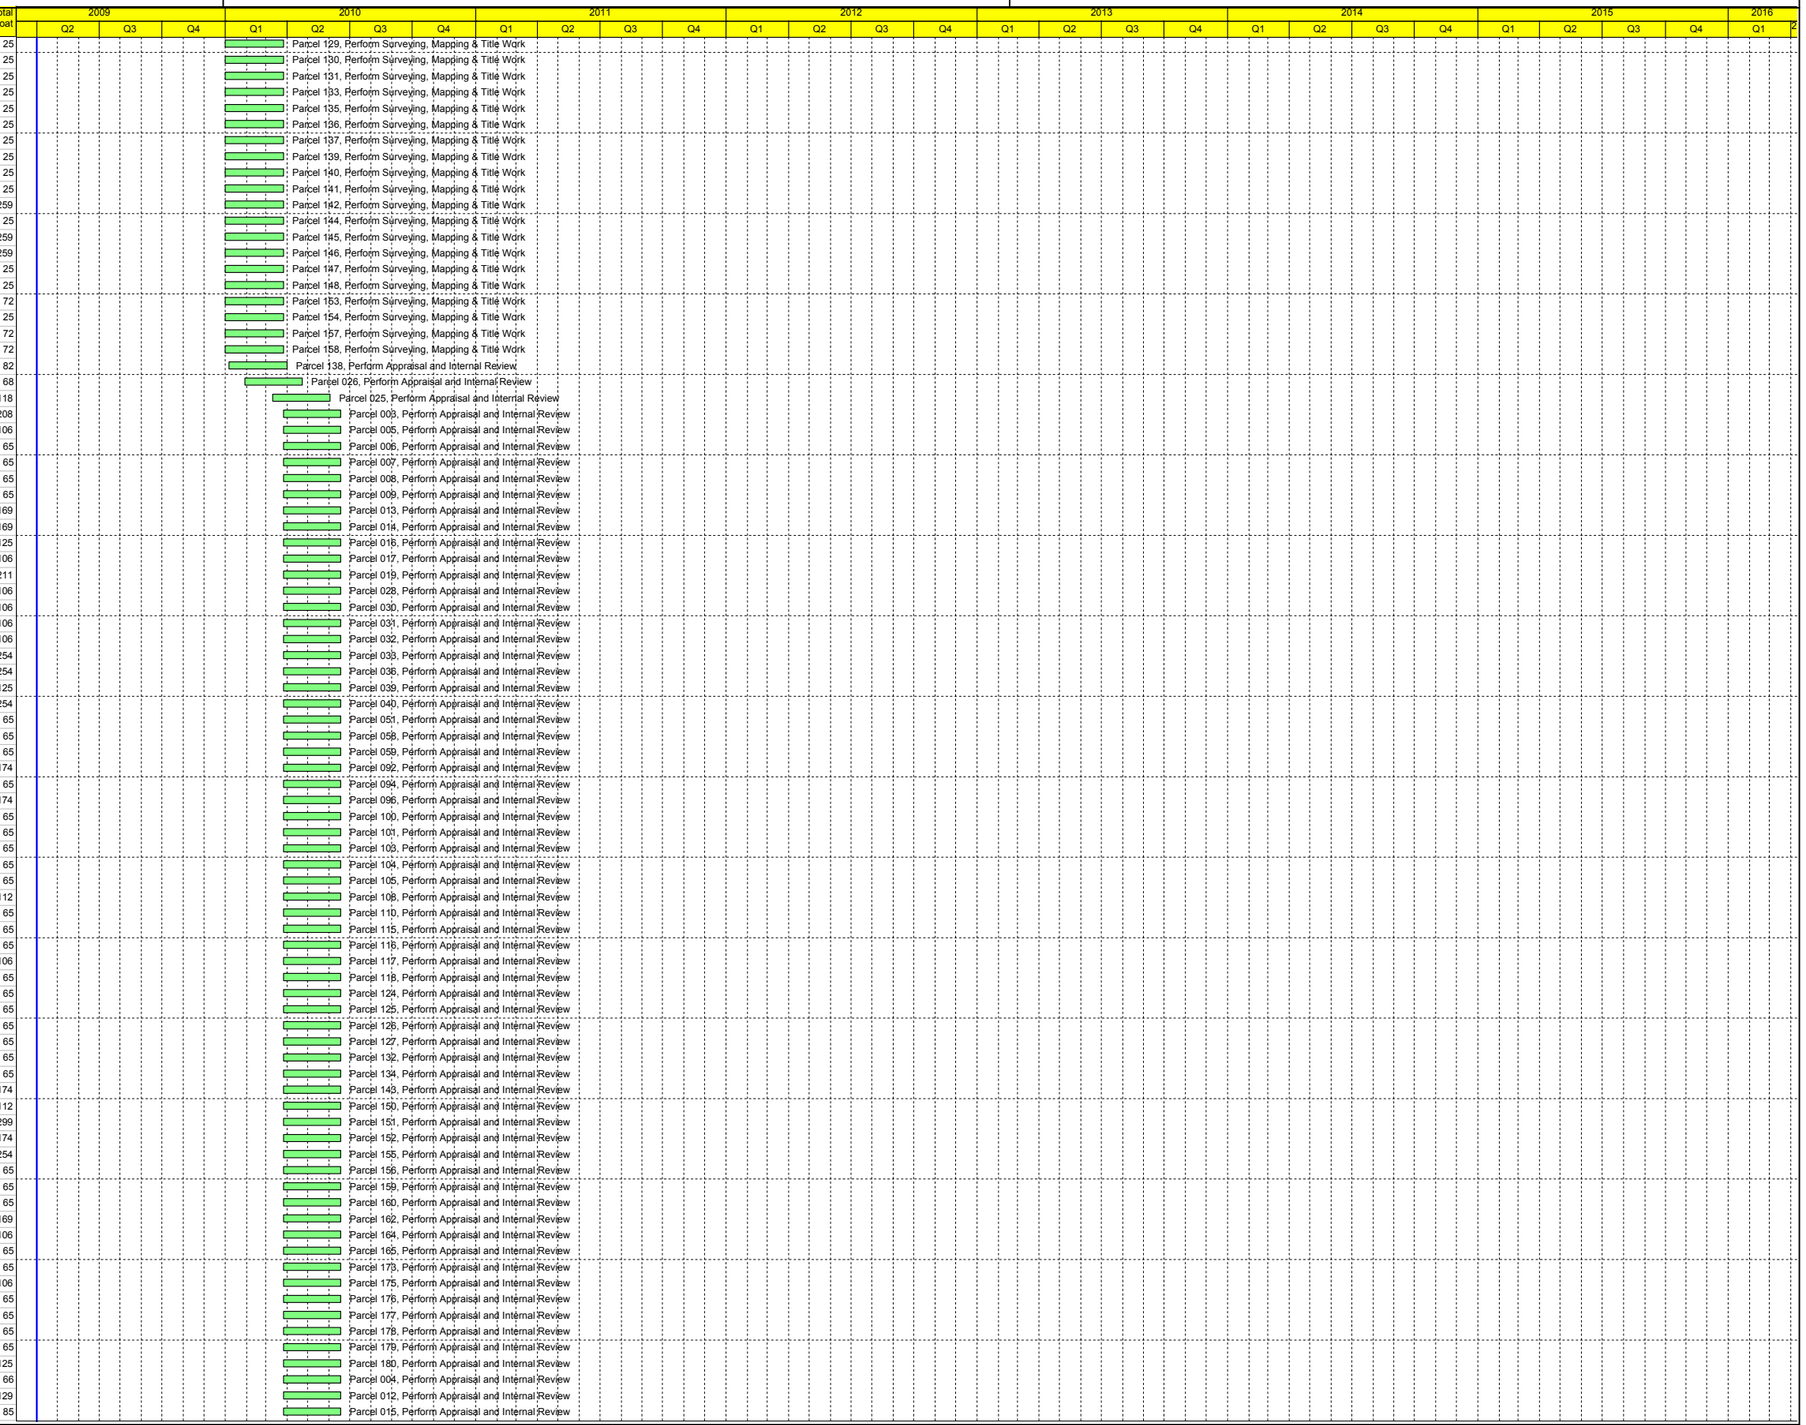

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.3.0	1BR0P0180R20	Parcel 018, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	85
1.3.0	1BR0P0270R20	Parcel 027, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	66
1.3.0	1BR0P0340R20	Parcel 034, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	66
1.3.0	1BR0P0350R20	Parcel 035, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	214
1.3.0	1BR0P0370R20	Parcel 037, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	66
1.3.0	1BR0P0380R20	Parcel 038, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	85
1.3.0	1BR0P0930R20	Parcel 093, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	134
1.3.0	1BR0P1070R20	Parcel 107, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	25
1.3.0	1BR0P1110R20	Parcel 111, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	25
1.3.0	1BR0P1120R20	Parcel 112, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	25
1.3.0	1BR0P1130R20	Parcel 113, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	25
1.3.0	1BR0P1140R20	Parcel 114, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	25
1.3.0	1BR0P1200R20	Parcel 120, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	25
1.3.0	1BR0P1210R20	Parcel 121, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	25
1.3.0	1BR0P1220R20	Parcel 122, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	25
1.3.0	1BR0P1230R20	Parcel 123, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	25
1.3.0	1BR0P1290R20	Parcel 129, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	25
1.3.0	1BR0P1300R20	Parcel 130, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	25
1.3.0	1BR0P1310R20	Parcel 131, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	25
1.3.0	1BR0P1330R20	Parcel 133, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	25
1.3.0	1BR0P1350R20	Parcel 135, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	25
1.3.0	1BR0P1360R20	Parcel 136, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	25
1.3.0	1BR0P1370R20	Parcel 137, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	25
1.3.0	1BR0P1390R20	Parcel 139, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	25
1.3.0	1BR0P1400R20	Parcel 140, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	25
1.3.0	1BR0P1410R20	Parcel 141, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	25
1.3.0	1BR0P1420R20	Parcel 142, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	259
1.3.0	1BR0P1440R20	Parcel 144, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	25
1.3.0	1BR0P1450R20	Parcel 145, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	259
1.3.0	1BR0P1460R20	Parcel 146, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	259
1.3.0	1BR0P1470R20	Parcel 147, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	25
1.3.0	1BR0P1480R20	Parcel 148, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	25
1.3.0	1BR0P1530R20	Parcel 153, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	72
1.3.0	1BR0P1540R20	Parcel 154, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	25
1.3.0	1BR0P1570R20	Parcel 157, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	72
1.3.0	1BR0P1580R20	Parcel 158, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	72
1.3.0	1BR0P1380R30	Parcel 138, TxDOT Reviews Aquisition Pack...	10	31-Mar-10	14-Apr-10	82
1.3.0	1BR0P1380R40	Parcel 138, Present and Negotiate Offer	20	14-Apr-10	12-May-10	82
1.3.0	1BR0P1380R50	Parcel 138, Prepare for Relocation	60	14-Apr-10	07-Jul-10	172
1.3.0	1BR0P0260R30	Parcel 026, TxDOT Reviews Aquisition Pack...	10	16-Apr-10	30-Apr-10	68
1.3.0	1BR0P0260R40	Parcel 026, Present and Negotiate Offer	20	30-Apr-10	28-May-10	68
1.3.0	1BR0P0260R50	Parcel 026, Prepare for Relocation	60	30-Apr-10	23-Jul-10	158
1.3.0	1BR0P1380R60	Parcel 138, Condemnation Process (if requir...	130	12-May...	10-Nov-10	82
1.3.0	1BR0P0250R30	Parcel 025, TxDOT Reviews Aquisition Pack...	10	26-May...	09-Jun-10	118
1.3.0	1BR0P0260R60	Parcel 026, Condemnation Process (if requir...	130	28-May...	26-Nov-10	68
1.3.0	1BR0P0250R40	Parcel 025, Present and Negotiate Offer	20	09-Jun-10	07-Jul-10	118
1.3.0	1BR0P0030R30	Parcel 003, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	208
1.3.0	1BR0P0050R30	Parcel 005, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	106
1.3.0	1BR0P0060R30	Parcel 006, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	65
1.3.0	1BR0P0070R30	Parcel 007, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	65
1.3.0	1BR0P0080R30	Parcel 008, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	65
1.3.0	1BR0P0090R30	Parcel 009, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	65
1.3.0	1BR0P0130R30	Parcel 013, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	169
1.3.0	1BR0P0140R30	Parcel 014, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	169
1.3.0	1BR0P0160R30	Parcel 016, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	125
1.3.0	1BR0P0170R30	Parcel 017, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	106
1.3.0	1BR0P0190R30	Parcel 019, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	211
1.3.0	1BR0P0280R30	Parcel 028, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	106
1.3.0	1BR0P0300R30	Parcel 030, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	106
1.3.0	1BR0P0310R30	Parcel 031, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	106
1.3.0	1BR0P0320R30	Parcel 032, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	106
1.3.0	1BR0P0330R30	Parcel 033, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	254
1.3.0	1BR0P0360R30	Parcel 036, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	254
1.3.0	1BR0P0390R30	Parcel 039, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	125
1.3.0	1BR0P0400R30	Parcel 040, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	254
1.3.0	1BR0P0510R30	Parcel 051, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	65
1.3.0	1BR0P0580R30	Parcel 058, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	65
1.3.0	1BR0P0590R30	Parcel 059, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	65
1.3.0	1BR0P0920R30	Parcel 092, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	174
1.3.0	1BR0P0940R30	Parcel 094, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	65
1.3.0	1BR0P0960R30	Parcel 096, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	174
1.3.0	1BR0P1000R30	Parcel 100, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	65
1.3.0	1BR0P1010R30	Parcel 101, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	65
1.3.0	1BR0P1030R30	Parcel 103, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	65
1.3.0	1BR0P1040R30	Parcel 104, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	65
1.3.0	1BR0P1050R30	Parcel 105, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	65
1.3.0	1BR0P1080R30	Parcel 108, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	112
1.3.0	1BR0P1100R30	Parcel 110, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	65
1.3.0	1BR0P1150R30	Parcel 115, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	65
1.3.0	1BR0P1160R30	Parcel 116, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	65
1.3.0	1BR0P1170R30	Parcel 117, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	106
1.3.0	1BR0P1180R30	Parcel 118, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	65
1.3.0	1BR0P1240R30	Parcel 124, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	65
1.3.0	1BR0P1250R30	Parcel 125, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	65
1.3.0	1BR0P1260R30	Parcel 126, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	65
1.3.0	1BR0P1270R30	Parcel 127, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	65

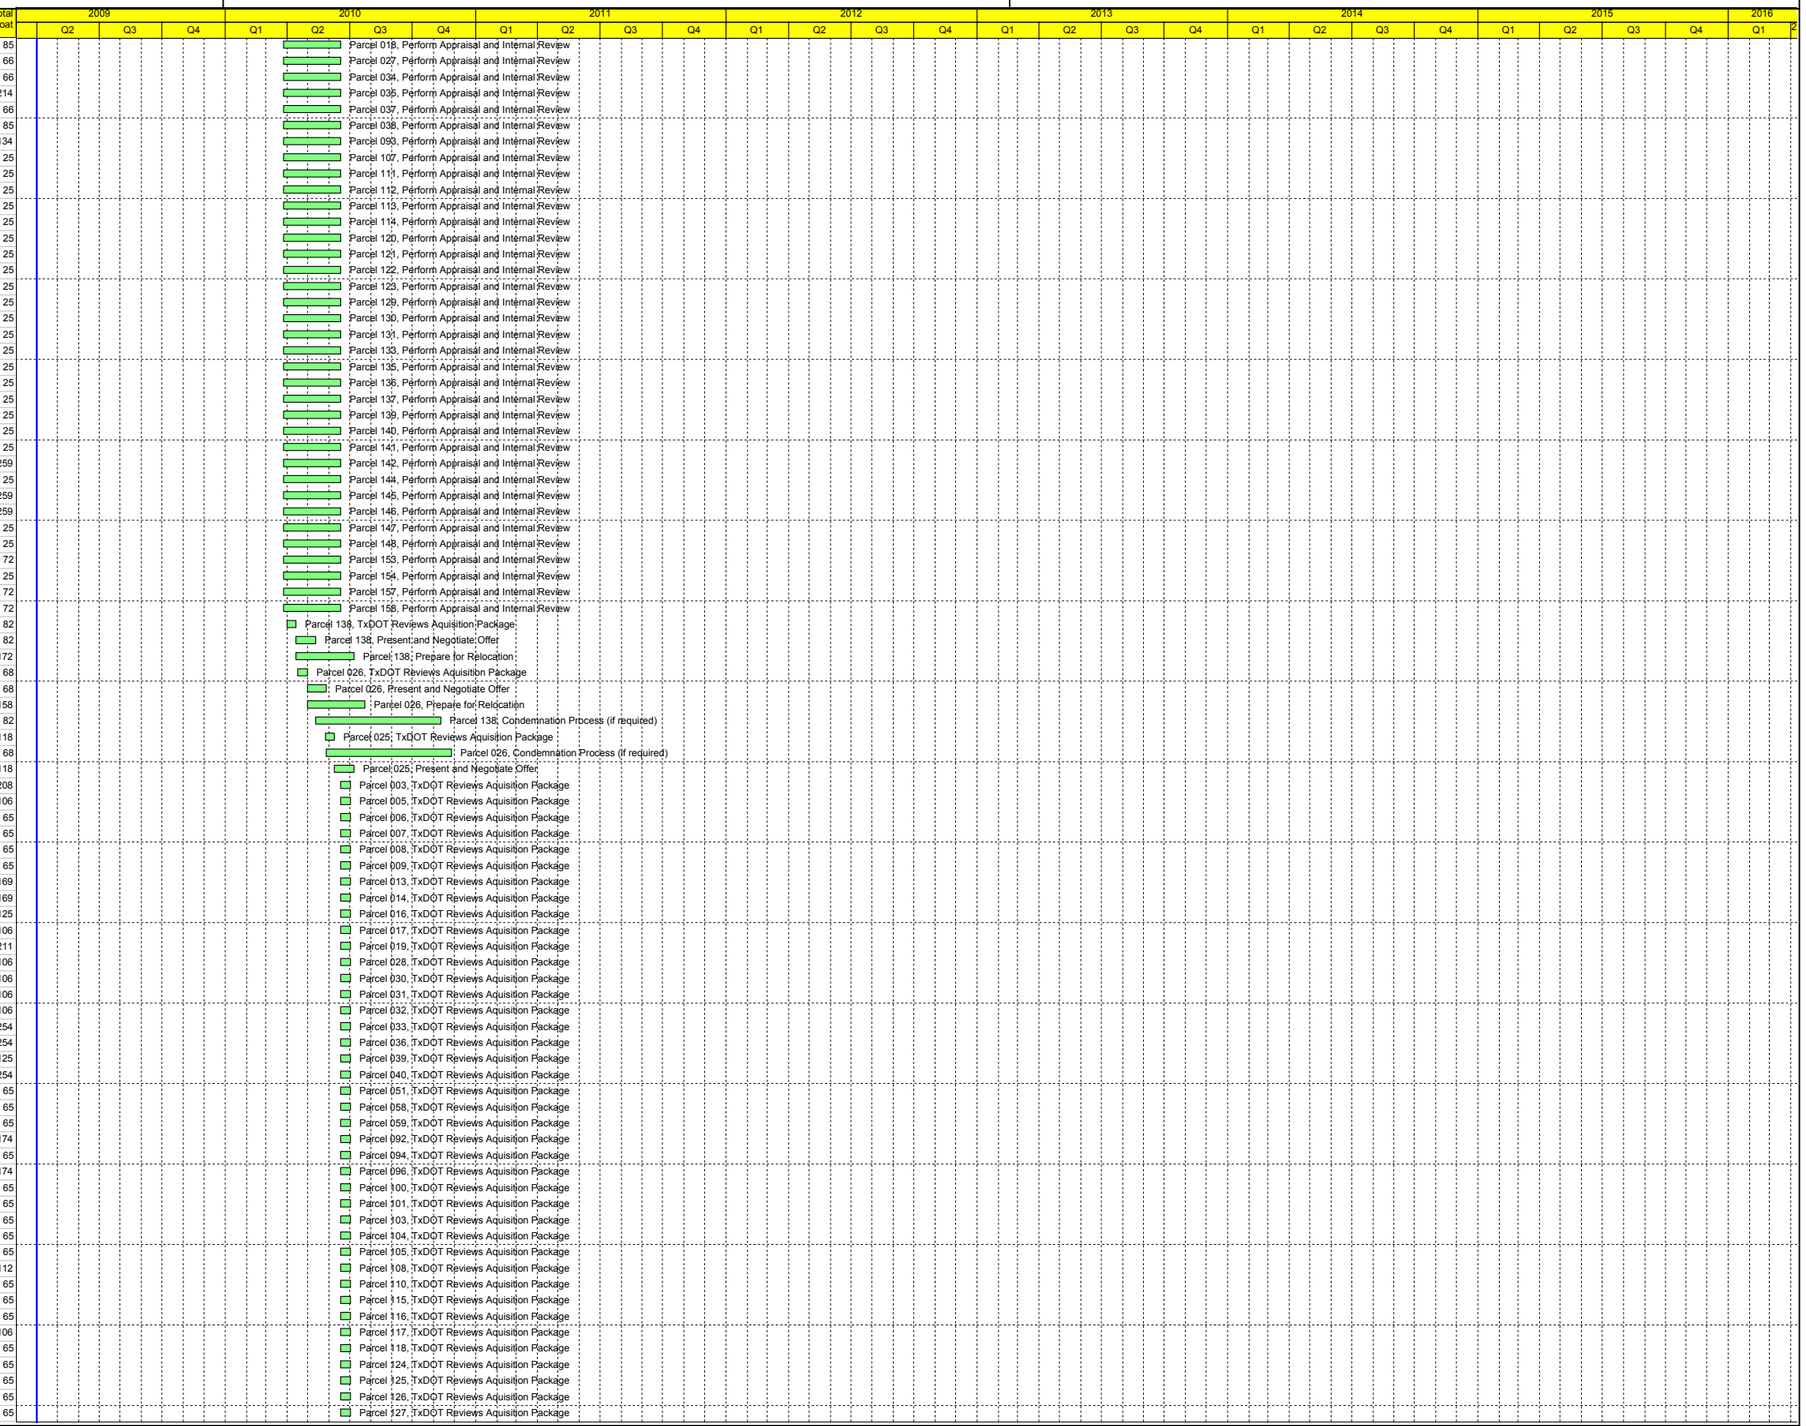

Remaining Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.3.0	1BR0P1320R30	Parcel 132, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	65
1.3.0	1BR0P1340R30	Parcel 134, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	65
1.3.0	1BR0P1430R30	Parcel 143, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	174
1.3.0	1BR0P1500R30	Parcel 150, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	112
1.3.0	1BR0P1510R30	Parcel 151, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	299
1.3.0	1BR0P1520R30	Parcel 152, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	174
1.3.0	1BR0P1550R30	Parcel 155, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	254
1.3.0	1BR0P1560R30	Parcel 156, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	65
1.3.0	1BR0P1590R30	Parcel 159, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	65
1.3.0	1BR0P1600R30	Parcel 160, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	65
1.3.0	1BR0P1620R30	Parcel 162, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	169
1.3.0	1BR0P1640R30	Parcel 164, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	106
1.3.0	1BR0P1650R30	Parcel 165, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	65
1.3.0	1BR0P1730R30	Parcel 173, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	65
1.3.0	1BR0P1750R30	Parcel 175, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	106
1.3.0	1BR0P1760R30	Parcel 176, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	65
1.3.0	1BR0P1770R30	Parcel 177, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	65
1.3.0	1BR0P1780R30	Parcel 178, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	65
1.3.0	1BR0P1790R30	Parcel 179, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	65
1.3.0	1BR0P1800R30	Parcel 180, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	125
1.3.0	1BR0P0040R30	Parcel 004, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	66
1.3.0	1BR0P0120R30	Parcel 012, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	129
1.3.0	1BR0P0150R30	Parcel 015, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	85
1.3.0	1BR0P0180R30	Parcel 018, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	85
1.3.0	1BR0P0270R30	Parcel 027, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	66
1.3.0	1BR0P0340R30	Parcel 034, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	66
1.3.0	1BR0P0350R30	Parcel 035, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	214
1.3.0	1BR0P0370R30	Parcel 037, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	66
1.3.0	1BR0P0380R30	Parcel 038, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	85
1.3.0	1BR0P0930R30	Parcel 093, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	134
1.3.0	1BR0P1070R30	Parcel 107, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	25
1.3.0	1BR0P1110R30	Parcel 111, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	25
1.3.0	1BR0P1120R30	Parcel 112, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	25
1.3.0	1BR0P1130R30	Parcel 113, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	25
1.3.0	1BR0P1140R30	Parcel 114, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	25
1.3.0	1BR0P1200R30	Parcel 120, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	25
1.3.0	1BR0P1210R30	Parcel 121, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	25
1.3.0	1BR0P1220R30	Parcel 122, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	25
1.3.0	1BR0P1230R30	Parcel 123, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	25
1.3.0	1BR0P1290R30	Parcel 129, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	25
1.3.0	1BR0P1300R30	Parcel 130, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	25
1.3.0	1BR0P1310R30	Parcel 131, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	25
1.3.0	1BR0P1330R30	Parcel 133, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	25
1.3.0	1BR0P1350R30	Parcel 135, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	25
1.3.0	1BR0P1360R30	Parcel 136, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	25
1.3.0	1BR0P1370R30	Parcel 137, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	25
1.3.0	1BR0P1390R30	Parcel 139, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	25
1.3.0	1BR0P1400R30	Parcel 140, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	25
1.3.0	1BR0P1410R30	Parcel 141, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	25
1.3.0	1BR0P1420R30	Parcel 142, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	259
1.3.0	1BR0P1440R30	Parcel 144, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	25
1.3.0	1BR0P1450R30	Parcel 145, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	259
1.3.0	1BR0P1460R30	Parcel 146, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	259
1.3.0	1BR0P1470R30	Parcel 147, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	25
1.3.0	1BR0P1480R30	Parcel 148, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	25
1.3.0	1BR0P1530R30	Parcel 153, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	72
1.3.0	1BR0P1540R30	Parcel 154, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	25
1.3.0	1BR0P1570R30	Parcel 157, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	72
1.3.0	1BR0P1580R30	Parcel 158, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	72
1.3.0	1BR0P0030R40	Parcel 003, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	208
1.3.0	1BR0P0050R40	Parcel 005, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	106
1.3.0	1BR0P0060R40	Parcel 006, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	65
1.3.0	1BR0P0070R40	Parcel 007, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	65
1.3.0	1BR0P0080R40	Parcel 008, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	65
1.3.0	1BR0P0090R40	Parcel 009, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	65
1.3.0	1BR0P0130R40	Parcel 013, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	169
1.3.0	1BR0P0140R40	Parcel 014, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	169
1.3.0	1BR0P0160R40	Parcel 016, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	125
1.3.0	1BR0P0170R40	Parcel 017, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	106
1.3.0	1BR0P0190R40	Parcel 019, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	211
1.3.0	1BR0P0280R40	Parcel 028, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	106
1.3.0	1BR0P0300R40	Parcel 030, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	106
1.3.0	1BR0P0310R40	Parcel 031, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	106
1.3.0	1BR0P0320R40	Parcel 032, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	106
1.3.0	1BR0P0330R40	Parcel 033, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	254
1.3.0	1BR0P0360R40	Parcel 036, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	254
1.3.0	1BR0P0390R40	Parcel 039, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	125
1.3.0	1BR0P0400R40	Parcel 040, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	254
1.3.0	1BR0P0510R40	Parcel 051, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	65
1.3.0	1BR0P0580R40	Parcel 058, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	65
1.3.0	1BR0P0590R40	Parcel 059, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	65
1.3.0	1BR0P0920R40	Parcel 092, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	174
1.3.0	1BR0P0940R40	Parcel 094, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	65
1.3.0	1BR0P0960R40	Parcel 096, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	174
1.3.0	1BR0P1000R40	Parcel 100, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	65
1.3.0	1BR0P1010R40	Parcel 101, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	65

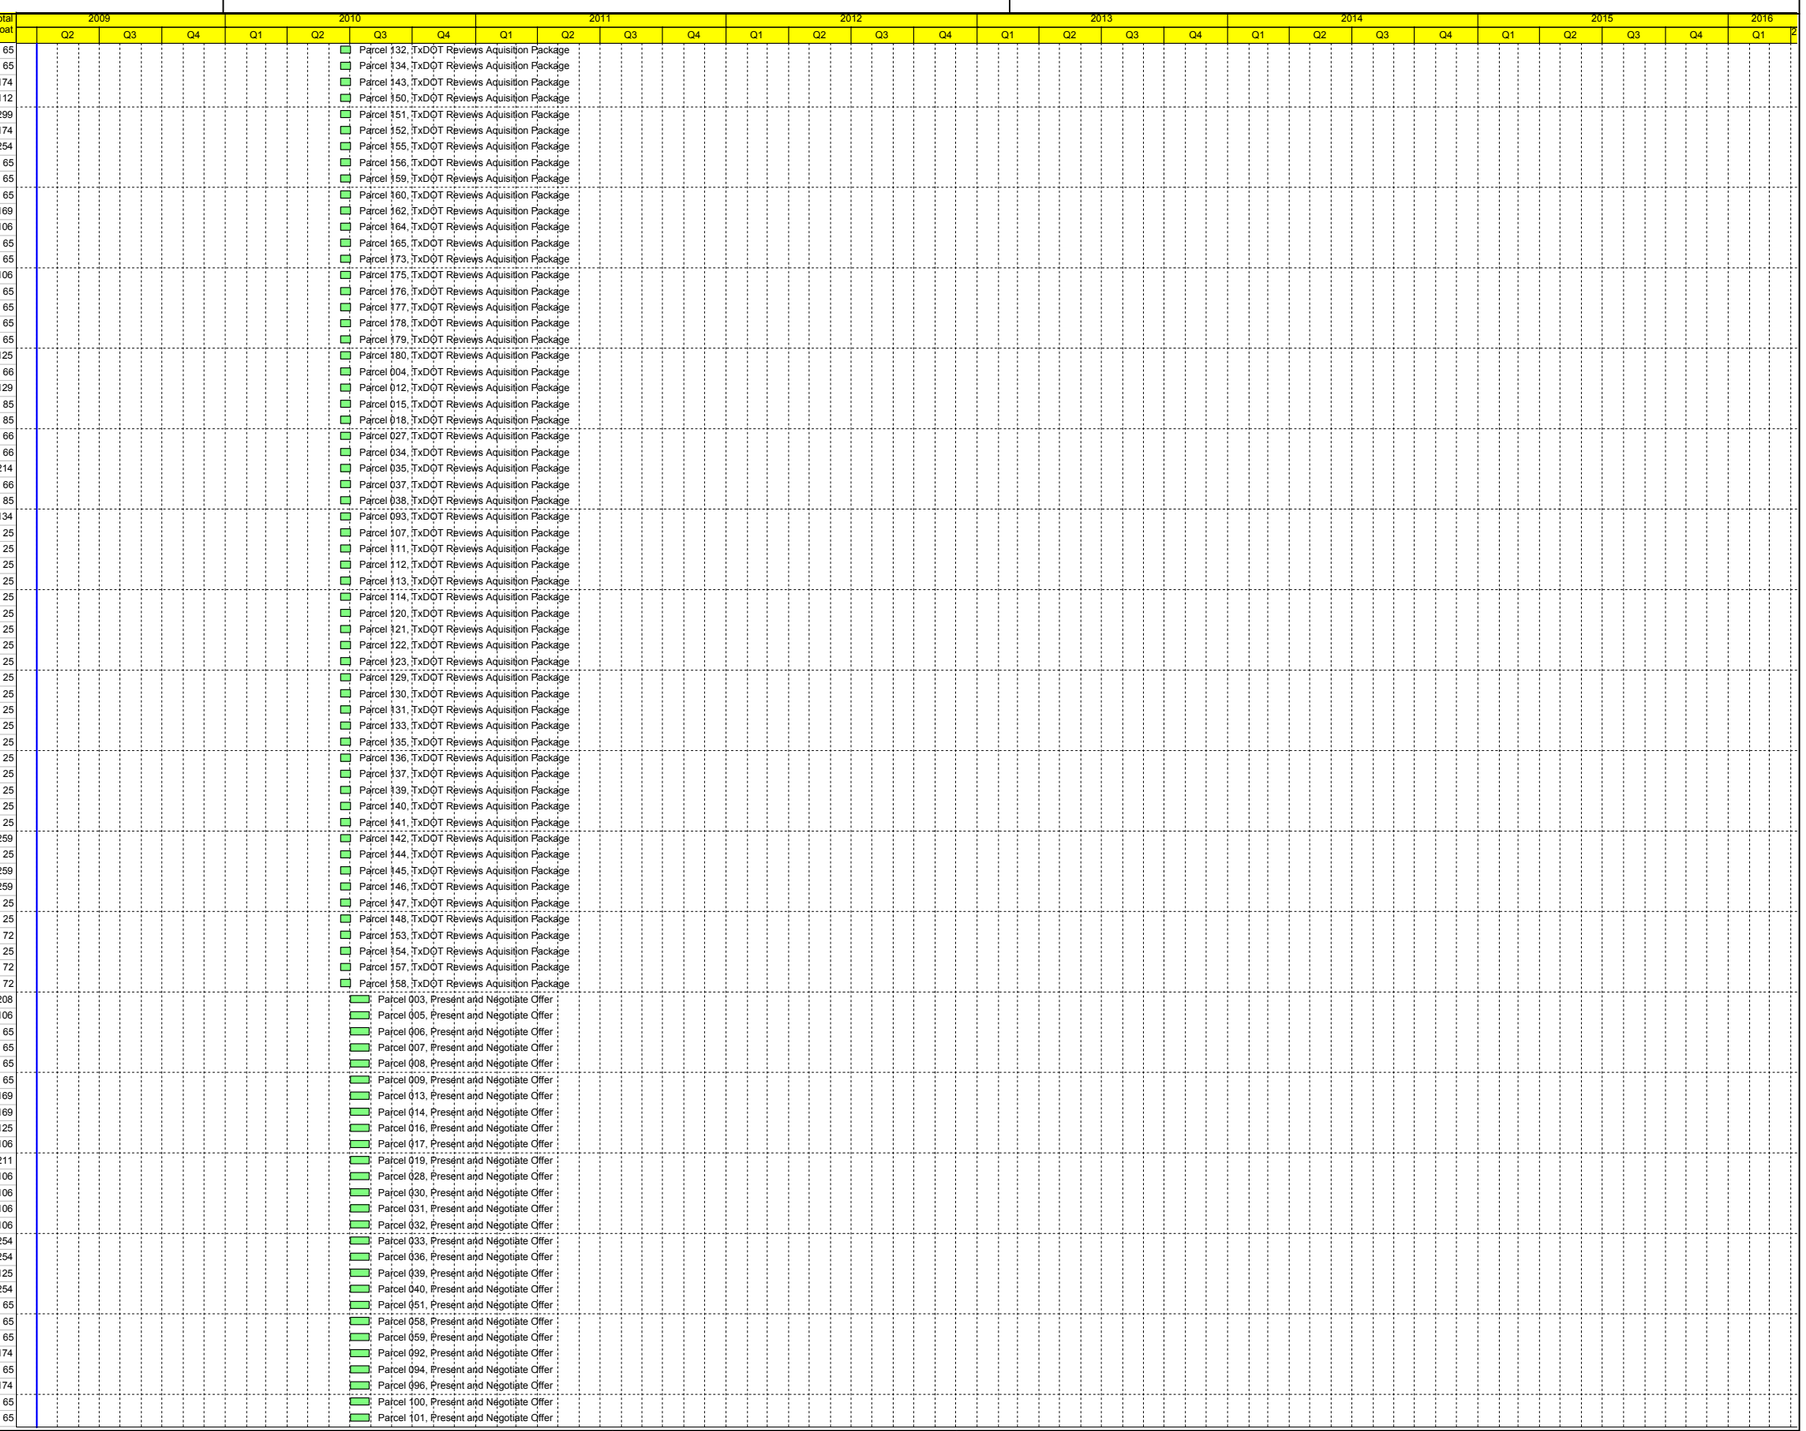

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.3.0	1BR0P1030R40	Parcel 103, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	65
1.3.0	1BR0P1040R40	Parcel 104, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	65
1.3.0	1BR0P1050R40	Parcel 105, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	65
1.3.0	1BR0P1080R40	Parcel 108, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	112
1.3.0	1BR0P1100R40	Parcel 110, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	65
1.3.0	1BR0P1150R40	Parcel 115, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	65
1.3.0	1BR0P1160R40	Parcel 116, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	65
1.3.0	1BR0P1170R40	Parcel 117, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	106
1.3.0	1BR0P1180R40	Parcel 118, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	65
1.3.0	1BR0P1240R40	Parcel 124, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	65
1.3.0	1BR0P1250R40	Parcel 125, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	65
1.3.0	1BR0P1260R40	Parcel 126, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	65
1.3.0	1BR0P1270R40	Parcel 127, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	65
1.3.0	1BR0P1320R40	Parcel 132, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	65
1.3.0	1BR0P1340R40	Parcel 134, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	65
1.3.0	1BR0P1430R40	Parcel 143, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	174
1.3.0	1BR0P1500R40	Parcel 150, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	112
1.3.0	1BR0P1510R40	Parcel 151, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	299
1.3.0	1BR0P1520R40	Parcel 152, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	174
1.3.0	1BR0P1550R40	Parcel 155, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	254
1.3.0	1BR0P1560R40	Parcel 156, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	65
1.3.0	1BR0P1590R40	Parcel 159, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	65
1.3.0	1BR0P1600R40	Parcel 160, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	65
1.3.0	1BR0P1620R40	Parcel 162, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	169
1.3.0	1BR0P1640R40	Parcel 164, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	106
1.3.0	1BR0P1650R40	Parcel 165, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	65
1.3.0	1BR0P1730R40	Parcel 173, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	65
1.3.0	1BR0P1750R40	Parcel 175, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	106
1.3.0	1BR0P1760R40	Parcel 176, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	65
1.3.0	1BR0P1770R40	Parcel 177, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	65
1.3.0	1BR0P1780R40	Parcel 178, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	65
1.3.0	1BR0P1790R40	Parcel 179, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	65
1.3.0	1BR0P1800R40	Parcel 180, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	125
1.3.0	1BR0P0040R40	Parcel 004, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	66
1.3.0	1BR0P0120R40	Parcel 012, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	129
1.3.0	1BR0P0150R40	Parcel 015, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	85
1.3.0	1BR0P0180R40	Parcel 018, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	85
1.3.0	1BR0P0270R40	Parcel 027, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	66
1.3.0	1BR0P0340R40	Parcel 034, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	66
1.3.0	1BR0P0350R40	Parcel 035, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	214
1.3.0	1BR0P0370R40	Parcel 037, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	66
1.3.0	1BR0P0380R40	Parcel 038, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	85
1.3.0	1BR0P0930R40	Parcel 093, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	134
1.3.0	1BR0P1070R40	Parcel 107, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	25
1.3.0	1BR0P1110R40	Parcel 111, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	25
1.3.0	1BR0P1120R40	Parcel 112, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	25
1.3.0	1BR0P1130R40	Parcel 113, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	25
1.3.0	1BR0P1140R40	Parcel 114, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	25
1.3.0	1BR0P1200R40	Parcel 120, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	25
1.3.0	1BR0P1210R40	Parcel 121, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	25
1.3.0	1BR0P1220R40	Parcel 122, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	25
1.3.0	1BR0P1230R40	Parcel 123, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	25
1.3.0	1BR0P1290R40	Parcel 129, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	25
1.3.0	1BR0P1300R40	Parcel 130, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	25
1.3.0	1BR0P1310R40	Parcel 131, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	25
1.3.0	1BR0P1330R40	Parcel 133, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	25
1.3.0	1BR0P1350R40	Parcel 135, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	25
1.3.0	1BR0P1360R40	Parcel 136, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	25
1.3.0	1BR0P1370R40	Parcel 137, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	25
1.3.0	1BR0P1390R40	Parcel 139, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	25
1.3.0	1BR0P1400R40	Parcel 140, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	25
1.3.0	1BR0P1410R40	Parcel 141, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	25
1.3.0	1BR0P1420R40	Parcel 142, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	259
1.3.0	1BR0P1440R40	Parcel 144, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	25
1.3.0	1BR0P1450R40	Parcel 145, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	259
1.3.0	1BR0P1460R40	Parcel 146, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	259
1.3.0	1BR0P1470R40	Parcel 147, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	25
1.3.0	1BR0P1480R40	Parcel 148, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	25
1.3.0	1BR0P1530R40	Parcel 153, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	72
1.3.0	1BR0P1540R40	Parcel 154, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	25
1.3.0	1BR0P1570R40	Parcel 157, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	72
1.3.0	1BR0P1580R40	Parcel 158, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	72
1.3.0	1BR0P0040R50	Parcel 004, Prepare for Relocation	60	02-Jul-10	24-Sep-10	156
1.3.0	1BR0P0120R50	Parcel 012, Prepare for Relocation	60	02-Jul-10	24-Sep-10	219
1.3.0	1BR0P0150R50	Parcel 015, Prepare for Relocation	60	02-Jul-10	24-Sep-10	175
1.3.0	1BR0P0180R50	Parcel 018, Prepare for Relocation	60	02-Jul-10	24-Sep-10	175
1.3.0	1BR0P0270R50	Parcel 027, Prepare for Relocation	60	02-Jul-10	24-Sep-10	156
1.3.0	1BR0P0340R50	Parcel 034, Prepare for Relocation	60	02-Jul-10	24-Sep-10	156
1.3.0	1BR0P0350R50	Parcel 035, Prepare for Relocation	60	02-Jul-10	24-Sep-10	304
1.3.0	1BR0P0370R50	Parcel 037, Prepare for Relocation	60	02-Jul-10	24-Sep-10	156
1.3.0	1BR0P0380R50	Parcel 038, Prepare for Relocation	60	02-Jul-10	24-Sep-10	175
1.3.0	1BR0P0930R50	Parcel 093, Prepare for Relocation	60	02-Jul-10	24-Sep-10	224
1.3.0	1BR0P1070R50	Parcel 107, Prepare for Relocation	60	02-Jul-10	24-Sep-10	115
1.3.0	1BR0P1110R50	Parcel 111, Prepare for Relocation	60	02-Jul-10	24-Sep-10	115
1.3.0	1BR0P1120R50	Parcel 112, Prepare for Relocation	60	02-Jul-10	24-Sep-10	115
1.3.0	1BR0P1130R50	Parcel 113, Prepare for Relocation	60	02-Jul-10	24-Sep-10	115

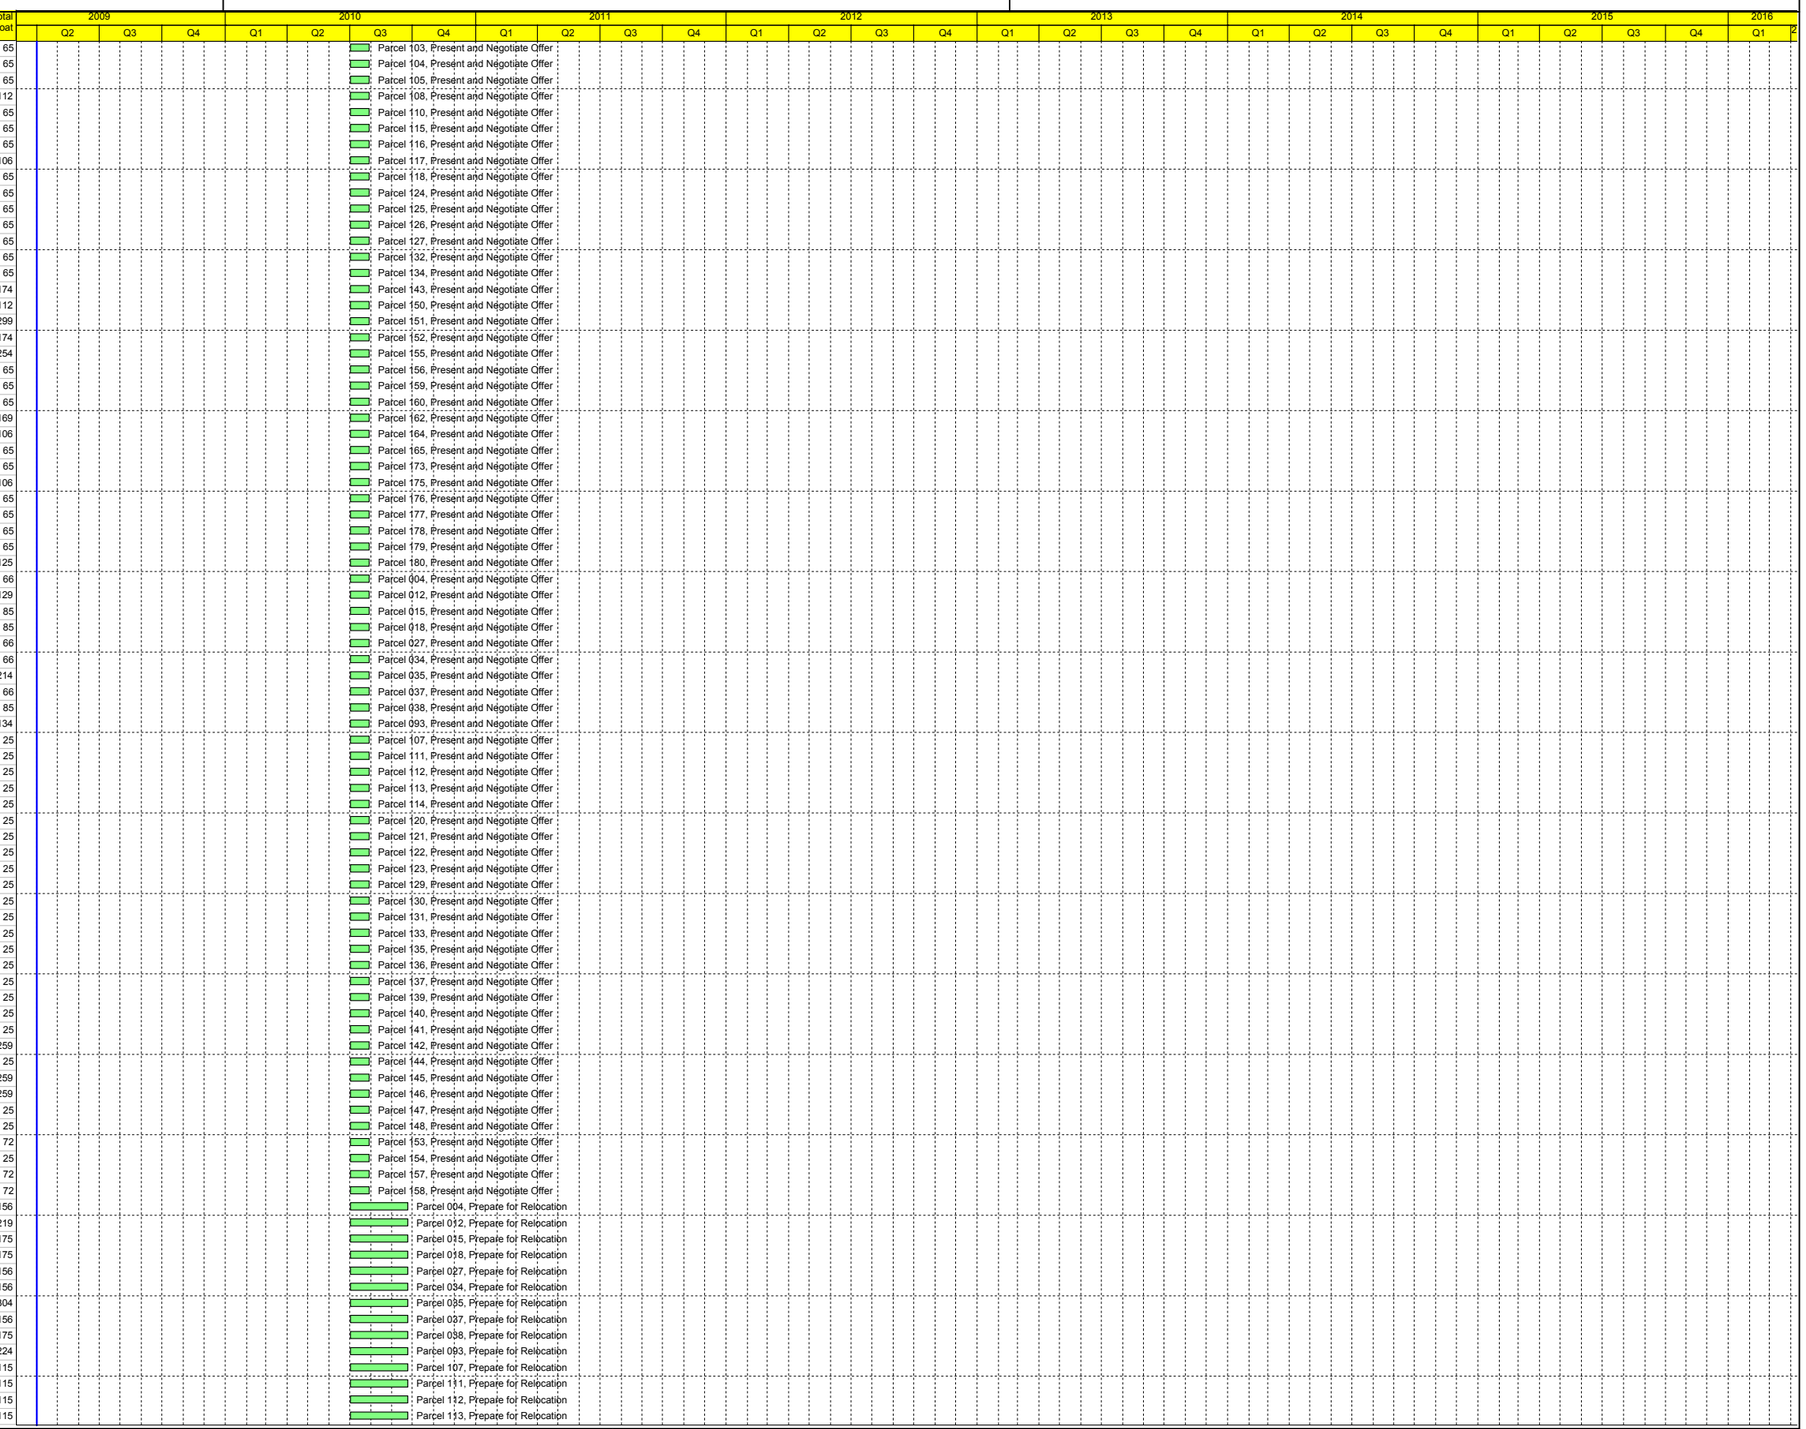

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.3.0	1BR0P1140R50	Parcel 114, Prepare for Relocation	60	02-Jul-10	24-Sep-10	115
1.3.0	1BR0P1200R50	Parcel 120, Prepare for Relocation	60	02-Jul-10	24-Sep-10	115
1.3.0	1BR0P1210R50	Parcel 121, Prepare for Relocation	60	02-Jul-10	24-Sep-10	115
1.3.0	1BR0P1220R50	Parcel 122, Prepare for Relocation	60	02-Jul-10	24-Sep-10	115
1.3.0	1BR0P1230R50	Parcel 123, Prepare for Relocation	60	02-Jul-10	24-Sep-10	115
1.3.0	1BR0P1290R50	Parcel 129, Prepare for Relocation	60	02-Jul-10	24-Sep-10	115
1.3.0	1BR0P1300R50	Parcel 130, Prepare for Relocation	60	02-Jul-10	24-Sep-10	115
1.3.0	1BR0P1310R50	Parcel 131, Prepare for Relocation	60	02-Jul-10	24-Sep-10	115
1.3.0	1BR0P1330R50	Parcel 133, Prepare for Relocation	60	02-Jul-10	24-Sep-10	115
1.3.0	1BR0P1350R50	Parcel 135, Prepare for Relocation	60	02-Jul-10	24-Sep-10	115
1.3.0	1BR0P1360R50	Parcel 136, Prepare for Relocation	60	02-Jul-10	24-Sep-10	115
1.3.0	1BR0P1370R50	Parcel 137, Prepare for Relocation	60	02-Jul-10	24-Sep-10	115
1.3.0	1BR0P1390R50	Parcel 139, Prepare for Relocation	60	02-Jul-10	24-Sep-10	115
1.3.0	1BR0P1400R50	Parcel 140, Prepare for Relocation	60	02-Jul-10	24-Sep-10	115
1.3.0	1BR0P1410R50	Parcel 141, Prepare for Relocation	60	02-Jul-10	24-Sep-10	115
1.3.0	1BR0P1420R50	Parcel 142, Prepare for Relocation	60	02-Jul-10	24-Sep-10	349
1.3.0	1BR0P1440R50	Parcel 144, Prepare for Relocation	60	02-Jul-10	24-Sep-10	115
1.3.0	1BR0P1450R50	Parcel 145, Prepare for Relocation	60	02-Jul-10	24-Sep-10	349
1.3.0	1BR0P1460R50	Parcel 146, Prepare for Relocation	60	02-Jul-10	24-Sep-10	349
1.3.0	1BR0P1470R50	Parcel 147, Prepare for Relocation	60	02-Jul-10	24-Sep-10	115
1.3.0	1BR0P1480R50	Parcel 148, Prepare for Relocation	60	02-Jul-10	24-Sep-10	115
1.3.0	1BR0P1530R50	Parcel 153, Prepare for Relocation	60	02-Jul-10	24-Sep-10	162
1.3.0	1BR0P1540R50	Parcel 154, Prepare for Relocation	60	02-Jul-10	24-Sep-10	115
1.3.0	1BR0P1570R50	Parcel 157, Prepare for Relocation	60	02-Jul-10	24-Sep-10	162
1.3.0	1BR0P1580R50	Parcel 158, Prepare for Relocation	60	02-Jul-10	24-Sep-10	162
1.3.0	1BR0P0250R60	Parcel 025, Condemnation Process (if requir...	130	07-Jul-10	05-Jan-11	118
1.3.0	1BR0P0030R60	Parcel 003, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	208
1.3.0	1BR0P0050R60	Parcel 005, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	106
1.3.0	1BR0P0060R60	Parcel 006, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	65
1.3.0	1BR0P0070R60	Parcel 007, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	65
1.3.0	1BR0P0080R60	Parcel 008, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	65
1.3.0	1BR0P0090R60	Parcel 009, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	65
1.3.0	1BR0P0130R60	Parcel 013, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	169
1.3.0	1BR0P0140R60	Parcel 014, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	169
1.3.0	1BR0P0160R60	Parcel 016, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	125
1.3.0	1BR0P0170R60	Parcel 017, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	106
1.3.0	1BR0P0190R60	Parcel 019, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	211
1.3.0	1BR0P0280R60	Parcel 028, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	106
1.3.0	1BR0P0300R60	Parcel 030, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	106
1.3.0	1BR0P0310R60	Parcel 031, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	106
1.3.0	1BR0P0320R60	Parcel 032, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	106
1.3.0	1BR0P0330R60	Parcel 033, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	254
1.3.0	1BR0P0360R60	Parcel 036, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	254
1.3.0	1BR0P0390R60	Parcel 039, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	125
1.3.0	1BR0P0400R60	Parcel 040, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	254
1.3.0	1BR0P0510R60	Parcel 051, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	65
1.3.0	1BR0P0580R60	Parcel 058, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	65
1.3.0	1BR0P0590R60	Parcel 059, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	65
1.3.0	1BR0P0920R60	Parcel 092, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	174
1.3.0	1BR0P0940R60	Parcel 094, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	65
1.3.0	1BR0P0960R60	Parcel 096, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	174
1.3.0	1BR0P1000R60	Parcel 100, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	65
1.3.0	1BR0P1010R60	Parcel 101, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	65
1.3.0	1BR0P1030R60	Parcel 103, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	65
1.3.0	1BR0P1040R60	Parcel 104, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	65
1.3.0	1BR0P1050R60	Parcel 105, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	65
1.3.0	1BR0P1080R60	Parcel 108, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	112
1.3.0	1BR0P1100R60	Parcel 110, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	65
1.3.0	1BR0P1150R60	Parcel 115, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	65
1.3.0	1BR0P1160R60	Parcel 116, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	65
1.3.0	1BR0P1170R60	Parcel 117, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	106
1.3.0	1BR0P1180R60	Parcel 118, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	65
1.3.0	1BR0P1240R60	Parcel 124, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	65
1.3.0	1BR0P1250R60	Parcel 125, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	65
1.3.0	1BR0P1260R60	Parcel 126, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	65
1.3.0	1BR0P1270R60	Parcel 127, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	65
1.3.0	1BR0P1320R60	Parcel 132, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	65
1.3.0	1BR0P1340R60	Parcel 134, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	65
1.3.0	1BR0P1430R60	Parcel 143, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	174
1.3.0	1BR0P1500R60	Parcel 150, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	112
1.3.0	1BR0P1510R60	Parcel 151, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	299
1.3.0	1BR0P1520R60	Parcel 152, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	174
1.3.0	1BR0P1550R60	Parcel 155, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	254
1.3.0	1BR0P1560R60	Parcel 156, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	65
1.3.0	1BR0P1590R60	Parcel 159, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	65
1.3.0	1BR0P1600R60	Parcel 160, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	65
1.3.0	1BR0P1620R60	Parcel 162, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	169
1.3.0	1BR0P1640R60	Parcel 164, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	106
1.3.0	1BR0P1650R60	Parcel 165, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	65
1.3.0	1BR0P1730R60	Parcel 173, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	65
1.3.0	1BR0P1750R60	Parcel 175, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	106
1.3.0	1BR0P1760R60	Parcel 176, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	65
1.3.0	1BR0P1770R60	Parcel 177, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	65
1.3.0	1BR0P1780R60	Parcel 178, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	65
1.3.0	1BR0P1790R60	Parcel 179, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	65
1.3.0	1BR0P1800R60	Parcel 180, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	125

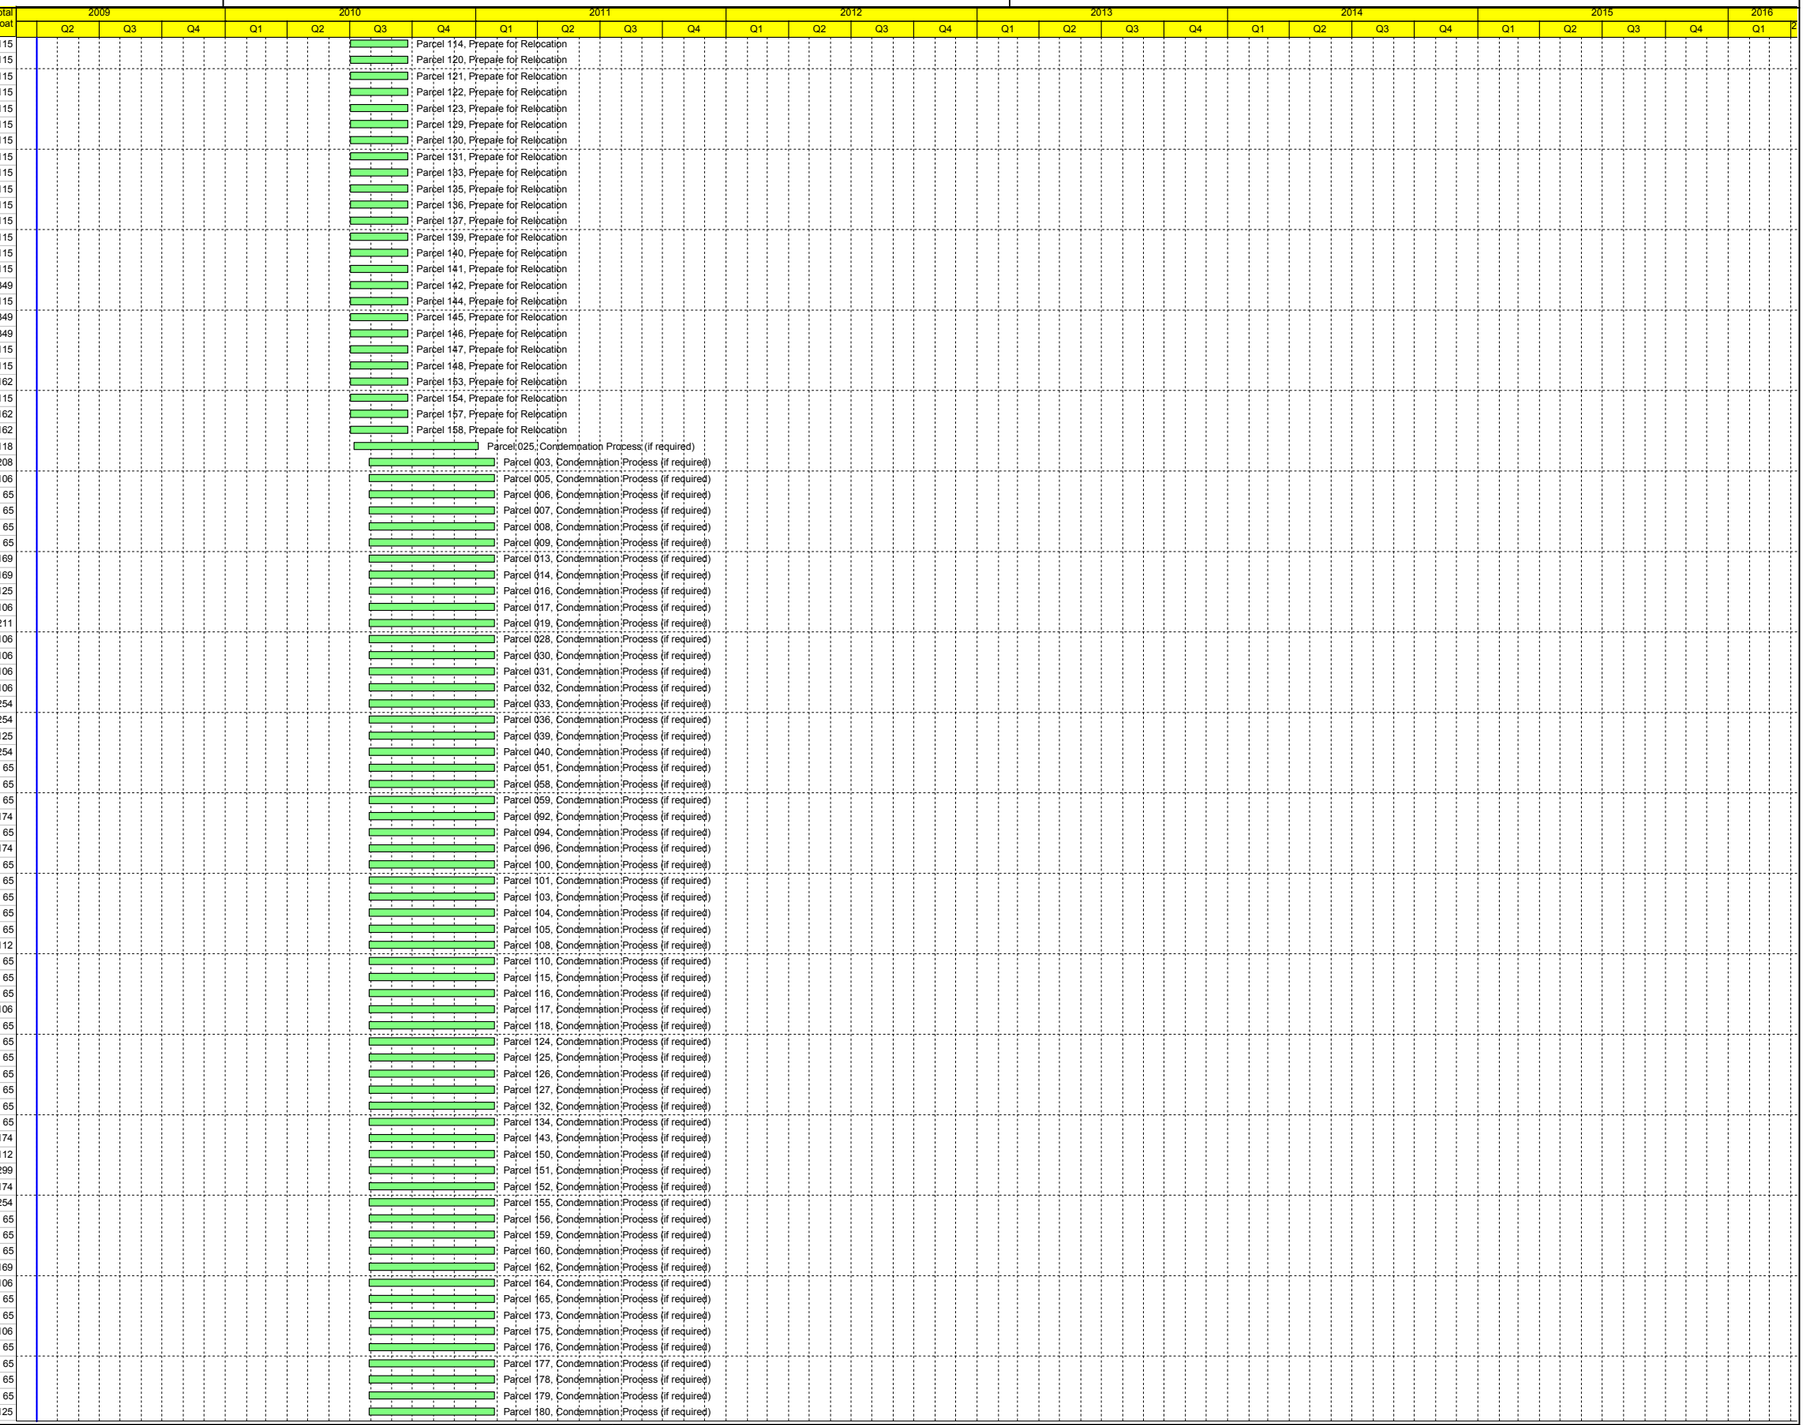

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.3.0	1BR0P0040R60	Parcel 004, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	66
1.3.0	1BR0P0120R60	Parcel 012, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	129
1.3.0	1BR0P0150R60	Parcel 015, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	85
1.3.0	1BR0P0180R60	Parcel 018, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	85
1.3.0	1BR0P0270R60	Parcel 027, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	66
1.3.0	1BR0P0340R60	Parcel 034, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	66
1.3.0	1BR0P0350R60	Parcel 035, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	214
1.3.0	1BR0P0370R60	Parcel 037, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	66
1.3.0	1BR0P0380R60	Parcel 038, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	85
1.3.0	1BR0P0930R60	Parcel 093, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	134
1.3.0	1BR0P1070R60	Parcel 107, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	25
1.3.0	1BR0P1110R60	Parcel 111, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	25
1.3.0	1BR0P1120R60	Parcel 112, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	25
1.3.0	1BR0P1130R60	Parcel 113, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	25
1.3.0	1BR0P1140R60	Parcel 114, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	25
1.3.0	1BR0P1200R60	Parcel 120, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	25
1.3.0	1BR0P1210R60	Parcel 121, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	25
1.3.0	1BR0P1220R60	Parcel 122, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	25
1.3.0	1BR0P1230R60	Parcel 123, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	25
1.3.0	1BR0P1290R60	Parcel 129, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	25
1.3.0	1BR0P1300R60	Parcel 130, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	25
1.3.0	1BR0P1310R60	Parcel 131, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	25
1.3.0	1BR0P1330R60	Parcel 133, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	25
1.3.0	1BR0P1350R60	Parcel 135, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	25
1.3.0	1BR0P1360R60	Parcel 136, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	25
1.3.0	1BR0P1370R60	Parcel 137, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	25
1.3.0	1BR0P1390R60	Parcel 139, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	25
1.3.0	1BR0P1400R60	Parcel 140, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	25
1.3.0	1BR0P1410R60	Parcel 141, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	25
1.3.0	1BR0P1420R60	Parcel 142, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	259
1.3.0	1BR0P1440R60	Parcel 144, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	25
1.3.0	1BR0P1450R60	Parcel 145, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	259
1.3.0	1BR0P1460R60	Parcel 146, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	259
1.3.0	1BR0P1470R60	Parcel 147, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	25
1.3.0	1BR0P1480R60	Parcel 148, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	25
1.3.0	1BR0P1530R60	Parcel 153, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	72
1.3.0	1BR0P1540R60	Parcel 154, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	25
1.3.0	1BR0P1570R60	Parcel 157, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	72
1.3.0	1BR0P1580R60	Parcel 158, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	72
1.3.0	1BR0P1380R70	Parcel 138, Execute Relocation	20	10-Nov-...	08-Dec-10	82
1.3.0	1BR0P0260R70	Parcel 026, Execute Relocation	20	26-Nov-...	24-Dec-10	68
1.3.0	1BR0P1380R80	Parcel 138, Demolish Existing Improvements	20	08-Dec-...	05-Jan-11	82
1.3.0	1BR0P0260R80	Parcel 026, Demolish Existing Improvements	20	24-Dec-...	21-Jan-11	68
1.3.0	1BR0P0250R99	Parcel 025, Cleared for Construction	0		05-Jan-11	118
1.3.0	1BR0P1380R99	Parcel 138, Cleared for Construction	0		05-Jan-11	82
1.3.0	1BR0P0260R99	Parcel 026, Cleared for Construction	0		21-Jan-11	68
1.3.0	1BR0P0030R99	Parcel 003, Cleared for Construction	0		28-Jan-11	208
1.3.0	1BR0P0050R99	Parcel 005, Cleared for Construction	0		28-Jan-11	106
1.3.0	1BR0P0060R99	Parcel 006, Cleared for Construction	0		28-Jan-11	65
1.3.0	1BR0P0070R99	Parcel 007, Cleared for Construction	0		28-Jan-11	65
1.3.0	1BR0P0080R99	Parcel 008, Cleared for Construction	0		28-Jan-11	65
1.3.0	1BR0P0090R99	Parcel 009, Cleared for Construction	0		28-Jan-11	65
1.3.0	1BR0P0130R99	Parcel 013, Cleared for Construction	0		28-Jan-11	169
1.3.0	1BR0P0140R99	Parcel 014, Cleared for Construction	0		28-Jan-11	169
1.3.0	1BR0P0160R99	Parcel 016, Cleared for Construction	0		28-Jan-11	125
1.3.0	1BR0P0170R99	Parcel 017, Cleared for Construction	0		28-Jan-11	106
1.3.0	1BR0P0190R99	Parcel 019, Cleared for Construction	0		28-Jan-11	211
1.3.0	1BR0P0280R99	Parcel 028, Cleared for Construction	0		28-Jan-11	106
1.3.0	1BR0P0300R99	Parcel 030, Cleared for Construction	0		28-Jan-11	106
1.3.0	1BR0P0310R99	Parcel 031, Cleared for Construction	0		28-Jan-11	106
1.3.0	1BR0P0320R99	Parcel 032, Cleared for Construction	0		28-Jan-11	106
1.3.0	1BR0P0330R99	Parcel 033, Cleared for Construction	0		28-Jan-11	254
1.3.0	1BR0P0360R99	Parcel 036, Cleared for Construction	0		28-Jan-11	254
1.3.0	1BR0P0390R99	Parcel 039, Cleared for Construction	0		28-Jan-11	125
1.3.0	1BR0P0400R99	Parcel 040, Cleared for Construction	0		28-Jan-11	254
1.3.0	1BR0P0510R99	Parcel 051, Cleared for Construction	0		28-Jan-11	65
1.3.0	1BR0P0580R99	Parcel 058, Cleared for Construction	0		28-Jan-11	65
1.3.0	1BR0P0590R99	Parcel 059, Cleared for Construction	0		28-Jan-11	65
1.3.0	1BR0P0920R99	Parcel 092, Cleared for Construction	0		28-Jan-11	174
1.3.0	1BR0P0940R99	Parcel 094, Cleared for Construction	0		28-Jan-11	65
1.3.0	1BR0P0960R99	Parcel 096, Cleared for Construction	0		28-Jan-11	174
1.3.0	1BR0P1000R99	Parcel 100, Cleared for Construction	0		28-Jan-11	65
1.3.0	1BR0P1010R99	Parcel 101, Cleared for Construction	0		28-Jan-11	65
1.3.0	1BR0P1030R99	Parcel 103, Cleared for Construction	0		28-Jan-11	65
1.3.0	1BR0P1040R99	Parcel 104, Cleared for Construction	0		28-Jan-11	65
1.3.0	1BR0P1050R99	Parcel 105, Cleared for Construction	0		28-Jan-11	65
1.3.0	1BR0P1080R99	Parcel 108, Cleared for Construction	0		28-Jan-11	112
1.3.0	1BR0P1100R99	Parcel 110, Cleared for Construction	0		28-Jan-11	65
1.3.0	1BR0P1150R99	Parcel 115, Cleared for Construction	0		28-Jan-11	65
1.3.0	1BR0P1160R99	Parcel 116, Cleared for Construction	0		28-Jan-11	65
1.3.0	1BR0P1170R99	Parcel 117, Cleared for Construction	0		28-Jan-11	106
1.3.0	1BR0P1180R99	Parcel 118, Cleared for Construction	0		28-Jan-11	65
1.3.0	1BR0P1240R99	Parcel 124, Cleared for Construction	0		28-Jan-11	65
1.3.0	1BR0P1250R99	Parcel 125, Cleared for Construction	0		28-Jan-11	65
1.3.0	1BR0P1260R99	Parcel 126, Cleared for Construction	0		28-Jan-11	65
1.3.0	1BR0P1270R99	Parcel 127, Cleared for Construction	0		28-Jan-11	65

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.3.0	1BR0P1320R99	Parcel 132, Cleared for Construction	0		28-Jan-11	65
1.3.0	1BR0P1340R99	Parcel 134, Cleared for Construction	0		28-Jan-11	65
1.3.0	1BR0P1430R99	Parcel 143, Cleared for Construction	0		28-Jan-11	174
1.3.0	1BR0P1500R99	Parcel 150, Cleared for Construction	0		28-Jan-11	112
1.3.0	1BR0P1510R99	Parcel 151, Cleared for Construction	0		28-Jan-11	299
1.3.0	1BR0P1520R99	Parcel 152, Cleared for Construction	0		28-Jan-11	174
1.3.0	1BR0P1550R99	Parcel 155, Cleared for Construction	0		28-Jan-11	254
1.3.0	1BR0P1560R99	Parcel 156, Cleared for Construction	0		28-Jan-11	65
1.3.0	1BR0P1590R99	Parcel 159, Cleared for Construction	0		28-Jan-11	65
1.3.0	1BR0P1600R99	Parcel 160, Cleared for Construction	0		28-Jan-11	65
1.3.0	1BR0P1620R99	Parcel 162, Cleared for Construction	0		28-Jan-11	169
1.3.0	1BR0P1640R99	Parcel 164, Cleared for Construction	0		28-Jan-11	106
1.3.0	1BR0P1650R99	Parcel 165, Cleared for Construction	0		28-Jan-11	65
1.3.0	1BR0P1730R99	Parcel 173, Cleared for Construction	0		28-Jan-11	65
1.3.0	1BR0P1750R99	Parcel 175, Cleared for Construction	0		28-Jan-11	106
1.3.0	1BR0P1760R99	Parcel 176, Cleared for Construction	0		28-Jan-11	65
1.3.0	1BR0P1770R99	Parcel 177, Cleared for Construction	0		28-Jan-11	65
1.3.0	1BR0P1780R99	Parcel 178, Cleared for Construction	0		28-Jan-11	65
1.3.0	1BR0P1790R99	Parcel 179, Cleared for Construction	0		28-Jan-11	65
1.3.0	1BR0P1800R99	Parcel 180, Cleared for Construction	0		28-Jan-11	125
1.3.0	1BR0P0040R70	Parcel 004, Execute Relocation	20	28-Jan-11	25-Feb-11	66
1.3.0	1BR0P0120R70	Parcel 012, Execute Relocation	20	28-Jan-11	25-Feb-11	129
1.3.0	1BR0P0150R70	Parcel 015, Execute Relocation	20	28-Jan-11	25-Feb-11	85
1.3.0	1BR0P0180R70	Parcel 018, Execute Relocation	20	28-Jan-11	25-Feb-11	85
1.3.0	1BR0P0270R70	Parcel 027, Execute Relocation	20	28-Jan-11	25-Feb-11	66
1.3.0	1BR0P0340R70	Parcel 034, Execute Relocation	20	28-Jan-11	25-Feb-11	66
1.3.0	1BR0P0350R70	Parcel 035, Execute Relocation	20	28-Jan-11	25-Feb-11	214
1.3.0	1BR0P0370R70	Parcel 037, Execute Relocation	20	28-Jan-11	25-Feb-11	66
1.3.0	1BR0P0380R70	Parcel 038, Execute Relocation	20	28-Jan-11	25-Feb-11	85
1.3.0	1BR0P0930R70	Parcel 093, Execute Relocation	20	28-Jan-11	25-Feb-11	134
1.3.0	1BR0P1070R70	Parcel 107, Execute Relocation	20	28-Jan-11	25-Feb-11	25
1.3.0	1BR0P1110R70	Parcel 111, Execute Relocation	20	28-Jan-11	25-Feb-11	25
1.3.0	1BR0P1120R70	Parcel 112, Execute Relocation	20	28-Jan-11	25-Feb-11	25
1.3.0	1BR0P1130R70	Parcel 113, Execute Relocation	20	28-Jan-11	25-Feb-11	25
1.3.0	1BR0P1140R70	Parcel 114, Execute Relocation	20	28-Jan-11	25-Feb-11	25
1.3.0	1BR0P1200R70	Parcel 120, Execute Relocation	20	28-Jan-11	25-Feb-11	25
1.3.0	1BR0P1210R70	Parcel 121, Execute Relocation	20	28-Jan-11	25-Feb-11	25
1.3.0	1BR0P1220R70	Parcel 122, Execute Relocation	20	28-Jan-11	25-Feb-11	25
1.3.0	1BR0P1230R70	Parcel 123, Execute Relocation	20	28-Jan-11	25-Feb-11	25
1.3.0	1BR0P1290R70	Parcel 129, Execute Relocation	20	28-Jan-11	25-Feb-11	25
1.3.0	1BR0P1300R70	Parcel 130, Execute Relocation	20	28-Jan-11	25-Feb-11	25
1.3.0	1BR0P1310R70	Parcel 131, Execute Relocation	20	28-Jan-11	25-Feb-11	25
1.3.0	1BR0P1330R70	Parcel 133, Execute Relocation	20	28-Jan-11	25-Feb-11	25
1.3.0	1BR0P1350R70	Parcel 135, Execute Relocation	20	28-Jan-11	25-Feb-11	25
1.3.0	1BR0P1360R70	Parcel 136, Execute Relocation	20	28-Jan-11	25-Feb-11	25
1.3.0	1BR0P1370R70	Parcel 137, Execute Relocation	20	28-Jan-11	25-Feb-11	25
1.3.0	1BR0P1390R70	Parcel 139, Execute Relocation	20	28-Jan-11	25-Feb-11	25
1.3.0	1BR0P1400R70	Parcel 140, Execute Relocation	20	28-Jan-11	25-Feb-11	25
1.3.0	1BR0P1410R70	Parcel 141, Execute Relocation	20	28-Jan-11	25-Feb-11	25
1.3.0	1BR0P1420R70	Parcel 142, Execute Relocation	20	28-Jan-11	25-Feb-11	259
1.3.0	1BR0P1440R70	Parcel 144, Execute Relocation	20	28-Jan-11	25-Feb-11	25
1.3.0	1BR0P1450R70	Parcel 145, Execute Relocation	20	28-Jan-11	25-Feb-11	259
1.3.0	1BR0P1460R70	Parcel 146, Execute Relocation	20	28-Jan-11	25-Feb-11	259
1.3.0	1BR0P1470R70	Parcel 147, Execute Relocation	20	28-Jan-11	25-Feb-11	25
1.3.0	1BR0P1480R70	Parcel 148, Execute Relocation	20	28-Jan-11	25-Feb-11	25
1.3.0	1BR0P1530R70	Parcel 153, Execute Relocation	20	28-Jan-11	25-Feb-11	72
1.3.0	1BR0P1540R70	Parcel 154, Execute Relocation	20	28-Jan-11	25-Feb-11	25
1.3.0	1BR0P1570R70	Parcel 157, Execute Relocation	20	28-Jan-11	25-Feb-11	72
1.3.0	1BR0P1580R70	Parcel 158, Execute Relocation	20	28-Jan-11	25-Feb-11	72
1.3.0	1BR0P0040R80	Parcel 004, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	66
1.3.0	1BR0P0120R80	Parcel 012, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	129
1.3.0	1BR0P0150R80	Parcel 015, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	85
1.3.0	1BR0P0180R80	Parcel 018, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	85
1.3.0	1BR0P0270R80	Parcel 027, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	66
1.3.0	1BR0P0340R80	Parcel 034, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	66
1.3.0	1BR0P0350R80	Parcel 035, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	214
1.3.0	1BR0P0370R80	Parcel 037, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	66
1.3.0	1BR0P0380R80	Parcel 038, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	85
1.3.0	1BR0P0930R80	Parcel 093, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	134
1.3.0	1BR0P1070R80	Parcel 107, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	25
1.3.0	1BR0P1110R80	Parcel 111, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	25
1.3.0	1BR0P1120R80	Parcel 112, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	25
1.3.0	1BR0P1130R80	Parcel 113, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	25
1.3.0	1BR0P1140R80	Parcel 114, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	25
1.3.0	1BR0P1200R80	Parcel 120, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	25
1.3.0	1BR0P1210R80	Parcel 121, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	25
1.3.0	1BR0P1220R80	Parcel 122, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	25
1.3.0	1BR0P1230R80	Parcel 123, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	25
1.3.0	1BR0P1290R80	Parcel 129, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	25
1.3.0	1BR0P1300R80	Parcel 130, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	25
1.3.0	1BR0P1310R80	Parcel 131, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	25
1.3.0	1BR0P1330R80	Parcel 133, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	25
1.3.0	1BR0P1350R80	Parcel 135, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	25
1.3.0	1BR0P1360R80	Parcel 136, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	25
1.3.0	1BR0P1370R80	Parcel 137, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	25
1.3.0	1BR0P1390R80	Parcel 139, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	25

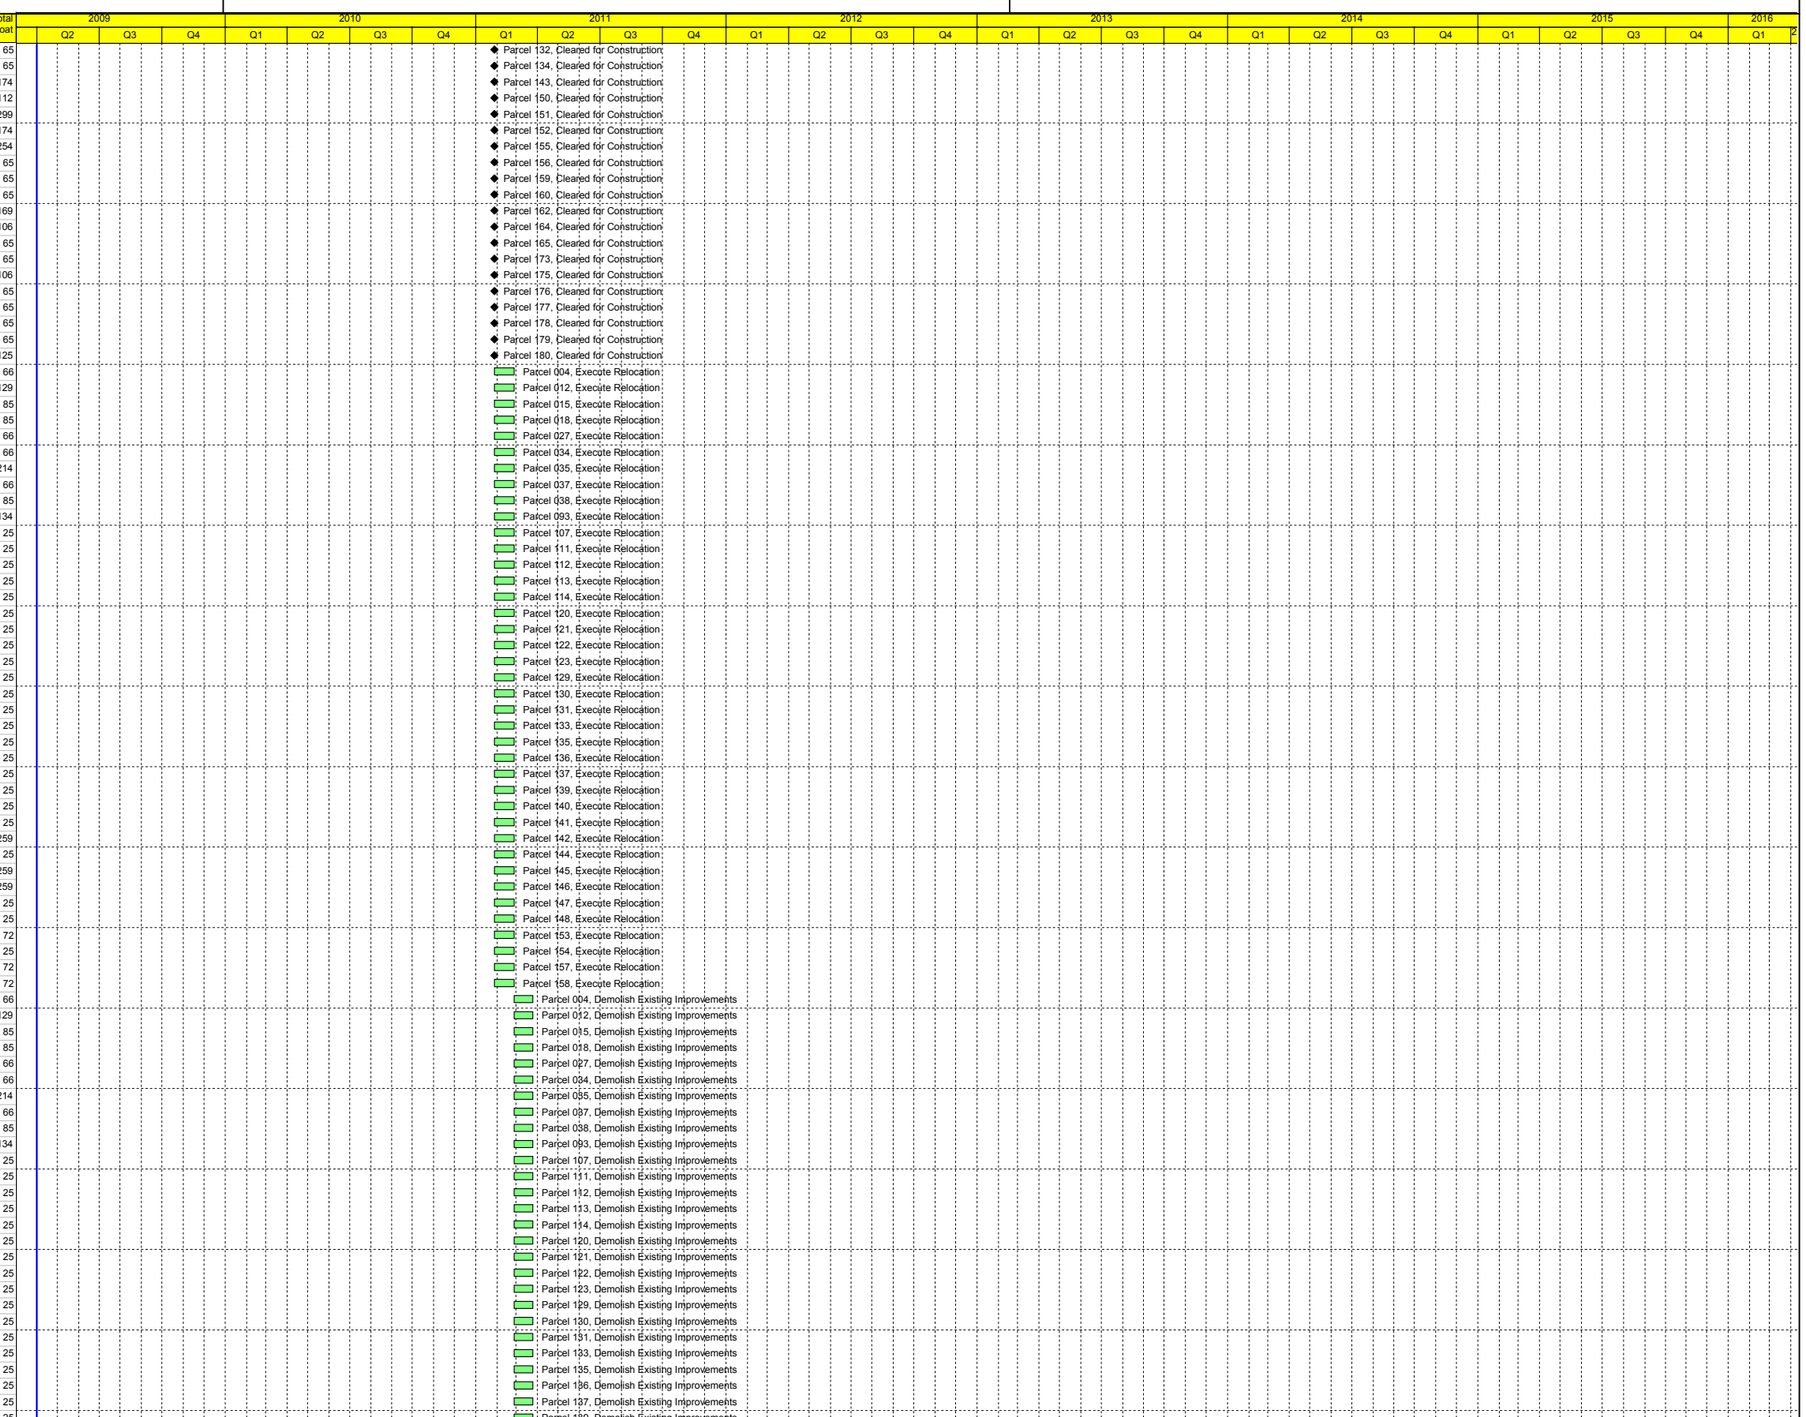

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.3.0	1BR0P1400R80	Parcel 140, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	25
1.3.0	1BR0P1410R80	Parcel 141, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	25
1.3.0	1BR0P1420R80	Parcel 142, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	259
1.3.0	1BR0P1440R80	Parcel 144, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	25
1.3.0	1BR0P1450R80	Parcel 145, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	259
1.3.0	1BR0P1460R80	Parcel 146, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	259
1.3.0	1BR0P1470R80	Parcel 147, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	25
1.3.0	1BR0P1480R80	Parcel 148, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	25
1.3.0	1BR0P1530R80	Parcel 153, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	72
1.3.0	1BR0P1540R80	Parcel 154, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	25
1.3.0	1BR0P1570R80	Parcel 157, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	72
1.3.0	1BR0P1580R80	Parcel 158, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	72
1.3.0	1BR0P0040R99	Parcel 004, Cleared for Construction	0		25-Mar-11	66
1.3.0	1BR0P0120R99	Parcel 012, Cleared for Construction	0		25-Mar-11	129
1.3.0	1BR0P0150R99	Parcel 015, Cleared for Construction	0		25-Mar-11	85
1.3.0	1BR0P0180R99	Parcel 018, Cleared for Construction	0		25-Mar-11	85
1.3.0	1BR0P0270R99	Parcel 027, Cleared for Construction	0		25-Mar-11	66
1.3.0	1BR0P0340R99	Parcel 034, Cleared for Construction	0		25-Mar-11	66
1.3.0	1BR0P0350R99	Parcel 035, Cleared for Construction	0		25-Mar-11	214
1.3.0	1BR0P0370R99	Parcel 037, Cleared for Construction	0		25-Mar-11	66
1.3.0	1BR0P0380R99	Parcel 038, Cleared for Construction	0		25-Mar-11	85
1.3.0	1BR0P0930R99	Parcel 093, Cleared for Construction	0		25-Mar-11	134
1.3.0	1BR0P1070R99	Parcel 107, Cleared for Construction	0		25-Mar-11	25
1.3.0	1BR0P1110R99	Parcel 111, Cleared for Construction	0		25-Mar-11	25
1.3.0	1BR0P1120R99	Parcel 112, Cleared for Construction	0		25-Mar-11	25
1.3.0	1BR0P1130R99	Parcel 113, Cleared for Construction	0		25-Mar-11	25
1.3.0	1BR0P1140R99	Parcel 114, Cleared for Construction	0		25-Mar-11	25
1.3.0	1BR0P1200R99	Parcel 120, Cleared for Construction	0		25-Mar-11	25
1.3.0	1BR0P1210R99	Parcel 121, Cleared for Construction	0		25-Mar-11	25
1.3.0	1BR0P1220R99	Parcel 122, Cleared for Construction	0		25-Mar-11	25
1.3.0	1BR0P1230R99	Parcel 123, Cleared for Construction	0		25-Mar-11	25
1.3.0	1BR0P1290R99	Parcel 129, Cleared for Construction	0		25-Mar-11	25
1.3.0	1BR0P1300R99	Parcel 130, Cleared for Construction	0		25-Mar-11	25
1.3.0	1BR0P1310R99	Parcel 131, Cleared for Construction	0		25-Mar-11	25
1.3.0	1BR0P1330R99	Parcel 133, Cleared for Construction	0		25-Mar-11	25
1.3.0	1BR0P1350R99	Parcel 135, Cleared for Construction	0		25-Mar-11	25
1.3.0	1BR0P1360R99	Parcel 136, Cleared for Construction	0		25-Mar-11	25
1.3.0	1BR0P1370R99	Parcel 137, Cleared for Construction	0		25-Mar-11	25
1.3.0	1BR0P1390R99	Parcel 139, Cleared for Construction	0		25-Mar-11	25
1.3.0	1BR0P1400R99	Parcel 140, Cleared for Construction	0		25-Mar-11	25
1.3.0	1BR0P1410R99	Parcel 141, Cleared for Construction	0		25-Mar-11	25
1.3.0	1BR0P1420R99	Parcel 142, Cleared for Construction	0		25-Mar-11	259
1.3.0	1BR0P1440R99	Parcel 144, Cleared for Construction	0		25-Mar-11	25
1.3.0	1BR0P1450R99	Parcel 145, Cleared for Construction	0		25-Mar-11	259
1.3.0	1BR0P1460R99	Parcel 146, Cleared for Construction	0		25-Mar-11	259
1.3.0	1BR0P1470R99	Parcel 147, Cleared for Construction	0		25-Mar-11	25
1.3.0	1BR0P1480R99	Parcel 148, Cleared for Construction	0		25-Mar-11	25
1.3.0	1BR0P1530R99	Parcel 153, Cleared for Construction	0		25-Mar-11	72
1.3.0	1BR0P1540R99	Parcel 154, Cleared for Construction	0		25-Mar-11	25
1.3.0	1BR0P1570R99	Parcel 157, Cleared for Construction	0		25-Mar-11	72
1.3.0	1BR0P1580R99	Parcel 158, Cleared for Construction	0		25-Mar-11	72
UTILITY RELOCATIONS			554	19-Mar-10	03-May-12	25
1.4.T9	1B0UT09UAA	Prep Assembly, Seg 1B Comm, Level 3 (Opt 0)	20	19-Mar-10	16-Apr-10	421
1.4.C	1B0UC00UAA	Prep Assembly, Seg 1B Cable, Charter (Opt 0)	20	19-Mar-10	16-Apr-10	421
1.4.PL3	1B0UPL3UAA	Prep Assembly, Seg 1B Pipeline, Explorer (O...	20	19-Mar-10	16-Apr-10	420
1.4.WW7	1B0UWW7UAA	Prep Assembly, Seg 1B Wastewater, Watau...	20	19-Mar-10	16-Apr-10	419
1.4.PL2	1B0UPL2UAA	Prep Assembly, Seg 1B Pipeline, Exxon/Mobi...	20	19-Mar-10	16-Apr-10	413
1.4.T17	1B0UT17UAA	Prep Assembly, Seg 1B Comm, N. Richland ...	20	19-Mar-10	16-Apr-10	412
1.4.T13	1B0UT13UAA	Prep Assembly, Seg 1B Comm, MFN (Opt 0)	20	19-Mar-10	16-Apr-10	412
1.4.E1	1B0UE01UAA	Prep Assembly, Seg 1B Electric, TXU (Opt 0)	20	19-Mar-10	16-Apr-10	411
1.4.WW5	1B0UWW5UAA	Prep Assembly, Seg 1B Wastewater, Fort W...	20	19-Mar-10	16-Apr-10	407
1.4.E2	1B0UE02UAA	Prep Assembly, Seg 1B Electric, Fort Worth (...	20	19-Mar-10	16-Apr-10	406
1.4.T14	1B0UT14UAA	Prep Assembly, Seg 1B Comm, Esquire (Opt 0)	20	19-Mar-10	16-Apr-10	404
1.4.WW6	1B0UWW6UAA	Prep Assembly, Seg 1B Wastewater, Haltom...	20	19-Mar-10	16-Apr-10	385
1.4.G2	1B0UG02UAA	Prep Assembly, Seg 1B Gas, Atmos (Opt 0)	20	19-Mar-10	16-Apr-10	369
1.4.G1	1B0UG01UAA	Prep Assembly, Seg 1B Gas/Petro, Citgo (Op...	20	19-Mar-10	16-Apr-10	364
1.4.W6	1B0UW06UAA	Prep Assembly, Seg 1B Water, Haltom (Opt 0)	26	19-Mar-10	26-Apr-10	314
1.4.WW4	1B0UWW4UAA	Prep Assembly, Seg 1B Wastewater, N. Rich...	28	19-Mar-10	28-Apr-10	299
1.4.T1	1B0UT01UAA	Prep Assembly, Seg 1B Comm, AT&T (Opt 0)	30	19-Mar-10	30-Apr-10	291
1.4.W5	1B0UW05UAA	Prep Assembly, Seg 1B Water, N. Richland ...	58	19-Mar-10	09-Jun-10	222
1.4.T9	1B0UT09TX	TxDOT Review, Seg 1B Comm, Level 3 (Opt 0)	10	16-Apr-10	30-Apr-10	421
1.4.C	1B0UC00TX	TxDOT Review, Seg 1B Cable, Charter (Opt 0)	10	16-Apr-10	30-Apr-10	421
1.4.PL3	1B0UPL3TX	TxDOT Review, Seg 1B Pipeline, Explorer (O...	10	16-Apr-10	30-Apr-10	420
1.4.WW7	1B0UWW7TX	TxDOT Review, Seg 1B Wastewater, Watau...	10	16-Apr-10	30-Apr-10	419
1.4.PL2	1B0UPL2TX	TxDOT Review, Seg 1B Pipeline, Exxon/Mobi...	10	16-Apr-10	30-Apr-10	413
1.4.T17	1B0UT17TX	TxDOT Review, Seg 1B Comm, N. Richland ...	10	16-Apr-10	30-Apr-10	412
1.4.T13	1B0UT13TX	TxDOT Review, Seg 1B Comm, MFN (Opt 0)	10	16-Apr-10	30-Apr-10	412
1.4.E1	1B0UE01TX	TxDOT Review, Seg 1B Electric, TXU (Opt 0)	10	16-Apr-10	30-Apr-10	411
1.4.WW5	1B0UWW5TX	TxDOT Review, Seg 1B Wastewater, Fort W...	10	16-Apr-10	30-Apr-10	407
1.4.E2	1B0UE02TX	TxDOT Review, Seg 1B Electric, Fort Worth (...	10	16-Apr-10	30-Apr-10	406
1.4.T14	1B0UT14TX	TxDOT Review, Seg 1B Comm, Esquire (Opt 0)	10	16-Apr-10	30-Apr-10	404
1.4.WW6	1B0UWW6TX	TxDOT Review, Seg 1B Wastewater, Haltom ...	10	16-Apr-10	30-Apr-10	385
1.4.G2	1B0UG02TX	TxDOT Review, Seg 1B Gas, Atmos (Opt 0)	10	16-Apr-10	30-Apr-10	369
1.4.G1	1B0UG01TX	TxDOT Review, Seg 1B Gas/Petro, Citgo (Op...	10	16-Apr-10	30-Apr-10	364
1.4.W6	1B0UW06TX	TxDOT Review, Seg 1B Water, Haltom (Opt 0)	10	26-Apr-10	10-May-10	314
1.4.WW4	1B0UWW4TX	TxDOT Review, Seg 1B Wastewater, N. Rich...	10	28-Apr-10	12-May-10	299

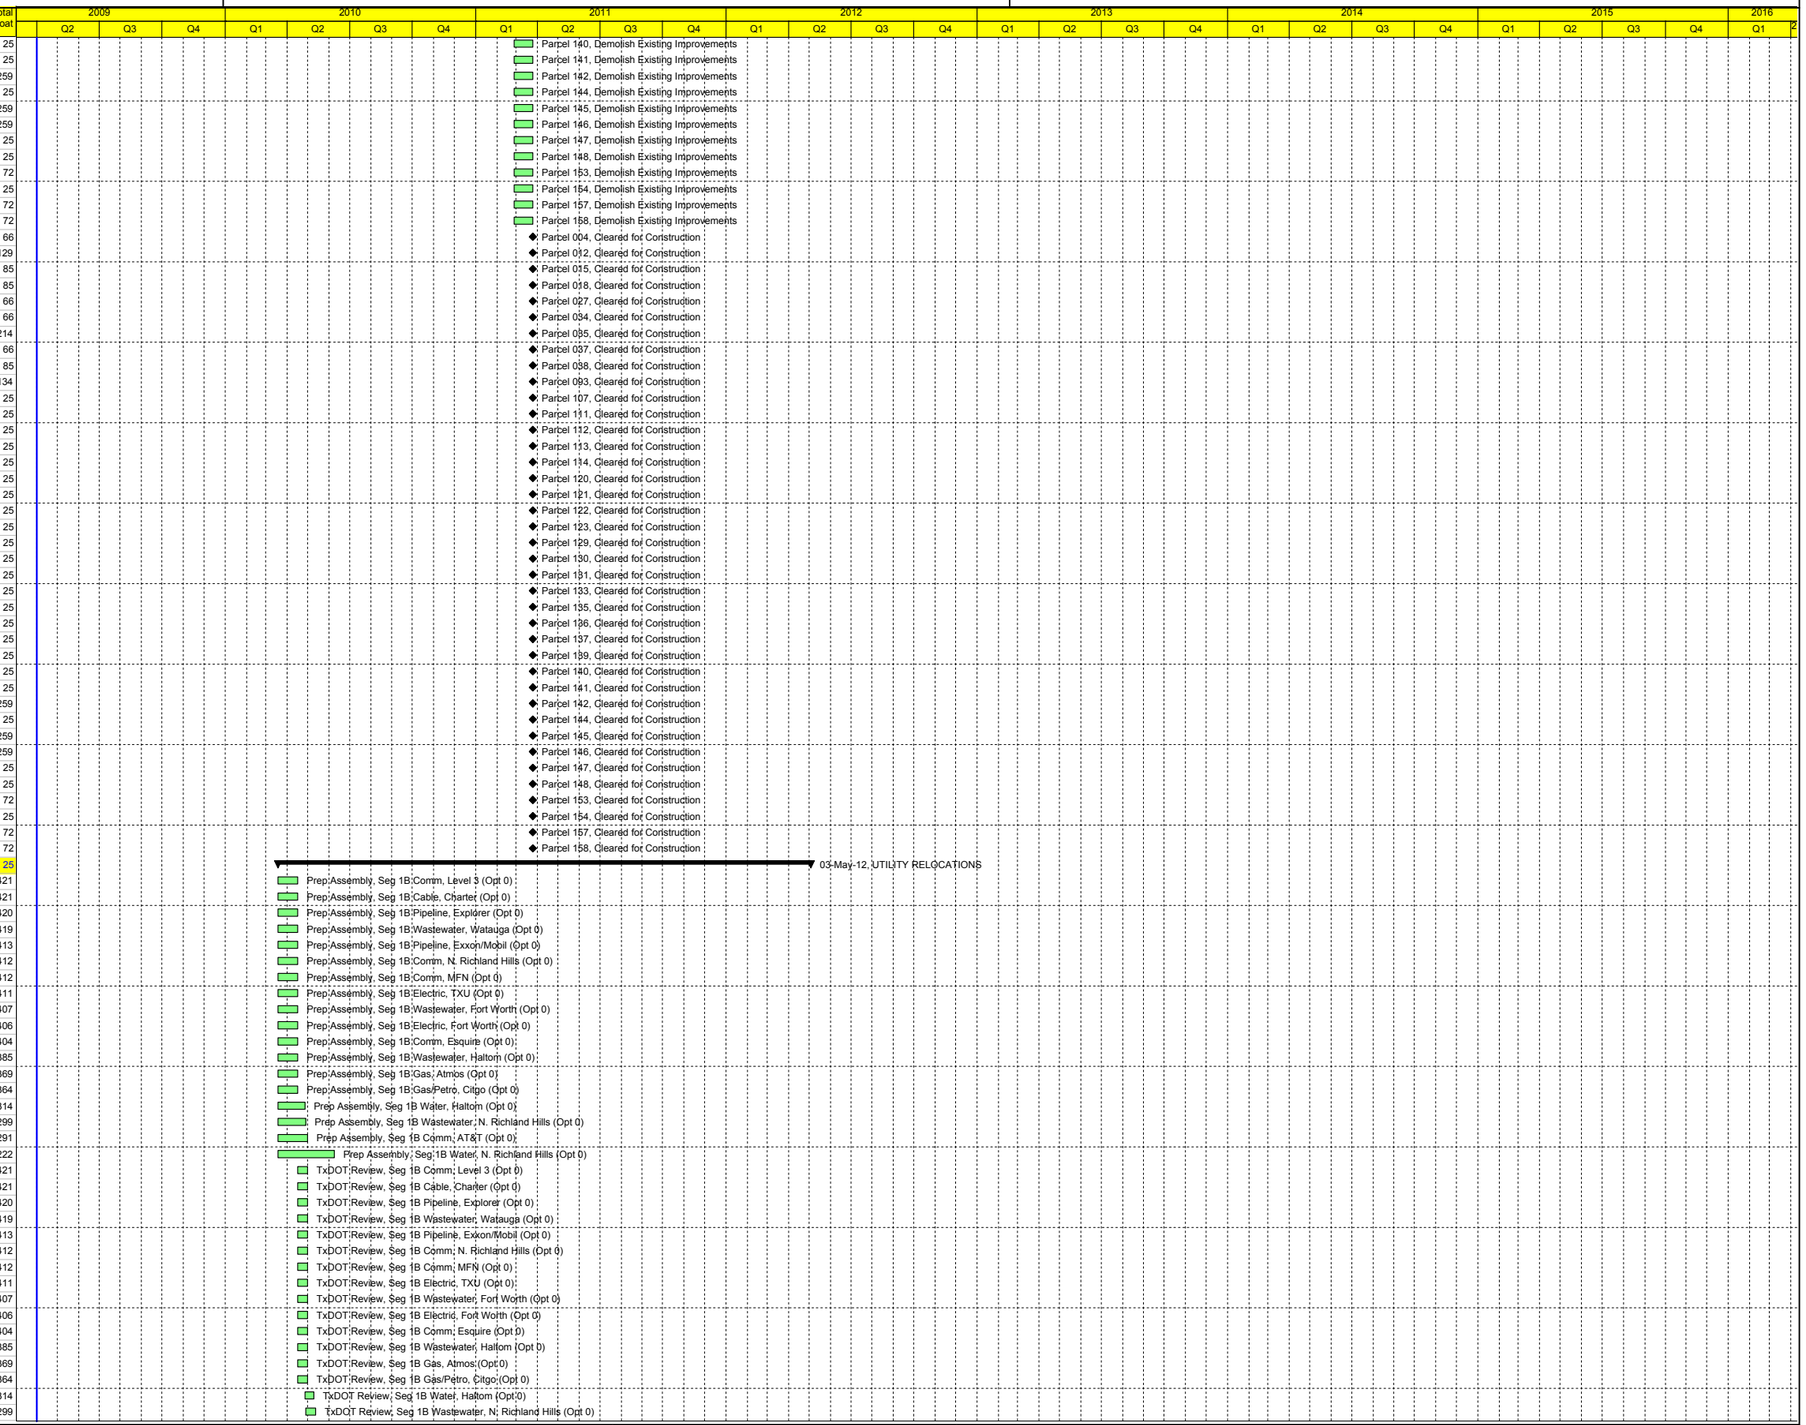

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.4.T1	1B0UT01TX	TxDOT Review, Seg 1B Comm, AT&T (Opt 0)	10	30-Apr-10	14-May-10	291
1.4.WW7	1B0UWW7	Seg 1B, Relocate Wastewater, Watauga (Op...	30	30-Apr-10	11-Jun-10	419
1.4.W5	1B0UW05TX	TxDOT Review, Seg 1B Water, N. Richland ...	10	09-Jun-10	23-Jun-10	222
1.4.PL3	1B0UPL3	Seg 1B, Relocate Pipeline, Explorer (Opt 0)	29	28-Jan-11	10-Mar-11	225
1.4.T13	1B0UT13	Seg 1B, Relocate Comm, MFN (Opt 0)	37	28-Jan-11	22-Mar-11	217
1.4.E1	1B0UE01	Seg 1B, Relocate Electric, TXU (Opt 0)	38	28-Jan-11	23-Mar-11	216
1.4.T9	1B0UT09	Seg 1B, Relocate Comm, Level 3 (Opt 0)	28	25-Mar-11	04-May-11	186
1.4.C	1B0UC00	Seg 1B, Relocate Cable, Charter (Opt 0)	28	25-Mar-11	04-May-11	186
1.4.PL2	1B0UPL2	Seg 1B, Relocate Pipeline, Exxon/Mobil (Opt 0)	36	25-Mar-11	16-May-11	178
1.4.T17	1B0UT17	Seg 1B, Relocate Comm, N. Richland Hills (...	37	25-Mar-11	17-May-11	177
1.4.WW5	1B0UWW5	Seg 1B, Relocate Wastewater, Fort Worth (O...	42	25-Mar-11	24-May-11	172
1.4.E2	1B0UE02	Seg 1B, Relocate Electric, Fort Worth (Opt 0)	43	25-Mar-11	25-May-11	171
1.4.T14	1B0UT14	Seg 1B, Relocate Comm, Esquire (Opt 0)	45	25-Mar-11	27-May-11	169
1.4.WW6	1B0UWW6	Seg 1B, Relocate Wastewater, Haltom (Opt 0)	64	25-Mar-11	23-Jun-11	150
1.4.G2	1B0UG02	Seg 1B, Relocate Gas, Atmos (Opt 0)	80	25-Mar-11	15-Jul-11	134
1.4.G1	1B0UG01	Seg 1B, Relocate Gas/Petro, Citgo (Opt 0)	85	25-Mar-11	22-Jul-11	129
1.4.W6	1B0UW06	Seg 1B, Relocate Water, Haltom (Opt 0)	129	25-Mar-11	22-Sep-11	85
1.4.WW4	1B0UWW4	Seg 1B, Relocate Wastewater, N. Richland ...	142	25-Mar-11	11-Oct-11	72
1.4.T1	1B0UT01	Seg 1B, Relocate Comm, AT&T (Opt 0)	148	25-Mar-11	19-Oct-11	66
1.4.W5	1B0UW05	Seg 1B, Relocate Water, N. Richland Hills (O...	289	25-Mar-11	03-May-12	25
CONSTRUCTION MILESTONES			1601	01-Apr-09	20-May-15	25
1.5	1B00LA00000001	START Landscaped Areas - IH 820	0	01-Apr-09		1588
1.5	1B00EF00000001	START EB Frontage Roads - IH 820	0	15-Dec-...		70
1.5	1B00WF00000001	START WB Frontage Roads - IH 820	0	15-Dec-...		25
1.5	1B00EG00000001	START EB General Purpose Lanes - IH 820	0	03-May...		29
1.5	1B00RP00000001	START Ramps - IH 820	0	03-May...		84
1.5	1B00ML00000001	START EB/WB Managed Lanes - IH 820	0	03-May...		424
1.5	1B00WG000000...	START WB General Purpose Lanes - IH 820	0	03-May...		177
1.5	1B00XR00000001	START Crossroad Overpasses - IH 820	0	03-May...		121
1.5	1B00XU00000001	START Crossroad Underpasses - IH 820	0	03-May...		98
1.5	1B00XR00099999	FINISH Crossroad Overpasses - IH 820	0		05-Oct-12	708
1.5	1B00EG00099999	FINISH EB General Purpose Lanes - IH 820	0		20-Oct-14	177
1.5	1B00WF00099999	FINISH WB Frontage Roads - IH 820	0		25-Nov-14	151
1.5	1B00LA00099999	FINISH Landscaped Areas - IH 820	0		16-Dec-14	136
1.5	1B00EF00099999	FINISH EB Frontage Roads - IH 820	0		19-Dec-14	133
1.5	1B00XU00099999	FINISH Crossroad Underpasses - IH 820	0		26-Dec-14	128
1.5	1B00RP00099999	FINISH Ramps - IH 820	0		04-Mar-15	80
1.5	1B00ML00099999	FINISH EB/WB Managed Lanes - IH 820	0		05-May-15	36
1.5	1B00WG000999...	FINISH WB General Purpose Lanes - IH 820	0		20-May-15	25
1.5	1B00	SUBSEGMENT 1B CONSTRUCTION	1179	11-Nov-...	20-May-15	25
CONSTRUCTION PHASE 1			592	11-Nov-...	18-Feb-13	25
1.5	1B10EF00000001	Area EF0, PH 1, Start	0	15-Dec-...		70
1.5	1B10WF00000001	Area WF0, PH 1, Start	0	15-Dec-...		25
1.5.2.0	1B10EF00050600	Area EF0, PH 1, Place Temp Erosion Control	32	15-Dec-...	30-Jan-12	70
1.5.2.0	1B10WF00050600	Area WF0, PH 1, Place Temp Erosion Control	44	15-Dec-...	15-Feb-12	25
1.5.4.0	1B10EF00042310	Area EF0, PH 1, Install Fill Wall Complete	16	16-Dec-...	09-Jan-12	171
1.5.2.0	1B10EF00013210	Area EF0, PH 1, Place Embankment	81	16-Dec-...	09-Apr-12	106
1.5.2.0	1B10EF00011010	Area EF0, PH 1, Excavate Cut Areas	123	16-Dec-...	06-Jun-12	104
1.5.7.0	1B10WF00090010	Area WF0, PH 1, Install Noise Walls	8	29-Dec-...	10-Jan-12	40
1.5.7.0	1B10EF00090010	Area EF0, PH 1, Install Noise Walls	15	29-Dec-...	19-Jan-12	70
1.5.4.0	1B10EF00042325	Area EF0, PH 1, Install Cut Wall, Stage 2 (3 ...	117	30-Dec-...	12-Jun-12	149
1.5.2.0	1B10WF00010410	Area WF0, PH 1, Rem Conc Pavement	21	10-Jan-12	08-Feb-12	40
1.5.2.0	1B10EF00010410	Area EF0, PH 1, Rem Conc Pavement	20	19-Jan-12	16-Feb-12	70
1.5.4.0	1B10EF00042320	Area EF0, PH 1, Install Cut Wall, Stage 1 (3 ...	79	02-Feb-12	23-May-12	104
1.5.3.0	1B10WF00046210	Area WF0, PH 1, Install Small CBC	20	15-Feb-12	14-Mar-12	48
1.5.4.0	1B10WF00042320	Area WF0, PH 1, Install Cut Wall, Stage 1 (3 ...	78	15-Feb-12	04-Jun-12	25
1.5.3.0	1B10EF00046210	Area EF0, PH 1, Install Small CBC	19	16-Feb-12	14-Mar-12	70
1.5.4.0	1B10WF00042310	Area WF0, PH 1, Install Fill Wall Complete	28	29-Feb-12	09-Apr-12	155
1.5.2.0	1B10WF00013210	Area WF0, PH 1, Place Embankment	86	29-Feb-12	28-Jun-12	35
1.5.2.0	1B10WF00011010	Area WF0, PH 1, Excavate Cut Areas	131	29-Feb-12	30-Aug-12	25
1.5.3.0	1B10EF00046420	Area EF0, PH 1, Install Medium RCP	59	14-Mar-12	05-Jun-12	70
1.5.3.0	1B10WF00046420	Area WF0, PH 1, Install Medium RCP	63	14-Mar-12	11-Jun-12	48
1.5.4.0	1B10WF00042325	Area WF0, PH 1, Install Cut Wall, Stage 2 (3 ...	117	03-Apr-12	13-Sep-12	70
1.5.2.0	1B10EF00026010	Area EF0, PH 1, Lime Treat Subgrade (2 Cre...	41	11-Apr-12	07-Jun-12	104
1.5	1B10EG00000001	Area EG0, PH 1, Start	0	03-May...		29
1.5	1B10RP00000001	Area RP0, PH 1, Start	0	03-May...		84
1.5	1B10WG000000...	Area WG0, PH 1, Start	0	03-May...		177
1.5	1B10XR00000001	Area XR0, PH 1, Start	0	03-May...		121
1.5	1B10XU00000001	Area XU0, PH 1, Start	0	03-May...		98
1.5.2.0	1B10XR00050600	Area XR0, PH 1, Place Temp Erosion Control	2	03-May...	07-May-12	170
1.5.2.0	1B10EG00054210	Area EG0, PH 1, Rem MBGF	4	03-May...	09-May-12	43
1.5.2.0	1B10RP00010410	Area RP0, PH 1, Rem Conc Pavement	5	03-May...	10-May-12	84
1.5.9.0	1B10WG000512...	Area WG0, PH 1, Place Temp Conc Barrier	5	03-May...	10-May-12	227
1.5.2.0	1B10EG00063010	Area EG0, PH 1, Rem Overhead Sign Supports	7	03-May...	14-May-12	40
1.5.2.0	1B10XU00050600	Area XU0, PH 1, Place Temp Erosion Control	8	03-May...	15-May-12	98
1.5.2.0	1B10EG00050600	Area EG0, PH 1, Place Temp Erosion Control	18	03-May...	29-May-12	29
1.5.2.0	1B10XR00010410	Area XR0, PH 1, Rem Conc Pavement	1	07-May...	08-May-12	179
1.5.2.0	1B10XR00067910	Area XR0, PH 1, Rem Traffic Signals	10	07-May...	21-May-12	170
1.5.4.0	1B10RP00042320	Area RP0, PH 1, Install Cut Wall, Stage 1	3	10-May...	15-May-12	84
1.5.2.0	1B10XU00010410	Area XU0, PH 1, Rem Conc Pavement	2	15-May...	17-May-12	109
1.5.2.0	1B10XU00067910	Area XU0, PH 1, Rem Traffic Signals	13	15-May...	01-Jun-12	98
1.5.2.0	1B10RP00013210	Area RP0, PH 1, Place Embankment	20	15-May...	12-Jun-12	85
1.5.4.0	1B10RP00042310	Area RP0, PH 1, Install Fill Wall Complete	29	15-May...	25-Jun-12	85
1.5.2.0	1B10RP00011010	Area RP0, PH 1, Excavate Cut Areas	30	15-May...	26-Jun-12	84
1.5.2.0	1B10WF00026010	Area WF0, PH 1, Lime Treat Subgrade	82	15-May...	06-Sep-12	52
1.5.8.0	1B10XR00061899	Area XR0, PH 1, Install ITS Duct Bank	2	21-May...	23-May-12	214

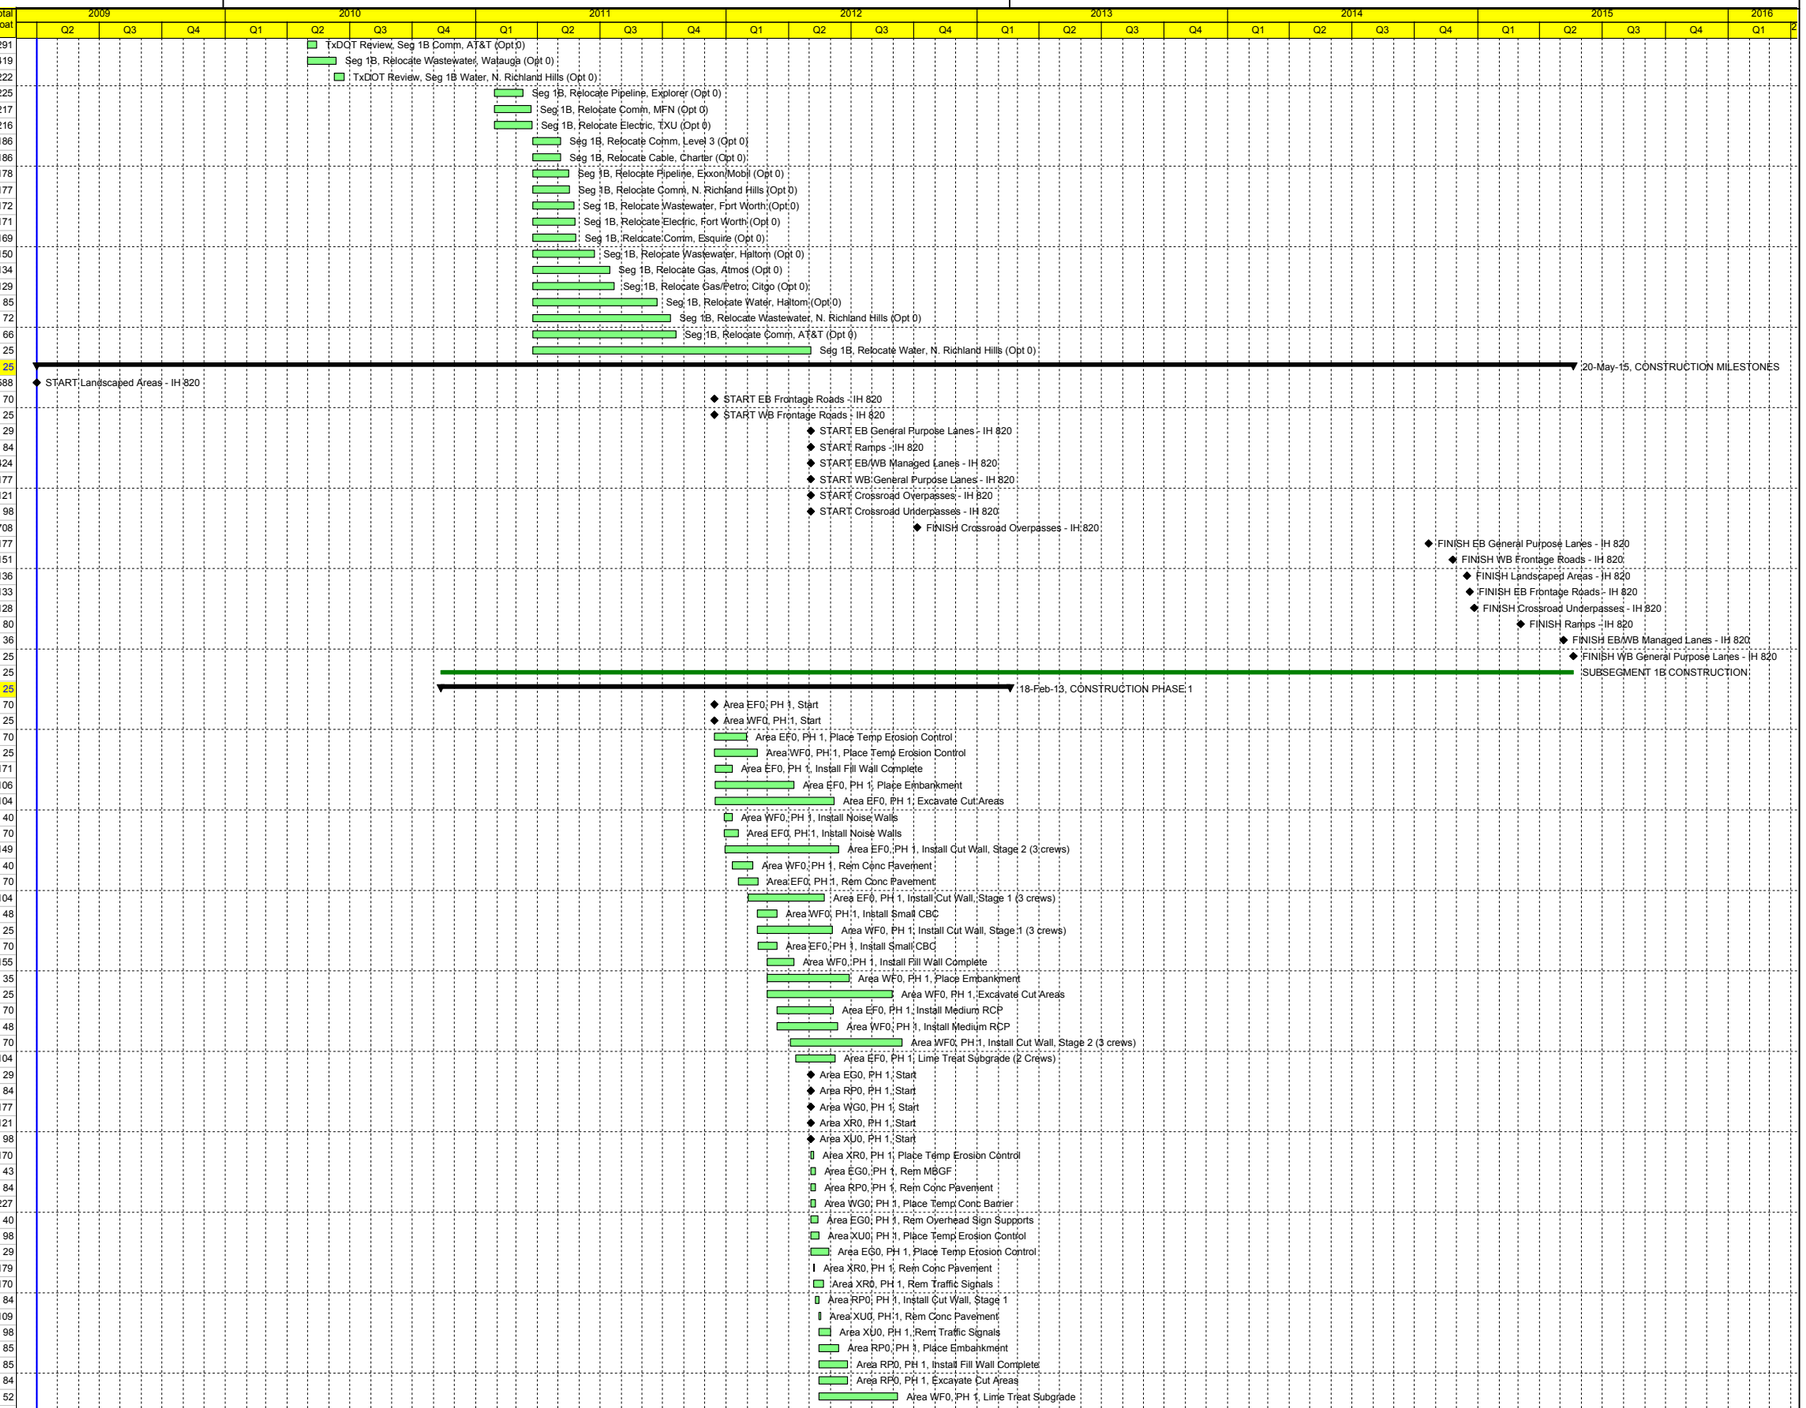

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.5.2.0	1B10XR00026010	Area XR0, PH 1, Lime Treat Subgrade	4	21-May...	25-May-12	170
1.5.8.0	1B10XR00062899	Area XR0, PH 1, Install Elec Service for ITS/...	9	21-May...	01-Jun-12	207
1.5.2.0	1B10XR00024711	Area XR0, PH 1, Place Flexible Base	2	25-May...	29-May-12	170
1.5.2.0	1B10XR00052910	Area XR0, PH 1, Place Curb & Gutter	1	29-May...	30-May-12	170
1.5.2.0	1B10EG00010430	Area EG0, PH 1, Rem Concrete Barrier	6	29-May...	06-Jun-12	29
1.5.2.0	1B10XR00053110	Area XR0, PH 1, Place Sidewalks & Driveways	1	30-May...	31-May-12	208
1.5.2.0	1B10XR00034011	Area XR0, PH 1, Place HMA Base	2	30-May...	01-Jun-12	170
1.5.9.0	1B10XR00066200	Area XR0, PH 1, Place Temp Marking & Sign...	1	01-Jun-12	04-Jun-12	210
1.5.2.0	1B10XR00034610	Area XR0, PH 1, Place SMA Surface	3	01-Jun-12	06-Jun-12	207
1.5.8.0	1B10XU00061899	Area XU0, PH 1, Install ITS Duct Bank	3	01-Jun-12	06-Jun-12	186
1.5.8.0	1B10XU00062899	Area XU0, PH 1, Install Elec Service for ITS/...	11	01-Jun-12	18-Jun-12	178
1.5.2.0	1B10XU00026010	Area XU0, PH 1, Lime Treat Subgrade	30	01-Jun-12	13-Jul-12	98
1.5.7.0	1B10XR00068010	Area XR0, PH 1, Install Traffic Signal Systems	41	01-Jun-12	30-Jul-12	170
1.5.3.0	1B10EF00046510	Area EF0, PH 1, Install MHs and Inlets	36	05-Jun-12	25-Jul-12	70
1.5.3.0	1B10EF00046410	Area EF0, PH 1, Install Small RCP	43	05-Jun-12	03-Aug-12	70
1.5.8.0	1B10EF00061899	Area EF0, PH 1, Install ITS Duct Bank	55	05-Jun-12	21-Aug-12	115
1.5.7.0	1B10XR00066610	Area XR0, PH 1, Install Perm Markings	1	06-Jun-12	07-Jun-12	207
1.5.2.0	1B10EG00010410	Area EG0, PH 1, Rem Conc Pavement	5	06-Jun-12	13-Jun-12	29
1.5.4.0	1B10EF00042315	Area EF0, PH 1, Install Moment Slabs	7	07-Jun-12	18-Jun-12	107
1.5.3.0	1B10EG00046230	Area EG0, PH 1, Install Large CBC	14	13-Jun-12	03-Jul-12	32
1.5.2.0	1B10EG00013210	Area EG0, PH 1, Place Embankment	19	13-Jun-12	10-Jul-12	38
1.5.2.0	1B10EG00011010	Area EG0, PH 1, Excavate Cut Areas	28	13-Jun-12	23-Jul-12	29
1.5.2.0	1B10EF00024711	Area EF0, PH 1, Place Flexible Base	35	13-Jun-12	01-Aug-12	75
1.5.3.0	1B10RP00046410	Area RP0, PH 1, Install Small RCP	1	26-Jun-12	27-Jun-12	116
1.5.4.0	1B10RP00042325	Area RP0, PH 1, Install Cut Wall, Stage 2	4	26-Jun-12	02-Jul-12	127
1.5.2.0	1B10RP00026010	Area RP0, PH 1, Lime Treat Subgrade	34	26-Jun-12	13-Aug-12	84
1.5.3.0	1B10RP00046510	Area RP0, PH 1, Install MHs and Inlets	1	27-Jun-12	28-Jun-12	116
1.5.3.0	1B10EG00046220	Area EG0, PH 1, Install Medium CBC	28	03-Jul-12	10-Aug-12	32
1.5.3.0	1B10WF00046410	Area WF0, PH 1, Install Small RCP	45	12-Jul-12	13-Sep-12	25
1.5.2.0	1B10XU00024711	Area XU0, PH 1, Place Flexible Base	13	13-Jul-12	01-Aug-12	98
1.5	1B10WG000999...	Area WG0, PH 1, Finish	0		19-Jul-12	177
1.5.2.0	1B10EG00026010	Area EG0, PH 1, Lime Treat Subgrade (2 Cr...	46	23-Jul-12	25-Sep-12	29
1.5.2.0	1B10EF00052910	Area EF0, PH 1, Place Curb & Gutter	20	25-Jul-12	22-Aug-12	70
1.5.2.0	1B10XU00052910	Area XU0, PH 1, Place Curb & Gutter	2	01-Aug-...	03-Aug-12	98
1.5.2.0	1B10XU00053110	Area XU0, PH 1, Place Sidewalks & Driveways	3	03-Aug-...	08-Aug-12	144
1.5.2.0	1B10XU00034011	Area XU0, PH 1, Place HMA Base	16	03-Aug-...	27-Aug-12	98
1.5.2.0	1B10EF00034011	Area EF0, PH 1, Place HMA Base	43	08-Aug-...	08-Oct-12	70
1.5.3.0	1B10EG00046210	Area EG0, PH 1, Install Small CBC	5	10-Aug-...	17-Aug-12	32
1.5.2.0	1B10RP00024711	Area RP0, PH 1, Place Flexible Base	8	13-Aug-...	23-Aug-12	84
1.5.4.0	1B10RP00042315	Area RP0, PH 1, Install Moment Slabs	10	13-Aug-...	27-Aug-12	87
1.5.2.0	1B10EF00045010	Area EF0, PH 1, Place Conc Rail (Ret Wall)	45	13-Aug-...	15-Oct-12	111
1.5.3.0	1B10EG00046420	Area EG0, PH 1, Install Medium RCP	1	17-Aug-...	20-Aug-12	32
1.5.8.0	1B10EG00061899	Area EG0, PH 1, Install ITS Duct Bank	5	20-Aug-...	27-Aug-12	108
1.5.3.0	1B10EG00046410	Area EG0, PH 1, Install Small RCP	12	20-Aug-...	05-Sep-12	32
1.5.2.0	1B10EF00053110	Area EF0, PH 1, Place Sidewalks & Driveways	26	22-Aug-...	27-Sep-12	109
1.5.2.0	1B10RP00052910	Area RP0, PH 1, Place Curb & Gutter	5	23-Aug-...	30-Aug-12	84
1.5.2.0	1B10EF00043210	Area EF0, PH 1, Place Conc RipRap	36	24-Aug-...	15-Oct-12	104
1.5.9.0	1B10XU00066200	Area XU0, PH 1, Place Temp Marking & Sign...	1	27-Aug-...	28-Aug-12	149
1.5.7.0	1B10XU00061020	Area XU0, PH 1, Install Rdwy Illumination	3	27-Aug-...	30-Aug-12	128
1.5.8.0	1B10EG00041699	Area EG0, PH 1, Install ITS Structures & Equip	36	27-Aug-...	16-Oct-12	108
1.5.7.0	1B10XU00068010	Area XU0, PH 1, Install Traffic Signal Systems	51	27-Aug-...	06-Nov-12	98
1.5.2.0	1B10RP00034012	Area RP0, PH 1, Place HMA Base	9	30-Aug-...	12-Sep-12	84
1.5.2.0	1B10XU00034610	Area XU0, PH 1, Place SMA Surface	17	30-Aug-...	24-Sep-12	128
1.5.8.0	1B10WF00061899	Area WF0, PH 1, Install ITS Duct Bank	58	30-Aug-...	20-Nov-12	39
1.5.2.0	1B10EG00024711	Area EG0, PH 1, Place Flexible Base	20	04-Sep-...	02-Oct-12	29
1.5.3.0	1B10EG00046510	Area EG0, PH 1, Install MHs and Inlets	11	05-Sep-...	20-Sep-12	32
1.5.7.0	1B10EF00061020	Area EF0, PH 1, Install Rdwy Illumination	23	05-Sep-...	08-Oct-12	104
1.5.2.0	1B10EG00034012	Area EG0, PH 1, Place HMA Base	24	05-Sep-...	09-Oct-12	29
1.5.4.0	1B10WF00042315	Area WF0, PH 1, Install Moment Slabs	13	06-Sep-...	25-Sep-12	52
1.5.2.0	1B10RP00045010	Area RP0, PH 1, Place Conc Rail (Ret Wall)	11	12-Sep-...	27-Sep-12	126
1.5.7.0	1B10RP00065010	Area RP0, PH 1, Install OH Sign Structures	28	12-Sep-...	22-Oct-12	84
1.5.3.0	1B10WF00046510	Area WF0, PH 1, Install MHs and Inlets	35	13-Sep-...	01-Nov-12	25
1.5.2.0	1B10EG00034610	Area EG0, PH 1, Place SMA Surface	26	17-Sep-...	23-Oct-12	107
1.5.2.0	1B10WF00024711	Area WF0, PH 1, Place Flexible Base	35	20-Sep-...	08-Nov-12	25
1.5.7.0	1B10XU00066610	Area XU0, PH 1, Install Perm Markings	2	24-Sep-...	26-Sep-12	128
1.5.2.0	1B10WF00034011	Area WF0, PH 1, Place HMA Base	44	28-Sep-...	29-Nov-12	25
1.5.2.0	1B10EF00016010	Area EF0, PH 1, Place Topsoil	12	04-Oct-12	22-Oct-12	104
1.5	1B10XR00099999	Area XR0, PH 1, Finish	0		05-Oct-12	121
1.5.9.0	1B10EF00066200	Area EF0, PH 1, Place Temp Marking & Sign...	3	08-Oct-12	11-Oct-12	117
1.5.2.0	1B10EF00034610	Area EF0, PH 1, Place SMA Surface	46	08-Oct-12	11-Dec-12	70
1.5.2.0	1B10EG00054010	Area EG0, PH 1, Install MBGF	18	09-Oct-12	02-Nov-12	96
1.5.7.0	1B10EG00065010	Area EG0, PH 1, Install OH Sign Structures	26	09-Oct-12	14-Nov-12	87
1.5.9.0	1B10EG00050820	Area EG0, PH 1, Const Temp Detour	76	09-Oct-12	23-Jan-13	29
1.5.2.0	1B10WF00052910	Area WF0, PH 1, Place Curb & Gutter	21	17-Oct-12	15-Nov-12	25
1.5.7.0	1B10EF00064410	Area EF0, PH 1, Install Small Signs	1	22-Oct-12	23-Oct-12	104
1.5.7.0	1B10RP00061020	Area RP0, PH 1, Install Rdwy Illumination	6	22-Oct-12	30-Oct-12	84
1.5.6.0	1B10EF00016410	Area EF0, PH 1, Place Seeding and Sodding	5	23-Oct-12	30-Oct-12	104
1.5.2.0	1B10RP00043210	Area RP0, PH 1, Place Conc RipRap	9	30-Oct-12	12-Nov-12	84
1.5.2.0	1B10EG00054510	Area EG0, PH 1, Install Attenuators	3	02-Nov-...	07-Nov-12	96
1.5.7.0	1B10XU00064410	Area XU0, PH 1, Install Small Signs	1	06-Nov-...	07-Nov-12	98
1.5	1B10XU00099999	Area XU0, PH 1, Finish	0		07-Nov-12	98
1.5.7.0	1B10EG00066610	Area EG0, PH 1, Install Perm Markings	2	07-Nov-...	09-Nov-12	96
1.5.7.0	1B10RP00064410	Area RP0, PH 1, Install Small Signs	1	12-Nov-...	13-Nov-12	94
1.5.2.0	1B10RP00034610	Area RP0, PH 1, Place SMA Surface	10	12-Nov-...	26-Nov-12	84
1.5.7.0	1B10EG00061020	Area EG0, PH 1, Install Rdwy Illumination	6	14-Nov-...	22-Nov-12	87
1.5.2.0	1B10WF00053110	Area WF0, PH 1, Place Sidewalks & Driveways	27	15-Nov-...	24-Dec-12	45

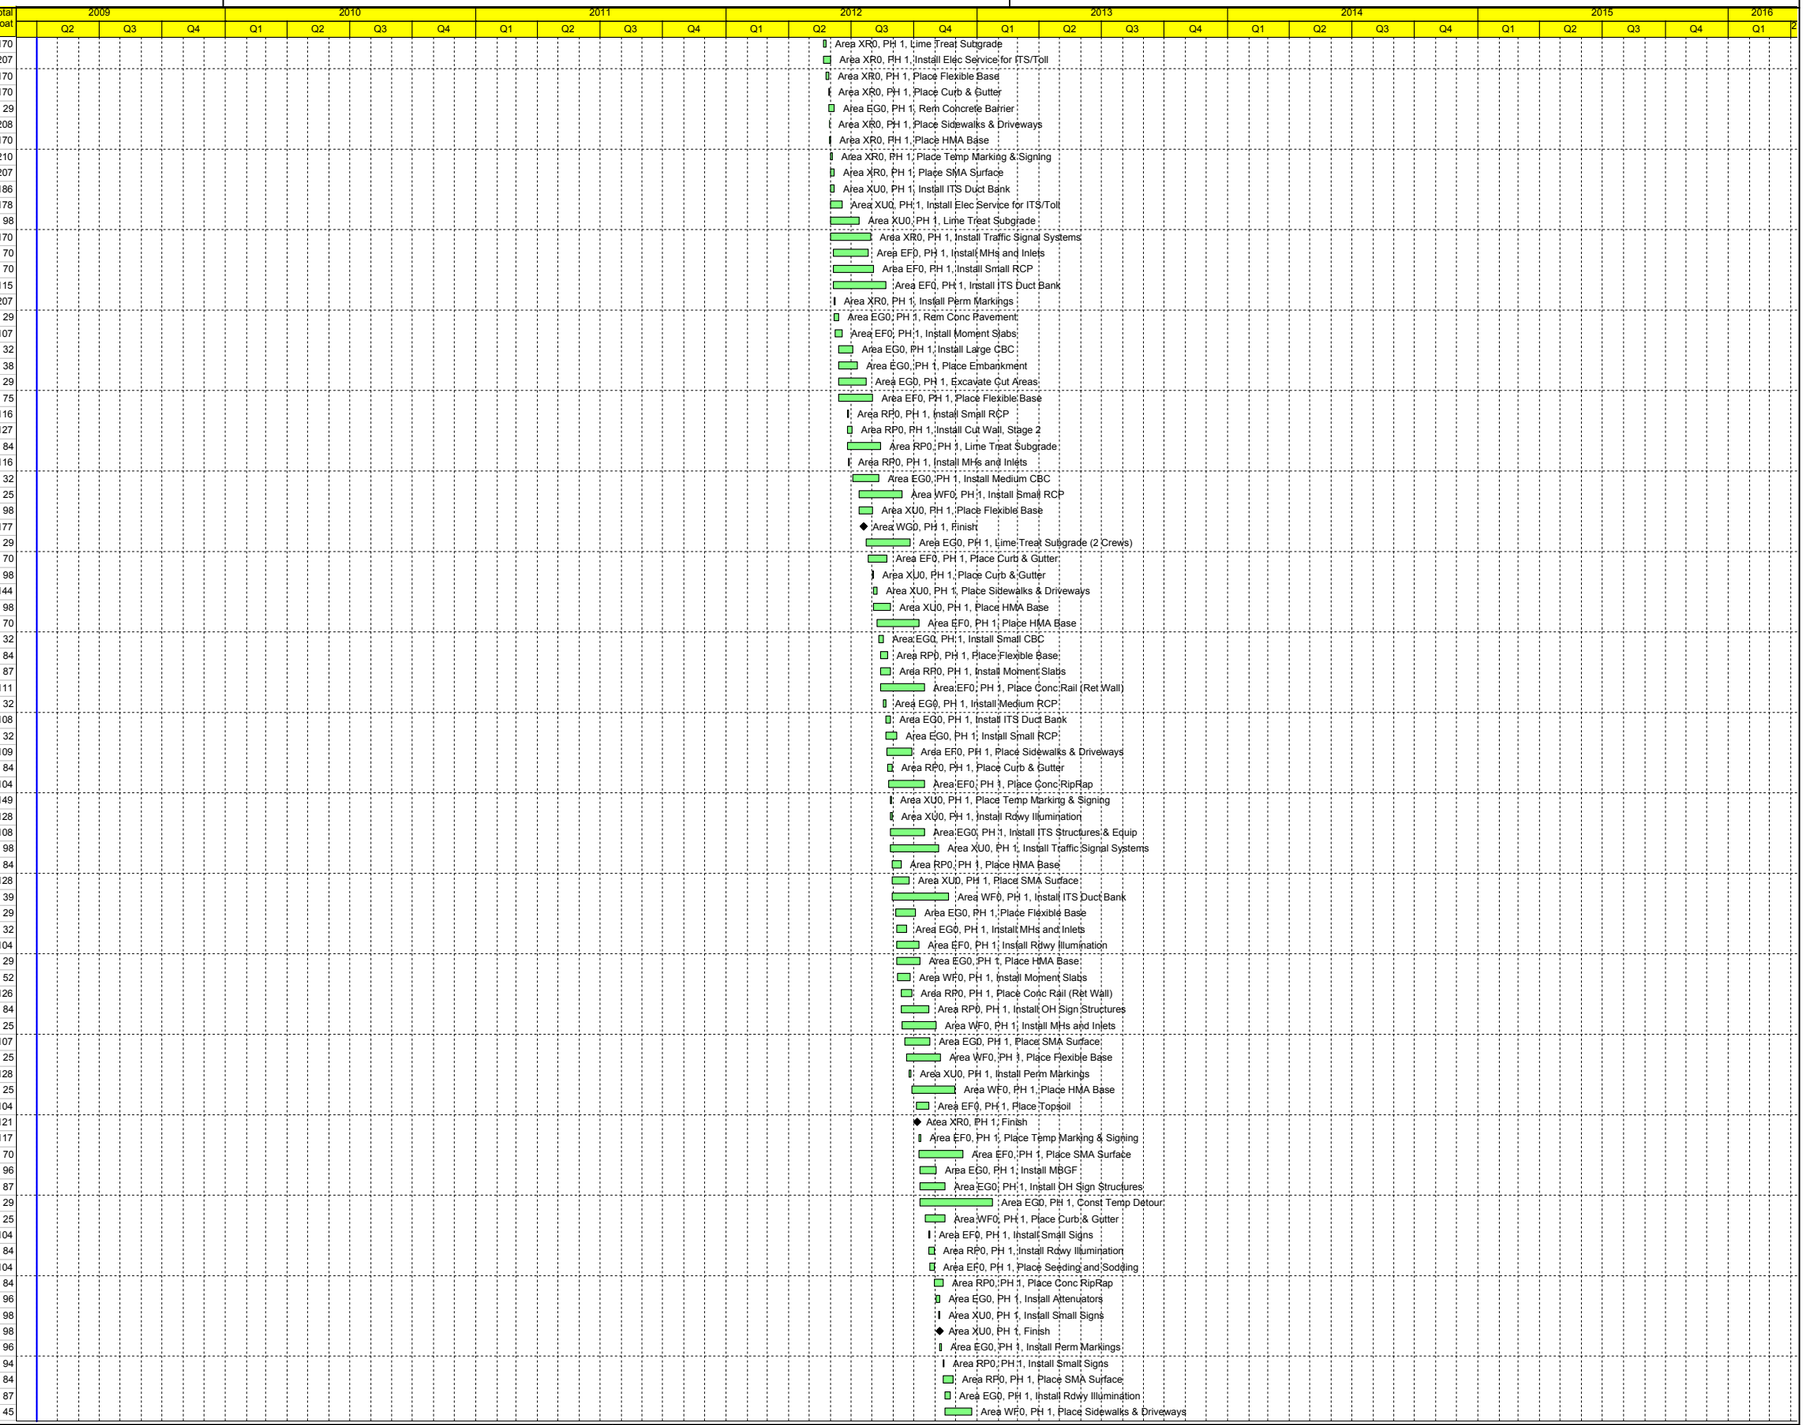

Remaining Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.5.7.0	1B10WF00061020	Area WF0, PH 1, Install Rdwy Illumination	23	20-Nov-...	21-Dec-12	49
1.5.2.0	1B10WF00043210	Area WF0, PH 1, Place Conc RipRap	38	20-Nov-...	11-Jan-13	39
1.5.7.0	1B10RP00066610	Area RP0, PH 1, Install Perm Markings	1	26-Nov-...	27-Nov-12	84
1.5	1B10RP00099999	Area RP0, PH 1, Finish	0		27-Nov-12	84
1.5.9.0	1B10WF00066200	Area WF0, PH 1, Place Temp Marking & Sig...	3	29-Nov-...	04-Dec-12	79
1.5.2.0	1B10WF00045010	Area WF0, PH 1, Place Conc Rail (Ret Wall)	48	29-Nov-...	05-Feb-13	25
1.5.2.0	1B10WF00034610	Area WF0, PH 1, Place SMA Surface	47	07-Dec-...	12-Feb-13	25
1.5.7.0	1B10EF00066610	Area EF0, PH 1, Install Perm Markings	4	11-Dec-...	17-Dec-12	70
1.5	1B10EF00099999	Area EF0, PH 1, Finish	0		17-Dec-12	70
1.5.2.0	1B10WF00016010	Area WF0, PH 1, Place Topsoil	13	01-Jan-13	18-Jan-13	39
1.5.7.0	1B10WF00064410	Area WF0, PH 1, Install Small Signs	1	18-Jan-13	21-Jan-13	39
1.5.6.0	1B10WF00016410	Area WF0, PH 1, Place Seeding and Sodding	6	21-Jan-13	29-Jan-13	39
1.5.9.0	1B10EG00051200	Area EG0, PH 1, Place Temp Conc Barrier	11	23-Jan-13	07-Feb-13	29
1.5.9.0	1B10EG00066200	Area EG0, PH 1, Place Temp Marking & Sig...	3	07-Feb-13	12-Feb-13	29
1.5	1B10EG00099999	Area EG0, PH 1, Finish	0		12-Feb-13	29
1.5.7.0	1B10WF00066610	Area WF0, PH 1, Install Perm Markings	4	12-Feb-13	18-Feb-13	25
1.5	1B10WF00099999	Area WF0, PH 1, Finish	0		18-Feb-13	25
1.5.4.0.1.36A	1B10B306A00001	BR 36A, PH 1, Start	0	11-Nov-...		530
1.5.4.0.1.36A	1B10B306A49610	BR 36A, PH 1, Demo Extg Bridge	12	11-Nov-...	29-Nov-10	530
1.5.4.0.1.36A	1B10B306A41600	BR 36A, PH 1, Install Drill Shafts	6	29-Nov-...	07-Dec-10	530
1.5.4.0.1.36A	1B10B306A42020	BR 36A, PH 1, Install Columns	3	07-Dec-...	10-Dec-10	534
1.5.4.0.1.36A	1B10B306A42040	BR 36A, PH 1, Install Abutments	12	07-Dec-...	23-Dec-10	530
1.5.4.0.1.36A	1B10B306A42030	BR 36A, PH 1, Install Bent Caps	5	10-Dec-...	17-Dec-10	534
1.5.4.0.1.36A	1B10B306A42510	BR 36A, PH 1, Install Conc Beams	3	23-Dec-...	28-Dec-10	530
1.5.4.0.1.36A	1B10B306A45410	BR 36A, PH 1, Install Exp Joints	3	28-Dec-...	31-Dec-10	530
1.5.4.0.1.36A	1B10B306A42210	BR 36A, PH 1, Install Deck Slab	24	31-Dec-...	03-Feb-11	530
1.5.4.0.1.36A	1B10B306A42050	BR 36A, PH 1, Install Apprch Slabs	25	03-Feb-11	10-Mar-11	530
1.5.4.0.1.36A	1B10B306A45020	BR 36A, PH 1, Install Conc Rail	2	10-Mar-11	14-Mar-11	530
1.5.4.0.1.36A	1B10B306A99999	BR 36A, PH 1, Finish	0		14-Mar-11	530
1.5.4.0.1.36B	1B10B036B00001	BR 36B, PH 1, Start	0	03-May...		177
1.5.4.0.1.36B	1B10B036B41600	BR 36B, PH 1, Install Drill Shafts	6	03-May...	11-May-12	177
1.5.4.0.1.36B	1B10B036B42020	BR 36B, PH 1, Install Columns	3	11-May...	16-May-12	178
1.5.4.0.1.36B	1B10B036B42040	BR 36B, PH 1, Install Abutments	7	11-May...	22-May-12	177
1.5.4.0.1.36B	1B10B036B42030	BR 36B, PH 1, Install Bent Caps	3	16-May...	21-May-12	178
1.5.4.0.1.36B	1B10B036B42510	BR 36B, PH 1, Install Conc Beams	2	22-May...	24-May-12	177
1.5.4.0.1.36B	1B10B036B45410	BR 36B, PH 1, Install Exp Joints	2	24-May...	28-May-12	177
1.5.4.0.1.36B	1B10B036B42210	BR 36B, PH 1, Install Deck Slab	18	28-May...	21-Jun-12	177
1.5.4.0.1.36B	1B10B036B42050	BR 36B, PH 1, Install Apprch Slabs	18	21-Jun-12	17-Jul-12	177
1.5.4.0.1.36B	1B10B036B45020	BR 36B, PH 1, Install Conc Rail	2	17-Jul-12	19-Jul-12	177
1.5.4.0.1.36B	1B10B036B99999	BR 36B, PH 1, Finish	0		19-Jul-12	177
1.5.4.0.1.36C	1B10B036C00001	BR 36C, PH 1, Start	0	03-May...		174
1.5.4.0.1.36C	1B10B036C41600	BR 36C, PH 1, Install Drill Shafts	6	03-May...	11-May-12	174
1.5.4.0.1.36C	1B10B036C42020	BR 36C, PH 1, Install Columns	3	11-May...	16-May-12	176
1.5.4.0.1.36C	1B10B036C42040	BR 36C, PH 1, Install Abutments	8	11-May...	23-May-12	174
1.5.4.0.1.36C	1B10B036C42030	BR 36C, PH 1, Install Bent Caps	3	16-May...	21-May-12	176
1.5.4.0.1.36C	1B10B036C42510	BR 36C, PH 1, Install Conc Beams	3	23-May...	28-May-12	174
1.5.4.0.1.36C	1B10B036C45410	BR 36C, PH 1, Install Exp Joints	2	28-May...	30-May-12	174
1.5.4.0.1.36C	1B10B036C42210	BR 36C, PH 1, Install Deck Slab	19	30-May...	26-Jun-12	174
1.5.4.0.1.36C	1B10B036C42050	BR 36C, PH 1, Install Apprch Slabs	20	26-Jun-12	24-Jul-12	174
1.5.4.0.1.36C	1B10B036C99999	BR 36C, PH 1, Finish	0		24-Jul-12	174
1.5.4.0.1.39	1B10B039000001	BR 39, PH 1, Start	0	03-May...		147
1.5.4.0.1.39	1B10B039049610	BR 39, PH 1, Demo Extg Bridge	12	03-May...	21-May-12	147
1.5.4.0.1.39	1B10B039041600	BR 39, PH 1, Install Drill Shafts	13	21-May...	07-Jun-12	147
1.5.4.0.1.39	1B10B039042020	BR 39, PH 1, Install Columns	4	07-Jun-12	13-Jun-12	149
1.5.4.0.1.39	1B10B039042040	BR 39, PH 1, Install Abutments	11	07-Jun-12	22-Jun-12	147
1.5.4.0.1.39	1B10B039042030	BR 39, PH 1, Install Bent Caps	5	13-Jun-12	20-Jun-12	149
1.5.4.0.1.39	1B10B039042510	BR 39, PH 1, Install Conc Beams	3	22-Jun-12	27-Jun-12	147
1.5.4.0.1.39	1B10B039045410	BR 39, PH 1, Install Exp Joints	3	27-Jun-12	02-Jul-12	147
1.5.4.0.1.39	1B10B039042210	BR 39, PH 1, Install Deck Slab	22	02-Jul-12	01-Aug-12	147
1.5.4.0.1.39	1B10B039042050	BR 39, PH 1, Install Apprch Slabs	18	01-Aug-...	27-Aug-12	147
1.5.4.0.1.39	1B10B039045020	BR 39, PH 1, Install Conc Rail	3	27-Aug-...	30-Aug-12	147
1.5.4.0.1.39	1B10B039099999	BR 39, PH 1, Finish	0		30-Aug-12	147
1.5.5.1.1.40	1B10B040000001	BR 40, PH 1, Start	0	03-May...		159
1.5.5.1.1.40	1B10B040049610	BR 40, PH 1, Demo Extg Bridge	4	03-May...	09-May-12	159
1.5.5.1.1.40	1B10B040041600	BR 40, PH 1, Install Drill Shafts	4	09-May...	15-May-12	159
1.5.5.1.1.40	1B10B040042020	BR 40, PH 1, Install Columns	3	15-May...	18-May-12	159
1.5.5.1.1.40	1B10B040042040	BR 40, PH 1, Install Abutments	6	15-May...	23-May-12	159
1.5.5.1.1.40	1B10B040042030	BR 40, PH 1, Install Bent Caps	3	18-May...	23-May-12	159
1.5.5.1.1.40	1B10B040044210	BR 40, PH 1, Install Plate Girders	34	23-May...	10-Jul-12	159
1.5.5.1.1.40	1B10B040045410	BR 40, PH 1, Install Exp Joints	2	10-Jul-12	12-Jul-12	159
1.5.5.1.1.40	1B10B040042210	BR 40, PH 1, Install Deck Slab	10	12-Jul-12	26-Jul-12	159
1.5.5.1.1.40	1B10B040042050	BR 40, PH 1, Install Apprch Slabs	8	26-Jul-12	07-Aug-12	161
1.5.5.1.1.40	1B10B040045020	BR 40, PH 1, Install Conc Rail	3	09-Aug-...	14-Aug-12	159
1.5.5.1.1.40	1B10B040099999	BR 40, PH 1, Finish	0		14-Aug-12	159
1.5.5.1.1.40A	1B10B040A00001	BR 40A, PH 1, Start	0	03-May...		163
1.5.5.1.1.40A	1B10B040A41600	BR 40A, PH 1, Install Drill Shafts	4	03-May...	09-May-12	163
1.5.5.1.1.40A	1B10B040A42020	BR 40A, PH 1, Install Columns	3	09-May...	14-May-12	163
1.5.5.1.1.40A	1B10B040A42040	BR 40A, PH 1, Install Abutments	6	09-May...	17-May-12	163
1.5.5.1.1.40A	1B10B040A42030	BR 40A, PH 1, Install Bent Caps	3	14-May...	17-May-12	163
1.5.5.1.1.40A	1B10B040A44210	BR 40A, PH 1, Install Plate Girders	34	17-May...	04-Jul-12	163
1.5.5.1.1.40A	1B10B040A45410	BR 40A, PH 1, Install Exp Joints	2	04-Jul-12	06-Jul-12	163
1.5.5.1.1.40A	1B10B040A42210	BR 40A, PH 1, Install Deck Slab	10	06-Jul-12	20-Jul-12	163
1.5.5.1.1.40A	1B10B040A42050	BR 40A, PH 1, Install Apprch Slabs	8	20-Jul-12	01-Aug-12	165
1.5.5.1.1.40A	1B10B040A45020	BR 40A, PH 1, Install Conc Rail	3	03-Aug-...	08-Aug-12	163
1.5.5.1.1.40A	1B10B040A99999	BR 40A, PH 1, Finish	0		08-Aug-12	163
1.5.4.0.1.41	1B10B041000001	BR 41, PH 1, Start	0	03-May...		121

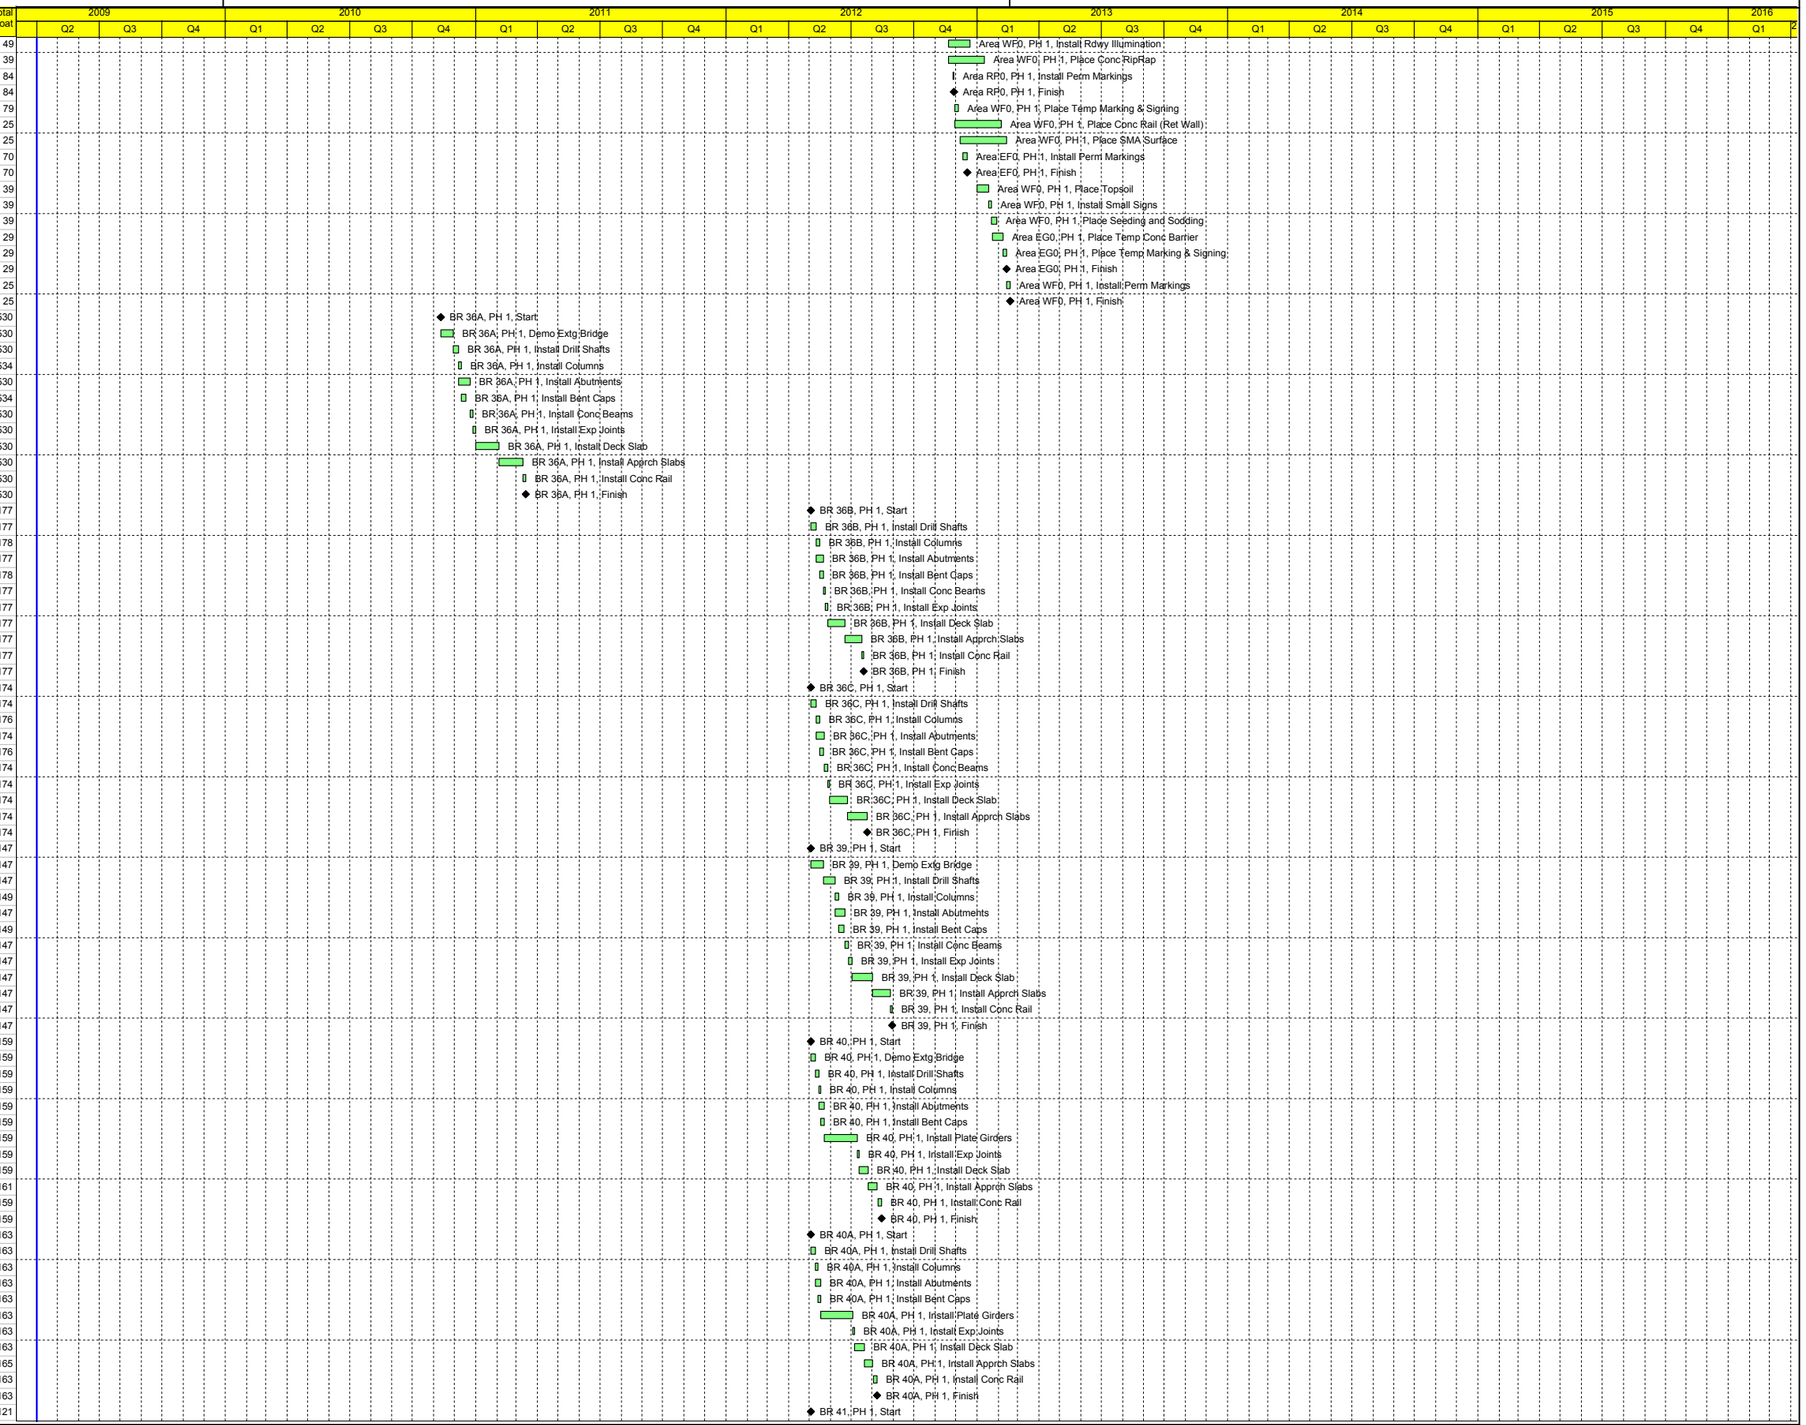

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.5.4.0.1.41	1B10B041049610	BR 41, PH 1, Demo Extg Bridge	12	03-May...	21-May-12	121
1.5.4.0.1.41	1B10B041041600	BR 41, PH 1, Install Drill Shafts	10	21-May...	04-Jun-12	121
1.5.4.0.1.41	1B10B041042020	BR 41, PH 1, Install Columns	2	04-Jun-12	06-Jun-12	133
1.5.4.0.1.41	1B10B041042040	BR 41, PH 1, Install Abutments	17	04-Jun-12	27-Jun-12	121
1.5.4.0.1.41	1B10B041042030	BR 41, PH 1, Install Bent Caps	3	06-Jun-12	11-Jun-12	133
1.5.4.0.1.41	1B10B041042510	BR 41, PH 1, Install Conc Beams	4	27-Jun-12	03-Jul-12	121
1.5.4.0.1.41	1B10B041045410	BR 41, PH 1, Install Exp Joints	3	03-Jul-12	06-Jul-12	121
1.5.4.0.1.41	1B10B041042210	BR 41, PH 1, Install Deck Slab	27	06-Jul-12	14-Aug-12	121
1.5.4.0.1.41	1B10B041042050	BR 41, PH 1, Install Apprch Slabs	36	14-Aug-...	03-Oct-12	121
1.5.4.0.1.41	1B10B041045020	BR 41, PH 1, Install Conc Rail	2	03-Oct-12	05-Oct-12	121
1.5.4.0.1.41	1B10B041099999	BR 41, PH 1, Finish	0		05-Oct-12	121
1.5.4.0.1.42	1B10B042000001	BR 42, PH 1, Start	0	03-May...		203
1.5.4.0.1.42	1B10B042041600	BR 42, PH 1, Install Drill Shafts	3	03-May...	08-May-12	203
1.5.4.0.1.42	1B10B042042020	BR 42, PH 1, Install Columns	1	08-May...	09-May-12	207
1.5.4.0.1.42	1B10B042042040	BR 42, PH 1, Install Abutments	6	08-May...	16-May-12	203
1.5.4.0.1.42	1B10B042042030	BR 42, PH 1, Install Bent Caps	1	09-May...	10-May-12	207
1.5.4.0.1.42	1B10B042042510	BR 42, PH 1, Install Conc Beams	1	16-May...	17-May-12	203
1.5.4.0.1.42	1B10B042045410	BR 42, PH 1, Install Exp Joints	1	17-May...	18-May-12	203
1.5.4.0.1.42	1B10B042042210	BR 42, PH 1, Install Deck Slab	6	18-May...	28-May-12	203
1.5.4.0.1.42	1B10B042042050	BR 42, PH 1, Install Apprch Slabs	7	28-May...	06-Jun-12	206
1.5.4.0.1.42	1B10B042045020	BR 42, PH 1, Install Conc Rail	2	11-Jun-12	13-Jun-12	203
1.5.4.0.1.42	1B10B042099999	BR 42, PH 1, Finish	0		13-Jun-12	203
1.5.5.2.1.50	1B10B050000001	BR 50, PH 1, Start	0	03-May...		178
1.5.5.2.1.50	1B10B050049610	BR 50, PH 1, Demo Extg Bridge	3	03-May...	08-May-12	178
1.5.5.2.1.50	1B10B050041600	BR 50, PH 1, Install Drill Shafts	2	08-May...	10-May-12	178
1.5.5.2.1.50	1B10B050042020	BR 50, PH 1, Install Columns	2	10-May...	14-May-12	179
1.5.5.2.1.50	1B10B050042040	BR 50, PH 1, Install Abutments	6	10-May...	18-May-12	178
1.5.5.2.1.50	1B10B050042030	BR 50, PH 1, Install Bent Caps	3	14-May...	17-May-12	179
1.5.5.2.1.50	1B10B050044210	BR 50, PH 1, Install Plate Girders	20	18-May...	15-Jun-12	178
1.5.5.2.1.50	1B10B050045410	BR 50, PH 1, Install Exp Joints	2	15-Jun-12	19-Jun-12	178
1.5.5.2.1.50	1B10B050042210	BR 50, PH 1, Install Deck Slab	8	19-Jun-12	29-Jun-12	178
1.5.5.2.1.50	1B10B050042050	BR 50, PH 1, Install Apprch Slabs	8	29-Jun-12	11-Jul-12	180
1.5.5.2.1.50	1B10B050045020	BR 50, PH 1, Install Conc Rail	3	13-Jul-12	18-Jul-12	178
1.5.5.2.1.50	1B10B050099999	BR 50, PH 1, Finish	0		18-Jul-12	178
1.5.5.2.1.50A	1B10B050A00001	BR 50A, PH 1, Start	0	03-May...		181
1.5.5.2.1.50A	1B10B050A41600	BR 50A, PH 1, Install Drill Shafts	2	03-May...	07-May-12	181
1.5.5.2.1.50A	1B10B050A42020	BR 50A, PH 1, Install Columns	2	07-May...	09-May-12	182
1.5.5.2.1.50A	1B10B050A42040	BR 50A, PH 1, Install Abutments	6	07-May...	15-May-12	181
1.5.5.2.1.50A	1B10B050A42030	BR 50A, PH 1, Install Bent Caps	3	09-May...	14-May-12	182
1.5.5.2.1.50A	1B10B050A44210	BR 50A, PH 1, Install Plate Girders	20	15-May...	12-Jun-12	181
1.5.5.2.1.50A	1B10B050A45410	BR 50A, PH 1, Install Exp Joints	2	12-Jun-12	14-Jun-12	181
1.5.5.2.1.50A	1B10B050A42210	BR 50A, PH 1, Install Deck Slab	8	14-Jun-12	26-Jun-12	181
1.5.5.2.1.50A	1B10B050A42050	BR 50A, PH 1, Install Apprch Slabs	8	26-Jun-12	06-Jul-12	183
1.5.5.2.1.50A	1B10B050A45020	BR 50A, PH 1, Install Conc Rail	3	10-Jul-12	13-Jul-12	181
1.5.5.2.1.50A	1B10B050A99999	BR 50A, PH 1, Finish	0		13-Jul-12	181
1.5.4.0.1.51	1B10B051000001	BR 51, PH 1, Start	0	03-May...		166
1.5.4.0.1.51	1B10B051049610	BR 51, PH 1, Demo Extg Bridge	7	03-May...	14-May-12	166
1.5.4.0.1.51	1B10B051041600	BR 51, PH 1, Install Drill Shafts	2	14-May...	16-May-12	166
1.5.4.0.1.51	1B10B051042020	BR 51, PH 1, Install Columns	4	16-May...	22-May-12	167
1.5.4.0.1.51	1B10B051042040	BR 51, PH 1, Install Abutments	10	16-May...	30-May-12	166
1.5.4.0.1.51	1B10B051042030	BR 51, PH 1, Install Bent Caps	5	22-May...	29-May-12	167
1.5.4.0.1.51	1B10B051042510	BR 51, PH 1, Install Conc Beams	2	30-May...	01-Jun-12	166
1.5.4.0.1.51	1B10B051045410	BR 51, PH 1, Install Exp Joints	3	01-Jun-12	06-Jun-12	166
1.5.4.0.1.51	1B10B051042210	BR 51, PH 1, Install Deck Slab	19	06-Jun-12	03-Jul-12	166
1.5.4.0.1.51	1B10B051042050	BR 51, PH 1, Install Apprch Slabs	21	03-Jul-12	01-Aug-12	166
1.5.4.0.1.51	1B10B051045020	BR 51, PH 1, Install Conc Rail	2	01-Aug-...	03-Aug-12	166
1.5.4.0.1.51	1B10B051099999	BR 51, PH 1, Finish	0		03-Aug-12	166
1.5	1B100000000001	START PHASE 1, SUBSEGMENT 1B	0	11-Nov-...		310
1.5	1B100000099999	FINISH PHASE 1, SUBSEGMENT 1B	0		18-Feb-13	25
CONSTRUCTION PHASE 2			**163**	**08-Feb-13**	**25-Sep-13**	**25**
1.5.7.0	1B20RP00065010	Area RP0, PH 2, Install OH Sign Structures	82	08-Feb-13	04-Jun-13	100
1.5	1B20EF00000001	Area EF0, PH 2, Start	0	18-Feb-13		93
1.5	1B20EG00000001	Area EG0, PH 2, Start	0	18-Feb-13		41
1.5	1B20RP00000001	Area RP0, PH 2, Start	0	18-Feb-13		25
1.5	1B20WF00000001	Area WF0, PH 2, Start	0	18-Feb-13		94
1.5	1B20WG000000...	Area WG0, PH 2, Start	0	18-Feb-13		60
1.5.2.0	1B20WG000600...	Area WG0, PH 2, Rem Light Poles	1	18-Feb-13	19-Feb-13	71
1.5.2.0	1B20EF00050600	Area EF0, PH 2, Place Temp Erosion Control	2	18-Feb-13	20-Feb-13	93
1.5.2.0	1B20WF00050600	Area WF0, PH 2, Place Temp Erosion Control	2	18-Feb-13	20-Feb-13	159
1.5.2.0	1B20WG000542...	Area WG0, PH 2, Rem MBGF	3	18-Feb-13	21-Feb-13	69
1.5.2.0	1B20WG000630...	Area WG0, PH 2, Rem Overhead Sign Supp...	7	18-Feb-13	27-Feb-13	65
1.5.2.0	1B20EG00050600	Area EG0, PH 2, Place Temp Erosion Control	10	18-Feb-13	04-Mar-13	41
1.5.2.0	1B20RP00010410	Area RP0, PH 2, Rem Conc Pavement	14	18-Feb-13	08-Mar-13	25
1.5.2.0	1B20WG000506...	Area WG0, PH 2, Place Temp Erosion Control	17	18-Feb-13	13-Mar-13	60
1.5.7.0	1B20EF00090010	Area EF0, PH 2, Install Noise Walls	1	20-Feb-13	21-Feb-13	93
1.5.7.0	1B20WF00090010	Area WF0, PH 2, Install Noise Walls	1	20-Feb-13	21-Feb-13	159
1.5.2.0	1B20EF00010410	Area EF0, PH 2, Rem Conc Pavement	1	21-Feb-13	22-Feb-13	93
1.5.2.0	1B20WF00010410	Area WF0, PH 2, Rem Conc Pavement	1	21-Feb-13	22-Feb-13	159
1.5.3.0	1B20EF00046220	Area EF0, PH 2, Install Medium CBC	1	22-Feb-13	25-Feb-13	163
1.5.3.0	1B20WF00046210	Area WF0, PH 2, Install Small CBC	1	22-Feb-13	25-Feb-13	163
1.5.4.0	1B20WF00042320	Area WF0, PH 2, Install Cut Wall, Stage 1	4	22-Feb-13	28-Feb-13	159
1.5.4.0	1B20EF00042320	Area EF0, PH 2, Install Cut Wall, Stage 1 (2 ...	30	22-Feb-13	05-Apr-13	93
1.5.3.0	1B20EF00046210	Area EF0, PH 2, Install Small CBC	1	25-Feb-13	26-Feb-13	163
1.5.3.0	1B20WF00046420	Area WF0, PH 2, Install Medium RCP	2	25-Feb-13	27-Feb-13	163
1.5.3.0	1B20EF00046420	Area EF0, PH 2, Install Medium RCP	2	26-Feb-13	28-Feb-13	163
1.5.2.0	1B20WG000104...	Area WG0, PH 2, Rem Concrete Barrier	5	27-Feb-13	06-Mar-13	65

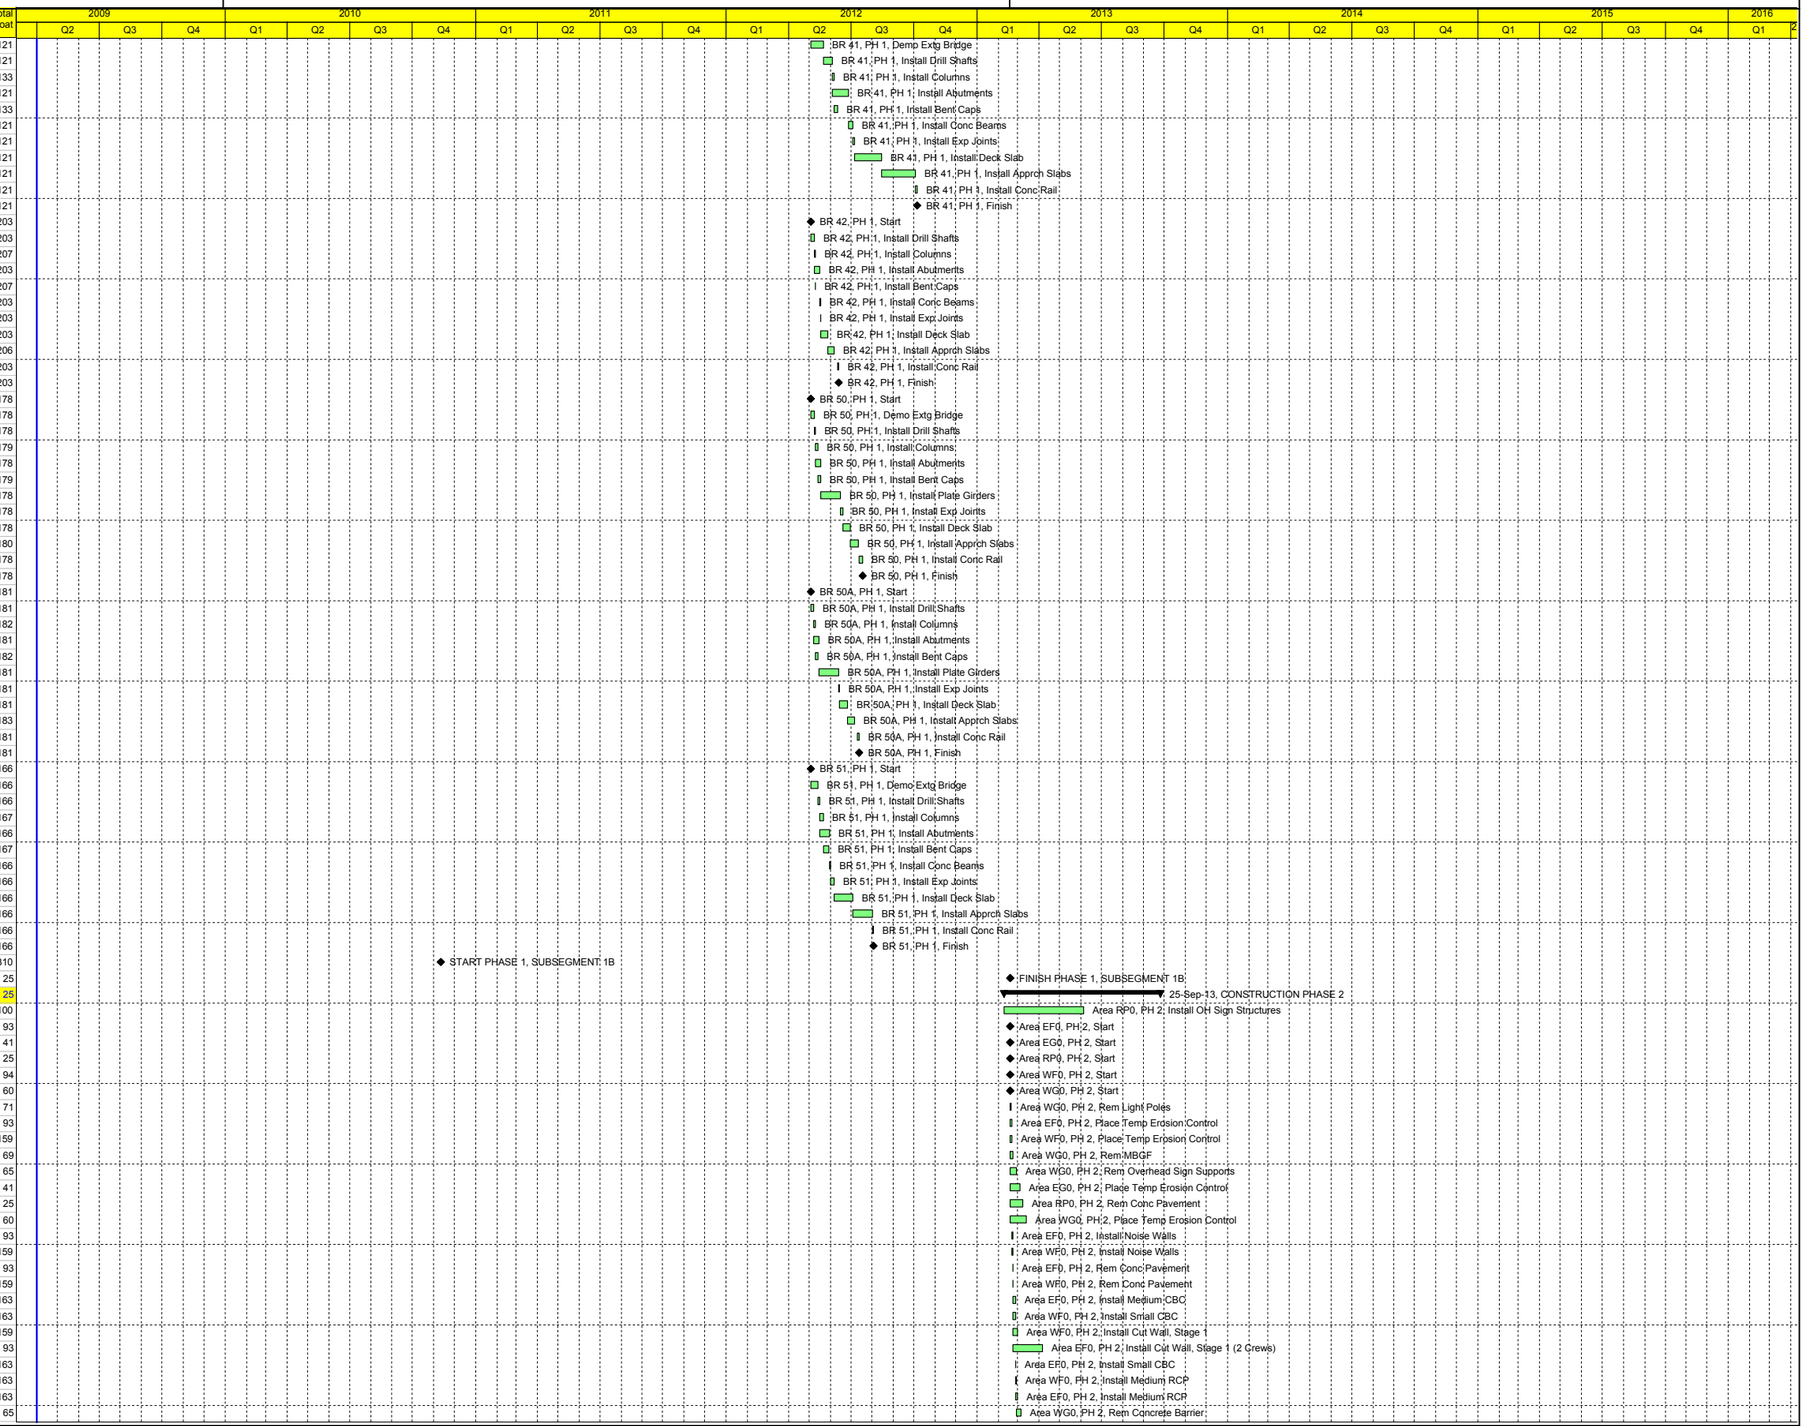

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.5.4.0	1B20WF00042310	Area WF0, PH 2, Install Fill Wall Complete	1	28-Feb-13	01-Mar-13	162
1.5.2.0	1B20WF00013210	Area WF0, PH 2, Place Embankment	2	28-Feb-13	04-Mar-13	160
1.5.2.0	1B20WF00011010	Area WF0, PH 2, Excavate Cut Areas	3	28-Feb-13	05-Mar-13	159
1.5.2.0	1B20EG00054210	Area EG0, PH 2, Rem MBGF	2	04-Mar-13	06-Mar-13	43
1.5.2.0	1B20EG00063010	Area EG0, PH 2, Rem Overhead Sign Supports	4	04-Mar-13	08-Mar-13	41
1.5.2.0	1B20WF00026010	Area WF0, PH 2, Lime Treat Subgrade	2	05-Mar-13	07-Mar-13	160
1.5.8.0	1B20WF00061899	Area WF0, PH 2, Install ITS Duct Bank	2	05-Mar-13	07-Mar-13	163
1.5.3.0	1B20WF00046410	Area WF0, PH 2, Install Small RCP	2	05-Mar-13	07-Mar-13	159
1.5.4.0	1B20WF00042325	Area WF0, PH 2, Install Cut Wall, Stage 2	5	05-Mar-13	12-Mar-13	159
1.5.3.0	1B20WF00046510	Area WF0, PH 2, Install MHs and Inlets	1	07-Mar-13	08-Mar-13	159
1.5.4.0	1B20WF00042315	Area WF0, PH 2, Install Moment Slabs	1	07-Mar-13	08-Mar-13	161
1.5.2.0	1B20WF00024711	Area WF0, PH 2, Place Flexible Base	1	08-Mar-13	11-Mar-13	159
1.5.2.0	1B20EG00010430	Area EG0, PH 2, Rem Concrete Barrier	3	08-Mar-13	13-Mar-13	41
1.5.4.0	1B20RP00042320	Area RP0, PH 2, Install Cut Wall, Stage 1	3	08-Mar-13	13-Mar-13	25
1.5.2.0	1B20WF00052910	Area WF0, PH 2, Place Curb & Gutter	1	11-Mar-13	12-Mar-13	159
1.5.2.0	1B20WF00034011	Area WF0, PH 2, Place HMA Base	1	12-Mar-13	13-Mar-13	159
1.5.2.0	1B20WF00053110	Area WF0, PH 2, Place Sidewalks & Driveways	1	12-Mar-13	13-Mar-13	162
1.5.7.0	1B20WF00061020	Area WF0, PH 2, Install Rdwy Illumination	1	13-Mar-13	14-Mar-13	159
1.5.9.0	1B20WF00066200	Area WF0, PH 2, Place Temp Marking & Sig...	1	13-Mar-13	14-Mar-13	164
1.5.2.0	1B20WF00045010	Area WF0, PH 2, Place Conc Rail (Ret Wall)	2	13-Mar-13	15-Mar-13	162
1.5.2.0	1B20EG00010410	Area EG0, PH 2, Rem Conc Pavement	3	13-Mar-13	18-Mar-13	41
1.5.2.0	1B20WG000104...	Area WG0, PH 2, Rem Conc Pavement	5	13-Mar-13	20-Mar-13	60
1.5.2.0	1B20RP00013210	Area RP0, PH 2, Place Embankment (2 Crews)	29	13-Mar-13	23-Apr-13	25
1.5.4.0	1B20RP00042310	Area RP0, PH 2, Install Fill Wall Complete (2...	42	13-Mar-13	10-May-13	25
1.5.2.0	1B20RP00011010	Area RP0, PH 2, Excavate Cut Areas (2 Crews)	44	13-Mar-13	14-May-13	25
1.5.2.0	1B20WF00043210	Area WF0, PH 2, Place Conc RipRap	2	14-Mar-13	18-Mar-13	159
1.5.2.0	1B20WF00016010	Area WF0, PH 2, Place Topsoil	1	18-Mar-13	19-Mar-13	159
1.5.3.0	1B20EG00046230	Area EG0, PH 2, Install Large CBC	7	18-Mar-13	27-Mar-13	66
1.5.2.0	1B20EG00013210	Area EG0, PH 2, Place Embankment	10	18-Mar-13	01-Apr-13	45
1.5.4.0	1B20EG00042310	Area EG0, PH 2, Install Fill Wall Complete	13	18-Mar-13	04-Apr-13	45
1.5.2.0	1B20EG00011010	Area EG0, PH 2, Excavate Cut Areas	15	18-Mar-13	08-Apr-13	41
1.5.9.0	1B20EG00040390	Area EG0, PH 2, Construct Temp Walls/Shor...	17	18-Mar-13	10-Apr-13	41
1.5.2.0	1B20WF00034610	Area WF0, PH 2, Place SMA Surface	1	19-Mar-13	20-Mar-13	159
1.5.7.0	1B20WF00064410	Area WF0, PH 2, Install Small Signs	1	19-Mar-13	20-Mar-13	159
1.5.6.0	1B20WF00016410	Area WF0, PH 2, Place Seeding and Sodding	1	20-Mar-13	21-Mar-13	159
1.5.7.0	1B20WF00066610	Area WF0, PH 2, Install Perm Markings	1	20-Mar-13	21-Mar-13	159
1.5.9.0	1B20WG000403...	Area WG0, PH 2, Construct Temp Walls/Sho...	10	20-Mar-13	03-Apr-13	93
1.5.3.0	1B20WG000462...	Area WG0, PH 2, Install Large CBC	13	20-Mar-13	08-Apr-13	61
1.5.2.0	1B20WG000132...	Area WG0, PH 2, Place Embankment	18	20-Mar-13	15-Apr-13	60
1.5.2.0	1B20WG000110...	Area WG0, PH 2, Excavate Cut Areas	27	20-Mar-13	26-Apr-13	60
1.5.4.0	1B20WG000423...	Area WG0, PH 2, Install Fill Wall Complete	43	20-Mar-13	20-May-13	60
1.5.2.0	1B20WG000260...	Area WG0, PH 2, Lime Treat Subgrade (2 Cr...	44	26-Mar-13	27-May-13	60
1.5.3.0	1B20EG00046220	Area EG0, PH 2, Install Medium CBC	15	27-Mar-13	17-Apr-13	66
1.5.2.0	1B20EF00013210	Area EF0, PH 2, Place Embankment	2	05-Apr-13	09-Apr-13	124
1.5.2.0	1B20EF00011010	Area EF0, PH 2, Excavate Cut Areas	3	05-Apr-13	10-Apr-13	93
1.5.4.0	1B20EF00042310	Area EF0, PH 2, Install Fill Wall Complete	11	05-Apr-13	22-Apr-13	124
1.5.3.0	1B20WG000462...	Area WG0, PH 2, Install Medium CBC	27	08-Apr-13	15-May-13	61
1.5.3.0	1B20EF00046410	Area EF0, PH 2, Install Small RCP	1	10-Apr-13	11-Apr-13	134
1.5.8.0	1B20EF00061899	Area EF0, PH 2, Install ITS Duct Bank	2	10-Apr-13	12-Apr-13	137
1.5.4.0	1B20EF00042325	Area EF0, PH 2, Install Cut Wall, Stage 2 (2 ...	45	10-Apr-13	12-Jun-13	93
1.5.2.0	1B20EG00026010	Area EG0, PH 2, Lime Treat Subgrade	48	10-Apr-13	17-Jun-13	41
1.5.3.0	1B20EF00046510	Area EF0, PH 2, Install MHs and Inlets	1	11-Apr-13	12-Apr-13	134
1.5.3.0	1B20EG00046210	Area EG0, PH 2, Install Small CBC	3	17-Apr-13	22-Apr-13	66
1.5.3.0	1B20EG00046420	Area EG0, PH 2, Install Medium RCP	1	22-Apr-13	23-Apr-13	66
1.5.2.0	1B20EF00026010	Area EF0, PH 2, Lime Treat Subgrade	2	22-Apr-13	24-Apr-13	124
1.5.8.0	1B20EG00061899	Area EG0, PH 2, Install ITS Duct Bank	1	23-Apr-13	24-Apr-13	112
1.5.3.0	1B20EG00046410	Area EG0, PH 2, Install Small RCP	7	23-Apr-13	02-May-13	66
1.5.2.0	1B20EF00024711	Area EF0, PH 2, Place Flexible Base	1	24-Apr-13	25-Apr-13	126
1.5.4.0	1B20EF00042315	Area EF0, PH 2, Install Moment Slabs	4	24-Apr-13	30-Apr-13	124
1.5.8.0	1B20EG00041699	Area EG0, PH 2, Install ITS Structures & Equip	5	24-Apr-13	01-May-13	112
1.5.2.0	1B20EF00052910	Area EF0, PH 2, Place Curb & Gutter	1	25-Apr-13	26-Apr-13	126
1.5.2.0	1B20EF00053110	Area EF0, PH 2, Place Sidewalks & Driveways	1	26-Apr-13	29-Apr-13	129
1.5.3.0	1B20EG00046510	Area EG0, PH 2, Install MHs and Inlets	7	02-May...	13-May-13	66
1.5.2.0	1B20RP00026010	Area RP0, PH 2, Lime Treat Subgrade (2 Cre...	45	10-May...	12-Jul-13	25
1.5.3.0	1B20RP00046410	Area RP0, PH 2, Install Small RCP	2	14-May...	16-May-13	75
1.5.4.0	1B20RP00042325	Area RP0, PH 2, Install Cut Wall, Stage 2	5	14-May...	21-May-13	68
1.5.3.0	1B20WG000462...	Area WG0, PH 2, Install Small CBC	5	15-May...	22-May-13	61
1.5.3.0	1B20RP00046510	Area RP0, PH 2, Install MHs and Inlets	3	16-May...	21-May-13	75
1.5.2.0	1B20WG000247...	Area WG0, PH 2, Place Flexible Base	19	20-May...	14-Jun-13	61
1.5.3.0	1B20WG000464...	Area WG0, PH 2, Install Medium RCP	1	22-May...	23-May-13	61
1.5.8.0	1B20WG000618...	Area WG0, PH 2, Install ITS Duct Bank	4	23-May...	29-May-13	78
1.5.3.0	1B20WG000465...	Area WG0, PH 2, Install MHs and Inlets	11	23-May...	07-Jun-13	61
1.5.3.0	1B20WG000464...	Area WG0, PH 2, Install Small RCP	12	23-May...	10-Jun-13	61
1.5.4.0	1B20WG000423...	Area WG0, PH 2, Install Moment Slabs	20	27-May...	24-Jun-13	60
1.5.2.0	1B20WG000340...	Area WG0, PH 2, Place HMA Base	24	28-May...	01-Jul-13	60
1.5.8.0	1B20WG000416...	Area WG0, PH 2, Install ITS Structures & Equip	27	29-May...	05-Jul-13	78
1.5.2.0	1B20WG000346...	Area WG0, PH 2, Place SMA Surface	25	03-Jun-13	08-Jul-13	80
1.5.7.0	1B20WG000650...	Area WG0, PH 2, Install OH Sign Structures	26	07-Jun-13	15-Jul-13	72
1.5.4.0	1B20RP00042315	Area RP0, PH 2, Install Moment Slabs	30	07-Jun-13	19-Jul-13	25
1.5.2.0	1B20EF00034011	Area EF0, PH 2, Place HMA Base	1	12-Jun-13	13-Jun-13	93
1.5.7.0	1B20EF00061020	Area EF0, PH 2, Install Rdwy Illumination	1	13-Jun-13	14-Jun-13	93
1.5.9.0	1B20EF00066200	Area EF0, PH 2, Place Temp Marking & Sign...	1	13-Jun-13	14-Jun-13	98
1.5.2.0	1B20EF00045010	Area EF0, PH 2, Place Conc Rail (Ret Wall)	2	13-Jun-13	17-Jun-13	96
1.5.2.0	1B20EF00043210	Area EF0, PH 2, Place Conc RipRap	2	14-Jun-13	18-Jun-13	93
1.5.4.0	1B20EG00042315	Area EG0, PH 2, Install Moment Slabs	5	17-Jun-13	24-Jun-13	47
1.5.2.0	1B20EG00024711	Area EG0, PH 2, Place Flexible Base	11	17-Jun-13	02-Jul-13	41

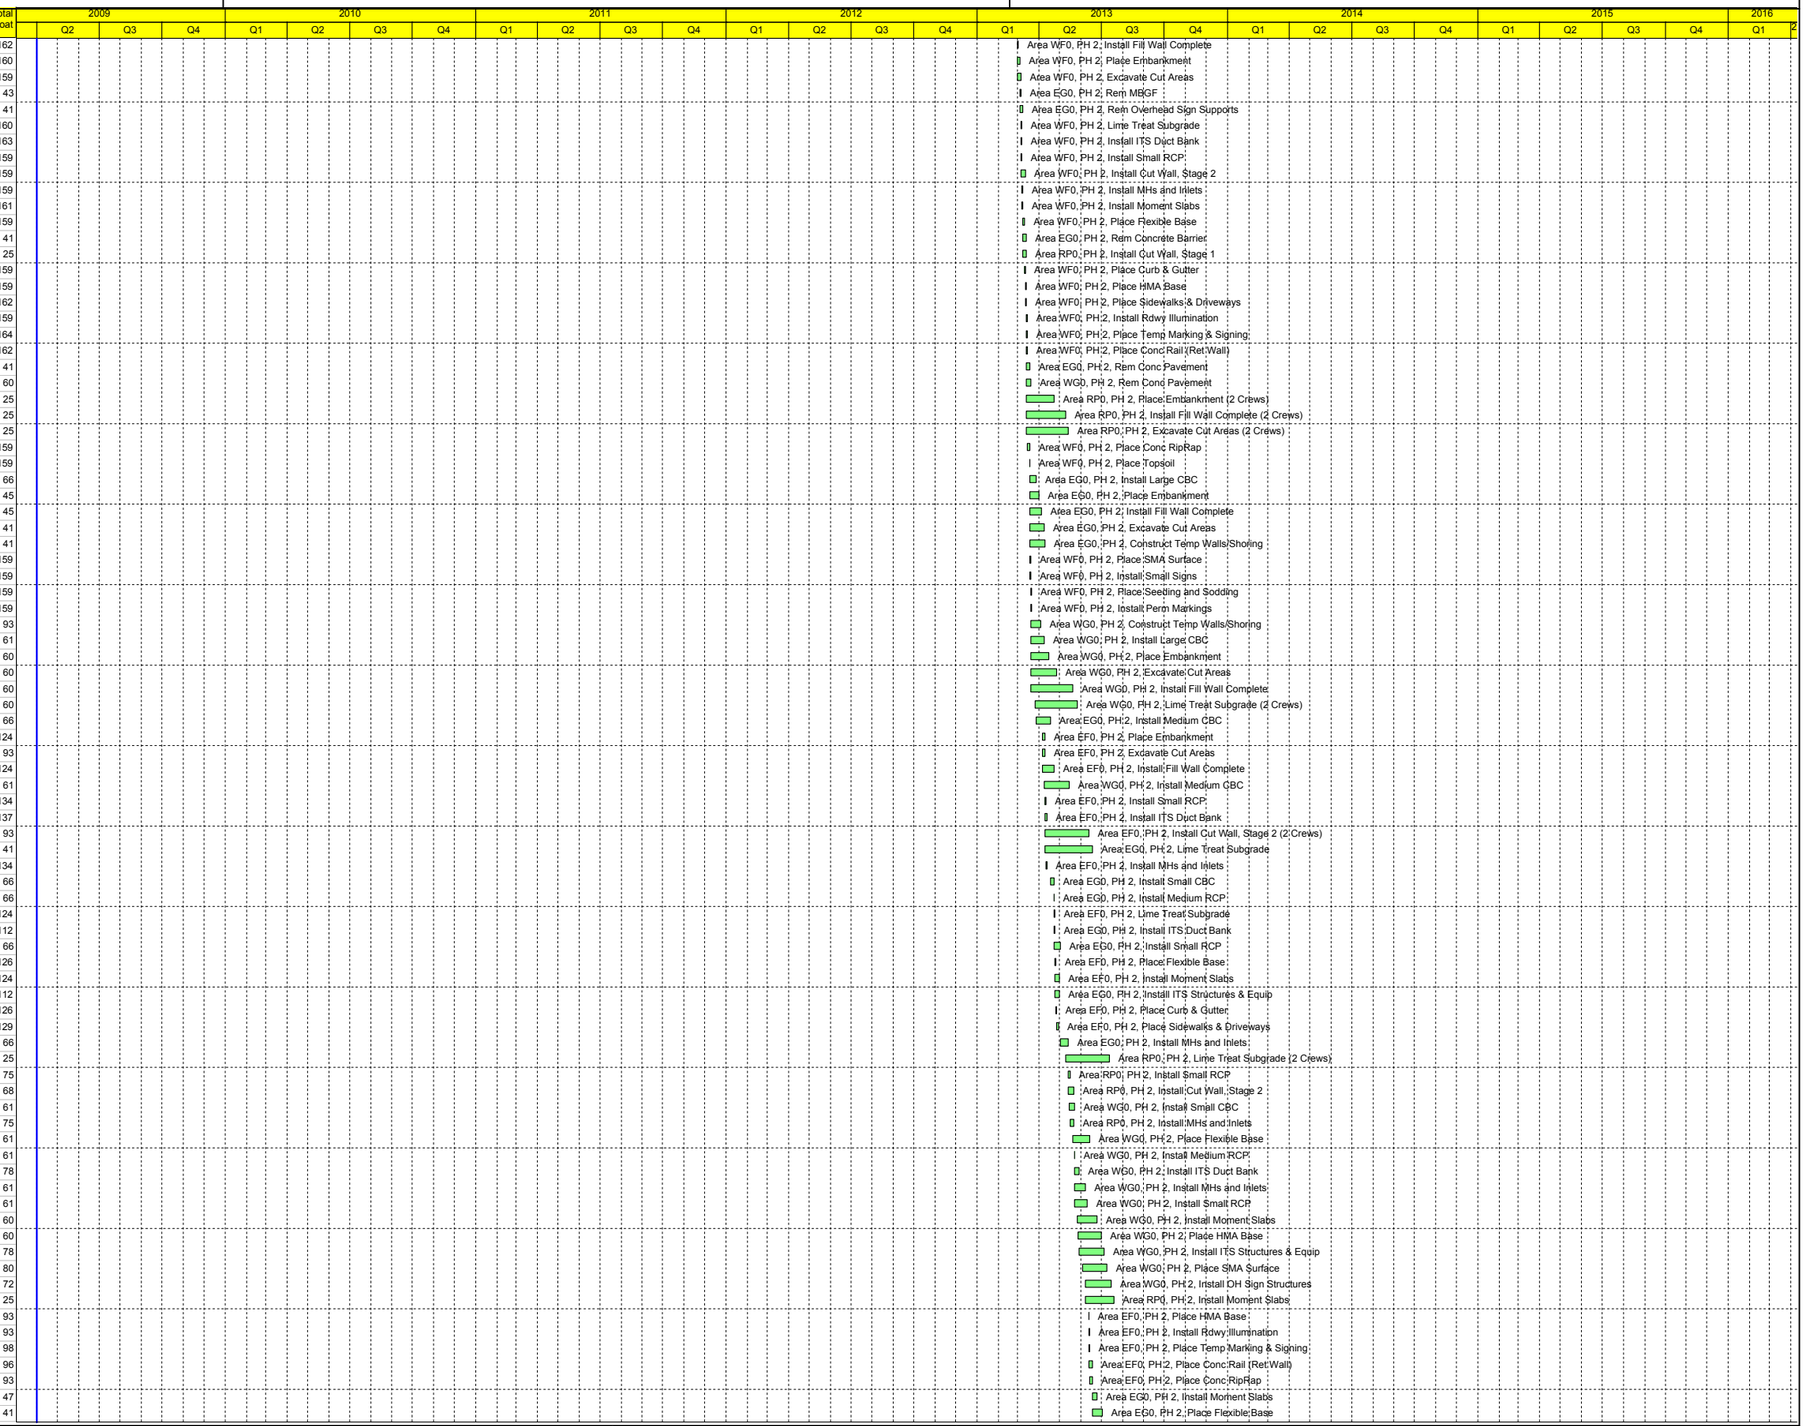

Remaining Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.5.2.0	1B20EF00016010	Area EF0, PH 2, Place Topsoil	1	18-Jun-13	19-Jun-13	93
1.5.2.0	1B20EF00034610	Area EF0, PH 2, Place SMA Surface	1	19-Jun-13	20-Jun-13	93
1.5.7.0	1B20EF00064410	Area EF0, PH 2, Install Small Signs	1	19-Jun-13	20-Jun-13	93
1.5.2.0	1B20RP00024711	Area RP0, PH 2, Place Flexible Base	22	19-Jun-13	19-Jul-13	37
1.5	1B20WF00099999	Area WF0, PH 2, Finish	0		20-Jun-13	94
1.5.6.0	1B20EF00016410	Area EF0, PH 2, Place Seeding and Sodding	1	20-Jun-13	21-Jun-13	93
1.5.7.0	1B20EF00066610	Area EF0, PH 2, Install Perm Markings	1	20-Jun-13	21-Jun-13	93
1.5	1B20EF00099999	Area EF0, PH 2, Finish	0		21-Jun-13	93
1.5.2.0	1B20WG000450...	Area WG0, PH 2, Place Conc Rail (Ret Wall)	10	24-Jun-13	08-Jul-13	60
1.5.9.0	1B20WG000512...	Area WG0, PH 2, Place Temp Conc Barrier	5	01-Jul-13	08-Jul-13	79
1.5.2.0	1B20EG00034012	Area EG0, PH 2, Place HMA Base	13	02-Jul-13	19-Jul-13	41
1.5.9.0	1B20WG000662...	Area WG0, PH 2, Place Temp Marking & Sig...	3	08-Jul-13	11-Jul-13	79
1.5.2.0	1B20RP00052910	Area RP0, PH 2, Place Curb & Gutter	14	08-Jul-13	26-Jul-13	37
1.5.2.0	1B20WG000540...	Area WG0, PH 2, Install MBGF	17	08-Jul-13	31-Jul-13	60
1.5.7.0	1B20WG000610...	Area WG0, PH 2, Install Rdwy Illumination	5	15-Jul-13	22-Jul-13	72
1.5.2.0	1B20EG00045010	Area EG0, PH 2, Place Conc Rail (Ret Wall)	6	19-Jul-13	29-Jul-13	55
1.5.7.0	1B20EG00065010	Area EG0, PH 2, Install OH Sign Structures	14	19-Jul-13	08-Aug-13	41
1.5.9.0	1B20EG00051200	Area EG0, PH 2, Place Temp Conc Barrier	15	19-Jul-13	09-Aug-13	56
1.5.2.0	1B20RP00034012	Area RP0, PH 2, Place HMA Base	27	19-Jul-13	27-Aug-13	25
1.5.2.0	1B20RP00045010	Area RP0, PH 2, Place Conc Rail (Ret Wall)	32	19-Jul-13	03-Sep-13	25
1.5.2.0	1B20EG00054010	Area EG0, PH 2, Install MBGF	10	29-Jul-13	12-Aug-13	55
1.5.2.0	1B20WG000545...	Area WG0, PH 2, Install Attenuators	3	31-Jul-13	05-Aug-13	60
1.5.7.0	1B20WG000666...	Area WG0, PH 2, Install Perm Markings	2	05-Aug-...	07-Aug-13	60
1.5	1B20WG000999...	Area WG0, PH 2, Finish	0		07-Aug-13	60
1.5.2.0	1B20RP00034610	Area RP0, PH 2, Place SMA Surface	29	07-Aug-...	17-Sep-13	29
1.5.7.0	1B20EG00061020	Area EG0, PH 2, Install Rdwy Illumination	3	08-Aug-...	13-Aug-13	41
1.5.9.0	1B20EG00066200	Area EG0, PH 2, Place Temp Marking & Sig...	2	09-Aug-...	13-Aug-13	56
1.5.2.0	1B20EG00054510	Area EG0, PH 2, Install Attenuators	1	12-Aug-...	13-Aug-13	55
1.5.2.0	1B20EG00034610	Area EG0, PH 2, Place SMA Surface	14	13-Aug-...	02-Sep-13	41
1.5.2.0	1B20RP00043210	Area RP0, PH 2, Place Conc RipRap	25	20-Aug-...	24-Sep-13	25
1.5.7.0	1B20RP00061020	Area RP0, PH 2, Install Rdwy Illumination	16	26-Aug-...	17-Sep-13	25
1.5.7.0	1B20EG00066610	Area EG0, PH 2, Install Perm Markings	1	02-Sep-...	03-Sep-13	41
1.5	1B20EG00099999	Area EG0, PH 2, Finish	0		03-Sep-13	41
1.5.7.0	1B20RP00066610	Area RP0, PH 2, Install Perm Markings	2	17-Sep-...	19-Sep-13	29
1.5.7.0	1B20RP00064410	Area RP0, PH 2, Install Small Signs	1	24-Sep-...	25-Sep-13	25
1.5	1B20RP00099999	Area RP0, PH 2, Finish	0		25-Sep-13	25
1.5.4.0.1.37	1B20B037000001	BR 37, PH 2, Start	0	18-Feb-13		111
1.5.4.0.1.37	1B20B037041600	BR 37, PH 2, Install Drill Shafts	8	18-Feb-13	28-Feb-13	111
1.5.4.0.1.37	1B20B037042040	BR 37, PH 2, Install Abutments	3	28-Feb-13	05-Mar-13	138
1.5.4.0.1.37	1B20B037042010	BR 37, PH 2, Install Footings	12	28-Feb-13	18-Mar-13	111
1.5.4.0.1.37	1B20B037042020	BR 37, PH 2, Install Columns	5	18-Mar-13	25-Mar-13	111
1.5.4.0.1.37	1B20B037042030	BR 37, PH 2, Install Bent Caps	13	25-Mar-13	11-Apr-13	111
1.5.4.0.1.37	1B20B037042510	BR 37, PH 2, Install Conc Beams	3	11-Apr-13	16-Apr-13	111
1.5.4.0.1.37	1B20B037045410	BR 37, PH 2, Install Exp Joints	1	16-Apr-13	17-Apr-13	111
1.5.4.0.1.37	1B20B037042210	BR 37, PH 2, Install Deck Slab	15	17-Apr-13	08-May-13	111
1.5.4.0.1.37	1B20B037042050	BR 37, PH 2, Install Apprch Slabs	8	08-May...	20-May-13	113
1.5.4.0.1.37	1B20B037045020	BR 37, PH 2, Install Conc Rail	4	22-May...	28-May-13	111
1.5.4.0.1.37	1B20B037099999	BR 37, PH 2, Finish	0		28-May-13	111
1.5.4.0.1.43	1B20B043000001	BR 43, PH 2, Start	0	18-Feb-13		100
1.5.4.0.1.43	1B20B043049610	BR 43, PH 2, Demo Extg Bridge	13	18-Feb-13	07-Mar-13	100
1.5.4.0.1.43	1B20B043041600	BR 43, PH 2, Install Drill Shafts	5	07-Mar-13	14-Mar-13	100
1.5.4.0.1.43	1B20B043042020	BR 43, PH 2, Install Columns	3	14-Mar-13	19-Mar-13	103
1.5.4.0.1.43	1B20B043042040	BR 43, PH 2, Install Abutments	10	14-Mar-13	28-Mar-13	100
1.5.4.0.1.43	1B20B043042030	BR 43, PH 2, Install Bent Caps	4	19-Mar-13	25-Mar-13	103
1.5.4.0.1.43	1B20B043042510	BR 43, PH 2, Install Conc Beams	3	28-Mar-13	02-Apr-13	100
1.5.4.0.1.43	1B20B043045410	BR 43, PH 2, Install Exp Joints	3	02-Apr-13	05-Apr-13	100
1.5.4.0.1.43	1B20B043042210	BR 43, PH 2, Install Deck Slab	21	05-Apr-13	06-May-13	100
1.5.4.0.1.43	1B20B043042050	BR 43, PH 2, Install Apprch Slabs	24	06-May...	07-Jun-13	100
1.5.4.0.1.43	1B20B043045020	BR 43, PH 2, Install Conc Rail	3	07-Jun-13	12-Jun-13	100
1.5.4.0.1.43	1B20B043099999	BR 43, PH 2, Finish	0		12-Jun-13	100
1.5.4.0.1.45	1B20B045000001	BR 45, PH 2, Start	0	18-Feb-13		115
1.5.4.0.1.45	1B20B045049610	BR 45, PH 2, Demo Extg Bridge	15	18-Feb-13	11-Mar-13	115
1.5.4.0.1.45	1B20B045041600	BR 45, PH 2, Install Drill Shafts	4	11-Mar-13	15-Mar-13	115
1.5.4.0.1.45	1B20B045042020	BR 45, PH 2, Install Columns	2	15-Mar-13	19-Mar-13	120
1.5.4.0.1.45	1B20B045042040	BR 45, PH 2, Install Abutments	10	15-Mar-13	29-Mar-13	115
1.5.4.0.1.45	1B20B045042030	BR 45, PH 2, Install Bent Caps	3	19-Mar-13	22-Mar-13	120
1.5.4.0.1.45	1B20B045042510	BR 45, PH 2, Install Conc Beams	3	29-Mar-13	03-Apr-13	115
1.5.4.0.1.45	1B20B045045410	BR 45, PH 2, Install Exp Joints	2	03-Apr-13	05-Apr-13	115
1.5.4.0.1.45	1B20B045042210	BR 45, PH 2, Install Deck Slab	15	05-Apr-13	26-Apr-13	115
1.5.4.0.1.45	1B20B045042050	BR 45, PH 2, Install Apprch Slabs	16	26-Apr-13	20-May-13	115
1.5.4.0.1.45	1B20B045045020	BR 45, PH 2, Install Conc Rail	2	20-May...	22-May-13	115
1.5.4.0.1.45	1B20B045099999	BR 45, PH 2, Finish	0		22-May-13	115
1.5.4.0.1.46	1B20B046000001	BR 46, PH 2, Start	0	18-Feb-13		94
1.5.4.0.1.46	1B20B046041600	BR 46, PH 2, Install Drill Shafts	8	18-Feb-13	28-Feb-13	94
1.5.4.0.1.46	1B20B046042040	BR 46, PH 2, Install Abutments	5	28-Feb-13	07-Mar-13	108
1.5.4.0.1.46	1B20B046042020	BR 46, PH 2, Install Columns	11	28-Feb-13	15-Mar-13	94
1.5.4.0.1.46	1B20B046042030	BR 46, PH 2, Install Bent Caps	8	15-Mar-13	27-Mar-13	94
1.5.4.0.1.46	1B20B046042510	BR 46, PH 2, Install Conc Beams	5	27-Mar-13	03-Apr-13	94
1.5.4.0.1.46	1B20B046045410	BR 46, PH 2, Install Exp Joints	3	03-Apr-13	08-Apr-13	94
1.5.4.0.1.46	1B20B046042210	BR 46, PH 2, Install Deck Slab	37	08-Apr-13	29-May-13	94
1.5.4.0.1.46	1B20B046042050	BR 46, PH 2, Install Apprch Slabs	11	29-May...	13-Jun-13	94
1.5.4.0.1.46	1B20B046045020	BR 46, PH 2, Install Conc Rail	5	13-Jun-13	20-Jun-13	94
1.5.4.0.1.46	1B20B046099999	BR 46, PH 2, Finish	0		20-Jun-13	94
1.5.4.0.1.47	1B20B047000001	BR 47, PH 2, Start	0	18-Feb-13		110
1.5.4.0.1.47	1B20B047041600	BR 47, PH 2, Install Drill Shafts	6	18-Feb-13	26-Feb-13	110
1.5.4.0.1.47	1B20B047042040	BR 47, PH 2, Install Abutments	2	26-Feb-13	28-Feb-13	146

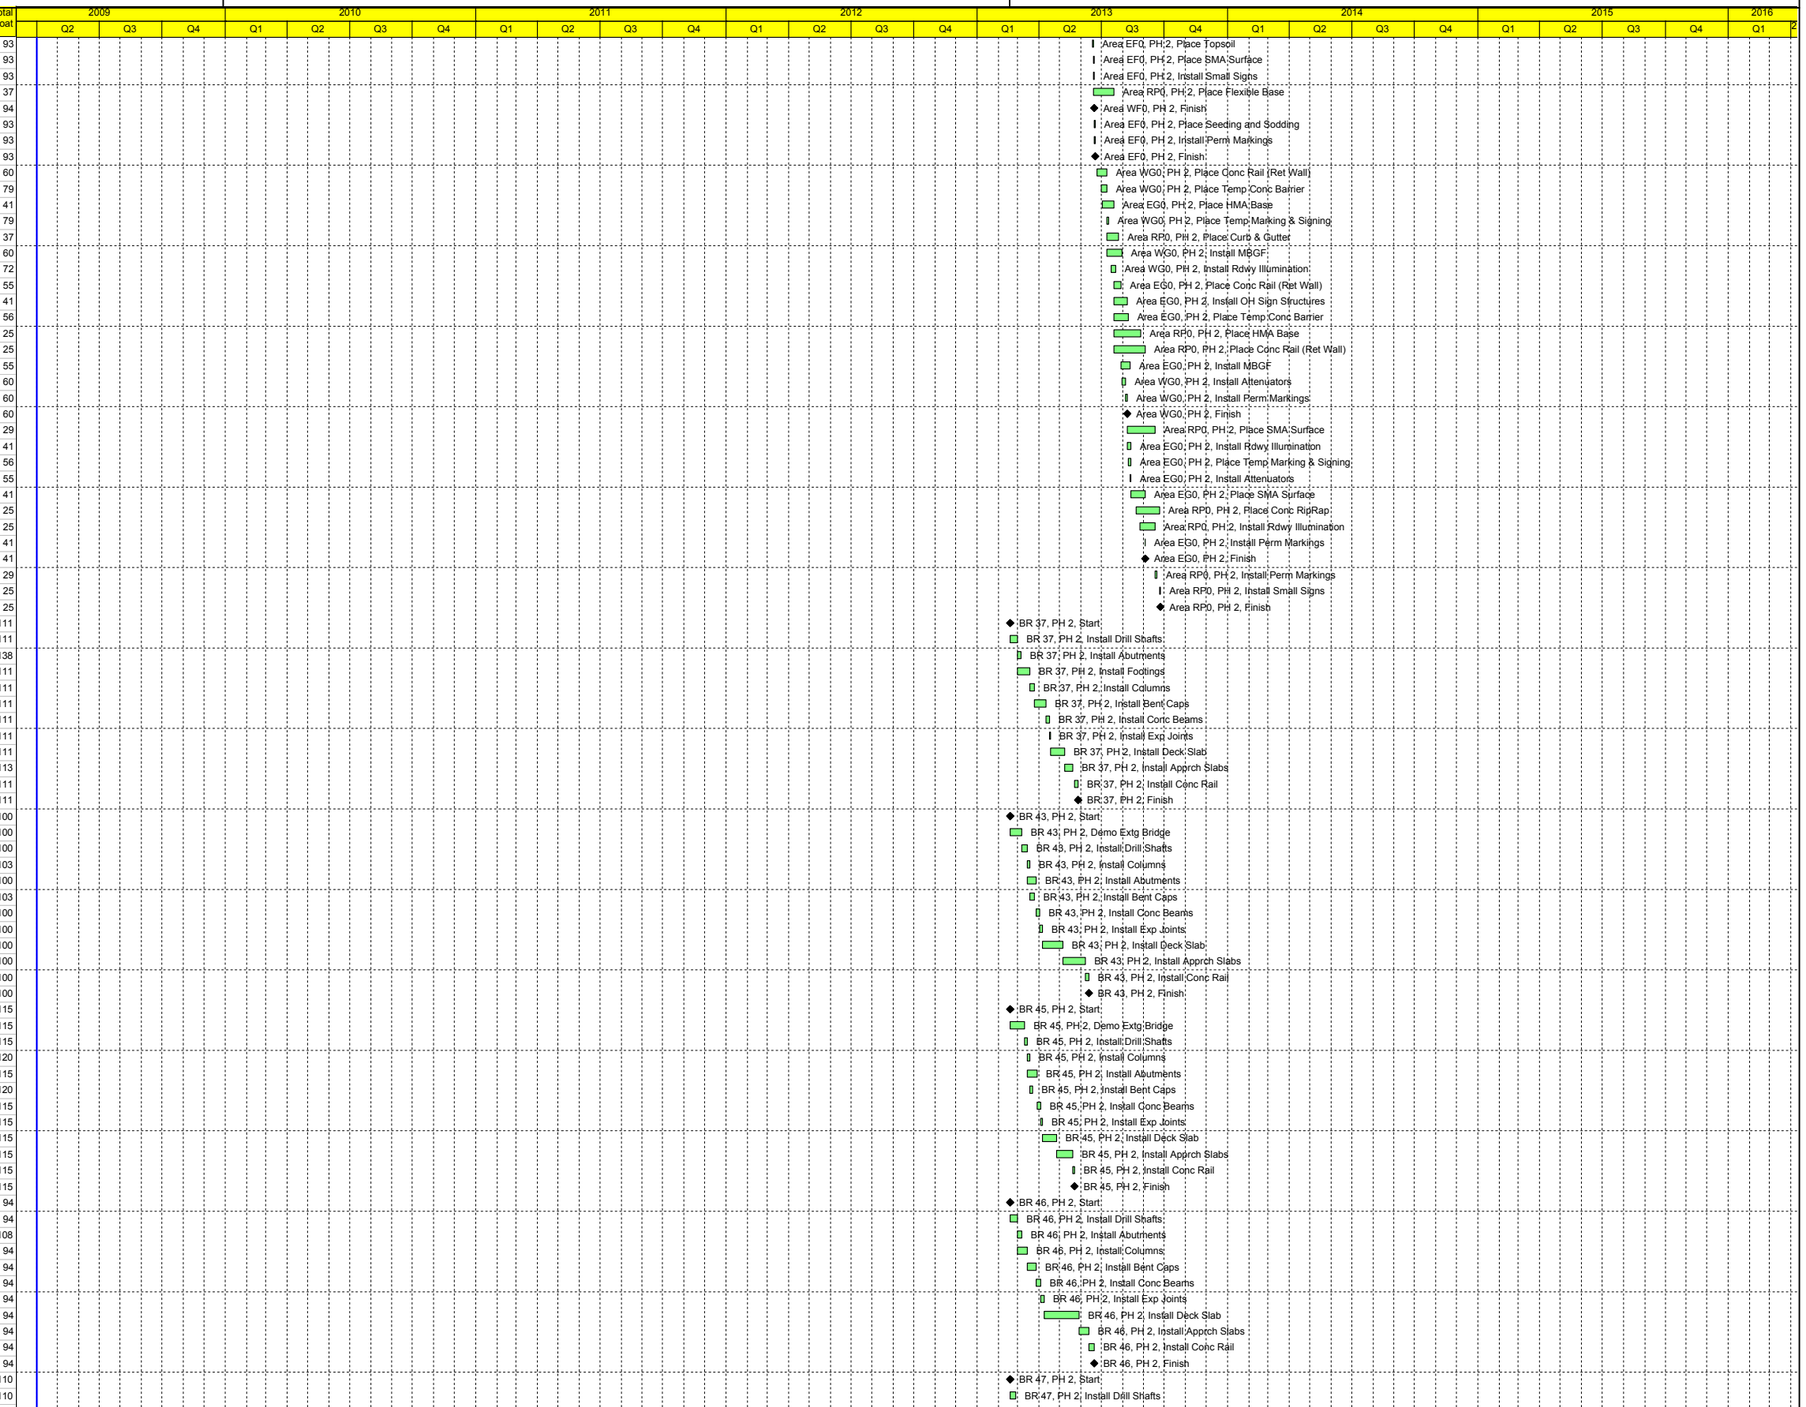

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.5.4.0.1.47	1B20B047042010	BR 47, PH 2, Install Footings	13	26-Feb-13	15-Mar-13	110
1.5.4.0.1.47	1B20B047042020	BR 47, PH 2, Install Columns	9	15-Mar-13	28-Mar-13	110
1.5.4.0.1.47	1B20B047042030	BR 47, PH 2, Install Bent Caps	16	28-Mar-13	19-Apr-13	110
1.5.4.0.1.47	1B20B047042510	BR 47, PH 2, Install Conc Beams	2	19-Apr-13	23-Apr-13	110
1.5.4.0.1.47	1B20B047045410	BR 47, PH 2, Install Exp Joints	1	23-Apr-13	24-Apr-13	110
1.5.4.0.1.47	1B20B047042210	BR 47, PH 2, Install Deck Slab	12	24-Apr-13	10-May-13	110
1.5.4.0.1.47	1B20B047042050	BR 47, PH 2, Install Apprch Slabs	4	10-May...	16-May-13	116
1.5.4.0.1.47	1B20B047045020	BR 47, PH 2, Install Conc Rail	3	24-May...	29-May-13	110
1.5.4.0.1.47	1B20B047099999	BR 47, PH 2, Finish	0		29-May-13	110
1.5.4.0.1.48	1B20B048000001	BR 48, PH 2, Start	0	18-Feb-13		126
1.5.4.0.1.48	1B20B048041600	BR 48, PH 2, Install Drill Shafts	4	18-Feb-13	22-Feb-13	126
1.5.4.0.1.48	1B20B048042040	BR 48, PH 2, Install Abutments	4	22-Feb-13	28-Feb-13	131
1.5.4.0.1.48	1B20B048042020	BR 48, PH 2, Install Columns	4	22-Feb-13	28-Feb-13	126
1.5.4.0.1.48	1B20B048042030	BR 48, PH 2, Install Bent Caps	5	28-Feb-13	07-Mar-13	126
1.5.4.0.1.48	1B20B048042510	BR 48, PH 2, Install Conc Beams	4	07-Mar-13	13-Mar-13	126
1.5.4.0.1.48	1B20B048045410	BR 48, PH 2, Install Exp Joints	2	13-Mar-13	15-Mar-13	126
1.5.4.0.1.48	1B20B048042210	BR 48, PH 2, Install Deck Slab	22	15-Mar-13	16-Apr-13	126
1.5.4.0.1.48	1B20B048042050	BR 48, PH 2, Install Apprch Slabs	8	16-Apr-13	26-Apr-13	128
1.5.4.0.1.48	1B20B048045020	BR 48, PH 2, Install Conc Rail	5	30-Apr-13	07-May-13	126
1.5.4.0.1.48	1B20B048099999	BR 48, PH 2, Finish	0		07-May-13	126
1.5.4.0.1.49	1B20B049000001	BR 49, PH 2, Start	0	18-Feb-13		95
1.5.4.0.1.49	1B20B049041600	BR 49, PH 2, Install Drill Shafts	4	18-Feb-13	22-Feb-13	95
1.5.4.0.1.49	1B20B049042040	BR 49, PH 2, Install Abutments	2	22-Feb-13	26-Feb-13	142
1.5.4.0.1.49	1B20B049042010	BR 49, PH 2, Install Footings	17	22-Feb-13	19-Mar-13	95
1.5.4.0.1.49	1B20B049042020	BR 49, PH 2, Install Columns	13	19-Mar-13	05-Apr-13	95
1.5.4.0.1.49	1B20B049042030	BR 49, PH 2, Install Bent Caps	19	05-Apr-13	02-May-13	95
1.5.4.0.1.49	1B20B049042510	BR 49, PH 2, Install Conc Beams	3	02-May...	07-May-13	95
1.5.4.0.1.49	1B20B049045410	BR 49, PH 2, Install Exp Joints	1	07-May...	08-May-13	95
1.5.4.0.1.49	1B20B049042210	BR 49, PH 2, Install Deck Slab	16	08-May...	30-May-13	95
1.5.4.0.1.49	1B20B049042050	BR 49, PH 2, Install Apprch Slabs	4	30-May...	05-Jun-13	101
1.5.4.0.1.49	1B20B049045020	BR 49, PH 2, Install Conc Rail	4	13-Jun-13	19-Jun-13	95
1.5.4.0.1.49	1B20B049099999	BR 49, PH 2, Finish	0		19-Jun-13	95
1.5.4.0.1.52	1B20B052000001	BR 52, PH 2, Start	0	18-Feb-13		154
1.5.4.0.1.52	1B20B052041600	BR 52, PH 2, Install Drill Shafts	2	18-Feb-13	20-Feb-13	154
1.5.4.0.1.52	1B20B052042040	BR 52, PH 2, Install Abutments	1	20-Feb-13	21-Feb-13	162
1.5.4.0.1.52	1B20B052042010	BR 52, PH 2, Install Footings	4	20-Feb-13	26-Feb-13	154
1.5.4.0.1.52	1B20B052042020	BR 52, PH 2, Install Columns	2	26-Feb-13	28-Feb-13	154
1.5.4.0.1.52	1B20B052042030	BR 52, PH 2, Install Bent Caps	3	28-Feb-13	05-Mar-13	154
1.5.4.0.1.52	1B20B052042510	BR 52, PH 2, Install Conc Beams	1	05-Mar-13	06-Mar-13	154
1.5.4.0.1.52	1B20B052045410	BR 52, PH 2, Install Exp Joints	1	06-Mar-13	07-Mar-13	154
1.5.4.0.1.52	1B20B052042210	BR 52, PH 2, Install Deck Slab	4	07-Mar-13	13-Mar-13	154
1.5.4.0.1.52	1B20B052042050	BR 52, PH 2, Install Apprch Slabs	3	13-Mar-13	18-Mar-13	161
1.5.4.0.1.52	1B20B052045020	BR 52, PH 2, Install Conc Rail	1	27-Mar-13	28-Mar-13	154
1.5.4.0.1.52	1B20B052099999	BR 52, PH 2, Finish	0		28-Mar-13	154
1.5.4.0.1.55	1B20B055000001	BR 55, PH 2, Start	0	18-Feb-13		159
1.5.4.0.1.55	1B20B055041600	BR 55, PH 2, Install Drill Shafts	3	18-Feb-13	21-Feb-13	159
1.5.4.0.1.55	1B20B055042030	BR 55, PH 2, Install Bent Caps	8	21-Feb-13	05-Mar-13	159
1.5.4.0.1.55	1B20B055044210	BR 55, PH 2, Install Plate Girders	2	05-Mar-13	07-Mar-13	159
1.5.4.0.1.55	1B20B055099999	BR 55, PH 2, Finish	0		21-Mar-13	159
1.5	1B200000000001	START PHASE 2, SUBSEGMENT 1B	0	18-Feb-13		25
1.5	1B200000099999	FINISH PHASE 2, SUBSEGMENT 1B	0		25-Sep-13	25
CONSTRUCTION PHASE 3			281	25-Sep-...	23-Oct-14	25
1.5	1B30EG00000001	Area EG0, PH 3, Start	0	25-Sep-...		28
1.5	1B30RP00000001	Area RP0, PH 3, Start	0	25-Sep-...		72
1.5	1B30ML00000001	Area ML0, PH 3, Start	0	25-Sep-...		60
1.5	1B30WF00000001	Area WF0, PH 3, Start	0	25-Sep-...		159
1.5	1B30WG000000...	Area WG0, PH 3, Start	0	25-Sep-...		25
1.5.3.0	1B30ML00046420	Area ML0, PH 3, Install Medium RCP	1	25-Sep-...	26-Sep-13	121
1.5.2.0	1B30EG00060010	Area EG0, PH 3, Rem Light Poles	2	25-Sep-...	27-Sep-13	32
1.5.2.0	1B30WF00050600	Area WF0, PH 3, Place Temp Erosion Control	2	25-Sep-...	27-Sep-13	159
1.5.2.0	1B30RP00010410	Area RP0, PH 3, Rem Conc Pavement	7	25-Sep-...	04-Oct-13	72
1.5.2.0	1B30EG00054210	Area EG0, PH 3, Rem MBGF	12	25-Sep-...	11-Oct-13	29
1.5.2.0	1B30EG00063010	Area EG0, PH 3, Rem Overhead Sign Supports	21	25-Sep-...	24-Oct-13	28
1.5.2.0	1B30EG00050600	Area EG0, PH 3, Place Temp Erosion Control	32	25-Sep-...	08-Nov-13	28
1.5.4.0	1B30ML00042320	Area ML0, PH 3, Install Cut Wall, Stage 1	38	25-Sep-...	18-Nov-13	60
1.5.2.0	1B30WG000506...	Area WG0, PH 3, Place Temp Erosion Control	55	25-Sep-...	11-Dec-13	25
1.5.7.0	1B30WF00090010	Area WF0, PH 3, Install Noise Walls	1	27-Sep-...	30-Sep-13	159
1.5.2.0	1B30WF00010410	Area WF0, PH 3, Rem Conc Pavement	1	30-Sep-...	01-Oct-13	159
1.5.3.0	1B30WF00046210	Area WF0, PH 3, Install Small CBC	1	01-Oct-13	02-Oct-13	287
1.5.4.0	1B30WF00042320	Area WF0, PH 3, Install Cut Wall, Stage 1	53	01-Oct-13	13-Dec-13	159
1.5.3.0	1B30WF00046420	Area WF0, PH 3, Install Medium RCP	2	02-Oct-13	04-Oct-13	287
1.5.4.0	1B30ML00042310	Area ML0, PH 3, Install Fill Wall Complete	8	02-Oct-13	14-Oct-13	60
1.5.2.0	1B30ML00011010	Area ML0, PH 3, Excavate Cut Areas (2 Crews)	43	02-Oct-13	02-Dec-13	60
1.5.2.0	1B30ML00013210	Area ML0, PH 3, Place Embankment	57	02-Oct-13	20-Dec-13	60
1.5.2.0	1B30EG00010430	Area EG0, PH 3, Rem Concrete Barrier	20	03-Oct-13	31-Oct-13	28
1.5.4.0	1B30RP00042320	Area RP0, PH 3, Install Cut Wall, Stage 1	4	04-Oct-13	10-Oct-13	72
1.5.4.0	1B30ML00042325	Area ML0, PH 3, Install Cut Wall, Stage 2	57	09-Oct-13	27-Dec-13	61
1.5.2.0	1B30RP00013210	Area RP0, PH 3, Place Embankment	31	10-Oct-13	22-Nov-13	72
1.5.2.0	1B30RP00011010	Area RP0, PH 3, Excavate Cut Areas	47	10-Oct-13	16-Dec-13	72
1.5.4.0	1B30RP00042310	Area RP0, PH 3, Install Fill Wall Complete	49	10-Oct-13	18-Dec-13	72
1.5.2.0	1B30ML00026010	Area ML0, PH 3, Lime Treat Subgrade (3 cre...	75	21-Oct-13	03-Feb-14	60
1.5.2.0	1B30EG00010410	Area EG0, PH 3, Rem Conc Pavement	16	31-Oct-13	22-Nov-13	28
1.5.4.0	1B30EG00042320	Area EG0, PH 3, Install Cut Wall, Stage 1	4	22-Nov-...	28-Nov-13	55
1.5.3.0	1B30EG00046230	Area EG0, PH 3, Install Large CBC (2 Crews)	25	22-Nov-...	27-Dec-13	28
1.5.2.0	1B30EG00013210	Area EG0, PH 3, Place Embankment (2 Crews)	34	28-Nov-...	15-Jan-14	55
1.5.4.0	1B30EG00042310	Area EG0, PH 3, Install Fill Wall Complete	42	28-Nov-...	27-Jan-14	55

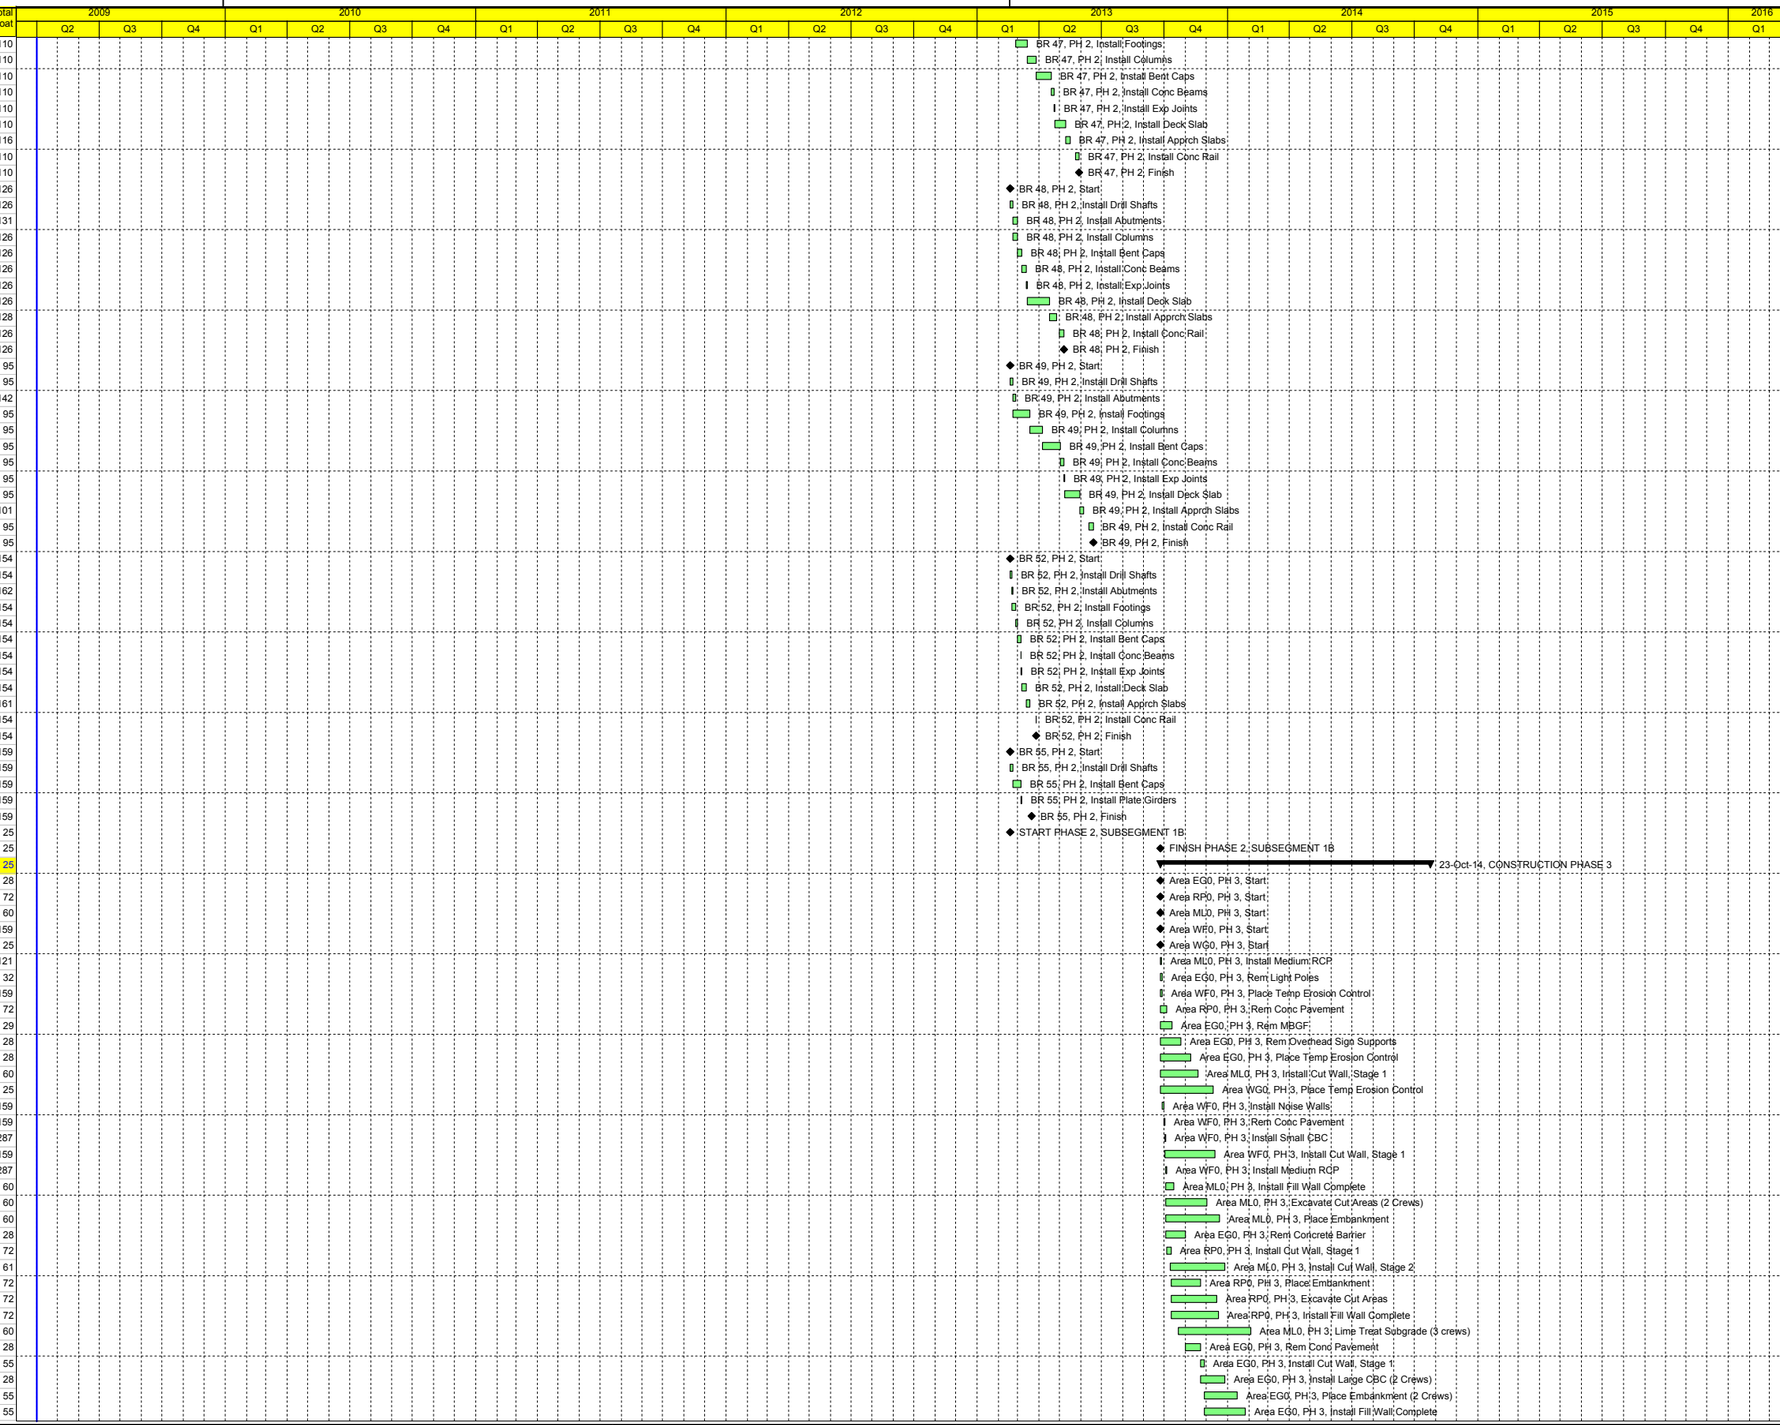

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.5.2.0	1B30EG00011010	Area EG0, PH 3, Excavate Cut Areas (2 crews)	52	28-Nov-...	10-Feb-14	55
1.5.2.0	1B30WG000600...	Area WG0, PH 3, Rem Light Poles	1	11-Dec-...	12-Dec-13	42
1.5.2.0	1B30WG000542...	Area WG0, PH 3, Rem MBGF	10	11-Dec-...	25-Dec-13	33
1.5.2.0	1B30WG000630...	Area WG0, PH 3, Rem Overhead Sign Supp...	18	11-Dec-...	06-Jan-14	25
1.5.2.0	1B30WF00013210	Area WF0, PH 3, Place Embankment	2	13-Dec-...	17-Dec-13	230
1.5.2.0	1B30WF00011010	Area WF0, PH 3, Excavate Cut Areas	3	13-Dec-...	18-Dec-13	159
1.5.4.0	1B30WF00042310	Area WF0, PH 3, Install Fill Wall Complete	7	13-Dec-...	24-Dec-13	230
1.5.3.0	1B30RP00046410	Area RP0, PH 3, Install Small RCP	1	16-Dec-...	17-Dec-13	125
1.5.4.0	1B30RP00042325	Area RP0, PH 3, Install Cut Wall, Stage 2	6	16-Dec-...	24-Dec-13	142
1.5.3.0	1B30RP00046510	Area RP0, PH 3, Install MHs and Inlets	2	17-Dec-...	19-Dec-13	125
1.5.8.0	1B30WF00061899	Area WF0, PH 3, Install ITS Duct Bank	2	18-Dec-...	20-Dec-13	238
1.5.3.0	1B30WF00046410	Area WF0, PH 3, Install Small RCP	2	18-Dec-...	20-Dec-13	234
1.5.2.0	1B30RP00026010	Area RP0, PH 3, Lime Treat Subgrade	54	18-Dec-...	04-Mar-14	72
1.5.4.0	1B30WF00042325	Area WF0, PH 3, Install Cut Wall, Stage 2	80	18-Dec-...	09-Apr-14	159
1.5.3.0	1B30ML00046410	Area ML0, PH 3, Install Small RCP	1	20-Dec-...	23-Dec-13	60
1.5.3.0	1B30WF00046510	Area WF0, PH 3, Install MHs and Inlets	1	20-Dec-...	23-Dec-13	234
1.5.8.0	1B30ML00061899	Area ML0, PH 3, Install ITS Duct Bank	4	20-Dec-...	26-Dec-13	203
1.5.2.0	1B30ML00024710	Area ML0, PH 3, Place Flexible Base	40	23-Dec-...	17-Feb-14	60
1.5.2.0	1B30WF00026010	Area WF0, PH 3, Lime Treat Subgrade	2	24-Dec-...	26-Dec-13	230
1.5.2.0	1B30WF00024711	Area WF0, PH 3, Place Flexible Base	1	26-Dec-...	27-Dec-13	231
1.5.4.0	1B30WF00042315	Area WF0, PH 3, Install Moment Slabs	3	26-Dec-...	31-Dec-13	230
1.5.8.0	1B30ML00041699	Area ML0, PH 3, Install ITS Structures & Equip	9	26-Dec-...	08-Jan-14	231
1.5.10.0	1B30ML00041698	Area ML0, PH 3, Install Tolling Systems	37	26-Dec-...	17-Feb-14	203
1.5.2.0	1B30WF00052910	Area WF0, PH 3, Place Curb & Gutter	1	27-Dec-...	30-Dec-13	231
1.5.3.0	1B30EG00046220	Area EG0, PH 3, Install Medium CBC (2 Cre...	51	27-Dec-...	10-Mar-14	28
1.5.2.0	1B30WF00053110	Area WF0, PH 3, Place Sidewalks & Driveways	1	30-Dec-...	31-Dec-13	234
1.5.2.0	1B30ML00034010	Area ML0, PH 3, Place HMA Base	53	30-Dec-...	13-Mar-14	60
1.5.2.0	1B30WG000104...	Area WG0, PH 3, Rem Concrete Barrier	16	06-Jan-14	28-Jan-14	25
1.5.2.0	1B30ML00051410	Area ML0, PH 3, Place Median Barrier (3 cre...	95	06-Jan-14	19-May-14	60
1.5.2.0	1B30WG000104...	Area WG0, PH 3, Rem Conc Pavement	13	28-Jan-14	14-Feb-14	25
1.5.4.0	1B30ML00042315	Area ML0, PH 3, Install Moment Slabs	3	03-Feb-14	06-Feb-14	210
1.5.2.0	1B30EG00026010	Area EG0, PH 3, Lime Treat Subgrade (3 cre...	80	03-Feb-14	26-May-14	55
1.5.2.0	1B30ML00045010	Area ML0, PH 3, Place Conc Rail (Ret Wall)	32	04-Feb-14	20-Mar-14	175
1.5.4.0	1B30EG00042325	Area EG0, PH 3, Install Cut Wall, Stage 2	5	10-Feb-14	17-Feb-14	130
1.5.7.0	1B30EG00065010	Area EG0, PH 3, Install OH Sign Structures	97	10-Feb-14	25-Jun-14	111
1.5.7.0	1B30ML00065010	Area ML0, PH 3, Install OH Sign Structures	79	11-Feb-14	02-Jun-14	60
1.5.3.0	1B30WG000462...	Area WG0, PH 3, Install Large CBC	41	14-Feb-14	14-Apr-14	50
1.5.2.0	1B30WG000132...	Area WG0, PH 3, Place Embankment	56	14-Feb-14	05-May-14	25
1.5.4.0	1B30WG000423...	Area WG0, PH 3, Install Fill Wall Complete	76	14-Feb-14	02-Jun-14	41
1.5.2.0	1B30WG000110...	Area WG0, PH 3, Excavate Cut Areas	86	14-Feb-14	16-Jun-14	25
1.5.2.0	1B30WG000260...	Area WG0, PH 3, Lime Treat Subgrade (3 Cr...	92	21-Feb-14	01-Jul-14	25
1.5.3.0	1B30WG000462...	Area WG0, PH 3, Install Medium CBC (2 Cre...	43	03-Mar-14	01-May-14	50
1.5.2.0	1B30RP00024711	Area RP0, PH 3, Place Flexible Base	12	04-Mar-14	20-Mar-14	72
1.5.4.0	1B30RP00042315	Area RP0, PH 3, Install Moment Slabs	18	04-Mar-14	28-Mar-14	74
1.5.3.0	1B30EG00046210	Area EG0, PH 3, Install Small CBC	17	10-Mar-14	02-Apr-14	28
1.5.2.0	1B30RP00052910	Area RP0, PH 3, Place Curb & Gutter	8	20-Mar-14	01-Apr-14	72
1.5.2.0	1B30RP00034012	Area RP0, PH 3, Place HMA Base	15	01-Apr-14	22-Apr-14	72
1.5.8.0	1B30EG00061899	Area EG0, PH 3, Install ITS Duct Bank	5	02-Apr-14	09-Apr-14	107
1.5.3.0	1B30EG00046510	Area EG0, PH 3, Install MHs and Inlets	38	02-Apr-14	26-May-14	28
1.5.3.0	1B30EG00046410	Area EG0, PH 3, Install Small RCP	43	02-Apr-14	02-Jun-14	28
1.5.2.0	1B30WF00034011	Area WF0, PH 3, Place HMA Base	1	09-Apr-14	10-Apr-14	159
1.5.8.0	1B30EG00041699	Area EG0, PH 3, Install ITS Structures & Equip	41	09-Apr-14	05-Jun-14	107
1.5.7.0	1B30WF00061020	Area WF0, PH 3, Install Rdwy Illumination	1	10-Apr-14	11-Apr-14	159
1.5.9.0	1B30WF00066200	Area WF0, PH 3, Place Temp Marking & Sig...	1	10-Apr-14	11-Apr-14	164
1.5.2.0	1B30WF00045010	Area WF0, PH 3, Place Conc Rail (Ret Wall)	2	10-Apr-14	14-Apr-14	162
1.5.2.0	1B30WF00043210	Area WF0, PH 3, Place Conc RipRap	2	11-Apr-14	15-Apr-14	159
1.5.2.0	1B30WF00016010	Area WF0, PH 3, Place Topsoil	1	15-Apr-14	16-Apr-14	159
1.5.2.0	1B30WF00034610	Area WF0, PH 3, Place SMA Surface	1	16-Apr-14	17-Apr-14	159
1.5.7.0	1B30WF00064410	Area WF0, PH 3, Install Small Signs	1	16-Apr-14	17-Apr-14	159
1.5.6.0	1B30WF00016410	Area WF0, PH 3, Place Seeding and Sodding	1	17-Apr-14	18-Apr-14	159
1.5.7.0	1B30WF00066610	Area WF0, PH 3, Install Perm Markings	1	17-Apr-14	18-Apr-14	159
1.5	1B30WF00099999	Area WF0, PH 3, Finish	0		18-Apr-14	159
1.5.2.0	1B30RP00045010	Area RP0, PH 3, Place Conc Rail (Ret Wall)	17	22-Apr-14	15-May-14	138
1.5.7.0	1B30RP00065010	Area RP0, PH 3, Install OH Sign Structures	44	22-Apr-14	23-Jun-14	72
1.5.7.0	1B30WG000650...	Area WG0, PH 3, Install OH Sign Structures	81	29-Apr-14	20-Aug-14	71
1.5.3.0	1B30WG000464...	Area WG0, PH 3, Install Medium RCP	1	01-May...	02-May-14	63
1.5.3.0	1B30WG000462...	Area WG0, PH 3, Install Small CBC	14	01-May...	21-May-14	50
1.5.7.0	1B30ML00061020	Area ML0, PH 3, Install Rdwy Illumination	15	05-May...	26-May-14	65
1.5.4.0	1B30EG00042315	Area EG0, PH 3, Install Moment Slabs	17	08-May...	02-Jun-14	55
1.5.2.0	1B30WG000247...	Area WG0, PH 3, Place Flexible Base	60	23-May...	15-Aug-14	25
1.5.2.0	1B30EG00024711	Area EG0, PH 3, Place Flexible Base	72	26-May...	03-Sep-14	28
1.5.2.0	1B30WG000340...	Area WG0, PH 3, Place HMA Base	74	30-May...	11-Sep-14	25
1.5.2.0	1B30ML00034610	Area ML0, PH 3, Place SMA Surface	63	02-Jun-14	28-Aug-14	60
1.5.2.0	1B30WG000346...	Area WG0, PH 3, Place SMA Surface	79	06-Jun-14	25-Sep-14	39
1.5.8.0	1B30WG000618...	Area WG0, PH 3, Install ITS Duct Bank	6	16-Jun-14	24-Jun-14	50
1.5.3.0	1B30WG000465...	Area WG0, PH 3, Install MHs and Inlets	32	16-Jun-14	30-Jul-14	32
1.5.3.0	1B30WG000464...	Area WG0, PH 3, Install Small RCP	36	16-Jun-14	05-Aug-14	32
1.5.7.0	1B30RP00061020	Area RP0, PH 3, Install Rdwy Illumination	9	23-Jun-14	04-Jul-14	72
1.5.8.0	1B30WG000416...	Area WG0, PH 3, Install ITS Structures & Equip	47	24-Jun-14	28-Aug-14	50
1.5.2.0	1B30EG00054010	Area EG0, PH 3, Install MBGF	65	25-Jun-14	24-Sep-14	28
1.5.4.0	1B30WG000423...	Area WG0, PH 3, Install Moment Slabs	28	01-Jul-14	08-Aug-14	25
1.5.2.0	1B30RP00043210	Area RP0, PH 3, Place Conc RipRap	14	04-Jul-14	24-Jul-14	72
1.5.2.0	1B30EG00034012	Area EG0, PH 3, Place HMA Base (2 Crews)	45	09-Jul-14	10-Sep-14	28
1.5.2.0	1B30EG00034610	Area EG0, PH 3, Place SMA Surface (2 Crews)	48	18-Jul-14	24-Sep-14	39
1.5.2.0	1B30WG000540...	Area WG0, PH 3, Install MBGF	54	18-Jul-14	02-Oct-14	25
1.5.7.0	1B30RP00064410	Area RP0, PH 3, Install Small Signs	1	24-Jul-14	25-Jul-14	89

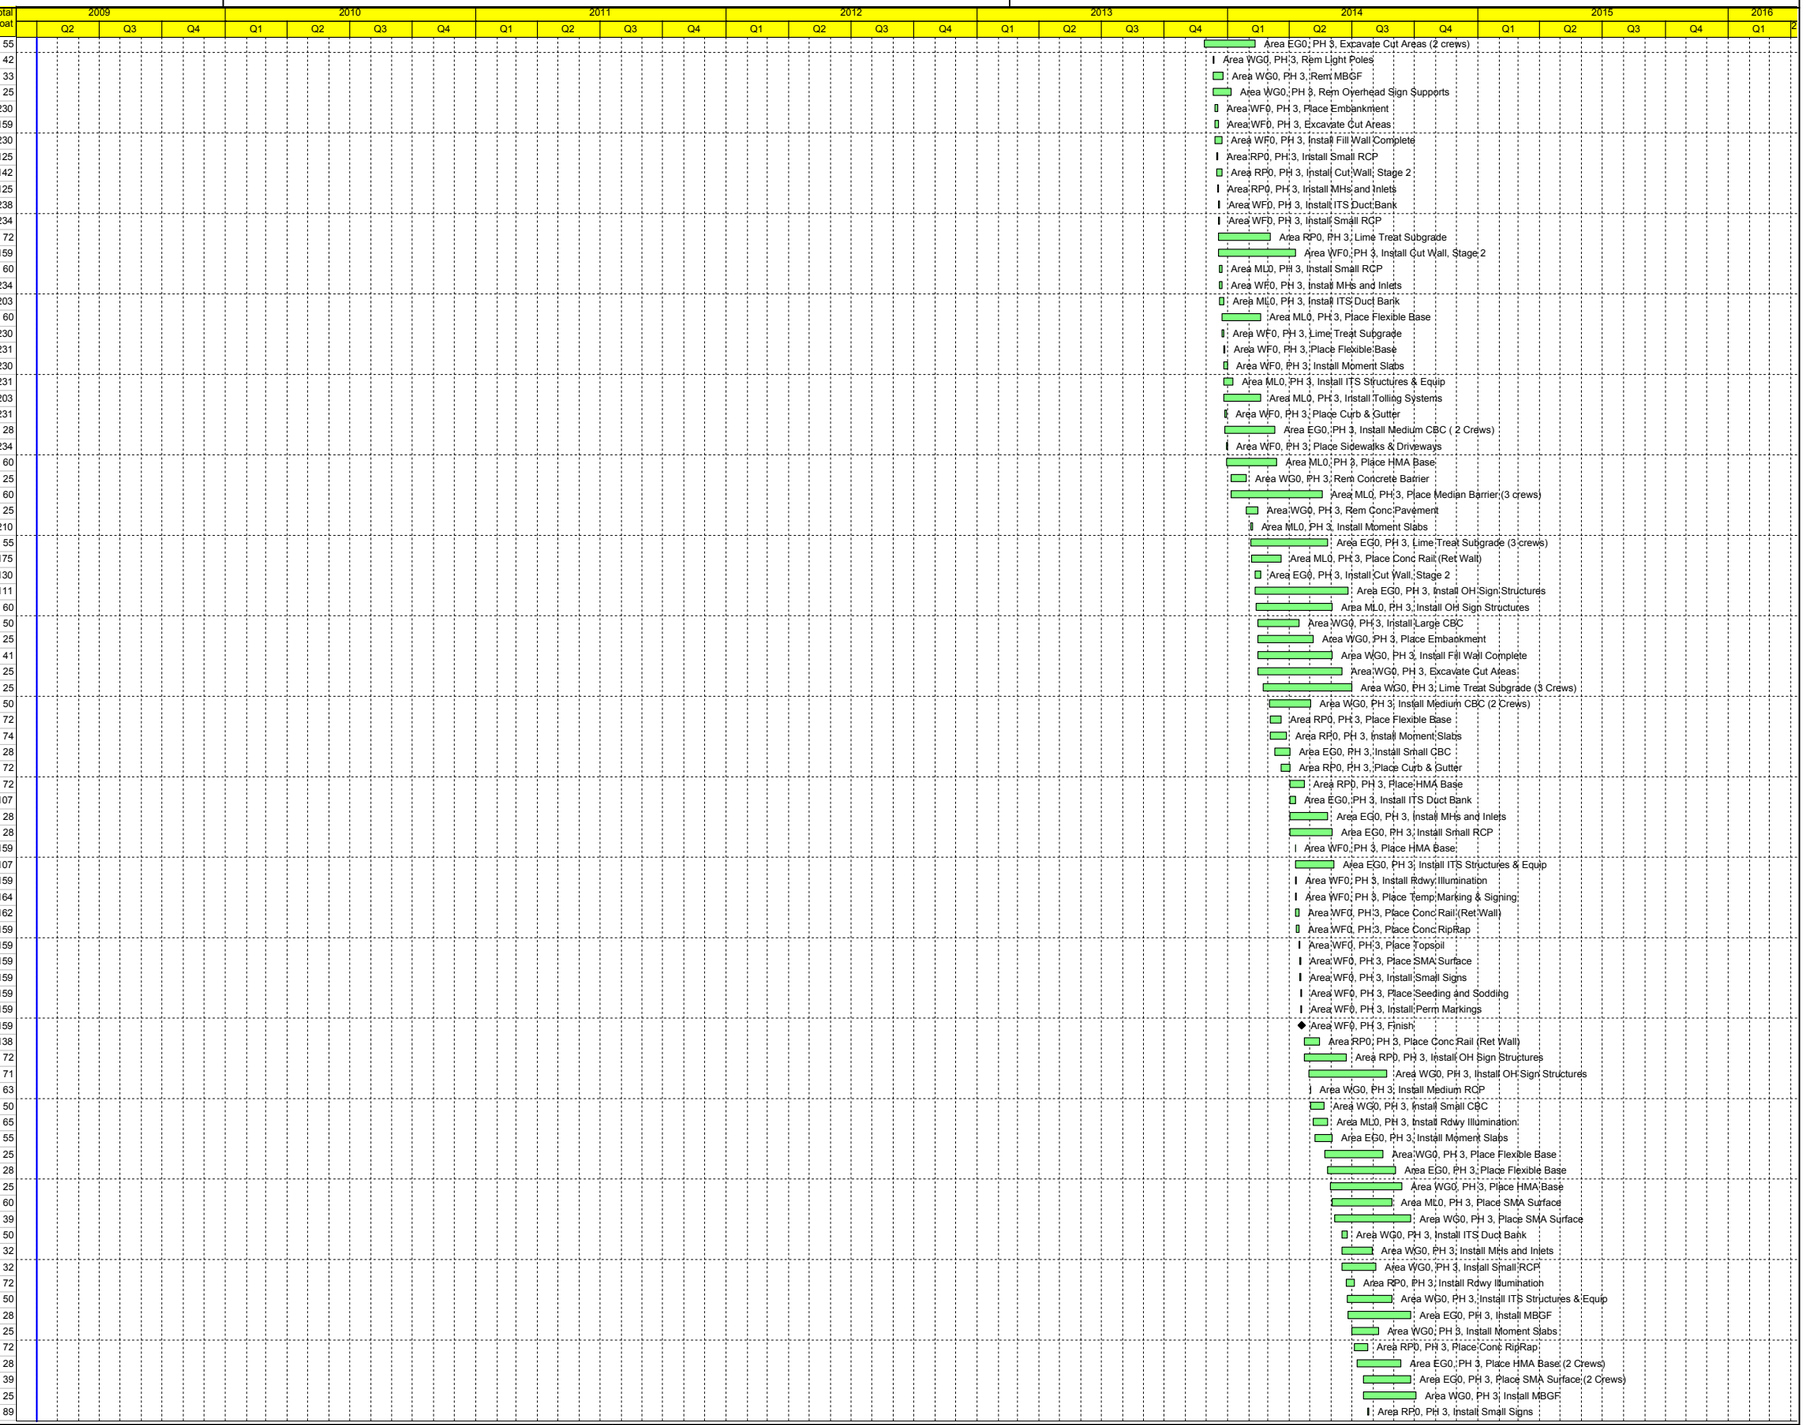

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.5.2.0	1B30RP00034610	Area RP0, PH 3, Place SMA Surface	16	24-Jul-14	15-Aug-14	72
1.5.2.0	1B30EG00045010	Area EG0, PH 3, Place Conc Rail (Ret Wall)	38	25-Jul-14	17-Sep-14	28
1.5.2.0	1B30WG000450...	Area WG0, PH 3, Place Conc Rail (Ret Wall)	32	05-Aug-...	18-Sep-14	25
1.5.7.0	1B30RP00066610	Area RP0, PH 3, Install Perm Markings	2	15-Aug-...	19-Aug-14	72
1.5	1B30RP00099999	Area RP0, PH 3, Finish	0		19-Aug-14	72
1.5.7.0	1B30ML00066610	Area ML0, PH 3, Install Perm Markings	5	28-Aug-...	04-Sep-14	60
1.5.7.0	1B30EG00061020	Area EG0, PH 3, Install Rdwy Illumination	18	29-Aug-...	24-Sep-14	46
1.5	1B30ML00099999	Area ML0, PH 3, Finish	0		04-Sep-14	60
1.5.7.0	1B30WG000610...	Area WG0, PH 3, Install Rdwy Illumination	15	04-Sep-...	25-Sep-14	45
1.5.9.0	1B30EG00050820	Area EG0, PH 3, Const Temp Detour	16	10-Sep-...	02-Oct-14	29
1.5.9.0	1B30WG000662...	Area WG0, PH 3, Place Temp Marking & Sig...	9	11-Sep-...	24-Sep-14	46
1.5.2.0	1B30EG00054510	Area EG0, PH 3, Install Attenuators	11	24-Sep-...	09-Oct-14	28
1.5.2.0	1B30WG000545...	Area WG0, PH 3, Install Attenuators	9	02-Oct-14	15-Oct-14	25
1.5.9.0	1B30EG00066200	Area EG0, PH 3, Place Temp Marking & Sig...	11	02-Oct-14	17-Oct-14	29
1.5.7.0	1B30EG00066610	Area EG0, PH 3, Install Perm Markings	7	09-Oct-14	20-Oct-14	28
1.5.7.0	1B30WG000666...	Area WG0, PH 3, Install Perm Markings	6	15-Oct-14	23-Oct-14	25
1.5	1B30EG00099999	Area EG0, PH 3, Finish	0		20-Oct-14	28
1.5	1B30WG000999...	Area WG0, PH 3, Finish	0		23-Oct-14	25
1.5.4.0.1.38	1B30B038000001	BR 38, PH 3, Start	0	25-Sep-...		223
1.5.4.0.1.38	1B30B038041600	BR 38, PH 3, Install Drill Shafts	15	25-Sep-...	16-Oct-13	223
1.5.4.0.1.38	1B30B038042040	BR 38, PH 3, Install Abutments	3	16-Oct-13	21-Oct-13	253
1.5.4.0.1.38	1B30B038042010	BR 38, PH 3, Install Footings	14	16-Oct-13	05-Nov-13	223
1.5.4.0.1.38	1B30B038042020	BR 38, PH 3, Install Columns	5	05-Nov-...	12-Nov-13	223
1.5.4.0.1.38	1B30B038042030	BR 38, PH 3, Install Bent Caps	14	12-Nov-...	02-Dec-13	223
1.5.4.0.1.38	1B30B038042510	BR 38, PH 3, Install Conc Beams	3	02-Dec-...	05-Dec-13	223
1.5.4.0.1.38	1B30B038045410	BR 38, PH 3, Install Exp Joints	1	05-Dec-...	06-Dec-13	223
1.5.4.0.1.38	1B30B038042210	BR 38, PH 3, Install Deck Slab	17	06-Dec-...	31-Dec-13	223
1.5.4.0.1.38	1B30B038042050	BR 38, PH 3, Install Apprch Slabs	8	31-Dec-...	10-Jan-14	225
1.5.4.0.1.38	1B30B038045020	BR 38, PH 3, Install Conc Rail	4	14-Jan-14	20-Jan-14	223
1.5.4.0.1.38	1B30B038099999	BR 38, PH 3, Finish	0		20-Jan-14	223
1.5.4.0.1.44	1B30B044000001	BR 44, PH 3, Start	0	25-Sep-...		230
1.5.4.0.1.44	1B30B044041600	BR 44, PH 3, Install Drill Shafts	6	25-Sep-...	03-Oct-13	230
1.5.4.0.1.44	1B30B044042020	BR 44, PH 3, Install Columns	2	03-Oct-13	07-Oct-13	236
1.5.4.0.1.44	1B30B044042040	BR 44, PH 3, Install Abutments	12	03-Oct-13	21-Oct-13	230
1.5.4.0.1.44	1B30B044042030	BR 44, PH 3, Install Bent Caps	4	07-Oct-13	11-Oct-13	236
1.5.4.0.1.44	1B30B044042510	BR 44, PH 3, Install Conc Beams	3	21-Oct-13	24-Oct-13	230
1.5.4.0.1.44	1B30B044045410	BR 44, PH 3, Install Exp Joints	2	24-Oct-13	28-Oct-13	230
1.5.4.0.1.44	1B30B044042210	BR 44, PH 3, Install Deck Slab	21	28-Oct-13	26-Nov-13	230
1.5.4.0.1.44	1B30B044042050	BR 44, PH 3, Install Apprch Slabs	30	26-Nov-...	07-Jan-14	230
1.5.4.0.1.44	1B30B044045020	BR 44, PH 3, Install Conc Rail	2	07-Jan-14	09-Jan-14	230
1.5.4.0.1.44	1B30B044099999	BR 44, PH 3, Finish	0		09-Jan-14	230
1.5.4.0.1.52	1B30B052000001	BR 52, PH 3, Start	0	25-Sep-...		259
1.5.4.0.1.52	1B30B052041600	BR 52, PH 3, Install Drill Shafts	4	25-Sep-...	01-Oct-13	259
1.5.4.0.1.52	1B30B052042040	BR 52, PH 3, Install Abutments	3	01-Oct-13	04-Oct-13	274
1.5.4.0.1.52	1B30B052042010	BR 52, PH 3, Install Footings	8	01-Oct-13	11-Oct-13	259
1.5.4.0.1.52	1B30B052042020	BR 52, PH 3, Install Columns	4	11-Oct-13	17-Oct-13	259
1.5.4.0.1.52	1B30B052042030	BR 52, PH 3, Install Bent Caps	6	17-Oct-13	25-Oct-13	259
1.5.4.0.1.52	1B30B052042510	BR 52, PH 3, Install Conc Beams	2	25-Oct-13	29-Oct-13	259
1.5.4.0.1.52	1B30B052045410	BR 52, PH 3, Install Exp Joints	1	29-Oct-13	30-Oct-13	259
1.5.4.0.1.52	1B30B052042210	BR 52, PH 3, Install Deck Slab	10	30-Oct-13	13-Nov-13	259
1.5.4.0.1.52	1B30B052042050	BR 52, PH 3, Install Apprch Slabs	6	13-Nov-...	21-Nov-13	263
1.5.4.0.1.52	1B30B052045020	BR 52, PH 3, Install Conc Rail	2	27-Nov-...	29-Nov-13	259
1.5.4.0.1.52	1B30B052099999	BR 52, PH 3, Finish	0		29-Nov-13	259
1.5.4.0.1.55	1B30B055000001	BR 55, PH 3, Start	0	25-Sep-...		283
1.5.4.0.1.55	1B30B055041600	BR 55, PH 3, Install Drill Shafts	3	25-Sep-...	30-Sep-13	283
1.5.4.0.1.55	1B30B055042030	BR 55, PH 3, Install Bent Caps	8	30-Sep-...	10-Oct-13	283
1.5.4.0.1.55	1B30B055044210	BR 55, PH 3, Install Plate Girders	2	10-Oct-13	14-Oct-13	283
1.5.4.0.1.55	1B30B055099999	BR 55, PH 3, Finish	0		28-Oct-13	283
1.5.4.0.1.56A	1B30B056A00001	BR 56A, PH 3, Start	0	25-Sep-...		190
1.5.4.0.1.56A	1B30B056A49610	BR 56A, PH 3, Demo Extg Bridge	14	25-Sep-...	15-Oct-13	190
1.5.4.0.1.56A	1B30B056A41600	BR 56A, PH 3, Install Drill Shafts	3	15-Oct-13	18-Oct-13	190
1.5.4.0.1.56A	1B30B056A42020	BR 56A, PH 3, Install Columns	4	18-Oct-13	24-Oct-13	194
1.5.4.0.1.56A	1B30B056A42040	BR 56A, PH 3, Install Abutments	13	18-Oct-13	06-Nov-13	190
1.5.4.0.1.56A	1B30B056A42030	BR 56A, PH 3, Install Bent Caps	5	24-Oct-13	31-Oct-13	194
1.5.4.0.1.56A	1B30B056A42510	BR 56A, PH 3, Install Conc Beams	3	06-Nov-...	11-Nov-13	190
1.5.4.0.1.56A	1B30B056A45410	BR 56A, PH 3, Install Exp Joints	3	11-Nov-...	14-Nov-13	190
1.5.4.0.1.56A	1B30B056A42210	BR 56A, PH 3, Install Deck Slab	25	14-Nov-...	19-Dec-13	190
1.5.4.0.1.56A	1B30B056A42050	BR 56A, PH 3, Install Apprch Slabs	51	19-Dec-...	28-Feb-14	190
1.5.4.0.1.56A	1B30B056A45020	BR 56A, PH 3, Install Conc Rail	2	28-Feb-14	04-Mar-14	190
1.5.4.0.1.56A	1B30B056A45500	BR 56A, PH 3, Install Conc Median Barrier	2	04-Mar-14	06-Mar-14	190
1.5.4.0.1.56A	1B30B056A99999	BR 56A, PH 3, Finish	0		06-Mar-14	190
1.5	1B300000000001	START PHASE 3, SUBSEGMENT 1B	0	25-Sep-...		25
1.5	1B300000099999	FINISH PHASE 3, SUBSEGMENT 1B	0		23-Oct-14	25
CONSTRUCTION PHASE 4			149	23-Oct-14	20-May-15	25
1.5	1B40EF00000001	Area EF0, PH 4, Start	0	23-Oct-14		133
1.5	1B40LA00000001	Area LA0, PH 4, Start	0	23-Oct-14		136
1.5	1B40RP00000001	Area RP0, PH 4, Start	0	23-Oct-14		80
1.5	1B40ML00000001	Area ML0, PH 4, Start	0	23-Oct-14		36
1.5	1B40WF00000001	Area WF0, PH 4, Start	0	23-Oct-14		151
1.5	1B40WG000000...	Area WG0, PH 4, Start	0	23-Oct-14		25
1.5	1B40XU00000001	Area XU0, PH 4, Start	0	23-Oct-14		128
1.5.3.0	1B40ML00046420	Area ML0, PH 4, Install Medium RCP	1	23-Oct-14	24-Oct-14	84
1.5.2.0	1B40WF00050600	Area WF0, PH 4, Place Temp Erosion Control	2	23-Oct-14	27-Oct-14	151
1.5.2.0	1B40RP00010410	Area RP0, PH 4, Rem Conc Pavement	3	23-Oct-14	28-Oct-14	80
1.5.2.0	1B40XU00050600	Area XU0, PH 4, Place Temp Erosion Control	3	23-Oct-14	28-Oct-14	128
1.5.2.0	1B40EF00050600	Area EF0, PH 4, Place Temp Erosion Control	4	23-Oct-14	29-Oct-14	133

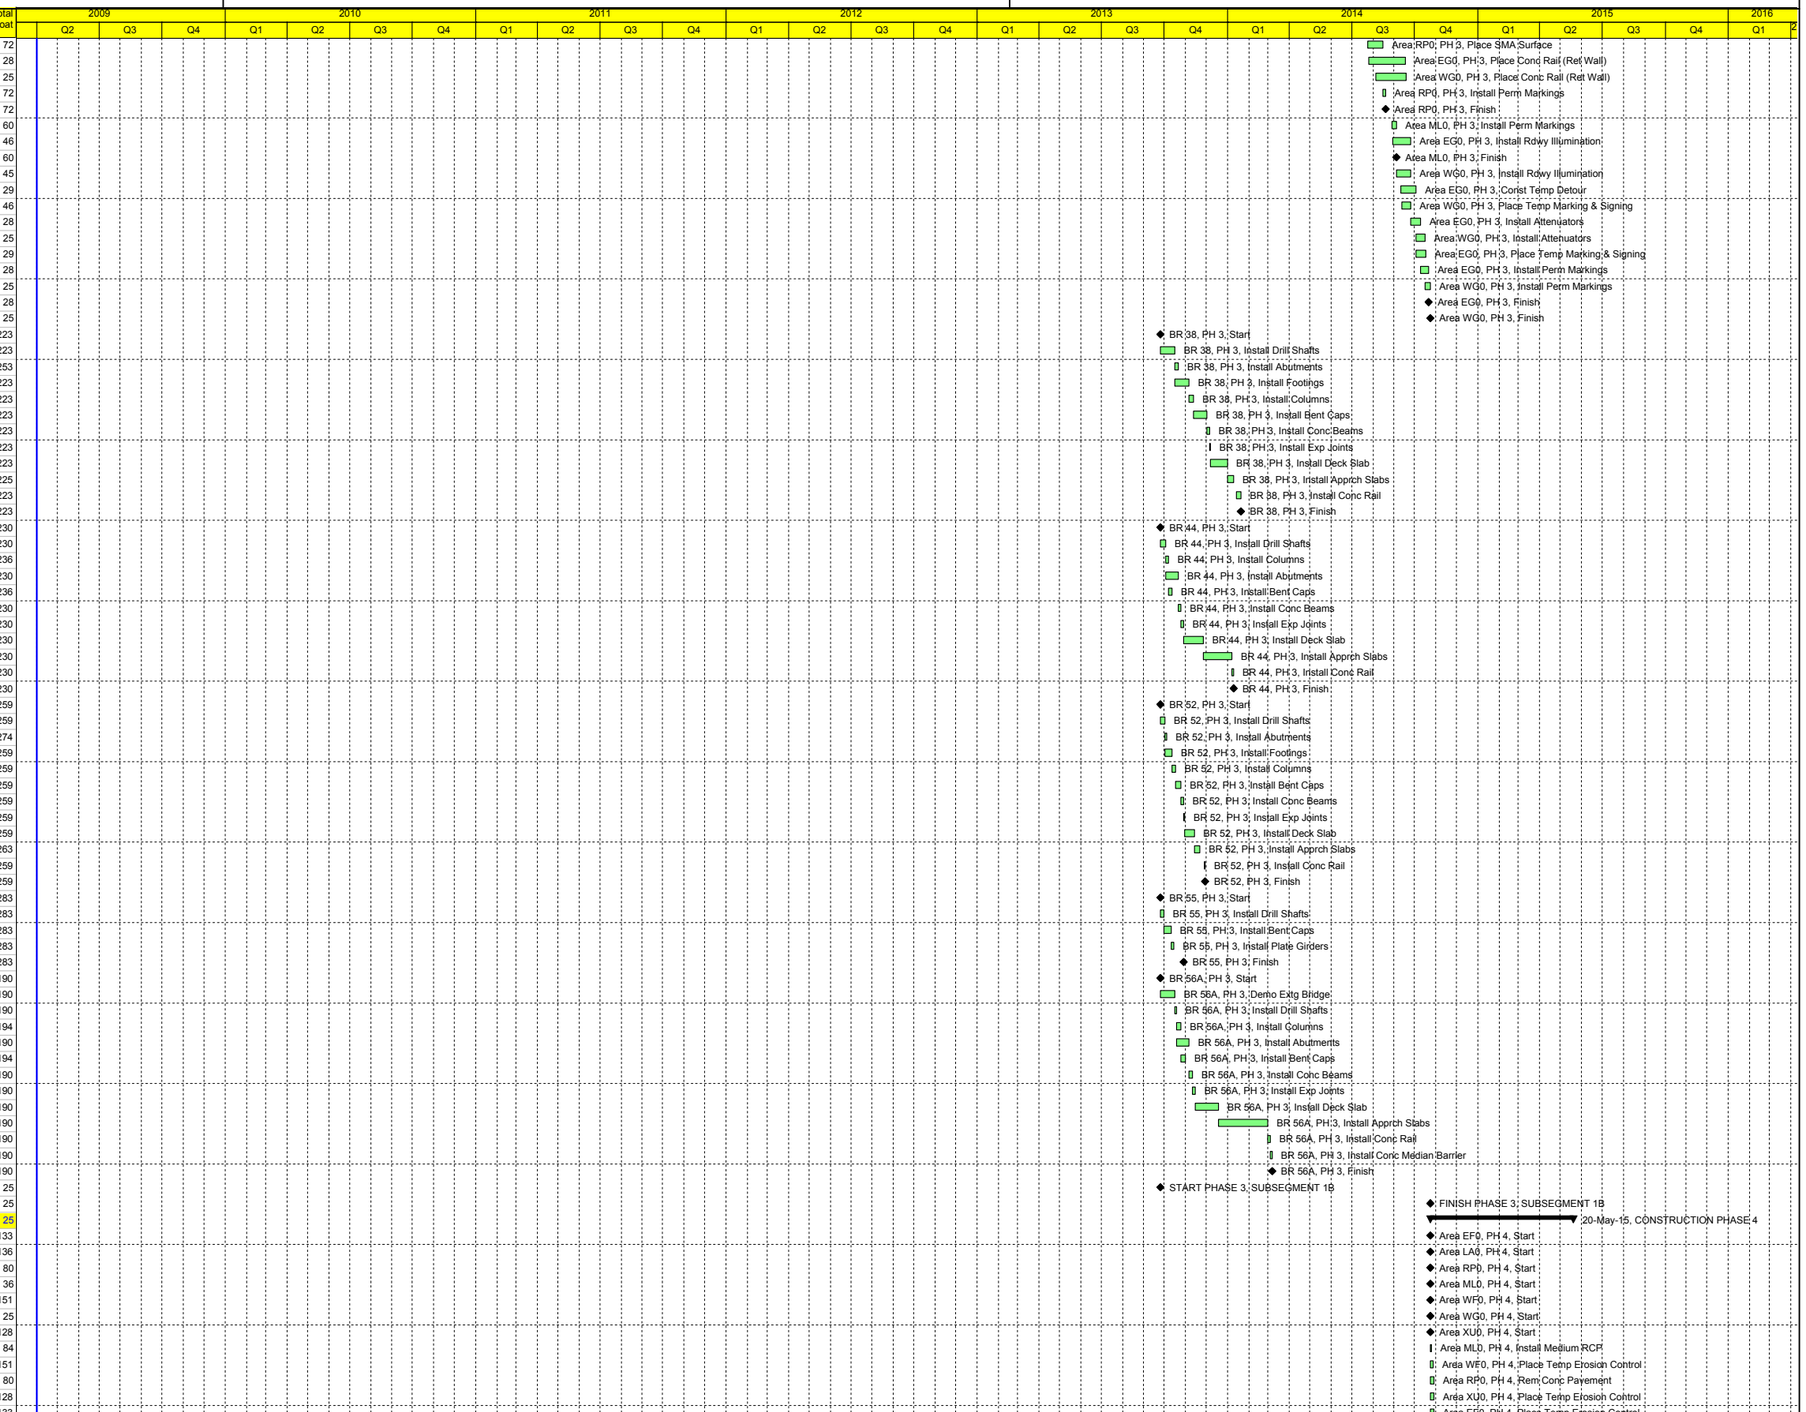

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.5.4.0	1B40ML00042320	Area ML0, PH 4, Install Cut Wall, Stage 1	5	23-Oct-14	30-Oct-14	36
1.5.2.0	1B40WG000506...	Area WG0, PH 4, Place Temp Erosion Control	14	23-Oct-14	12-Nov-14	25
1.5.2.0	1B40LA00016010	Area LA0, PH 4, Place Topsoil	27	23-Oct-14	01-Dec-14	136
1.5.7.0	1B40WF00090010	Area WF0, PH 4, Install Noise Walls	1	27-Oct-14	28-Oct-14	151
1.5.2.0	1B40WF00010410	Area WF0, PH 4, Rem Conc Pavement	1	28-Oct-14	29-Oct-14	151
1.5.2.0	1B40XU00010410	Area XU0, PH 4, Rem Conc Pavement	1	28-Oct-14	29-Oct-14	135
1.5.2.0	1B40XU00067910	Area XU0, PH 4, Rem Traffic Signals	8	28-Oct-14	07-Nov-14	128
1.5.2.0	1B40RP00013210	Area RP0, PH 4, Place Embankment	13	28-Oct-14	14-Nov-14	86
1.5.2.0	1B40RP00011010	Area RP0, PH 4, Excavate Cut Areas	19	28-Oct-14	24-Nov-14	80
1.5.7.0	1B40EF00090010	Area EF0, PH 4, Install Noise Walls	1	29-Oct-14	30-Oct-14	133
1.5.3.0	1B40WF00046210	Area WF0, PH 4, Install Small CBC	1	29-Oct-14	30-Oct-14	155
1.5.4.0	1B40WF00042320	Area WF0, PH 4, Install Cut Wall, Stage 1	4	29-Oct-14	04-Nov-14	151
1.5.2.0	1B40EF00010410	Area EF0, PH 4, Rem Conc Pavement	1	30-Oct-14	31-Oct-14	133
1.5.3.0	1B40WF00046420	Area WF0, PH 4, Install Medium RCP	2	30-Oct-14	03-Nov-14	155
1.5.2.0	1B40ML00013210	Area ML0, PH 4, Place Embankment	23	30-Oct-14	02-Dec-14	36
1.5.4.0	1B40ML00042310	Area ML0, PH 4, Install Fill Wall Complete	26	30-Oct-14	05-Dec-14	50
1.5.2.0	1B40ML00011010	Area ML0, PH 4, Excavate Cut Areas	35	30-Oct-14	18-Dec-14	36
1.5.3.0	1B40EF00046220	Area EF0, PH 4, Install Medium CBC	1	31-Oct-14	03-Nov-14	146
1.5.4.0	1B40EF00042320	Area EF0, PH 4, Install Cut Wall, Stage 1	8	31-Oct-14	12-Nov-14	133
1.5.3.0	1B40EF00046210	Area EF0, PH 4, Install Small CBC	1	03-Nov-...	04-Nov-14	146
1.5.4.0	1B40WF00042310	Area WF0, PH 4, Install Fill Wall Complete	1	04-Nov-...	05-Nov-14	154
1.5.2.0	1B40WF00013210	Area WF0, PH 4, Place Embankment	2	04-Nov-...	06-Nov-14	152
1.5.3.0	1B40EF00046420	Area EF0, PH 4, Install Medium RCP	3	04-Nov-...	07-Nov-14	146
1.5.2.0	1B40WF00011010	Area WF0, PH 4, Excavate Cut Areas	3	04-Nov-...	07-Nov-14	151
1.5.2.0	1B40ML00026010	Area ML0, PH 4, Lime Treat Subgrade (2 cre...	40	06-Nov-...	01-Jan-15	36
1.5.2.0	1B40WF00026010	Area WF0, PH 4, Lime Treat Subgrade	2	07-Nov-...	11-Nov-14	152
1.5.8.0	1B40WF00061899	Area WF0, PH 4, Install ITS Duct Bank	2	07-Nov-...	11-Nov-14	155
1.5.3.0	1B40WF00046410	Area WF0, PH 4, Install Small RCP	2	07-Nov-...	11-Nov-14	151
1.5.8.0	1B40XU00061899	Area XU0, PH 4, Install ITS Duct Bank	2	07-Nov-...	11-Nov-14	153
1.5.4.0	1B40WF00042325	Area WF0, PH 4, Install Cut Wall, Stage 2	5	07-Nov-...	14-Nov-14	151
1.5.8.0	1B40XU00062899	Area XU0, PH 4, Install Elec Service for ITS/...	7	07-Nov-...	18-Nov-14	148
1.5.2.0	1B40XU00026010	Area XU0, PH 4, Lime Treat Subgrade	11	07-Nov-...	24-Nov-14	128
1.5.3.0	1B40WF00046510	Area WF0, PH 4, Install MHs and Inlets	1	11-Nov-...	12-Nov-14	151
1.5.4.0	1B40WF00042315	Area WF0, PH 4, Install Moment Slabs	1	11-Nov-...	12-Nov-14	153
1.5.4.0	1B40EF00042310	Area EF0, PH 4, Install Fill Wall Complete	1	12-Nov-...	13-Nov-14	142
1.5.2.0	1B40WF00024711	Area WF0, PH 4, Place Flexible Base	1	12-Nov-...	13-Nov-14	151
1.5.2.0	1B40WG000600...	Area WG0, PH 4, Rem Light Poles	1	12-Nov-...	13-Nov-14	30
1.5.2.0	1B40WG000542...	Area WG0, PH 4, Rem MBGF	3	12-Nov-...	17-Nov-14	28
1.5.2.0	1B40EF00013210	Area EF0, PH 4, Place Embankment	4	12-Nov-...	18-Nov-14	139
1.5.2.0	1B40EF00011010	Area EF0, PH 4, Excavate Cut Areas	6	12-Nov-...	20-Nov-14	133
1.5.2.0	1B40WG000630...	Area WG0, PH 4, Rem Overhead Sign Supp...	6	12-Nov-...	20-Nov-14	25
1.5.2.0	1B40WF00052910	Area WF0, PH 4, Place Curb & Gutter	1	13-Nov-...	14-Nov-14	151
1.5.2.0	1B40WF00034011	Area WF0, PH 4, Place HMA Base	1	14-Nov-...	17-Nov-14	151
1.5.2.0	1B40WF00053110	Area WF0, PH 4, Place Sidewalks & Driveways	1	14-Nov-...	17-Nov-14	154
1.5.7.0	1B40WF00061020	Area WF0, PH 4, Install Rdwy Illumination	1	17-Nov-...	18-Nov-14	151
1.5.9.0	1B40WF00066200	Area WF0, PH 4, Place Temp Marking & Sig...	1	17-Nov-...	18-Nov-14	156
1.5.2.0	1B40WF00045010	Area WF0, PH 4, Place Conc Rail (Ret Wall)	2	17-Nov-...	19-Nov-14	154
1.5.2.0	1B40WF00043210	Area WF0, PH 4, Place Conc RipRap	2	18-Nov-...	20-Nov-14	151
1.5.2.0	1B40WF00016010	Area WF0, PH 4, Place Topsoil	1	20-Nov-...	21-Nov-14	151
1.5.3.0	1B40EF00046410	Area EF0, PH 4, Install Small RCP	2	20-Nov-...	24-Nov-14	137
1.5.8.0	1B40EF00061899	Area EF0, PH 4, Install ITS Duct Bank	3	20-Nov-...	25-Nov-14	143
1.5.2.0	1B40EF00026010	Area EF0, PH 4, Lime Treat Subgrade	4	20-Nov-...	26-Nov-14	137
1.5.2.0	1B40WG000104...	Area WG0, PH 4, Rem Concrete Barrier	5	20-Nov-...	27-Nov-14	25
1.5.4.0	1B40EF00042325	Area EF0, PH 4, Install Cut Wall, Stage 2	11	20-Nov-...	05-Dec-14	133
1.5.2.0	1B40WF00034610	Area WF0, PH 4, Place SMA Surface	1	21-Nov-...	24-Nov-14	151
1.5.7.0	1B40WF00064410	Area WF0, PH 4, Install Small Signs	1	21-Nov-...	24-Nov-14	151
1.5.3.0	1B40RP00046410	Area RP0, PH 4, Install Small RCP	1	24-Nov-...	25-Nov-14	100
1.5.6.0	1B40WF00016410	Area WF0, PH 4, Place Seeding and Sodding	1	24-Nov-...	25-Nov-14	151
1.5.7.0	1B40WF00066610	Area WF0, PH 4, Install Perm Markings	1	24-Nov-...	25-Nov-14	151
1.5.3.0	1B40EF00046510	Area EF0, PH 4, Install MHs and Inlets	2	24-Nov-...	26-Nov-14	137
1.5.2.0	1B40XU00024711	Area XU0, PH 4, Place Flexible Base	5	24-Nov-...	01-Dec-14	128
1.5.2.0	1B40RP00026010	Area RP0, PH 4, Lime Treat Subgrade	22	24-Nov-...	24-Dec-14	80
1.5	1B40WF00099999	Area WF0, PH 4, Finish	0		25-Nov-14	151
1.5.3.0	1B40RP00046510	Area RP0, PH 4, Install MHs and Inlets	1	25-Nov-...	26-Nov-14	100
1.5.4.0	1B40EF00042315	Area EF0, PH 4, Install Moment Slabs	1	26-Nov-...	27-Nov-14	139
1.5.2.0	1B40EF00024711	Area EF0, PH 4, Place Flexible Base	2	26-Nov-...	28-Nov-14	137
1.5.2.0	1B40WG000104...	Area WG0, PH 4, Rem Conc Pavement	4	27-Nov-...	03-Dec-14	25
1.5.2.0	1B40EF00052910	Area EF0, PH 4, Place Curb & Gutter	1	28-Nov-...	01-Dec-14	137
1.5.2.0	1B40XU00052910	Area XU0, PH 4, Place Curb & Gutter	1	01-Dec-...	02-Dec-14	128
1.5.2.0	1B40EF00053110	Area EF0, PH 4, Place Sidewalks & Driveways	2	01-Dec-...	03-Dec-14	141
1.5.6.0	1B40LA00016410	Area LA0, PH 4, Place Seeding and Sodding	11	01-Dec-...	16-Dec-14	136
1.5.2.0	1B40XU00053110	Area XU0, PH 4, Place Sidewalks & Driveways	1	02-Dec-...	03-Dec-14	138
1.5.2.0	1B40XU00034011	Area XU0, PH 4, Place HMA Base	6	02-Dec-...	10-Dec-14	128
1.5.3.0	1B40WG000462...	Area WG0, PH 4, Install Large CBC	11	03-Dec-...	18-Dec-14	25
1.5.2.0	1B40WG000132...	Area WG0, PH 4, Place Embankment	15	03-Dec-...	24-Dec-14	43
1.5.2.0	1B40WG000110...	Area WG0, PH 4, Excavate Cut Areas	22	03-Dec-...	02-Jan-15	36
1.5.2.0	1B40EF00034011	Area EF0, PH 4, Place HMA Base	2	05-Dec-...	09-Dec-14	133
1.5.9.0	1B40EF00066200	Area EF0, PH 4, Place Temp Marking & Sign...	1	09-Dec-...	10-Dec-14	140
1.5.7.0	1B40EF00061020	Area EF0, PH 4, Install Rdwy Illumination	2	09-Dec-...	11-Dec-14	133
1.5.2.0	1B40EF00045010	Area EF0, PH 4, Place Conc Rail (Ret Wall)	3	09-Dec-...	12-Dec-14	137
1.5.7.0	1B40XU00061020	Area XU0, PH 4, Install Rdwy Illumination	1	10-Dec-...	11-Dec-14	132
1.5.9.0	1B40XU00066200	Area XU0, PH 4, Place Temp Marking & Sign...	1	10-Dec-...	11-Dec-14	139
1.5.7.0	1B40XU00068010	Area XU0, PH 4, Install Traffic Signal Systems	11	10-Dec-...	25-Dec-14	128
1.5.2.0	1B40EF00043210	Area EF0, PH 4, Place Conc RipRap	2	11-Dec-...	15-Dec-14	133
1.5.2.0	1B40XU00034610	Area XU0, PH 4, Place SMA Surface	6	11-Dec-...	19-Dec-14	132
1.5.2.0	1B40EF00016010	Area EF0, PH 4, Place Topsoil	1	15-Dec-...	16-Dec-14	133

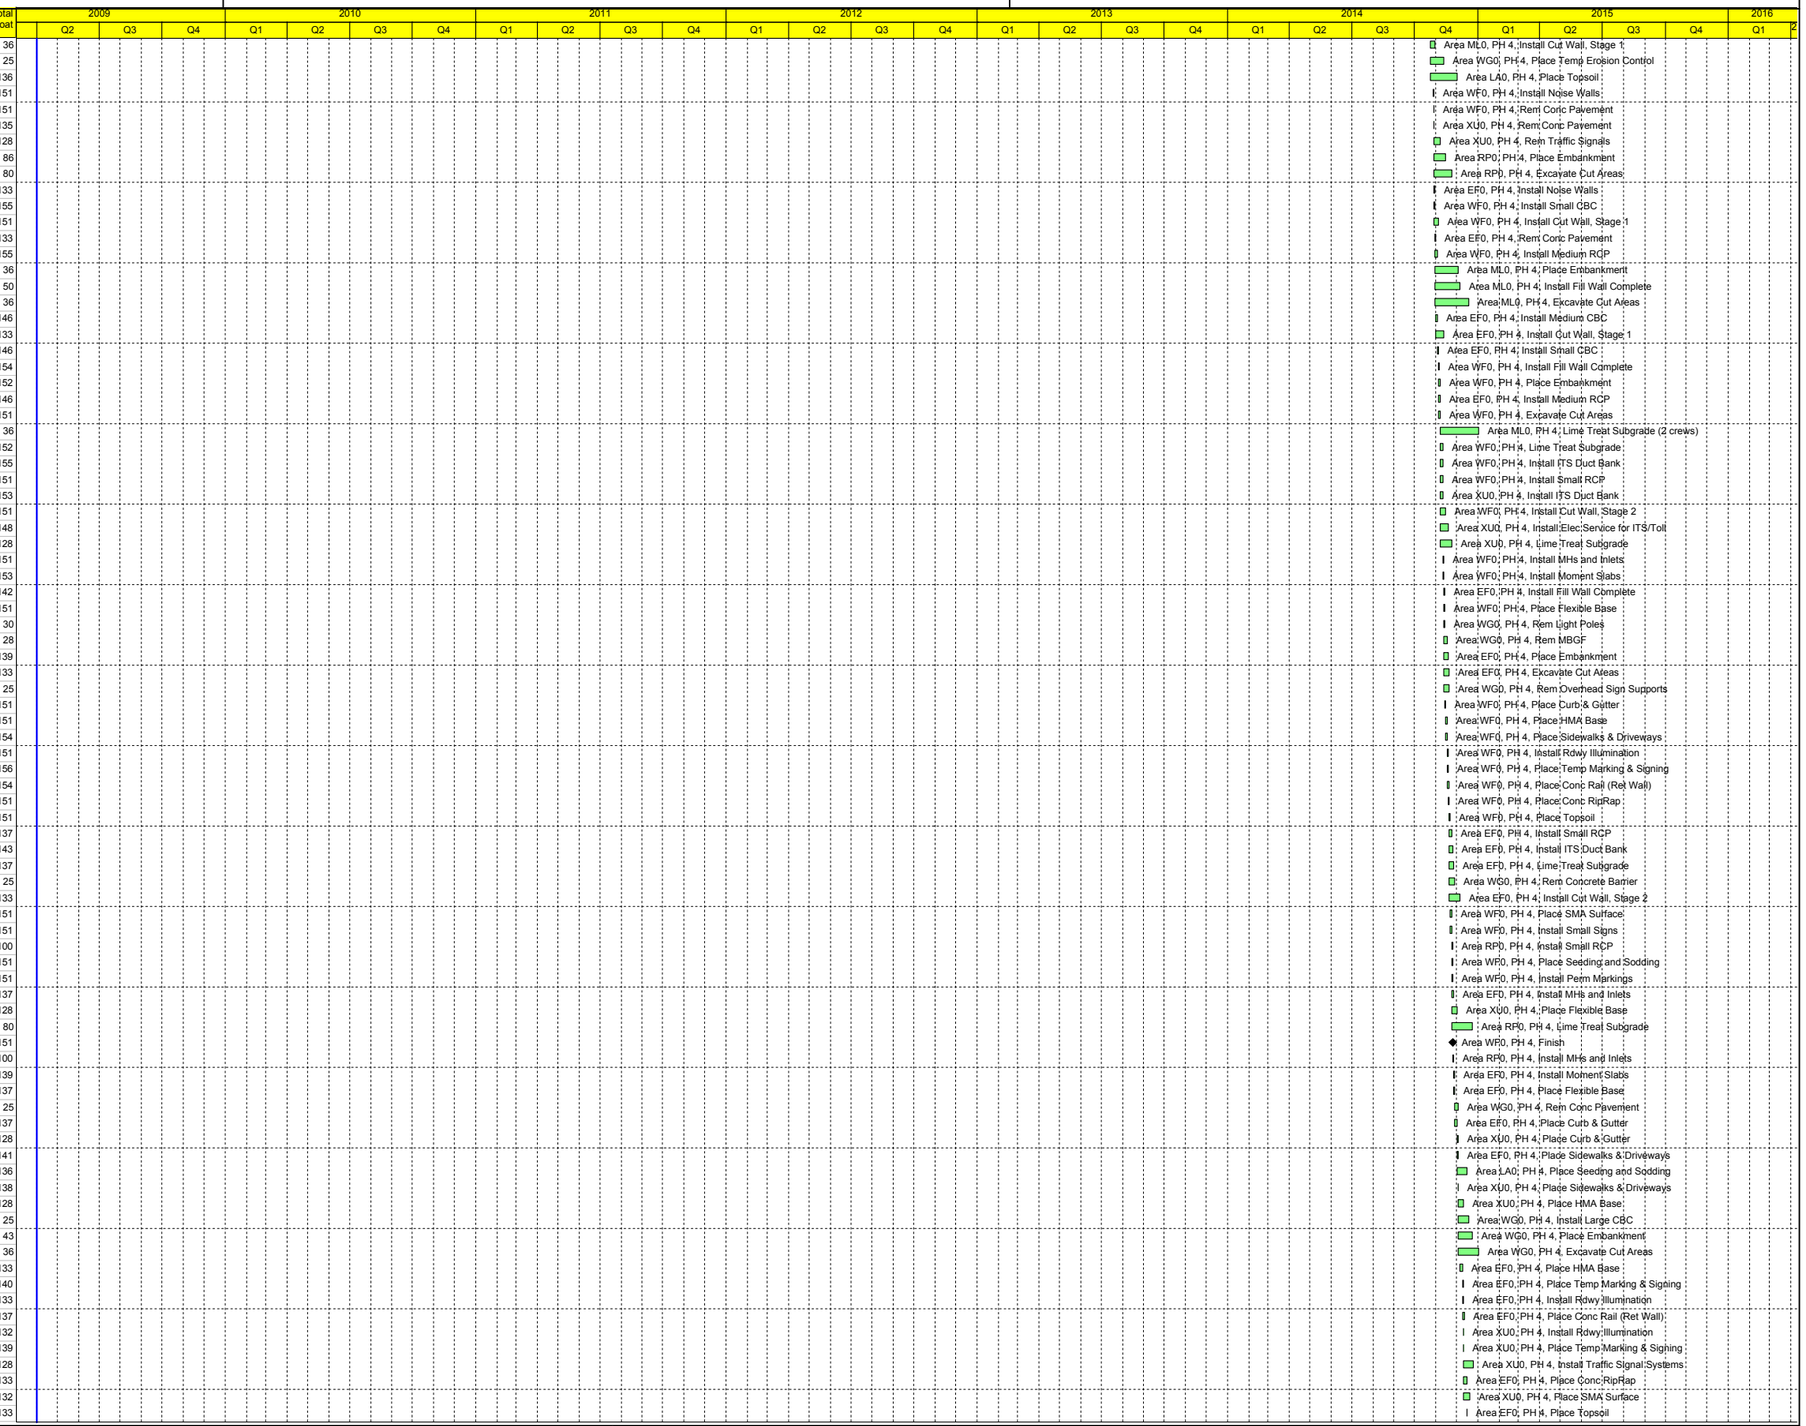

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.5	1B40LA00099999	Area LA0, PH 4, Finish	0		16-Dec-14	136
1.5.7.0	1B40EF00064410	Area EF0, PH 4, Install Small Signs	1	16-Dec-...	17-Dec-14	134
1.5.2.0	1B40EF00034610	Area EF0, PH 4, Place SMA Surface	2	16-Dec-...	18-Dec-14	133
1.5.6.0	1B40EF00016410	Area EF0, PH 4, Place Seeding and Sodding	1	17-Dec-...	18-Dec-14	134
1.5.7.0	1B40EF00066610	Area EF0, PH 4, Install Perm Markings	1	18-Dec-...	19-Dec-14	133
1.5.3.0	1B40ML00046410	Area ML0, PH 4, Install Small RCP	1	18-Dec-...	19-Dec-14	45
1.5.8.0	1B40ML00061899	Area ML0, PH 4, Install ITS Duct Bank	2	18-Dec-...	22-Dec-14	118
1.5.4.0	1B40ML00042325	Area ML0, PH 4, Install Cut Wall, Stage 2	7	18-Dec-...	29-Dec-14	55
1.5.3.0	1B40WG000462...	Area WG0, PH 4, Install Medium CBC	22	18-Dec-...	19-Jan-15	25
1.5	1B40EF00099999	Area EF0, PH 4, Finish	0		19-Dec-14	133
1.5.7.0	1B40XU00066610	Area XU0, PH 4, Install Perm Markings	1	19-Dec-...	22-Dec-14	132
1.5.8.0	1B40ML00041699	Area ML0, PH 4, Install ITS Structures & Equip	3	22-Dec-...	25-Dec-14	129
1.5.2.0	1B40RP00024711	Area RP0, PH 4, Place Flexible Base	5	24-Dec-...	31-Dec-14	80
1.5.7.0	1B40XU00064410	Area XU0, PH 4, Install Small Signs	1	25-Dec-...	26-Dec-14	128
1.5	1B40XU00099999	Area XU0, PH 4, Finish	0		26-Dec-14	128
1.5.2.0	1B40RP00052910	Area RP0, PH 4, Place Curb & Gutter	3	31-Dec-...	05-Jan-15	80
1.5.4.0	1B40ML00042315	Area ML0, PH 4, Install Moment Slabs	12	01-Jan-15	19-Jan-15	40
1.5.2.0	1B40ML00024710	Area ML0, PH 4, Place Flexible Base	16	01-Jan-15	23-Jan-15	36
1.5.2.0	1B40RP00034012	Area RP0, PH 4, Place HMA Base	6	05-Jan-15	13-Jan-15	80
1.5.2.0	1B40WG000260...	Area WG0, PH 4, Lime Treat Subgrade (2 cr...	28	09-Jan-15	18-Feb-15	36
1.5.2.0	1B40RP00045010	Area RP0, PH 4, Place Conc Rail (Ret Wall)	7	13-Jan-15	22-Jan-15	108
1.5.7.0	1B40RP00065010	Area RP0, PH 4, Install OH Sign Structures	18	13-Jan-15	06-Feb-15	80
1.5.3.0	1B40WG000462...	Area WG0, PH 4, Install Small CBC	4	19-Jan-15	23-Jan-15	25
1.5.3.0	1B40WG000464...	Area WG0, PH 4, Install Medium RCP	1	23-Jan-15	26-Jan-15	25
1.5.2.0	1B40ML00034010	Area ML0, PH 4, Place HMA Base	22	23-Jan-15	24-Feb-15	36
1.5.8.0	1B40WG000618...	Area WG0, PH 4, Install ITS Duct Bank	1	26-Jan-15	27-Jan-15	93
1.5.3.0	1B40WG000464...	Area WG0, PH 4, Install Small RCP	9	26-Jan-15	06-Feb-15	25
1.5.8.0	1B40WG000416...	Area WG0, PH 4, Install ITS Structures & Equip	9	27-Jan-15	09-Feb-15	93
1.5.2.0	1B40ML00051410	Area ML0, PH 4, Place Median Barrier (2 Cre...	60	27-Jan-15	21-Apr-15	36
1.5.7.0	1B40RP00061020	Area RP0, PH 4, Install Rdwy Illumination	4	06-Feb-15	12-Feb-15	80
1.5.3.0	1B40WG000465...	Area WG0, PH 4, Install MHs and Inlets	9	06-Feb-15	19-Feb-15	25
1.5.2.0	1B40RP00043210	Area RP0, PH 4, Place Conc RipRap	6	12-Feb-15	20-Feb-15	80
1.5.2.0	1B40WG000247...	Area WG0, PH 4, Place Flexible Base	15	19-Feb-15	12-Mar-15	25
1.5.7.0	1B40RP00064410	Area RP0, PH 4, Install Small Signs	1	20-Feb-15	23-Feb-15	87
1.5.2.0	1B40RP00034610	Area RP0, PH 4, Place SMA Surface	7	20-Feb-15	03-Mar-15	80
1.5.2.0	1B40ML00045010	Area ML0, PH 4, Place Conc Rail (Ret Wall)	13	24-Feb-15	13-Mar-15	71
1.5.10.0	1B40ML00041698	Area ML0, PH 4, Install Tolling Systems	14	24-Feb-15	16-Mar-15	72
1.5.7.0	1B40RP00066610	Area RP0, PH 4, Install Perm Markings	1	03-Mar-15	04-Mar-15	80
1.5	1B40RP00099999	Area RP0, PH 4, Finish	0		04-Mar-15	80
1.5.2.0	1B40WG000340...	Area WG0, PH 4, Place HMA Base	19	05-Mar-15	01-Apr-15	25
1.5.2.0	1B40ML00034610	Area ML0, PH 4, Place SMA Surface	26	18-Mar-15	23-Apr-15	42
1.5.7.0	1B40ML00065010	Area ML0, PH 4, Install OH Sign Structures	32	20-Mar-15	05-May-15	36
1.5.9.0	1B40WG000662...	Area WG0, PH 4, Place Temp Marking & Sig...	3	01-Apr-15	06-Apr-15	57
1.5.2.0	1B40WG000450...	Area WG0, PH 4, Place Conc Rail (Ret Wall)	8	01-Apr-15	13-Apr-15	25
1.5.7.0	1B40WG000650...	Area WG0, PH 4, Install OH Sign Structures	21	01-Apr-15	30-Apr-15	35
1.5.2.0	1B40WG000540...	Area WG0, PH 4, Install MBGF	14	13-Apr-15	01-May-15	34
1.5.2.0	1B40WG000346...	Area WG0, PH 4, Place SMA Surface	20	20-Apr-15	18-May-15	25
1.5.7.0	1B40ML00061020	Area ML0, PH 4, Install Rdwy Illumination	6	21-Apr-15	29-Apr-15	40
1.5.7.0	1B40ML00066610	Area ML0, PH 4, Install Perm Markings	2	23-Apr-15	27-Apr-15	42
1.5.7.0	1B40WG000610...	Area WG0, PH 4, Install Rdwy Illumination	4	30-Apr-15	06-May-15	35
1.5.2.0	1B40WG000545...	Area WG0, PH 4, Install Attenuators	2	01-May...	05-May-15	34
1.5	1B40ML00099999	Area ML0, PH 4, Finish	0		05-May-15	36
1.5.7.0	1B40WG000666...	Area WG0, PH 4, Install Perm Markings	2	18-May...	20-May-15	25
1.5	1B40WG000999...	Area WG0, PH 4, Finish	0		20-May-15	25
1.5.4.0.1.56B	1B40B056B00001	BR 56B, PH 4, Start	0	23-Oct-14		119
1.5.4.0.1.56B	1B40B056B41600	BR 56B, PH 4, Install Drill Shafts	2	23-Oct-14	27-Oct-14	119
1.5.4.0.1.56B	1B40B056B42020	BR 56B, PH 4, Install Columns	2	27-Oct-14	29-Oct-14	121
1.5.4.0.1.56B	1B40B056B42040	BR 56B, PH 4, Install Abutments	7	27-Oct-14	05-Nov-14	119
1.5.4.0.1.56B	1B40B056B42030	BR 56B, PH 4, Install Bent Caps	3	29-Oct-14	03-Nov-14	121
1.5.4.0.1.56B	1B40B056B42510	BR 56B, PH 4, Install Conc Beams	2	05-Nov-...	07-Nov-14	119
1.5.4.0.1.56B	1B40B056B45410	BR 56B, PH 4, Install Exp Joints	2	07-Nov-...	11-Nov-14	119
1.5.4.0.1.56B	1B40B056B42210	BR 56B, PH 4, Install Deck Slab	15	11-Nov-...	02-Dec-14	119
1.5.4.0.1.56B	1B40B056B42050	BR 56B, PH 4, Install Apprch Slabs	23	02-Dec-...	02-Jan-15	119
1.5.4.0.1.56B	1B40B056B45020	BR 56B, PH 4, Install Conc Rail	2	02-Jan-15	06-Jan-15	119
1.5.4.0.1.56B	1B40B056B45500	BR 56B, PH 4, Install Conc Median Barrier	2	06-Jan-15	08-Jan-15	119
1.5.4.0.1.56B	1B40B056B99999	BR 56B, PH 4, Finish	0		08-Jan-15	119
1.5.4.0.1.56C	1B40B056C00001	BR 56C, PH 4, Start	0	23-Oct-14		100
1.5.4.0.1.56C	1B40B056C41600	BR 56C, PH 4, Install Drill Shafts	3	23-Oct-14	28-Oct-14	100
1.5.4.0.1.56C	1B40B056C42020	BR 56C, PH 4, Install Columns	3	28-Oct-14	31-Oct-14	102
1.5.4.0.1.56C	1B40B056C42040	BR 56C, PH 4, Install Abutments	9	28-Oct-14	10-Nov-14	100
1.5.4.0.1.56C	1B40B056C42030	BR 56C, PH 4, Install Bent Caps	4	31-Oct-14	06-Nov-14	102
1.5.4.0.1.56C	1B40B056C42510	BR 56C, PH 4, Install Conc Beams	3	10-Nov-...	13-Nov-14	100
1.5.4.0.1.56C	1B40B056C45410	BR 56C, PH 4, Install Exp Joints	2	13-Nov-...	17-Nov-14	100
1.5.4.0.1.56C	1B40B056C42210	BR 56C, PH 4, Install Deck Slab	19	17-Nov-...	12-Dec-14	100
1.5.4.0.1.56C	1B40B056C42050	BR 56C, PH 4, Install Apprch Slabs	34	12-Dec-...	29-Jan-15	100
1.5.4.0.1.56C	1B40B056C45020	BR 56C, PH 4, Install Conc Rail	2	29-Jan-15	02-Feb-15	100
1.5.4.0.1.56C	1B40B056C45500	BR 56C, PH 4, Install Conc Median Barrier	2	02-Feb-15	04-Feb-15	100
1.5.4.0.1.56C	1B40B056C99999	BR 56C, PH 4, Finish	0		04-Feb-15	100
1.5.4.0.1.57	1B40B057000001	BR 57, PH 4, Start	0	23-Oct-14		105
1.5.4.0.1.57	1B40B057049610	BR 57, PH 4, Demo Extg Bridge	11	23-Oct-14	07-Nov-14	105
1.5.4.0.1.57	1B40B057041600	BR 57, PH 4, Install Drill Shafts	2	07-Nov-...	11-Nov-14	105
1.5.4.0.1.57	1B40B057042040	BR 57, PH 4, Install Abutments	3	11-Nov-...	14-Nov-14	125
1.5.4.0.1.57	1B40B057042010	BR 57, PH 4, Install Footings	11	11-Nov-...	26-Nov-14	105
1.5.4.0.1.57	1B40B057042020	BR 57, PH 4, Install Columns	5	26-Nov-...	03-Dec-14	105
1.5.4.0.1.57	1B40B057042030	BR 57, PH 4, Install Bent Caps	7	03-Dec-...	12-Dec-14	105
1.5.4.0.1.57	1B40B057042510	BR 57, PH 4, Install Conc Beams	3	12-Dec-...	17-Dec-14	105

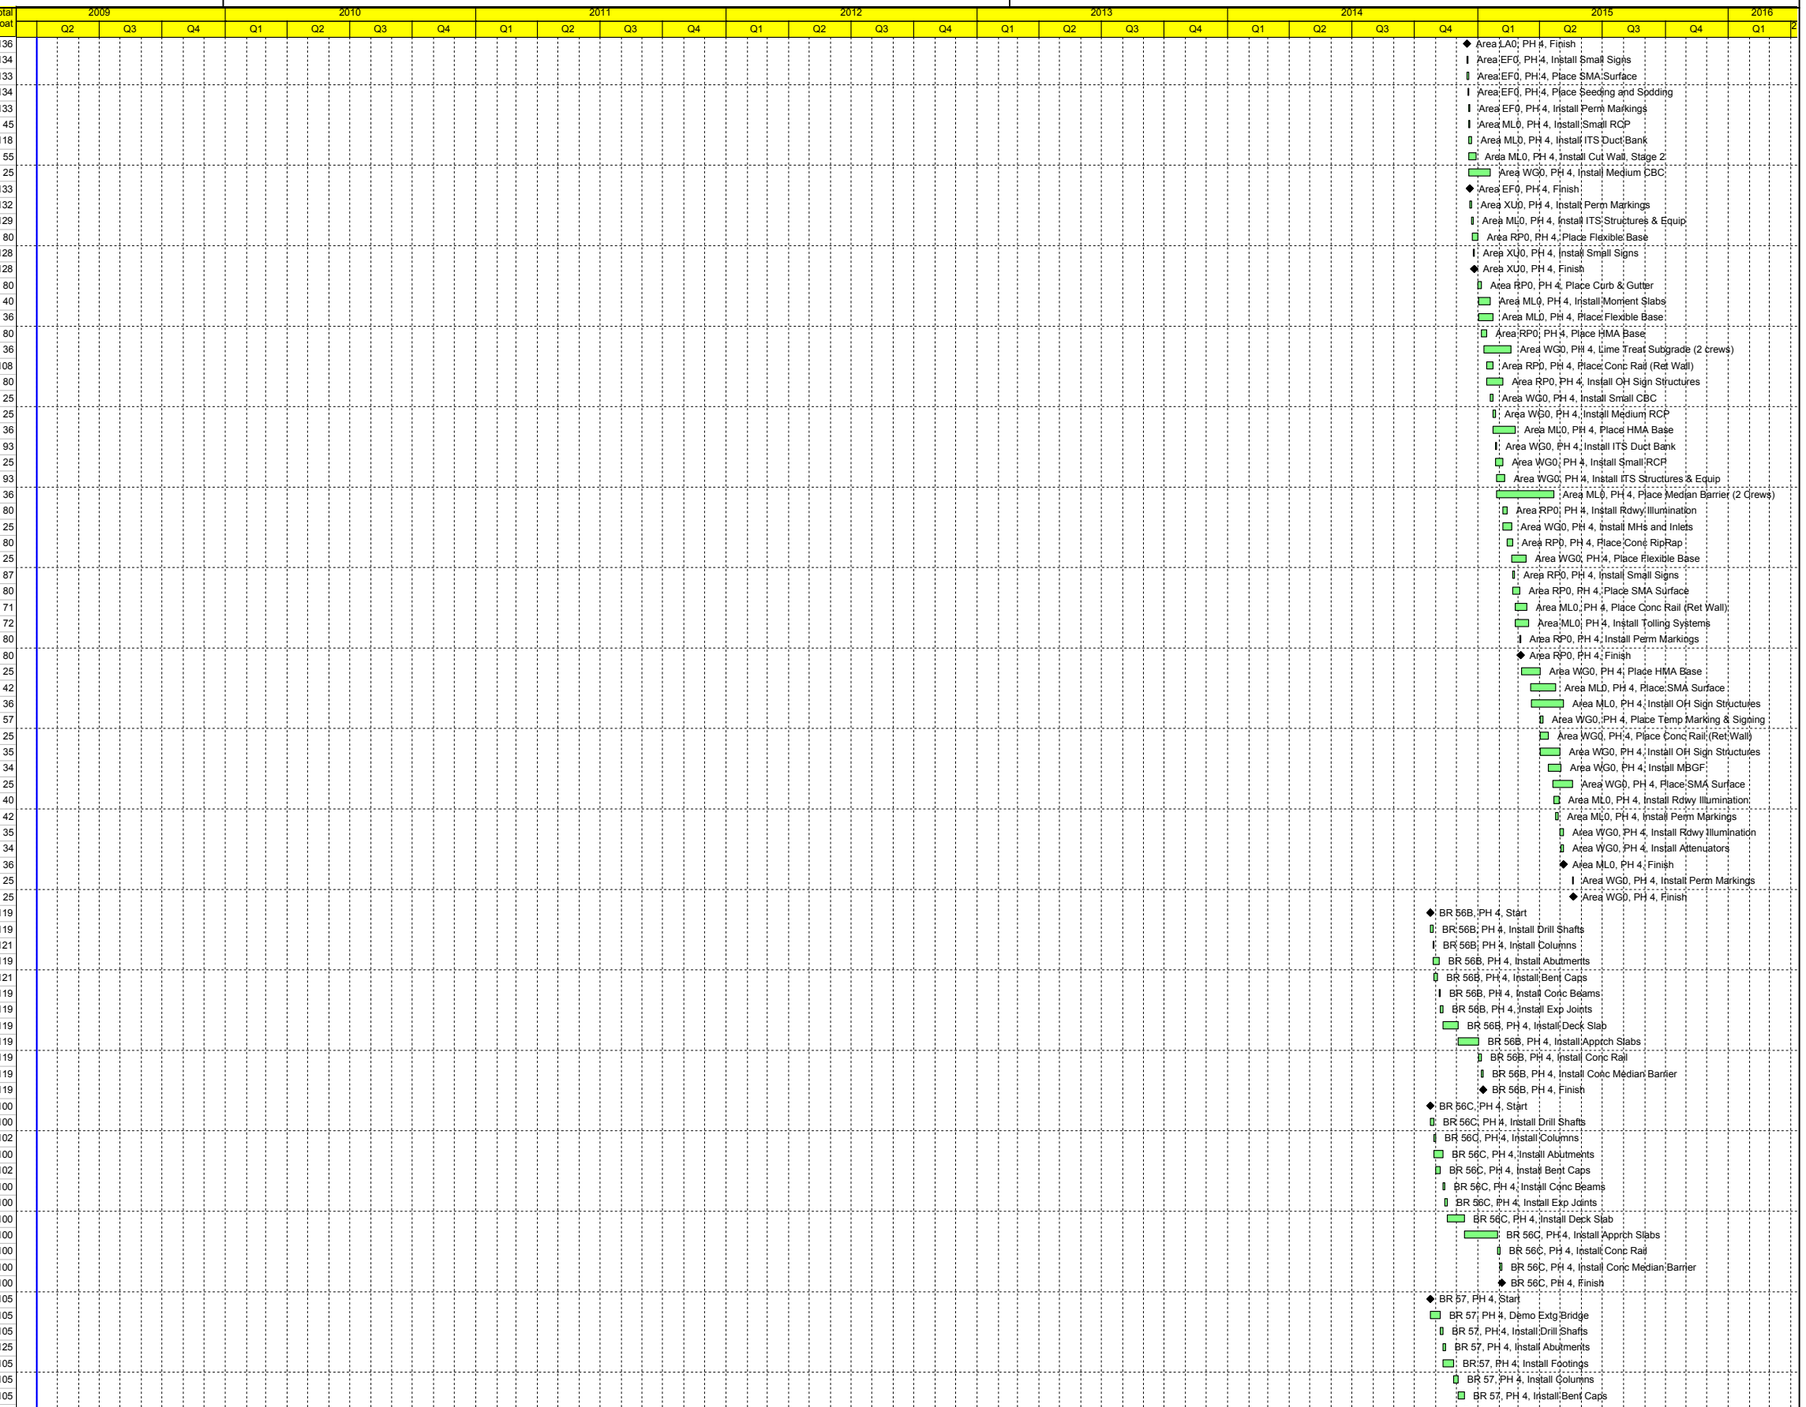

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.5.4.0.1.57	1B40B057045410	BR 57, PH 4, Install Exp Joints	1	17-Dec-...	18-Dec-14	105
1.5.4.0.1.57	1B40B057042210	BR 57, PH 4, Install Deck Slab	15	18-Dec-...	08-Jan-15	105
1.5.4.0.1.57	1B40B057042050	BR 57, PH 4, Install Apprch Slabs	8	08-Jan-15	20-Jan-15	107
1.5.4.0.1.57	1B40B057045020	BR 57, PH 4, Install Conc Rail	4	22-Jan-15	28-Jan-15	105
1.5.4.0.1.57	1B40B057099999	BR 57, PH 4, Finish	0		28-Jan-15	105
1.5	1B400000000001	START PHASE 4, SUBSEGMENT 1B	0	23-Oct-14		25
1.5	1B400000099999	FINISH PHASE 4, SUBSEGMENT 1B	0		20-May-15	25
Segment 2C - SH 121/183 - STA 955 to SH 121 North			1577	01-Apr-09	16-Apr-15	49
DESIGN			311	29-Jul-09	07-Oct-10	204
1.2.1.6	2C0D1201	DEVELOP SEGMENT 2C ENVIRONMENTA...	199	29-Jul-09	04-May-10	316
1.2.2.6	2C0D1202	DEVELOP SEGMENT 2C ROADWAY DESIGN	275	29-Jul-09	18-Aug-10	215
1.2.4.6	2C0D1241	DEVELOP SEGMENT 2C STRUCTURES DE...	275	02-Sep-...	22-Sep-10	215
1.2.3.6	2C0D1203	DEVELOP SEGMENT 2C DRAINAGE DESIGN	275	07-Sep-...	27-Sep-10	212
1.2.4.6	2C0D1242	DEVELOP SEGMENT 2C STRUCTURES DE...	275	17-Sep-...	07-Oct-10	204
1.2.9.6	2C0D1209	DEVELOP SEGMENT 2C TRAFFIC MGMT &...	199	29-Oct-09	04-Aug-10	250
1.2.7.6	2C0D1271	DEVELOP SEGMENT 2CTRAFFIC DESIGN	150	28-Dec-...	23-Jul-10	258
1.2.7.6	2C0D1272	DEVELOP SEGMENT 2C TRAFFIC DESIGN	150	28-Dec-...	23-Jul-10	258
1.2.7.6	2C0D1273	DEVELOP SEGMENT 2C TRAFFIC DESIGN	150	28-Dec-...	23-Jul-10	258
1.2.8.6	2C0D1208	DEVELOP SEGMENT 2C ITS DESIGN	150	28-Dec-...	23-Jul-10	258
1.2.10.6	2C0D1210	DEVELOP SEGMENT 2C TOLLING DESIGN	100	15-Feb-10	02-Jul-10	273
1.2.6.6	2C0D1206	DEVELOP SEGMENT 2C LANDSCAPE & A...	100	15-Feb-10	02-Jul-10	273
ROW ACQUISITION			518	01-Apr-09	25-Mar-11	1108
1.3.6	2CR0P5920R99	Parcel 592, Cleared for Construction	0		01-Apr-09	541
1.3.6	2CR0P2110R10	Parcel 211, Perform Surveying, Mapping & Ti...	60	30-Sep-...	23-Dec-09	68
1.3.6	2CR0P2330R10	Parcel 233, Perform Surveying, Mapping & Ti...	60	30-Sep-...	23-Dec-09	68
1.3.6	2CR0P3070R10	Parcel 307, Perform Surveying, Mapping & Ti...	60	30-Sep-...	23-Dec-09	68
1.3.6	2CR0P3160R10	Parcel 316, Perform Surveying, Mapping & Ti...	60	30-Sep-...	23-Dec-09	68
1.3.6	2CR0P3210R10	Parcel 321, Perform Surveying, Mapping & Ti...	60	30-Sep-...	23-Dec-09	68
1.3.6	2CR0P2080R10	Parcel 208, Perform Surveying, Mapping & Ti...	60	13-Oct-09	05-Jan-10	81
1.3.6	2CR0P2090R10	Parcel 209, Perform Surveying, Mapping & Ti...	60	13-Oct-09	05-Jan-10	93
1.3.6	2CR0P2180R10	Parcel 218, Perform Surveying, Mapping & Ti...	60	13-Oct-09	05-Jan-10	81
1.3.6	2CR0P2200R10	Parcel 220, Perform Surveying, Mapping & Ti...	60	13-Oct-09	05-Jan-10	81
1.3.6	2CR0P2340R10	Parcel 234, Perform Surveying, Mapping & Ti...	60	13-Oct-09	05-Jan-10	81
1.3.6	2CR0P2450R10	Parcel 245, Perform Surveying, Mapping & Ti...	60	13-Oct-09	05-Jan-10	81
1.3.6	2CR0P2490R10	Parcel 249, Perform Surveying, Mapping & Ti...	60	13-Oct-09	05-Jan-10	81
1.3.6	2CR0P2550R10	Parcel 255, Perform Surveying, Mapping & Ti...	60	13-Oct-09	05-Jan-10	81
1.3.6	2CR0P2650R10	Parcel 265, Perform Surveying, Mapping & Ti...	60	13-Oct-09	05-Jan-10	81
1.3.6	2CR0P2710R10	Parcel 271, Perform Surveying, Mapping & Ti...	60	13-Oct-09	05-Jan-10	81
1.3.6	2CR0P2750R10	Parcel 275, Perform Surveying, Mapping & Ti...	60	13-Oct-09	05-Jan-10	81
1.3.6	2CR0P2880R10	Parcel 288, Perform Surveying, Mapping & Ti...	60	13-Oct-09	05-Jan-10	81
1.3.6	2CR0P2900R10	Parcel 290, Perform Surveying, Mapping & Ti...	60	13-Oct-09	05-Jan-10	81
1.3.6	2CR0P2040R10	Parcel 204, Perform Surveying, Mapping & Ti...	60	14-Oct-09	06-Jan-10	93
1.3.6	2CR0P2130R10	Parcel 213, Perform Surveying, Mapping & Ti...	60	14-Oct-09	06-Jan-10	93
1.3.6	2CR0P2140R10	Parcel 214, Perform Surveying, Mapping & Ti...	60	14-Oct-09	06-Jan-10	93
1.3.6	2CR0P2150R10	Parcel 215, Perform Surveying, Mapping & Ti...	60	14-Oct-09	06-Jan-10	93
1.3.6	2CR0P2890R10	Parcel 289, Perform Surveying, Mapping & Ti...	60	14-Oct-09	06-Jan-10	118
1.3.6	2CR0P2930R10	Parcel 293, Perform Surveying, Mapping & Ti...	60	14-Oct-09	06-Jan-10	80
1.3.6	2CR0P3140R10	Parcel 314, Perform Surveying, Mapping & Ti...	60	14-Oct-09	06-Jan-10	96
1.3.6	2CR0P3150R10	Parcel 315, Perform Surveying, Mapping & Ti...	60	14-Oct-09	06-Jan-10	96
1.3.6	2CR0P3170R10	Parcel 317, Perform Surveying, Mapping & Ti...	60	14-Oct-09	06-Jan-10	96
1.3.6	2CR0P3230R10	Parcel 323, Perform Surveying, Mapping & Ti...	60	14-Oct-09	06-Jan-10	96
1.3.6	2CR0P3240R10	Parcel 324, Perform Surveying, Mapping & Ti...	60	14-Oct-09	06-Jan-10	96
1.3.6	2CR0P2160R10	Parcel 216, Perform Surveying, Mapping & Ti...	60	23-Nov-...	15-Feb-10	68
1.3.6	2CR0P3750R10	Parcel 375, Perform Surveying, Mapping & Ti...	60	25-Nov-...	17-Feb-10	68
1.3.6	2CR0P3760R10	Parcel 376, Perform Surveying, Mapping & Ti...	60	25-Nov-...	17-Feb-10	68
1.3.6	2CR0P3770R10	Parcel 377, Perform Surveying, Mapping & Ti...	60	25-Nov-...	17-Feb-10	68
1.3.6	2CR0P3780R10	Parcel 378, Perform Surveying, Mapping & Ti...	60	25-Nov-...	17-Feb-10	68
1.3.6	2CR0P3790R10	Parcel 379, Perform Surveying, Mapping & Ti...	60	25-Nov-...	17-Feb-10	68
1.3.6	2CR0P3800R10	Parcel 380, Perform Surveying, Mapping & Ti...	60	25-Nov-...	17-Feb-10	68
1.3.6	2CR0P3830R10	Parcel 383, Perform Surveying, Mapping & Ti...	60	25-Nov-...	17-Feb-10	68
1.3.6	2CR0P4310R10	Parcel 431, Perform Surveying, Mapping & Ti...	60	25-Nov-...	17-Feb-10	68
1.3.6	2CR0P4390R10	Parcel 439, Perform Surveying, Mapping & Ti...	60	25-Nov-...	17-Feb-10	68
1.3.6	2CR0P4400R10	Parcel 440, Perform Surveying, Mapping & Ti...	60	25-Nov-...	17-Feb-10	68
1.3.6	2CR0P4410R10	Parcel 441, Perform Surveying, Mapping & Ti...	60	25-Nov-...	17-Feb-10	68
1.3.6	2CR0P2010R10	Parcel 201, Perform Surveying, Mapping & Ti...	60	02-Dec-...	24-Feb-10	68
1.3.6	2CR0P2170R10	Parcel 217, Perform Surveying, Mapping & Ti...	60	02-Dec-...	24-Feb-10	68
1.3.6	2CR0P2260R10	Parcel 226, Perform Surveying, Mapping & Ti...	60	02-Dec-...	24-Feb-10	68
1.3.6	2CR0P2270R10	Parcel 227, Perform Surveying, Mapping & Ti...	60	02-Dec-...	24-Feb-10	68
1.3.6	2CR0P2280R10	Parcel 228, Perform Surveying, Mapping & Ti...	60	02-Dec-...	24-Feb-10	68
1.3.6	2CR0P2290R10	Parcel 229, Perform Surveying, Mapping & Ti...	60	02-Dec-...	24-Feb-10	68
1.3.6	2CR0P2300R10	Parcel 230, Perform Surveying, Mapping & Ti...	60	02-Dec-...	24-Feb-10	68
1.3.6	2CR0P2320R10	Parcel 232, Perform Surveying, Mapping & Ti...	60	02-Dec-...	24-Feb-10	68
1.3.6	2CR0P3050R10	Parcel 305, Perform Surveying, Mapping & Ti...	60	02-Dec-...	24-Feb-10	68
1.3.6	2CR0P3190R10	Parcel 319, Perform Surveying, Mapping & Ti...	60	02-Dec-...	24-Feb-10	68
1.3.6	2CR0P3260R10	Parcel 326, Perform Surveying, Mapping & Ti...	60	02-Dec-...	24-Feb-10	68
1.3.6	2CR0P3280R10	Parcel 328, Perform Surveying, Mapping & Ti...	60	02-Dec-...	24-Feb-10	68
1.3.6	2CR0P3440R10	Parcel 344, Perform Surveying, Mapping & Ti...	60	02-Dec-...	24-Feb-10	68
1.3.6	2CR0P3450R10	Parcel 345, Perform Surveying, Mapping & Ti...	60	02-Dec-...	24-Feb-10	68
1.3.6	2CR0P3470R10	Parcel 347, Perform Surveying, Mapping & Ti...	60	02-Dec-...	24-Feb-10	68
1.3.6	2CR0P3480R10	Parcel 348, Perform Surveying, Mapping & Ti...	60	02-Dec-...	24-Feb-10	68
1.3.6	2CR0P3500R10	Parcel 350, Perform Surveying, Mapping & Ti...	60	02-Dec-...	24-Feb-10	68
1.3.6	2CR0P3650R10	Parcel 365, Perform Surveying, Mapping & Ti...	60	02-Dec-...	24-Feb-10	68
1.3.6	2CR0P3680R10	Parcel 368, Perform Surveying, Mapping & Ti...	60	02-Dec-...	24-Feb-10	68
1.3.6	2CR0P3710R10	Parcel 371, Perform Surveying, Mapping & Ti...	60	02-Dec-...	24-Feb-10	68
1.3.6	2CR0P3720R10	Parcel 372, Perform Surveying, Mapping & Ti...	60	02-Dec-...	24-Feb-10	68

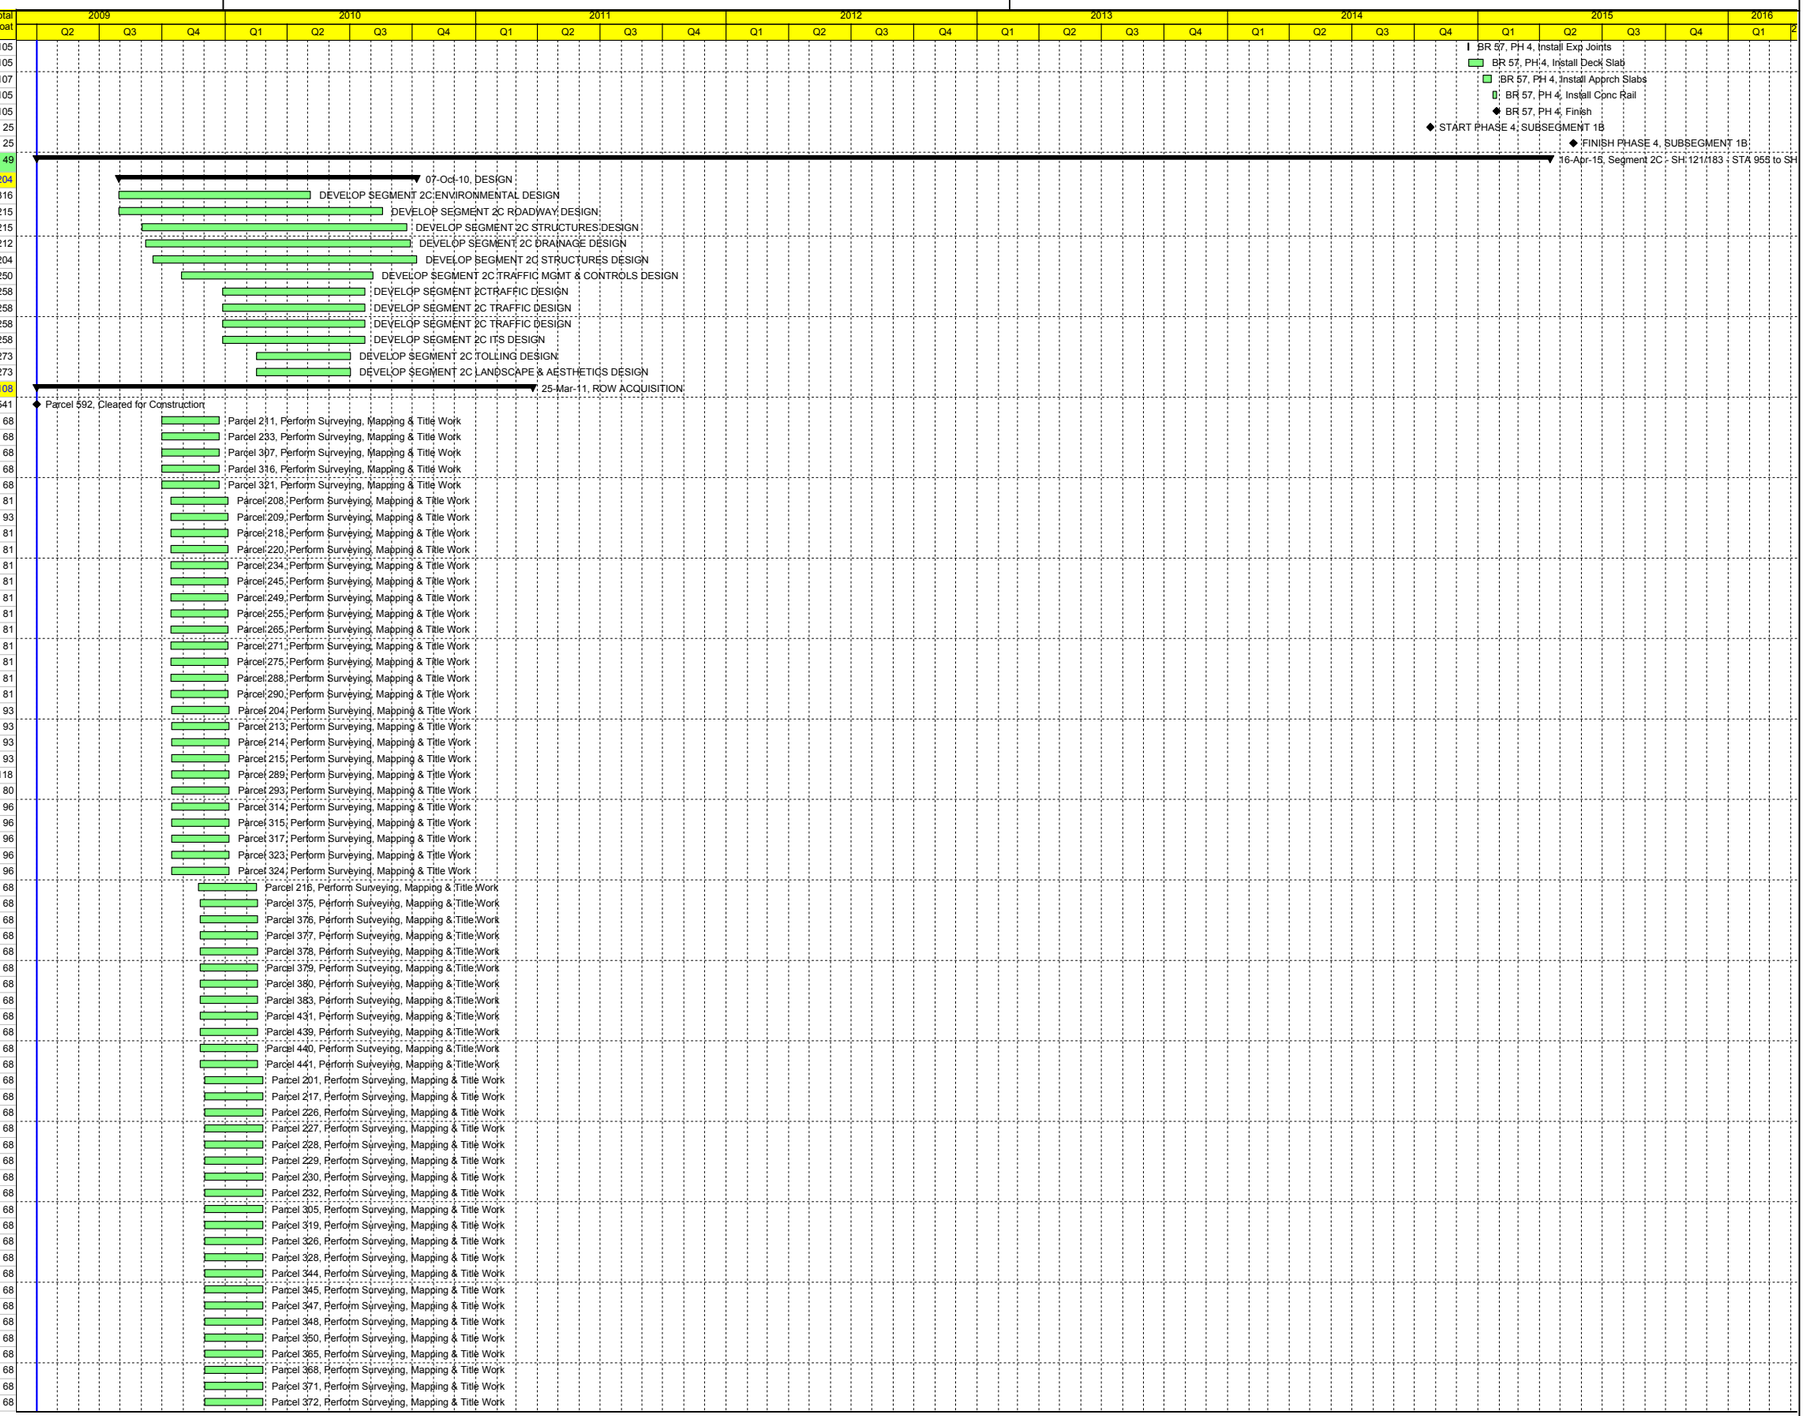

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.3.6	2CR0P3730R10	Parcel 373, Perform Surveying, Mapping & Ti...	60	02-Dec-...	24-Feb-10	68
1.3.6	2CR0P3740R10	Parcel 374, Perform Surveying, Mapping & Ti...	60	02-Dec-...	24-Feb-10	68
1.3.6	2CR0P3810R10	Parcel 381, Perform Surveying, Mapping & Ti...	60	09-Dec-...	03-Mar-10	96
1.3.6	2CR0P3820R10	Parcel 382, Perform Surveying, Mapping & Ti...	60	09-Dec-...	03-Mar-10	96
1.3.6	2CR0P3840R10	Parcel 384, Perform Surveying, Mapping & Ti...	60	09-Dec-...	03-Mar-10	96
1.3.6	2CR0P3870R10	Parcel 387, Perform Surveying, Mapping & Ti...	60	09-Dec-...	03-Mar-10	93
1.3.6	2CR0P4320R10	Parcel 432, Perform Surveying, Mapping & Ti...	60	09-Dec-...	03-Mar-10	93
1.3.6	2CR0P4330R10	Parcel 433, Perform Surveying, Mapping & Ti...	60	09-Dec-...	03-Mar-10	93
1.3.6	2CR0P4340R10	Parcel 434, Perform Surveying, Mapping & Ti...	60	09-Dec-...	03-Mar-10	93
1.3.6	2CR0P4350R10	Parcel 435, Perform Surveying, Mapping & Ti...	60	09-Dec-...	03-Mar-10	93
1.3.6	2CR0P4360R10	Parcel 436, Perform Surveying, Mapping & Ti...	60	09-Dec-...	03-Mar-10	93
1.3.6	2CR0P4370R10	Parcel 437, Perform Surveying, Mapping & Ti...	60	09-Dec-...	03-Mar-10	93
1.3.6	2CR0P2310R10	Parcel 231, Perform Surveying, Mapping & Ti...	60	15-Dec-...	09-Mar-10	81
1.3.6	2CR0P2400R10	Parcel 240, Perform Surveying, Mapping & Ti...	60	15-Dec-...	09-Mar-10	81
1.3.6	2CR0P2410R10	Parcel 241, Perform Surveying, Mapping & Ti...	60	15-Dec-...	09-Mar-10	81
1.3.6	2CR0P2910R10	Parcel 291, Perform Surveying, Mapping & Ti...	60	15-Dec-...	09-Mar-10	81
1.3.6	2CR0P2920R10	Parcel 292, Perform Surveying, Mapping & Ti...	60	15-Dec-...	09-Mar-10	81
1.3.6	2CR0P2990R10	Parcel 299, Perform Surveying, Mapping & Ti...	60	15-Dec-...	09-Mar-10	81
1.3.6	2CR0P3550R10	Parcel 355, Perform Surveying, Mapping & Ti...	60	15-Dec-...	09-Mar-10	81
1.3.6	2CR0P3670R10	Parcel 367, Perform Surveying, Mapping & Ti...	60	15-Dec-...	09-Mar-10	81
1.3.6	2CR0P2350R10	Parcel 235, Perform Surveying, Mapping & Ti...	60	15-Dec-...	09-Mar-10	68
1.3.6	2CR0P2020R10	Parcel 202, Perform Surveying, Mapping & Ti...	60	16-Dec-...	10-Mar-10	96
1.3.6	2CR0P2030R10	Parcel 203, Perform Surveying, Mapping & Ti...	60	16-Dec-...	10-Mar-10	96
1.3.6	2CR0P2070R10	Parcel 207, Perform Surveying, Mapping & Ti...	60	16-Dec-...	10-Mar-10	93
1.3.6	2CR0P2250R10	Parcel 225, Perform Surveying, Mapping & Ti...	60	16-Dec-...	10-Mar-10	80
1.3.6	2CR0P3010R10	Parcel 301, Perform Surveying, Mapping & Ti...	60	16-Dec-...	10-Mar-10	96
1.3.6	2CR0P3020R10	Parcel 302, Perform Surveying, Mapping & Ti...	60	16-Dec-...	10-Mar-10	96
1.3.6	2CR0P3040R10	Parcel 304, Perform Surveying, Mapping & Ti...	60	16-Dec-...	10-Mar-10	80
1.3.6	2CR0P3060R10	Parcel 306, Perform Surveying, Mapping & Ti...	60	16-Dec-...	10-Mar-10	93
1.3.6	2CR0P3080R10	Parcel 308, Perform Surveying, Mapping & Ti...	60	16-Dec-...	10-Mar-10	96
1.3.6	2CR0P3180R10	Parcel 318, Perform Surveying, Mapping & Ti...	60	16-Dec-...	10-Mar-10	96
1.3.6	2CR0P3290R10	Parcel 329, Perform Surveying, Mapping & Ti...	60	16-Dec-...	10-Mar-10	96
1.3.6	2CR0P3350R10	Parcel 335, Perform Surveying, Mapping & Ti...	60	16-Dec-...	10-Mar-10	96
1.3.6	2CR0P3490R10	Parcel 349, Perform Surveying, Mapping & Ti...	60	16-Dec-...	10-Mar-10	93
1.3.6	2CR0P3510R10	Parcel 351, Perform Surveying, Mapping & Ti...	60	16-Dec-...	10-Mar-10	80
1.3.6	2CR0P3600R10	Parcel 360, Perform Surveying, Mapping & Ti...	60	16-Dec-...	10-Mar-10	93
1.3.6	2CR0P3610R10	Parcel 361, Perform Surveying, Mapping & Ti...	60	16-Dec-...	10-Mar-10	93
1.3.6	2CR0P3620R10	Parcel 362, Perform Surveying, Mapping & Ti...	60	16-Dec-...	10-Mar-10	93
1.3.6	2CR0P3630R10	Parcel 363, Perform Surveying, Mapping & Ti...	60	16-Dec-...	10-Mar-10	93
1.3.6	2CR0P3640R10	Parcel 364, Perform Surveying, Mapping & Ti...	60	16-Dec-...	10-Mar-10	93
1.3.6	2CR0P2110R20	Parcel 211, Perform Appraisal and Internal R...	60	23-Dec-...	17-Mar-10	68
1.3.6	2CR0P2330R20	Parcel 233, Perform Appraisal and Internal R...	60	23-Dec-...	17-Mar-10	68
1.3.6	2CR0P3070R20	Parcel 307, Perform Appraisal and Internal R...	60	23-Dec-...	17-Mar-10	68
1.3.6	2CR0P3160R20	Parcel 316, Perform Appraisal and Internal R...	60	23-Dec-...	17-Mar-10	68
1.3.6	2CR0P3210R20	Parcel 321, Perform Appraisal and Internal R...	60	23-Dec-...	17-Mar-10	68
1.3.6	2CR0P3300R20	Parcel 330, Perform Appraisal and Internal R...	60	24-Dec-...	18-Mar-10	67
1.3.6	2CR0P3310R20	Parcel 331, Perform Appraisal and Internal R...	60	24-Dec-...	18-Mar-10	67
1.3.6	2CR0P3370R20	Parcel 337, Perform Appraisal and Internal R...	60	24-Dec-...	18-Mar-10	67
1.3.6	2CR0P3380R20	Parcel 338, Perform Appraisal and Internal R...	60	24-Dec-...	18-Mar-10	67
1.3.6	2CR0P3390R20	Parcel 339, Perform Appraisal and Internal R...	60	24-Dec-...	18-Mar-10	67
1.3.6	2CR0P3400R20	Parcel 340, Perform Appraisal and Internal R...	60	24-Dec-...	18-Mar-10	67
1.3.6	2CR0P3410R20	Parcel 341, Perform Appraisal and Internal R...	60	24-Dec-...	18-Mar-10	67
1.3.6	2CR0P3420R20	Parcel 342, Perform Appraisal and Internal R...	60	24-Dec-...	18-Mar-10	67
1.3.6	2CR0P3430R20	Parcel 343, Perform Appraisal and Internal R...	60	24-Dec-...	18-Mar-10	67
1.3.6	2CR0P3560R20	Parcel 356, Perform Appraisal and Internal R...	60	24-Dec-...	18-Mar-10	67
1.3.6	2CR0P3880R20	Parcel 388, Perform Appraisal and Internal R...	60	24-Dec-...	18-Mar-10	67
1.3.6	2CR0P4080R20	Parcel 408, Perform Appraisal and Internal R...	60	24-Dec-...	18-Mar-10	67
1.3.6	2CR0P4420R20	Parcel 442, Perform Appraisal and Internal R...	60	24-Dec-...	18-Mar-10	67
1.3.6	2CR0P3030R10	Parcel 303, Perform Surveying, Mapping & Ti...	60	25-Dec-...	19-Mar-10	68
1.3.6	2CR0P2000R00	Parcel 200, Initiate Aquisition	0	01-Jan-10		79
1.3.6	2CR0P2010R00	Parcel 201, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P2020R00	Parcel 202, Initiate Aquisition	0	01-Jan-10		96
1.3.6	2CR0P2030R00	Parcel 203, Initiate Aquisition	0	01-Jan-10		96
1.3.6	2CR0P2070R00	Parcel 207, Initiate Aquisition	0	01-Jan-10		93
1.3.6	2CR0P2170R00	Parcel 217, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P2250R00	Parcel 225, Initiate Aquisition	0	01-Jan-10		80
1.3.6	2CR0P2260R00	Parcel 226, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P2270R00	Parcel 227, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P2280R00	Parcel 228, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P2290R00	Parcel 229, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P2300R00	Parcel 230, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P2310R00	Parcel 231, Initiate Aquisition	0	01-Jan-10		81
1.3.6	2CR0P2320R00	Parcel 232, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P2380R00	Parcel 238, Initiate Aquisition	0	01-Jan-10		148
1.3.6	2CR0P2390R00	Parcel 239, Initiate Aquisition	0	01-Jan-10		148
1.3.6	2CR0P2400R00	Parcel 240, Initiate Aquisition	0	01-Jan-10		81
1.3.6	2CR0P2410R00	Parcel 241, Initiate Aquisition	0	01-Jan-10		81
1.3.6	2CR0P2420R00	Parcel 242, Initiate Aquisition	0	01-Jan-10		198
1.3.6	2CR0P2540R00	Parcel 254, Initiate Aquisition	0	01-Jan-10		148
1.3.6	2CR0P2590R00	Parcel 259, Initiate Aquisition	0	01-Jan-10		148
1.3.6	2CR0P2600R00	Parcel 260, Initiate Aquisition	0	01-Jan-10		198
1.3.6	2CR0P2910R00	Parcel 291, Initiate Aquisition	0	01-Jan-10		81
1.3.6	2CR0P2920R00	Parcel 292, Initiate Aquisition	0	01-Jan-10		81
1.3.6	2CR0P2990R00	Parcel 299, Initiate Aquisition	0	01-Jan-10		81
1.3.6	2CR0P3010R00	Parcel 301, Initiate Aquisition	0	01-Jan-10		96
1.3.6	2CR0P3020R00	Parcel 302, Initiate Aquisition	0	01-Jan-10		96

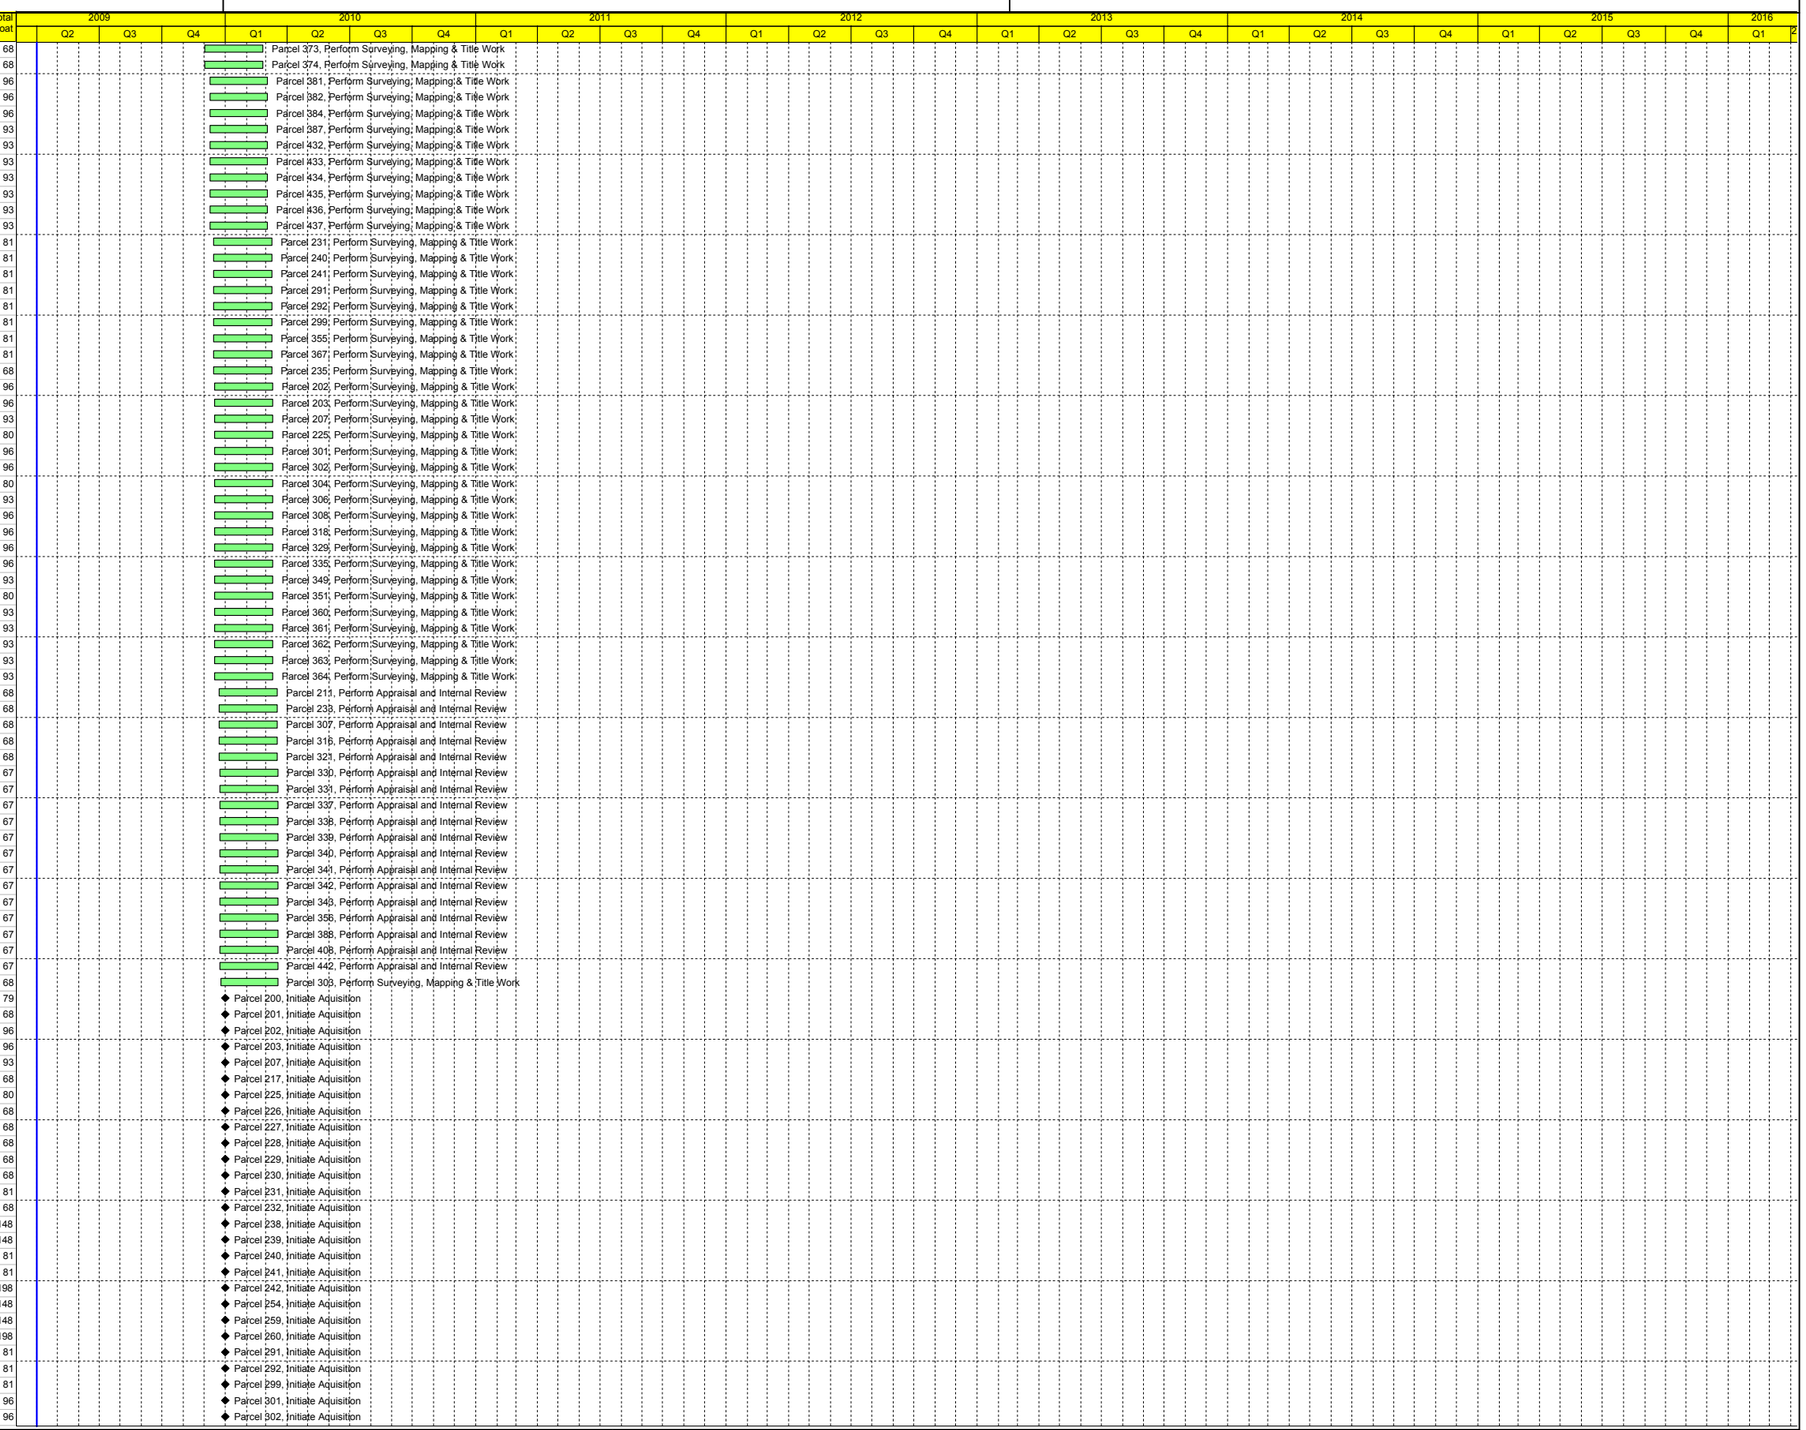

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.3.6	2CR0P3030R00	Parcel 303, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P3040R00	Parcel 304, Initiate Aquisition	0	01-Jan-10		80
1.3.6	2CR0P3050R00	Parcel 305, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P3060R00	Parcel 306, Initiate Aquisition	0	01-Jan-10		93
1.3.6	2CR0P3080R00	Parcel 308, Initiate Aquisition	0	01-Jan-10		96
1.3.6	2CR0P3180R00	Parcel 318, Initiate Aquisition	0	01-Jan-10		96
1.3.6	2CR0P3190R00	Parcel 319, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P3260R00	Parcel 326, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P3270R00	Parcel 327, Initiate Aquisition	0	01-Jan-10		198
1.3.6	2CR0P3280R00	Parcel 328, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P3290R00	Parcel 329, Initiate Aquisition	0	01-Jan-10		96
1.3.6	2CR0P3350R00	Parcel 335, Initiate Aquisition	0	01-Jan-10		96
1.3.6	2CR0P3440R00	Parcel 344, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P3450R00	Parcel 345, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P3470R00	Parcel 347, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P3480R00	Parcel 348, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P3490R00	Parcel 349, Initiate Aquisition	0	01-Jan-10		93
1.3.6	2CR0P3500R00	Parcel 350, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P3510R00	Parcel 351, Initiate Aquisition	0	01-Jan-10		80
1.3.6	2CR0P3520R00	Parcel 352, Initiate Aquisition	0	01-Jan-10		76
1.3.6	2CR0P3550R00	Parcel 355, Initiate Aquisition	0	01-Jan-10		81
1.3.6	2CR0P3590R00	Parcel 359, Initiate Aquisition	0	01-Jan-10		148
1.3.6	2CR0P3600R00	Parcel 360, Initiate Aquisition	0	01-Jan-10		93
1.3.6	2CR0P3610R00	Parcel 361, Initiate Aquisition	0	01-Jan-10		93
1.3.6	2CR0P3620R00	Parcel 362, Initiate Aquisition	0	01-Jan-10		93
1.3.6	2CR0P3630R00	Parcel 363, Initiate Aquisition	0	01-Jan-10		93
1.3.6	2CR0P3640R00	Parcel 364, Initiate Aquisition	0	01-Jan-10		93
1.3.6	2CR0P3650R00	Parcel 365, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P3660R00	Parcel 366, Initiate Aquisition	0	01-Jan-10		148
1.3.6	2CR0P3670R00	Parcel 367, Initiate Aquisition	0	01-Jan-10		81
1.3.6	2CR0P3680R00	Parcel 368, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P3690R00	Parcel 369, Initiate Aquisition	0	01-Jan-10		198
1.3.6	2CR0P3710R00	Parcel 371, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P3720R00	Parcel 372, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P3730R00	Parcel 373, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P3740R00	Parcel 374, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P3750R00	Parcel 375, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P3760R00	Parcel 376, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P3770R00	Parcel 377, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P3780R00	Parcel 378, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P3790R00	Parcel 379, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P3800R00	Parcel 380, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P3810R00	Parcel 381, Initiate Aquisition	0	01-Jan-10		96
1.3.6	2CR0P3820R00	Parcel 382, Initiate Aquisition	0	01-Jan-10		96
1.3.6	2CR0P3830R00	Parcel 383, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P3840R00	Parcel 384, Initiate Aquisition	0	01-Jan-10		96
1.3.6	2CR0P3870R00	Parcel 387, Initiate Aquisition	0	01-Jan-10		93
1.3.6	2CR0P3890R00	Parcel 389, Initiate Aquisition	0	01-Jan-10		76
1.3.6	2CR0P3900R00	Parcel 390, Initiate Aquisition	0	01-Jan-10		76
1.3.6	2CR0P3910R00	Parcel 391, Initiate Aquisition	0	01-Jan-10		76
1.3.6	2CR0P3920R00	Parcel 392, Initiate Aquisition	0	01-Jan-10		76
1.3.6	2CR0P3930R00	Parcel 393, Initiate Aquisition	0	01-Jan-10		76
1.3.6	2CR0P3940R00	Parcel 394, Initiate Aquisition	0	01-Jan-10		76
1.3.6	2CR0P3990R00	Parcel 399, Initiate Aquisition	0	01-Jan-10		95
1.3.6	2CR0P4000R00	Parcel 400, Initiate Aquisition	0	01-Jan-10		95
1.3.6	2CR0P4010R00	Parcel 401, Initiate Aquisition	0	01-Jan-10		76
1.3.6	2CR0P4020R00	Parcel 402, Initiate Aquisition	0	01-Jan-10		67
1.3.6	2CR0P4030R00	Parcel 403, Initiate Aquisition	0	01-Jan-10		67
1.3.6	2CR0P4040R00	Parcel 404, Initiate Aquisition	0	01-Jan-10		92
1.3.6	2CR0P4050R00	Parcel 405, Initiate Aquisition	0	01-Jan-10		92
1.3.6	2CR0P4060R00	Parcel 406, Initiate Aquisition	0	01-Jan-10		67
1.3.6	2CR0P4070R00	Parcel 407, Initiate Aquisition	0	01-Jan-10		67
1.3.6	2CR0P4090R00	Parcel 409, Initiate Aquisition	0	01-Jan-10		198
1.3.6	2CR0P4100R00	Parcel 410, Initiate Aquisition	0	01-Jan-10		198
1.3.6	2CR0P4110R00	Parcel 411, Initiate Aquisition	0	01-Jan-10		92
1.3.6	2CR0P4120R00	Parcel 412, Initiate Aquisition	0	01-Jan-10		92
1.3.6	2CR0P4130R00	Parcel 413, Initiate Aquisition	0	01-Jan-10		67
1.3.6	2CR0P4140R00	Parcel 414, Initiate Aquisition	0	01-Jan-10		67
1.3.6	2CR0P4150R00	Parcel 415, Initiate Aquisition	0	01-Jan-10		67
1.3.6	2CR0P4160R00	Parcel 416, Initiate Aquisition	0	01-Jan-10		198
1.3.6	2CR0P4170R00	Parcel 417, Initiate Aquisition	0	01-Jan-10		198
1.3.6	2CR0P4190R00	Parcel 419, Initiate Aquisition	0	01-Jan-10		198
1.3.6	2CR0P4220R00	Parcel 422, Initiate Aquisition	0	01-Jan-10		198
1.3.6	2CR0P4230R00	Parcel 423, Initiate Aquisition	0	01-Jan-10		198
1.3.6	2CR0P4240R00	Parcel 424, Initiate Aquisition	0	01-Jan-10		198
1.3.6	2CR0P4260R00	Parcel 426, Initiate Aquisition	0	01-Jan-10		198
1.3.6	2CR0P4270R00	Parcel 427, Initiate Aquisition	0	01-Jan-10		198
1.3.6	2CR0P4290R00	Parcel 429, Initiate Aquisition	0	01-Jan-10		198
1.3.6	2CR0P4300R00	Parcel 430, Initiate Aquisition	0	01-Jan-10		198
1.3.6	2CR0P4310R00	Parcel 431, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P4320R00	Parcel 432, Initiate Aquisition	0	01-Jan-10		93
1.3.6	2CR0P4330R00	Parcel 433, Initiate Aquisition	0	01-Jan-10		93
1.3.6	2CR0P4340R00	Parcel 434, Initiate Aquisition	0	01-Jan-10		93
1.3.6	2CR0P4350R00	Parcel 435, Initiate Aquisition	0	01-Jan-10		93
1.3.6	2CR0P4360R00	Parcel 436, Initiate Aquisition	0	01-Jan-10		93
1.3.6	2CR0P4370R00	Parcel 437, Initiate Aquisition	0	01-Jan-10		93

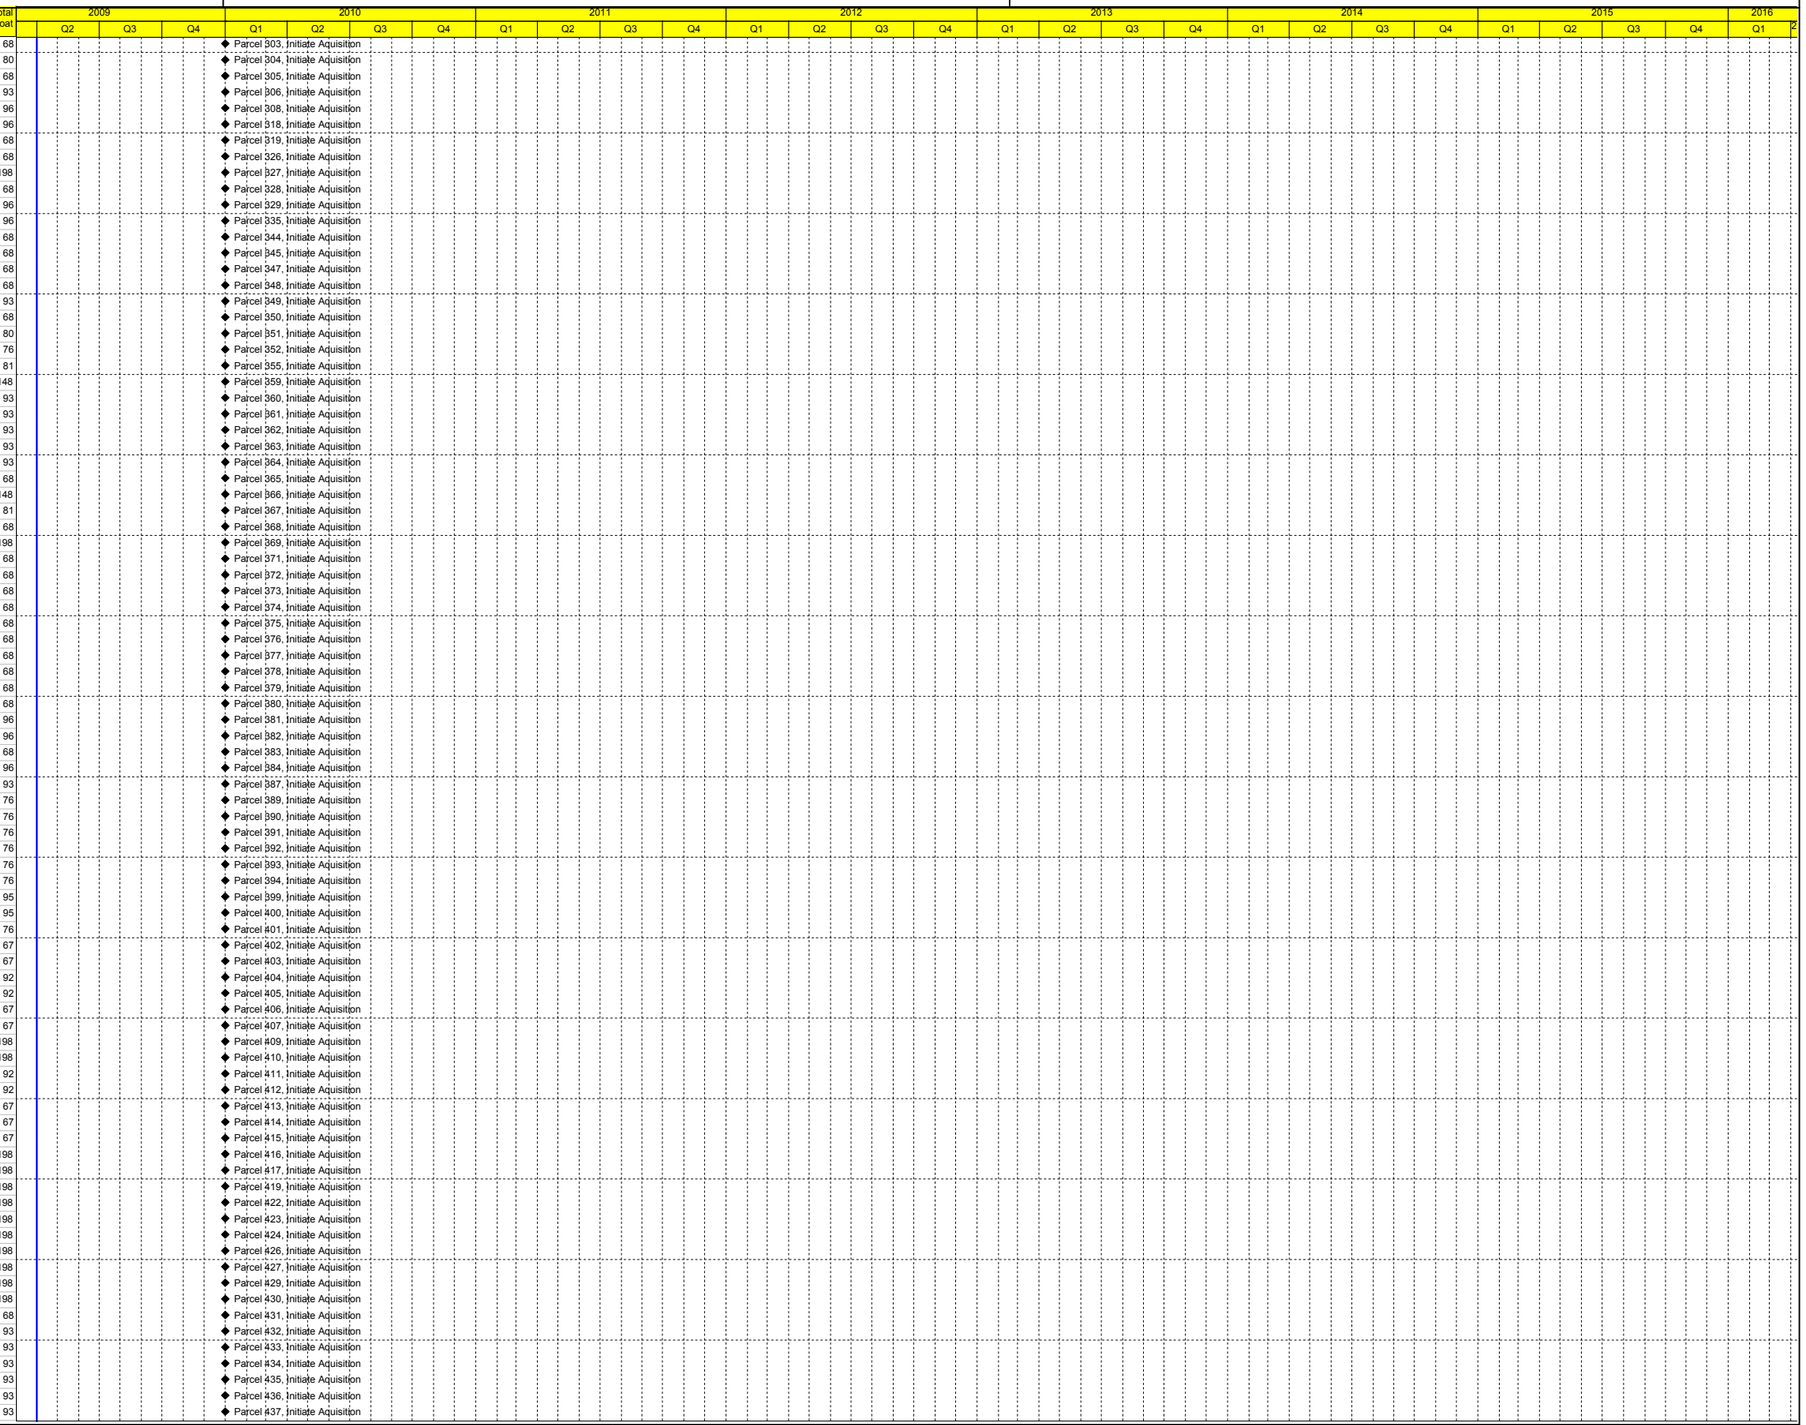

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.3.6	2CR0P4390R00	Parcel 439, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P4400R00	Parcel 440, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P4410R00	Parcel 441, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P4430R00	Parcel 443, Initiate Aquisition	0	01-Jan-10		148
1.3.6	2CR0P4440R00	Parcel 444, Initiate Aquisition	0	01-Jan-10		148
1.3.6	2CR0P4450R00	Parcel 445, Initiate Aquisition	0	01-Jan-10		148
1.3.6	2CR0P4460R00	Parcel 446, Initiate Aquisition	0	01-Jan-10		148
1.3.6	2CR0P4470R00	Parcel 447, Initiate Aquisition	0	01-Jan-10		148
1.3.6	2CR0P4490R00	Parcel 449, Initiate Aquisition	0	01-Jan-10		148
1.3.6	2CR0P4500R00	Parcel 450, Initiate Aquisition	0	01-Jan-10		148
1.3.6	2CR0P4510R00	Parcel 451, Initiate Aquisition	0	01-Jan-10		148
1.3.6	2CR0P2040R00	Parcel 204, Initiate Aquisition	0	01-Jan-10		93
1.3.6	2CR0P2050R00	Parcel 205, Initiate Aquisition	0	01-Jan-10		108
1.3.6	2CR0P2080R00	Parcel 208, Initiate Aquisition	0	01-Jan-10		81
1.3.6	2CR0P2090R00	Parcel 209, Initiate Aquisition	0	01-Jan-10		93
1.3.6	2CR0P2100R00	Parcel 210, Initiate Aquisition	0	01-Jan-10		108
1.3.6	2CR0P2110R00	Parcel 211, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P2130R00	Parcel 213, Initiate Aquisition	0	01-Jan-10		93
1.3.6	2CR0P2140R00	Parcel 214, Initiate Aquisition	0	01-Jan-10		93
1.3.6	2CR0P2150R00	Parcel 215, Initiate Aquisition	0	01-Jan-10		93
1.3.6	2CR0P2160R00	Parcel 216, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P2180R00	Parcel 218, Initiate Aquisition	0	01-Jan-10		81
1.3.6	2CR0P2190R00	Parcel 219, Initiate Aquisition	0	01-Jan-10		108
1.3.6	2CR0P2200R00	Parcel 220, Initiate Aquisition	0	01-Jan-10		81
1.3.6	2CR0P2230R00	Parcel 223, Initiate Aquisition	0	01-Jan-10		108
1.3.6	2CR0P2240R00	Parcel 224, Initiate Aquisition	0	01-Jan-10		108
1.3.6	2CR0P2330R00	Parcel 233, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P2340R00	Parcel 234, Initiate Aquisition	0	01-Jan-10		81
1.3.6	2CR0P2350R00	Parcel 235, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P2360R00	Parcel 236, Initiate Aquisition	0	01-Jan-10		108
1.3.6	2CR0P2370R00	Parcel 237, Initiate Aquisition	0	01-Jan-10		108
1.3.6	2CR0P2450R00	Parcel 245, Initiate Aquisition	0	01-Jan-10		81
1.3.6	2CR0P2490R00	Parcel 249, Initiate Aquisition	0	01-Jan-10		81
1.3.6	2CR0P2500R00	Parcel 250, Initiate Aquisition	0	01-Jan-10		158
1.3.6	2CR0P2520R00	Parcel 252, Initiate Aquisition	0	01-Jan-10		158
1.3.6	2CR0P2530R00	Parcel 253, Initiate Aquisition	0	01-Jan-10		158
1.3.6	2CR0P2550R00	Parcel 255, Initiate Aquisition	0	01-Jan-10		81
1.3.6	2CR0P2560R00	Parcel 256, Initiate Aquisition	0	01-Jan-10		108
1.3.6	2CR0P2570R00	Parcel 257, Initiate Aquisition	0	01-Jan-10		158
1.3.6	2CR0P2640R00	Parcel 264, Initiate Aquisition	0	01-Jan-10		158
1.3.6	2CR0P2650R00	Parcel 265, Initiate Aquisition	0	01-Jan-10		81
1.3.6	2CR0P2660R00	Parcel 266, Initiate Aquisition	0	01-Jan-10		158
1.3.6	2CR0P2670R00	Parcel 267, Initiate Aquisition	0	01-Jan-10		158
1.3.6	2CR0P2710R00	Parcel 271, Initiate Aquisition	0	01-Jan-10		81
1.3.6	2CR0P2750R00	Parcel 275, Initiate Aquisition	0	01-Jan-10		81
1.3.6	2CR0P2770R00	Parcel 277, Initiate Aquisition	0	01-Jan-10		158
1.3.6	2CR0P2780R00	Parcel 278, Initiate Aquisition	0	01-Jan-10		158
1.3.6	2CR0P2850R00	Parcel 285, Initiate Aquisition	0	01-Jan-10		158
1.3.6	2CR0P2880R00	Parcel 288, Initiate Aquisition	0	01-Jan-10		81
1.3.6	2CR0P2890R00	Parcel 289, Initiate Aquisition	0	01-Jan-10		118
1.3.6	2CR0P2900R00	Parcel 290, Initiate Aquisition	0	01-Jan-10		81
1.3.6	2CR0P5920R00	Parcel 592, Initiate Aquisition	0	01-Jan-10		1108
1.3.6	2CR0P2930R00	Parcel 293, Initiate Aquisition	0	01-Jan-10		80
1.3.6	2CR0P2940R00	Parcel 294, Initiate Aquisition	0	01-Jan-10		108
1.3.6	2CR0P2950R00	Parcel 295, Initiate Aquisition	0	01-Jan-10		108
1.3.6	2CR0P2960R00	Parcel 296, Initiate Aquisition	0	01-Jan-10		108
1.3.6	2CR0P2970R00	Parcel 297, Initiate Aquisition	0	01-Jan-10		108
1.3.6	2CR0P3070R00	Parcel 307, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P3140R00	Parcel 314, Initiate Aquisition	0	01-Jan-10		96
1.3.6	2CR0P3150R00	Parcel 315, Initiate Aquisition	0	01-Jan-10		96
1.3.6	2CR0P3160R00	Parcel 316, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P3170R00	Parcel 317, Initiate Aquisition	0	01-Jan-10		96
1.3.6	2CR0P3210R00	Parcel 321, Initiate Aquisition	0	01-Jan-10		68
1.3.6	2CR0P3220R00	Parcel 322, Initiate Aquisition	0	01-Jan-10		108
1.3.6	2CR0P3230R00	Parcel 323, Initiate Aquisition	0	01-Jan-10		96
1.3.6	2CR0P3240R00	Parcel 324, Initiate Aquisition	0	01-Jan-10		96
1.3.6	2CR0P3250R00	Parcel 325, Initiate Aquisition	0	01-Jan-10		92
1.3.6	2CR0P3300R00	Parcel 330, Initiate Aquisition	0	01-Jan-10		67
1.3.6	2CR0P3310R00	Parcel 331, Initiate Aquisition	0	01-Jan-10		67
1.3.6	2CR0P3320R00	Parcel 332, Initiate Aquisition	0	01-Jan-10		95
1.3.6	2CR0P3330R00	Parcel 333, Initiate Aquisition	0	01-Jan-10		95
1.3.6	2CR0P3340R00	Parcel 334, Initiate Aquisition	0	01-Jan-10		95
1.3.6	2CR0P3360R00	Parcel 336, Initiate Aquisition	0	01-Jan-10		95
1.3.6	2CR0P3370R00	Parcel 337, Initiate Aquisition	0	01-Jan-10		67
1.3.6	2CR0P3380R00	Parcel 338, Initiate Aquisition	0	01-Jan-10		67
1.3.6	2CR0P3390R00	Parcel 339, Initiate Aquisition	0	01-Jan-10		67
1.3.6	2CR0P3400R00	Parcel 340, Initiate Aquisition	0	01-Jan-10		67
1.3.6	2CR0P3410R00	Parcel 341, Initiate Aquisition	0	01-Jan-10		67
1.3.6	2CR0P3420R00	Parcel 342, Initiate Aquisition	0	01-Jan-10		67
1.3.6	2CR0P3430R00	Parcel 343, Initiate Aquisition	0	01-Jan-10		67
1.3.6	2CR0P3530R00	Parcel 353, Initiate Aquisition	0	01-Jan-10		79
1.3.6	2CR0P3560R00	Parcel 356, Initiate Aquisition	0	01-Jan-10		67
1.3.6	2CR0P3570R00	Parcel 357, Initiate Aquisition	0	01-Jan-10		79
1.3.6	2CR0P3580R00	Parcel 358, Initiate Aquisition	0	01-Jan-10		92
1.3.6	2CR0P3850R00	Parcel 385, Initiate Aquisition	0	01-Jan-10		92
1.3.6	2CR0P3860R00	Parcel 386, Initiate Aquisition	0	01-Jan-10		92

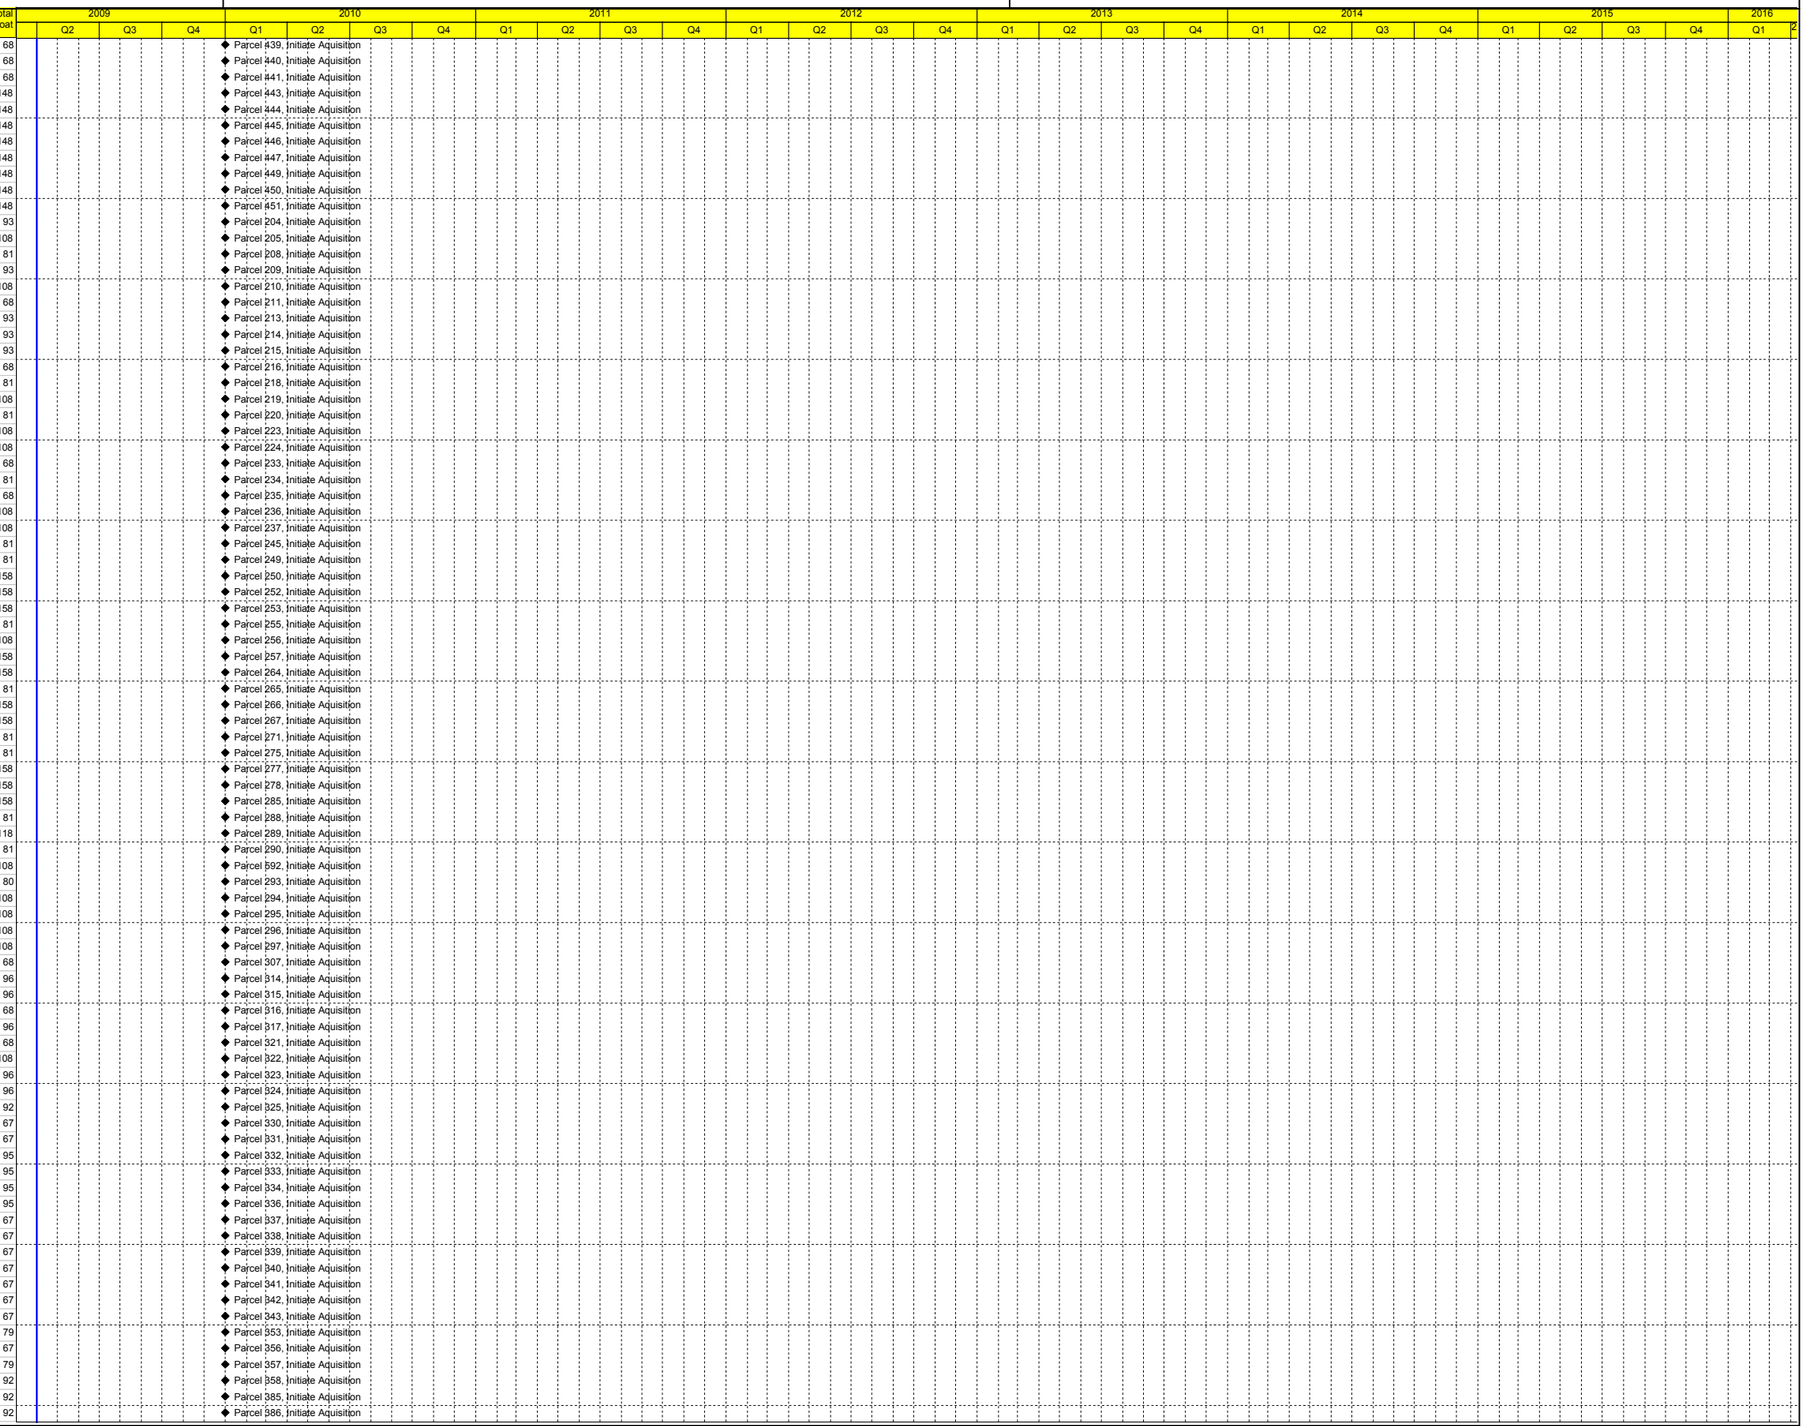

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.3.6	2CR0P3880R00	Parcel 388, Initiate Aquisition	0	01-Jan-10		67
1.3.6	2CR0P3950R00	Parcel 395, Initiate Aquisition	0	01-Jan-10		92
1.3.6	2CR0P3960R00	Parcel 396, Initiate Aquisition	0	01-Jan-10		92
1.3.6	2CR0P3970R00	Parcel 397, Initiate Aquisition	0	01-Jan-10		92
1.3.6	2CR0P3980R00	Parcel 398, Initiate Aquisition	0	01-Jan-10		95
1.3.6	2CR0P4080R00	Parcel 408, Initiate Aquisition	0	01-Jan-10		67
1.3.6	2CR0P4180R00	Parcel 418, Initiate Aquisition	0	01-Jan-10		158
1.3.6	2CR0P4200R00	Parcel 420, Initiate Aquisition	0	01-Jan-10		158
1.3.6	2CR0P4210R00	Parcel 421, Initiate Aquisition	0	01-Jan-10		158
1.3.6	2CR0P4280R00	Parcel 428, Initiate Aquisition	0	01-Jan-10		158
1.3.6	2CR0P4380R00	Parcel 438, Initiate Aquisition	0	01-Jan-10		92
1.3.6	2CR0P4420R00	Parcel 442, Initiate Aquisition	0	01-Jan-10		67
1.3.6	2CR0P4480R00	Parcel 448, Initiate Aquisition	0	01-Jan-10		108
1.3.6	2CR0P4520R00	Parcel 452, Initiate Aquisition	0	01-Jan-10		108
1.3.6	2CR0P2000R10	Parcel 200, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	79
1.3.6	2CR0P2380R10	Parcel 238, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	148
1.3.6	2CR0P2390R10	Parcel 239, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	148
1.3.6	2CR0P2420R10	Parcel 242, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	198
1.3.6	2CR0P2540R10	Parcel 254, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	148
1.3.6	2CR0P2590R10	Parcel 259, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	148
1.3.6	2CR0P2600R10	Parcel 260, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	198
1.3.6	2CR0P3270R10	Parcel 327, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	198
1.3.6	2CR0P3520R10	Parcel 352, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	76
1.3.6	2CR0P3590R10	Parcel 359, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	148
1.3.6	2CR0P3660R10	Parcel 366, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	148
1.3.6	2CR0P3690R10	Parcel 369, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	198
1.3.6	2CR0P3890R10	Parcel 389, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	76
1.3.6	2CR0P3900R10	Parcel 390, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	76
1.3.6	2CR0P3910R10	Parcel 391, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	76
1.3.6	2CR0P3920R10	Parcel 392, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	76
1.3.6	2CR0P3930R10	Parcel 393, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	76
1.3.6	2CR0P3940R10	Parcel 394, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	76
1.3.6	2CR0P3990R10	Parcel 399, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	95
1.3.6	2CR0P4000R10	Parcel 400, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	95
1.3.6	2CR0P4010R10	Parcel 401, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	76
1.3.6	2CR0P4020R10	Parcel 402, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	67
1.3.6	2CR0P4030R10	Parcel 403, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	67
1.3.6	2CR0P4040R10	Parcel 404, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	92
1.3.6	2CR0P4050R10	Parcel 405, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	92
1.3.6	2CR0P4060R10	Parcel 406, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	67
1.3.6	2CR0P4070R10	Parcel 407, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	67
1.3.6	2CR0P4090R10	Parcel 409, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	198
1.3.6	2CR0P4100R10	Parcel 410, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	198
1.3.6	2CR0P4110R10	Parcel 411, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	92
1.3.6	2CR0P4120R10	Parcel 412, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	92
1.3.6	2CR0P4130R10	Parcel 413, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	67
1.3.6	2CR0P4140R10	Parcel 414, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	67
1.3.6	2CR0P4150R10	Parcel 415, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	67
1.3.6	2CR0P4160R10	Parcel 416, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	198
1.3.6	2CR0P4170R10	Parcel 417, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	198
1.3.6	2CR0P4190R10	Parcel 419, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	198
1.3.6	2CR0P4220R10	Parcel 422, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	198
1.3.6	2CR0P4230R10	Parcel 423, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	198
1.3.6	2CR0P4240R10	Parcel 424, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	198
1.3.6	2CR0P4260R10	Parcel 426, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	198
1.3.6	2CR0P4270R10	Parcel 427, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	198
1.3.6	2CR0P4290R10	Parcel 429, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	198
1.3.6	2CR0P4300R10	Parcel 430, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	198
1.3.6	2CR0P4430R10	Parcel 443, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	148
1.3.6	2CR0P4440R10	Parcel 444, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	148
1.3.6	2CR0P4450R10	Parcel 445, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	148
1.3.6	2CR0P4460R10	Parcel 446, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	148
1.3.6	2CR0P4470R10	Parcel 447, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	148
1.3.6	2CR0P4490R10	Parcel 449, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	148
1.3.6	2CR0P4500R10	Parcel 450, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	148
1.3.6	2CR0P4510R10	Parcel 451, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	148
1.3.6	2CR0P2050R10	Parcel 205, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	108
1.3.6	2CR0P2100R10	Parcel 210, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	108
1.3.6	2CR0P2190R10	Parcel 219, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	108
1.3.6	2CR0P2230R10	Parcel 223, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	108
1.3.6	2CR0P2240R10	Parcel 224, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	108
1.3.6	2CR0P2360R10	Parcel 236, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	108
1.3.6	2CR0P2370R10	Parcel 237, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	108
1.3.6	2CR0P2500R10	Parcel 250, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	158
1.3.6	2CR0P2520R10	Parcel 252, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	158
1.3.6	2CR0P2530R10	Parcel 253, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	158
1.3.6	2CR0P2560R10	Parcel 256, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	108
1.3.6	2CR0P2570R10	Parcel 257, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	158
1.3.6	2CR0P2640R10	Parcel 264, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	158
1.3.6	2CR0P2660R10	Parcel 266, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	158
1.3.6	2CR0P2670R10	Parcel 267, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	158
1.3.6	2CR0P2770R10	Parcel 277, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	158
1.3.6	2CR0P2780R10	Parcel 278, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	158
1.3.6	2CR0P2850R10	Parcel 285, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	158
1.3.6	2CR0P5920R10	Parcel 592, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	1108
1.3.6	2CR0P2940R10	Parcel 294, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	108

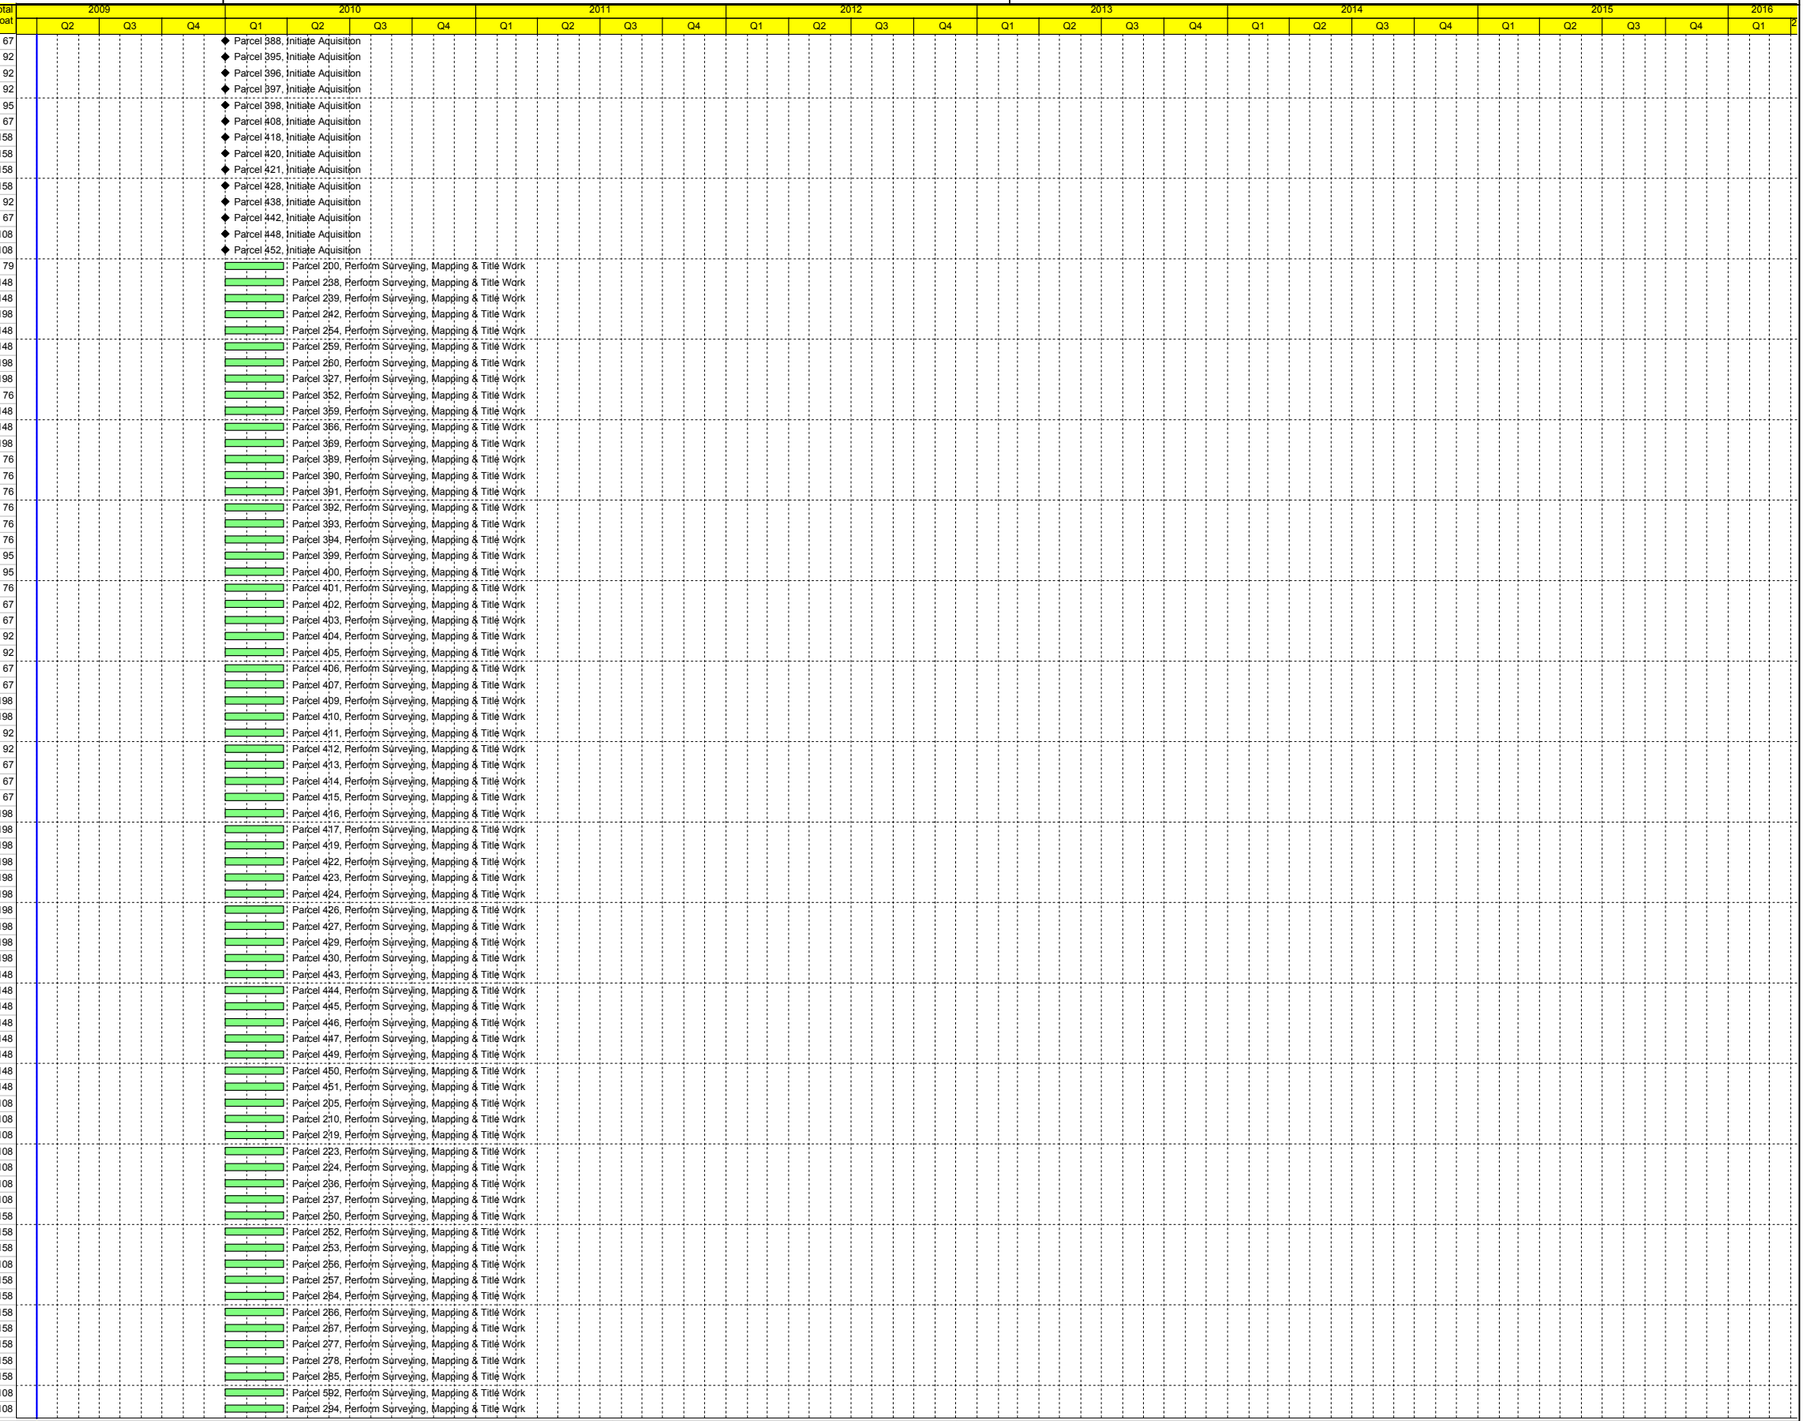

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.3.6	2CR0P2950R10	Parcel 295, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	108
1.3.6	2CR0P2960R10	Parcel 296, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	108
1.3.6	2CR0P2970R10	Parcel 297, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	108
1.3.6	2CR0P3220R10	Parcel 322, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	108
1.3.6	2CR0P3250R10	Parcel 325, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	92
1.3.6	2CR0P3300R10	Parcel 330, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	67
1.3.6	2CR0P3310R10	Parcel 331, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	67
1.3.6	2CR0P3320R10	Parcel 332, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	95
1.3.6	2CR0P3330R10	Parcel 333, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	95
1.3.6	2CR0P3340R10	Parcel 334, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	95
1.3.6	2CR0P3360R10	Parcel 336, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	95
1.3.6	2CR0P3370R10	Parcel 337, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	67
1.3.6	2CR0P3380R10	Parcel 338, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	67
1.3.6	2CR0P3390R10	Parcel 339, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	67
1.3.6	2CR0P3400R10	Parcel 340, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	67
1.3.6	2CR0P3410R10	Parcel 341, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	67
1.3.6	2CR0P3420R10	Parcel 342, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	67
1.3.6	2CR0P3430R10	Parcel 343, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	67
1.3.6	2CR0P3530R10	Parcel 353, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	79
1.3.6	2CR0P3560R10	Parcel 356, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	67
1.3.6	2CR0P3570R10	Parcel 357, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	79
1.3.6	2CR0P3580R10	Parcel 358, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	92
1.3.6	2CR0P3850R10	Parcel 385, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	92
1.3.6	2CR0P3860R10	Parcel 386, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	92
1.3.6	2CR0P3880R10	Parcel 388, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	67
1.3.6	2CR0P3950R10	Parcel 395, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	92
1.3.6	2CR0P3960R10	Parcel 396, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	92
1.3.6	2CR0P3970R10	Parcel 397, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	92
1.3.6	2CR0P3980R10	Parcel 398, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	95
1.3.6	2CR0P4080R10	Parcel 408, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	67
1.3.6	2CR0P4180R10	Parcel 418, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	158
1.3.6	2CR0P4200R10	Parcel 420, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	158
1.3.6	2CR0P4210R10	Parcel 421, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	158
1.3.6	2CR0P4280R10	Parcel 428, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	158
1.3.6	2CR0P4380R10	Parcel 438, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	92
1.3.6	2CR0P4420R10	Parcel 442, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	67
1.3.6	2CR0P4480R10	Parcel 448, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	108
1.3.6	2CR0P4520R10	Parcel 452, Perform Surveying, Mapping & Ti...	60	01-Jan-10	26-Mar-10	108
1.3.6	2CR0P2080R20	Parcel 208, Perform Appraisal and Internal R...	60	05-Jan-10	30-Mar-10	81
1.3.6	2CR0P2090R20	Parcel 209, Perform Appraisal and Internal R...	60	05-Jan-10	30-Mar-10	93
1.3.6	2CR0P2180R20	Parcel 218, Perform Appraisal and Internal R...	60	05-Jan-10	30-Mar-10	81
1.3.6	2CR0P2200R20	Parcel 220, Perform Appraisal and Internal R...	60	05-Jan-10	30-Mar-10	81
1.3.6	2CR0P2340R20	Parcel 234, Perform Appraisal and Internal R...	60	05-Jan-10	30-Mar-10	81
1.3.6	2CR0P2450R20	Parcel 245, Perform Appraisal and Internal R...	60	05-Jan-10	30-Mar-10	81
1.3.6	2CR0P2490R20	Parcel 249, Perform Appraisal and Internal R...	60	05-Jan-10	30-Mar-10	81
1.3.6	2CR0P2550R20	Parcel 255, Perform Appraisal and Internal R...	60	05-Jan-10	30-Mar-10	81
1.3.6	2CR0P2650R20	Parcel 265, Perform Appraisal and Internal R...	60	05-Jan-10	30-Mar-10	81
1.3.6	2CR0P2710R20	Parcel 271, Perform Appraisal and Internal R...	60	05-Jan-10	30-Mar-10	81
1.3.6	2CR0P2750R20	Parcel 275, Perform Appraisal and Internal R...	60	05-Jan-10	30-Mar-10	81
1.3.6	2CR0P2880R20	Parcel 288, Perform Appraisal and Internal R...	60	05-Jan-10	30-Mar-10	81
1.3.6	2CR0P2900R20	Parcel 290, Perform Appraisal and Internal R...	60	05-Jan-10	30-Mar-10	81
1.3.6	2CR0P2040R20	Parcel 204, Perform Appraisal and Internal R...	60	06-Jan-10	31-Mar-10	93
1.3.6	2CR0P2130R20	Parcel 213, Perform Appraisal and Internal R...	60	06-Jan-10	31-Mar-10	93
1.3.6	2CR0P2140R20	Parcel 214, Perform Appraisal and Internal R...	60	06-Jan-10	31-Mar-10	93
1.3.6	2CR0P2150R20	Parcel 215, Perform Appraisal and Internal R...	60	06-Jan-10	31-Mar-10	93
1.3.6	2CR0P2890R20	Parcel 289, Perform Appraisal and Internal R...	60	06-Jan-10	31-Mar-10	118
1.3.6	2CR0P2930R20	Parcel 293, Perform Appraisal and Internal R...	60	06-Jan-10	31-Mar-10	80
1.3.6	2CR0P3140R20	Parcel 314, Perform Appraisal and Internal R...	60	06-Jan-10	31-Mar-10	96
1.3.6	2CR0P3150R20	Parcel 315, Perform Appraisal and Internal R...	60	06-Jan-10	31-Mar-10	96
1.3.6	2CR0P3170R20	Parcel 317, Perform Appraisal and Internal R...	60	06-Jan-10	31-Mar-10	96
1.3.6	2CR0P3230R20	Parcel 323, Perform Appraisal and Internal R...	60	06-Jan-10	31-Mar-10	96
1.3.6	2CR0P3240R20	Parcel 324, Perform Appraisal and Internal R...	60	06-Jan-10	31-Mar-10	96
1.3.6	2CR0P3250R20	Parcel 325, Perform Appraisal and Internal R...	60	07-Jan-10	01-Apr-10	92
1.3.6	2CR0P3320R20	Parcel 332, Perform Appraisal and Internal R...	60	07-Jan-10	01-Apr-10	95
1.3.6	2CR0P3330R20	Parcel 333, Perform Appraisal and Internal R...	60	07-Jan-10	01-Apr-10	95
1.3.6	2CR0P3340R20	Parcel 334, Perform Appraisal and Internal R...	60	07-Jan-10	01-Apr-10	95
1.3.6	2CR0P3360R20	Parcel 336, Perform Appraisal and Internal R...	60	07-Jan-10	01-Apr-10	95
1.3.6	2CR0P3530R20	Parcel 353, Perform Appraisal and Internal R...	60	07-Jan-10	01-Apr-10	79
1.3.6	2CR0P3570R20	Parcel 357, Perform Appraisal and Internal R...	60	07-Jan-10	01-Apr-10	79
1.3.6	2CR0P3580R20	Parcel 358, Perform Appraisal and Internal R...	60	07-Jan-10	01-Apr-10	92
1.3.6	2CR0P3850R20	Parcel 385, Perform Appraisal and Internal R...	60	07-Jan-10	01-Apr-10	92
1.3.6	2CR0P3860R20	Parcel 386, Perform Appraisal and Internal R...	60	07-Jan-10	01-Apr-10	92
1.3.6	2CR0P3950R20	Parcel 395, Perform Appraisal and Internal R...	60	07-Jan-10	01-Apr-10	92
1.3.6	2CR0P3960R20	Parcel 396, Perform Appraisal and Internal R...	60	07-Jan-10	01-Apr-10	92
1.3.6	2CR0P3970R20	Parcel 397, Perform Appraisal and Internal R...	60	07-Jan-10	01-Apr-10	92
1.3.6	2CR0P3980R20	Parcel 398, Perform Appraisal and Internal R...	60	07-Jan-10	01-Apr-10	95
1.3.6	2CR0P4380R20	Parcel 438, Perform Appraisal and Internal R...	60	07-Jan-10	01-Apr-10	92
1.3.6	2CR0P2160R20	Parcel 216, Perform Appraisal and Internal R...	60	15-Feb-10	10-May-10	68
1.3.6	2CR0P2010R20	Parcel 201, Perform Appraisal and Internal R...	60	17-Feb-10	12-May-10	68
1.3.6	2CR0P2170R20	Parcel 217, Perform Appraisal and Internal R...	60	17-Feb-10	12-May-10	68
1.3.6	2CR0P2260R20	Parcel 226, Perform Appraisal and Internal R...	60	17-Feb-10	12-May-10	68
1.3.6	2CR0P2270R20	Parcel 227, Perform Appraisal and Internal R...	60	17-Feb-10	12-May-10	68
1.3.6	2CR0P2280R20	Parcel 228, Perform Appraisal and Internal R...	60	17-Feb-10	12-May-10	68
1.3.6	2CR0P2290R20	Parcel 229, Perform Appraisal and Internal R...	60	17-Feb-10	12-May-10	68
1.3.6	2CR0P2300R20	Parcel 230, Perform Appraisal and Internal R...	60	17-Feb-10	12-May-10	68
1.3.6	2CR0P2320R20	Parcel 232, Perform Appraisal and Internal R...	60	17-Feb-10	12-May-10	68

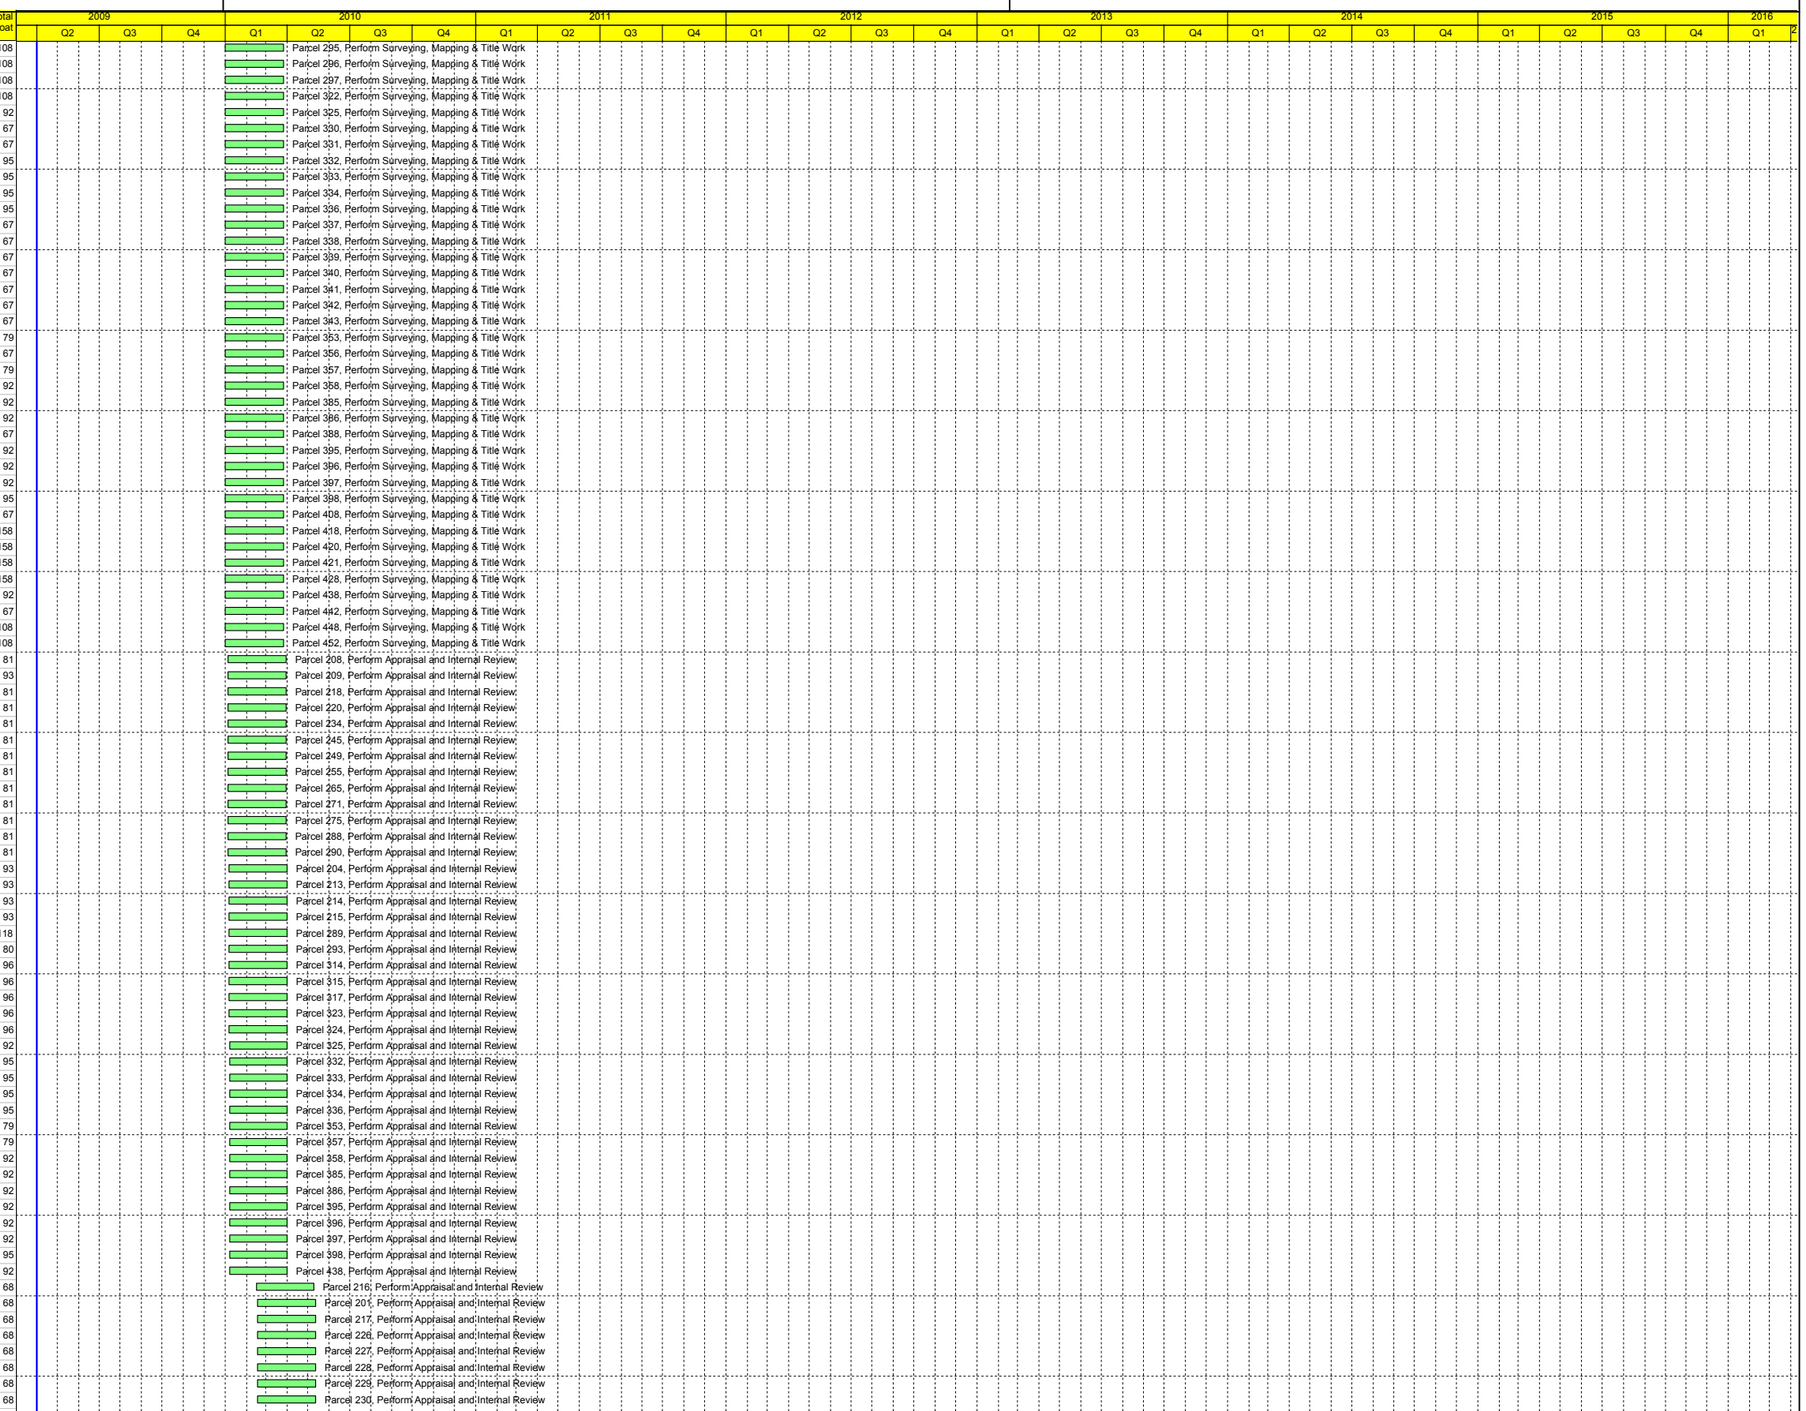

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.3.6	2CR0P3050R20	Parcel 305, Perform Appraisal and Internal R...	60	17-Feb-10	12-May-10	68
1.3.6	2CR0P3190R20	Parcel 319, Perform Appraisal and Internal R...	60	17-Feb-10	12-May-10	68
1.3.6	2CR0P3260R20	Parcel 326, Perform Appraisal and Internal R...	60	17-Feb-10	12-May-10	68
1.3.6	2CR0P3280R20	Parcel 328, Perform Appraisal and Internal R...	60	17-Feb-10	12-May-10	68
1.3.6	2CR0P3440R20	Parcel 344, Perform Appraisal and Internal R...	60	17-Feb-10	12-May-10	68
1.3.6	2CR0P3450R20	Parcel 345, Perform Appraisal and Internal R...	60	17-Feb-10	12-May-10	68
1.3.6	2CR0P3470R20	Parcel 347, Perform Appraisal and Internal R...	60	17-Feb-10	12-May-10	68
1.3.6	2CR0P3480R20	Parcel 348, Perform Appraisal and Internal R...	60	17-Feb-10	12-May-10	68
1.3.6	2CR0P3500R20	Parcel 350, Perform Appraisal and Internal R...	60	17-Feb-10	12-May-10	68
1.3.6	2CR0P3650R20	Parcel 365, Perform Appraisal and Internal R...	60	17-Feb-10	12-May-10	68
1.3.6	2CR0P3680R20	Parcel 368, Perform Appraisal and Internal R...	60	17-Feb-10	12-May-10	68
1.3.6	2CR0P3710R20	Parcel 371, Perform Appraisal and Internal R...	60	17-Feb-10	12-May-10	68
1.3.6	2CR0P3720R20	Parcel 372, Perform Appraisal and Internal R...	60	17-Feb-10	12-May-10	68
1.3.6	2CR0P3730R20	Parcel 373, Perform Appraisal and Internal R...	60	17-Feb-10	12-May-10	68
1.3.6	2CR0P3740R20	Parcel 374, Perform Appraisal and Internal R...	60	17-Feb-10	12-May-10	68
1.3.6	2CR0P3750R20	Parcel 375, Perform Appraisal and Internal R...	60	17-Feb-10	12-May-10	68
1.3.6	2CR0P3760R20	Parcel 376, Perform Appraisal and Internal R...	60	17-Feb-10	12-May-10	68
1.3.6	2CR0P3770R20	Parcel 377, Perform Appraisal and Internal R...	60	17-Feb-10	12-May-10	68
1.3.6	2CR0P3780R20	Parcel 378, Perform Appraisal and Internal R...	60	17-Feb-10	12-May-10	68
1.3.6	2CR0P3790R20	Parcel 379, Perform Appraisal and Internal R...	60	17-Feb-10	12-May-10	68
1.3.6	2CR0P3800R20	Parcel 380, Perform Appraisal and Internal R...	60	17-Feb-10	12-May-10	68
1.3.6	2CR0P3830R20	Parcel 383, Perform Appraisal and Internal R...	60	17-Feb-10	12-May-10	68
1.3.6	2CR0P4310R20	Parcel 431, Perform Appraisal and Internal R...	60	17-Feb-10	12-May-10	68
1.3.6	2CR0P4390R20	Parcel 439, Perform Appraisal and Internal R...	60	17-Feb-10	12-May-10	68
1.3.6	2CR0P4400R20	Parcel 440, Perform Appraisal and Internal R...	60	17-Feb-10	12-May-10	68
1.3.6	2CR0P4410R20	Parcel 441, Perform Appraisal and Internal R...	60	17-Feb-10	12-May-10	68
1.3.6	2CR0P4020R20	Parcel 402, Perform Appraisal and Internal R...	60	18-Feb-10	13-May-10	67
1.3.6	2CR0P4030R20	Parcel 403, Perform Appraisal and Internal R...	60	18-Feb-10	13-May-10	67
1.3.6	2CR0P4060R20	Parcel 406, Perform Appraisal and Internal R...	60	18-Feb-10	13-May-10	67
1.3.6	2CR0P4070R20	Parcel 407, Perform Appraisal and Internal R...	60	18-Feb-10	13-May-10	67
1.3.6	2CR0P4130R20	Parcel 413, Perform Appraisal and Internal R...	60	18-Feb-10	13-May-10	67
1.3.6	2CR0P4140R20	Parcel 414, Perform Appraisal and Internal R...	60	18-Feb-10	13-May-10	67
1.3.6	2CR0P4150R20	Parcel 415, Perform Appraisal and Internal R...	60	18-Feb-10	13-May-10	67
1.3.6	2CR0P2310R20	Parcel 231, Perform Appraisal and Internal R...	60	02-Mar-10	25-May-10	81
1.3.6	2CR0P2400R20	Parcel 240, Perform Appraisal and Internal R...	60	02-Mar-10	25-May-10	81
1.3.6	2CR0P2410R20	Parcel 241, Perform Appraisal and Internal R...	60	02-Mar-10	25-May-10	81
1.3.6	2CR0P2910R20	Parcel 291, Perform Appraisal and Internal R...	60	02-Mar-10	25-May-10	81
1.3.6	2CR0P2920R20	Parcel 292, Perform Appraisal and Internal R...	60	02-Mar-10	25-May-10	81
1.3.6	2CR0P2990R20	Parcel 299, Perform Appraisal and Internal R...	60	02-Mar-10	25-May-10	81
1.3.6	2CR0P3550R20	Parcel 355, Perform Appraisal and Internal R...	60	02-Mar-10	25-May-10	81
1.3.6	2CR0P3670R20	Parcel 367, Perform Appraisal and Internal R...	60	02-Mar-10	25-May-10	81
1.3.6	2CR0P2020R20	Parcel 202, Perform Appraisal and Internal R...	60	03-Mar-10	26-May-10	96
1.3.6	2CR0P2030R20	Parcel 203, Perform Appraisal and Internal R...	60	03-Mar-10	26-May-10	96
1.3.6	2CR0P2070R20	Parcel 207, Perform Appraisal and Internal R...	60	03-Mar-10	26-May-10	93
1.3.6	2CR0P2250R20	Parcel 225, Perform Appraisal and Internal R...	60	03-Mar-10	26-May-10	80
1.3.6	2CR0P3010R20	Parcel 301, Perform Appraisal and Internal R...	60	03-Mar-10	26-May-10	96
1.3.6	2CR0P3020R20	Parcel 302, Perform Appraisal and Internal R...	60	03-Mar-10	26-May-10	96
1.3.6	2CR0P3040R20	Parcel 304, Perform Appraisal and Internal R...	60	03-Mar-10	26-May-10	80
1.3.6	2CR0P3060R20	Parcel 306, Perform Appraisal and Internal R...	60	03-Mar-10	26-May-10	93
1.3.6	2CR0P3080R20	Parcel 308, Perform Appraisal and Internal R...	60	03-Mar-10	26-May-10	96
1.3.6	2CR0P3180R20	Parcel 318, Perform Appraisal and Internal R...	60	03-Mar-10	26-May-10	96
1.3.6	2CR0P3290R20	Parcel 329, Perform Appraisal and Internal R...	60	03-Mar-10	26-May-10	96
1.3.6	2CR0P3350R20	Parcel 335, Perform Appraisal and Internal R...	60	03-Mar-10	26-May-10	96
1.3.6	2CR0P3490R20	Parcel 349, Perform Appraisal and Internal R...	60	03-Mar-10	26-May-10	93
1.3.6	2CR0P3510R20	Parcel 351, Perform Appraisal and Internal R...	60	03-Mar-10	26-May-10	80
1.3.6	2CR0P3600R20	Parcel 360, Perform Appraisal and Internal R...	60	03-Mar-10	26-May-10	93
1.3.6	2CR0P3610R20	Parcel 361, Perform Appraisal and Internal R...	60	03-Mar-10	26-May-10	93
1.3.6	2CR0P3620R20	Parcel 362, Perform Appraisal and Internal R...	60	03-Mar-10	26-May-10	93
1.3.6	2CR0P3630R20	Parcel 363, Perform Appraisal and Internal R...	60	03-Mar-10	26-May-10	93
1.3.6	2CR0P3640R20	Parcel 364, Perform Appraisal and Internal R...	60	03-Mar-10	26-May-10	93
1.3.6	2CR0P3810R20	Parcel 381, Perform Appraisal and Internal R...	60	03-Mar-10	26-May-10	96
1.3.6	2CR0P3820R20	Parcel 382, Perform Appraisal and Internal R...	60	03-Mar-10	26-May-10	96
1.3.6	2CR0P3840R20	Parcel 384, Perform Appraisal and Internal R...	60	03-Mar-10	26-May-10	96
1.3.6	2CR0P3870R20	Parcel 387, Perform Appraisal and Internal R...	60	03-Mar-10	26-May-10	93
1.3.6	2CR0P4320R20	Parcel 432, Perform Appraisal and Internal R...	60	03-Mar-10	26-May-10	93
1.3.6	2CR0P4330R20	Parcel 433, Perform Appraisal and Internal R...	60	03-Mar-10	26-May-10	93
1.3.6	2CR0P4340R20	Parcel 434, Perform Appraisal and Internal R...	60	03-Mar-10	26-May-10	93
1.3.6	2CR0P4350R20	Parcel 435, Perform Appraisal and Internal R...	60	03-Mar-10	26-May-10	93
1.3.6	2CR0P4360R20	Parcel 436, Perform Appraisal and Internal R...	60	03-Mar-10	26-May-10	93
1.3.6	2CR0P4370R20	Parcel 437, Perform Appraisal and Internal R...	60	03-Mar-10	26-May-10	93
1.3.6	2CR0P3990R20	Parcel 399, Perform Appraisal and Internal R...	60	04-Mar-10	27-May-10	95
1.3.6	2CR0P4000R20	Parcel 400, Perform Appraisal and Internal R...	60	04-Mar-10	27-May-10	95
1.3.6	2CR0P4040R20	Parcel 404, Perform Appraisal and Internal R...	60	04-Mar-10	27-May-10	92
1.3.6	2CR0P4050R20	Parcel 405, Perform Appraisal and Internal R...	60	04-Mar-10	27-May-10	92
1.3.6	2CR0P4110R20	Parcel 411, Perform Appraisal and Internal R...	60	04-Mar-10	27-May-10	92
1.3.6	2CR0P4120R20	Parcel 412, Perform Appraisal and Internal R...	60	04-Mar-10	27-May-10	92
1.3.6	2CR0P2350R20	Parcel 235, Perform Appraisal and Internal R...	60	09-Mar-10	01-Jun-10	68
1.3.6	2CR0P2110R30	Parcel 211, TxDOT Reviews Aquisition Pack...	10	17-Mar-10	31-Mar-10	68
1.3.6	2CR0P2330R30	Parcel 233, TxDOT Reviews Aquisition Pack...	10	17-Mar-10	31-Mar-10	68
1.3.6	2CR0P3070R30	Parcel 307, TxDOT Reviews Aquisition Pack...	10	17-Mar-10	31-Mar-10	68
1.3.6	2CR0P3160R30	Parcel 316, TxDOT Reviews Aquisition Pack...	10	17-Mar-10	31-Mar-10	68
1.3.6	2CR0P3210R30	Parcel 321, TxDOT Reviews Aquisition Pack...	10	17-Mar-10	31-Mar-10	68
1.3.6	2CR0P3300R30	Parcel 330, TxDOT Reviews Aquisition Pack...	10	18-Mar-10	01-Apr-10	67
1.3.6	2CR0P3310R30	Parcel 331, TxDOT Reviews Aquisition Pack...	10	18-Mar-10	01-Apr-10	67
1.3.6	2CR0P3370R30	Parcel 337, TxDOT Reviews Aquisition Pack...	10	18-Mar-10	01-Apr-10	67
1.3.6	2CR0P3380R30	Parcel 338, TxDOT Reviews Aquisition Pack...	10	18-Mar-10	01-Apr-10	67

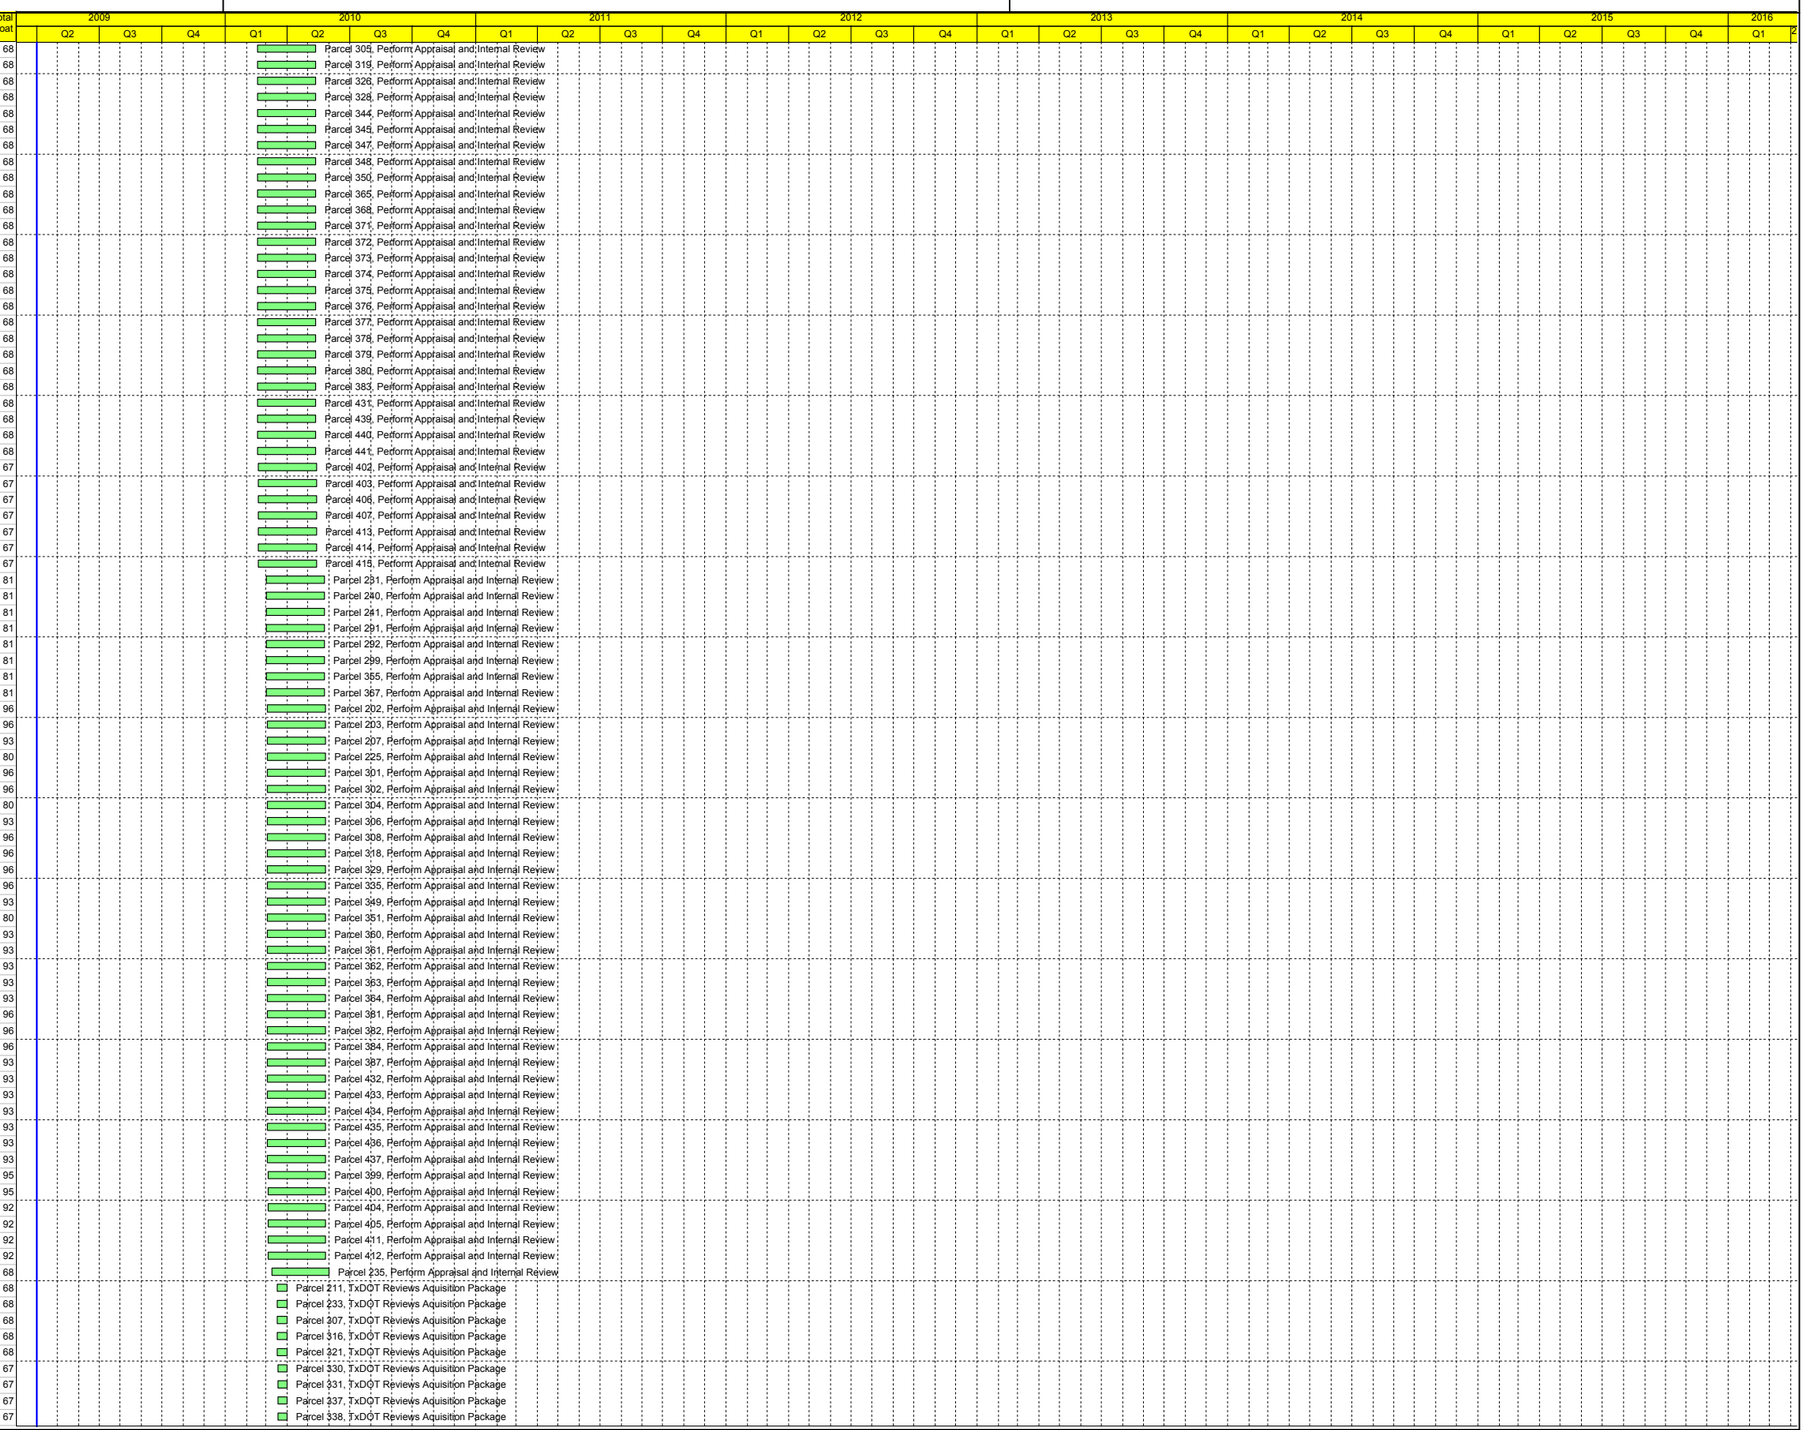

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.3.6	2CR0P3390R30	Parcel 339, TxDOT Reviews Aquisition Pack...	10	18-Mar-10	01-Apr-10	67
1.3.6	2CR0P3400R30	Parcel 340, TxDOT Reviews Aquisition Pack...	10	18-Mar-10	01-Apr-10	67
1.3.6	2CR0P3410R30	Parcel 341, TxDOT Reviews Aquisition Pack...	10	18-Mar-10	01-Apr-10	67
1.3.6	2CR0P3420R30	Parcel 342, TxDOT Reviews Aquisition Pack...	10	18-Mar-10	01-Apr-10	67
1.3.6	2CR0P3430R30	Parcel 343, TxDOT Reviews Aquisition Pack...	10	18-Mar-10	01-Apr-10	67
1.3.6	2CR0P3560R30	Parcel 356, TxDOT Reviews Aquisition Pack...	10	18-Mar-10	01-Apr-10	67
1.3.6	2CR0P3880R30	Parcel 388, TxDOT Reviews Aquisition Pack...	10	18-Mar-10	01-Apr-10	67
1.3.6	2CR0P4080R30	Parcel 408, TxDOT Reviews Aquisition Pack...	10	18-Mar-10	01-Apr-10	67
1.3.6	2CR0P4420R30	Parcel 442, TxDOT Reviews Aquisition Pack...	10	18-Mar-10	01-Apr-10	67
1.3.6	2CR0P3030R20	Parcel 303, Perform Appraisal and Internal R...	60	19-Mar-10	11-Jun-10	68
1.3.6	2CR0P2000R20	Parcel 200, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	79
1.3.6	2CR0P2380R20	Parcel 238, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	148
1.3.6	2CR0P2390R20	Parcel 239, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	148
1.3.6	2CR0P2420R20	Parcel 242, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	198
1.3.6	2CR0P2540R20	Parcel 254, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	148
1.3.6	2CR0P2590R20	Parcel 259, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	148
1.3.6	2CR0P2600R20	Parcel 260, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	198
1.3.6	2CR0P3270R20	Parcel 327, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	198
1.3.6	2CR0P3520R20	Parcel 352, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	76
1.3.6	2CR0P3590R20	Parcel 359, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	148
1.3.6	2CR0P3660R20	Parcel 366, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	148
1.3.6	2CR0P3690R20	Parcel 369, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	198
1.3.6	2CR0P3890R20	Parcel 389, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	76
1.3.6	2CR0P3900R20	Parcel 390, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	76
1.3.6	2CR0P3910R20	Parcel 391, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	76
1.3.6	2CR0P3920R20	Parcel 392, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	76
1.3.6	2CR0P3930R20	Parcel 393, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	76
1.3.6	2CR0P3940R20	Parcel 394, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	76
1.3.6	2CR0P4010R20	Parcel 401, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	76
1.3.6	2CR0P4090R20	Parcel 409, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	198
1.3.6	2CR0P4100R20	Parcel 410, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	198
1.3.6	2CR0P4160R20	Parcel 416, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	198
1.3.6	2CR0P4170R20	Parcel 417, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	198
1.3.6	2CR0P4190R20	Parcel 419, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	198
1.3.6	2CR0P4220R20	Parcel 422, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	198
1.3.6	2CR0P4230R20	Parcel 423, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	198
1.3.6	2CR0P4240R20	Parcel 424, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	198
1.3.6	2CR0P4260R20	Parcel 426, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	198
1.3.6	2CR0P4270R20	Parcel 427, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	198
1.3.6	2CR0P4290R20	Parcel 429, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	198
1.3.6	2CR0P4300R20	Parcel 430, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	198
1.3.6	2CR0P4430R20	Parcel 443, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	148
1.3.6	2CR0P4440R20	Parcel 444, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	148
1.3.6	2CR0P4450R20	Parcel 445, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	148
1.3.6	2CR0P4460R20	Parcel 446, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	148
1.3.6	2CR0P4470R20	Parcel 447, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	148
1.3.6	2CR0P4490R20	Parcel 449, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	148
1.3.6	2CR0P4500R20	Parcel 450, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	148
1.3.6	2CR0P4510R20	Parcel 451, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	148
1.3.6	2CR0P2050R20	Parcel 205, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	108
1.3.6	2CR0P2100R20	Parcel 210, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	108
1.3.6	2CR0P2190R20	Parcel 219, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	108
1.3.6	2CR0P2230R20	Parcel 223, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	108
1.3.6	2CR0P2240R20	Parcel 224, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	108
1.3.6	2CR0P2360R20	Parcel 236, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	108
1.3.6	2CR0P2370R20	Parcel 237, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	108
1.3.6	2CR0P2500R20	Parcel 250, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	158
1.3.6	2CR0P2520R20	Parcel 252, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	158
1.3.6	2CR0P2530R20	Parcel 253, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	158
1.3.6	2CR0P2560R20	Parcel 256, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	108
1.3.6	2CR0P2570R20	Parcel 257, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	158
1.3.6	2CR0P2640R20	Parcel 264, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	158
1.3.6	2CR0P2660R20	Parcel 266, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	158
1.3.6	2CR0P2670R20	Parcel 267, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	158
1.3.6	2CR0P2770R20	Parcel 277, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	158
1.3.6	2CR0P2780R20	Parcel 278, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	158
1.3.6	2CR0P2850R20	Parcel 285, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	158
1.3.6	2CR0P5920R20	Parcel 592, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	1108
1.3.6	2CR0P2940R20	Parcel 294, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	108
1.3.6	2CR0P2950R20	Parcel 295, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	108
1.3.6	2CR0P2960R20	Parcel 296, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	108
1.3.6	2CR0P2970R20	Parcel 297, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	108
1.3.6	2CR0P3220R20	Parcel 322, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	108
1.3.6	2CR0P4180R20	Parcel 418, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	158
1.3.6	2CR0P4200R20	Parcel 420, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	158
1.3.6	2CR0P4210R20	Parcel 421, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	158
1.3.6	2CR0P4280R20	Parcel 428, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	158
1.3.6	2CR0P4480R20	Parcel 448, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	108
1.3.6	2CR0P4520R20	Parcel 452, Perform Appraisal and Internal R...	60	26-Mar-10	18-Jun-10	108
1.3.6	2CR0P2080R30	Parcel 208, TxDOT Reviews Aquisition Pack...	10	30-Mar-10	13-Apr-10	81
1.3.6	2CR0P2090R30	Parcel 209, TxDOT Reviews Aquisition Pack...	10	30-Mar-10	13-Apr-10	93
1.3.6	2CR0P2180R30	Parcel 218, TxDOT Reviews Aquisition Pack...	10	30-Mar-10	13-Apr-10	81
1.3.6	2CR0P2200R30	Parcel 220, TxDOT Reviews Aquisition Pack...	10	30-Mar-10	13-Apr-10	81
1.3.6	2CR0P2340R30	Parcel 234, TxDOT Reviews Aquisition Pack...	10	30-Mar-10	13-Apr-10	81
1.3.6	2CR0P2450R30	Parcel 245, TxDOT Reviews Aquisition Pack...	10	30-Mar-10	13-Apr-10	81
1.3.6	2CR0P2490R30	Parcel 249, TxDOT Reviews Aquisition Pack...	10	30-Mar-10	13-Apr-10	81

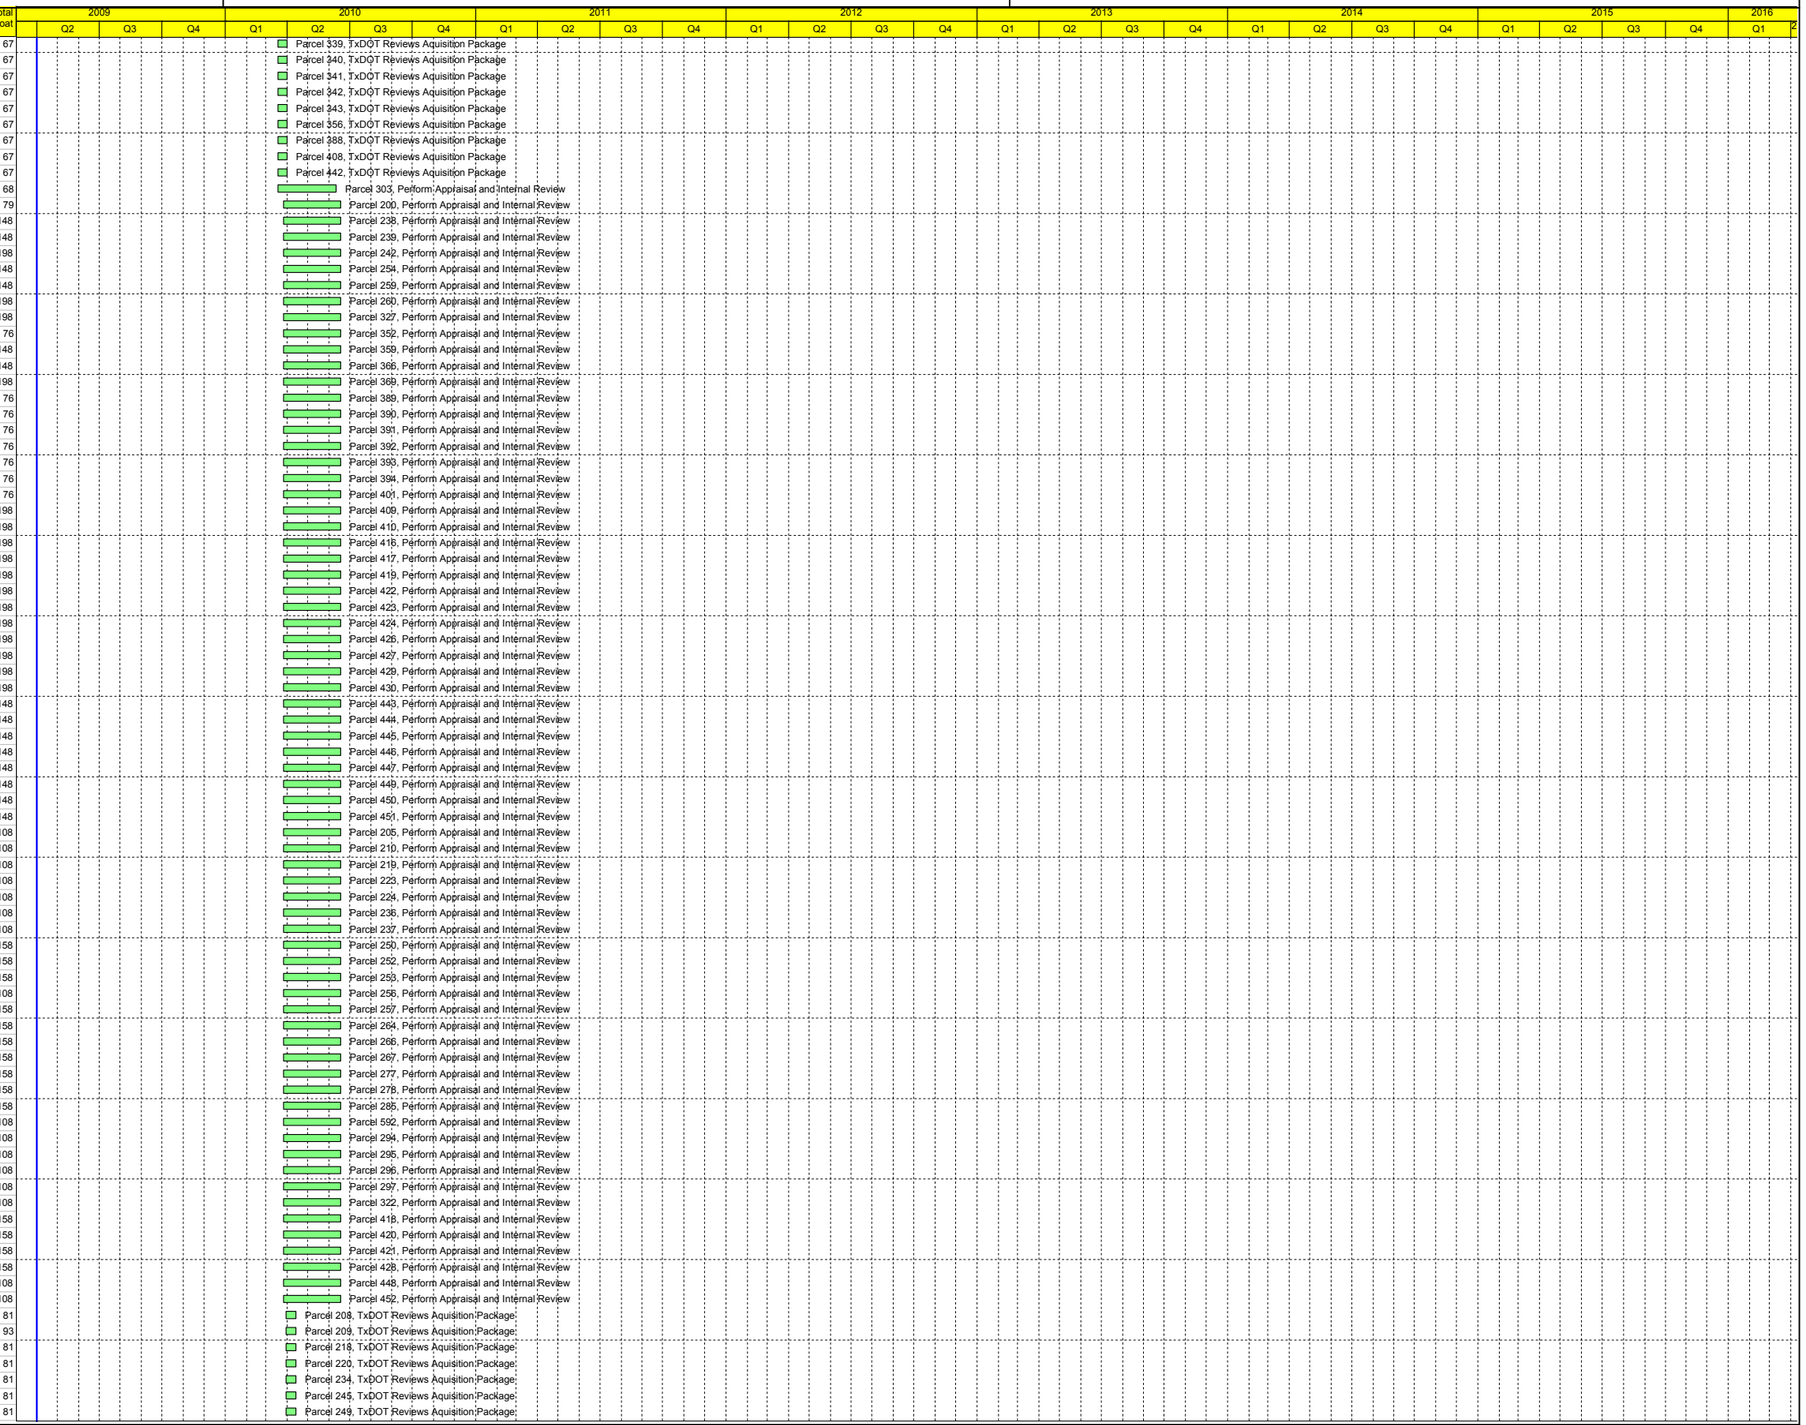

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.3.6	2CR0P2550R30	Parcel 255, TxDOT Reviews Aquisition Pack...	10	30-Mar-10	13-Apr-10	81
1.3.6	2CR0P2650R30	Parcel 265, TxDOT Reviews Aquisition Pack...	10	30-Mar-10	13-Apr-10	81
1.3.6	2CR0P2710R30	Parcel 271, TxDOT Reviews Aquisition Pack...	10	30-Mar-10	13-Apr-10	81
1.3.6	2CR0P2750R30	Parcel 275, TxDOT Reviews Aquisition Pack...	10	30-Mar-10	13-Apr-10	81
1.3.6	2CR0P2880R30	Parcel 288, TxDOT Reviews Aquisition Pack...	10	30-Mar-10	13-Apr-10	81
1.3.6	2CR0P2900R30	Parcel 290, TxDOT Reviews Aquisition Pack...	10	30-Mar-10	13-Apr-10	81
1.3.6	2CR0P2040R30	Parcel 204, TxDOT Reviews Aquisition Pack...	10	31-Mar-10	14-Apr-10	93
1.3.6	2CR0P2130R30	Parcel 213, TxDOT Reviews Aquisition Pack...	10	31-Mar-10	14-Apr-10	93
1.3.6	2CR0P2140R30	Parcel 214, TxDOT Reviews Aquisition Pack...	10	31-Mar-10	14-Apr-10	93
1.3.6	2CR0P2150R30	Parcel 215, TxDOT Reviews Aquisition Pack...	10	31-Mar-10	14-Apr-10	93
1.3.6	2CR0P2890R30	Parcel 289, TxDOT Reviews Aquisition Pack...	10	31-Mar-10	14-Apr-10	118
1.3.6	2CR0P2930R30	Parcel 293, TxDOT Reviews Aquisition Pack...	10	31-Mar-10	14-Apr-10	80
1.3.6	2CR0P3140R30	Parcel 314, TxDOT Reviews Aquisition Pack...	10	31-Mar-10	14-Apr-10	96
1.3.6	2CR0P3150R30	Parcel 315, TxDOT Reviews Aquisition Pack...	10	31-Mar-10	14-Apr-10	96
1.3.6	2CR0P3170R30	Parcel 317, TxDOT Reviews Aquisition Pack...	10	31-Mar-10	14-Apr-10	96
1.3.6	2CR0P3230R30	Parcel 323, TxDOT Reviews Aquisition Pack...	10	31-Mar-10	14-Apr-10	96
1.3.6	2CR0P3240R30	Parcel 324, TxDOT Reviews Aquisition Pack...	10	31-Mar-10	14-Apr-10	96
1.3.6	2CR0P2110R40	Parcel 211, Present and Negotiate Offer	20	31-Mar-10	28-Apr-10	68
1.3.6	2CR0P2330R40	Parcel 233, Present and Negotiate Offer	20	31-Mar-10	28-Apr-10	68
1.3.6	2CR0P3070R40	Parcel 307, Present and Negotiate Offer	20	31-Mar-10	28-Apr-10	68
1.3.6	2CR0P3160R40	Parcel 316, Present and Negotiate Offer	20	31-Mar-10	28-Apr-10	68
1.3.6	2CR0P3210R40	Parcel 321, Present and Negotiate Offer	20	31-Mar-10	28-Apr-10	68
1.3.6	2CR0P2110R50	Parcel 211, Prepare for Relocation	60	31-Mar-10	23-Jun-10	158
1.3.6	2CR0P2330R50	Parcel 233, Prepare for Relocation	60	31-Mar-10	23-Jun-10	158
1.3.6	2CR0P3070R50	Parcel 307, Prepare for Relocation	60	31-Mar-10	23-Jun-10	158
1.3.6	2CR0P3160R50	Parcel 316, Prepare for Relocation	60	31-Mar-10	23-Jun-10	158
1.3.6	2CR0P3210R50	Parcel 321, Prepare for Relocation	60	31-Mar-10	23-Jun-10	158
1.3.6	2CR0P3250R30	Parcel 325, TxDOT Reviews Aquisition Pack...	10	01-Apr-10	15-Apr-10	92
1.3.6	2CR0P3320R30	Parcel 332, TxDOT Reviews Aquisition Pack...	10	01-Apr-10	15-Apr-10	95
1.3.6	2CR0P3330R30	Parcel 333, TxDOT Reviews Aquisition Pack...	10	01-Apr-10	15-Apr-10	95
1.3.6	2CR0P3340R30	Parcel 334, TxDOT Reviews Aquisition Pack...	10	01-Apr-10	15-Apr-10	95
1.3.6	2CR0P3360R30	Parcel 336, TxDOT Reviews Aquisition Pack...	10	01-Apr-10	15-Apr-10	95
1.3.6	2CR0P3530R30	Parcel 353, TxDOT Reviews Aquisition Pack...	10	01-Apr-10	15-Apr-10	79
1.3.6	2CR0P3570R30	Parcel 357, TxDOT Reviews Aquisition Pack...	10	01-Apr-10	15-Apr-10	79
1.3.6	2CR0P3580R30	Parcel 358, TxDOT Reviews Aquisition Pack...	10	01-Apr-10	15-Apr-10	92
1.3.6	2CR0P3850R30	Parcel 385, TxDOT Reviews Aquisition Pack...	10	01-Apr-10	15-Apr-10	92
1.3.6	2CR0P3860R30	Parcel 386, TxDOT Reviews Aquisition Pack...	10	01-Apr-10	15-Apr-10	92
1.3.6	2CR0P3950R30	Parcel 395, TxDOT Reviews Aquisition Pack...	10	01-Apr-10	15-Apr-10	92
1.3.6	2CR0P3960R30	Parcel 396, TxDOT Reviews Aquisition Pack...	10	01-Apr-10	15-Apr-10	92
1.3.6	2CR0P3970R30	Parcel 397, TxDOT Reviews Aquisition Pack...	10	01-Apr-10	15-Apr-10	92
1.3.6	2CR0P3980R30	Parcel 398, TxDOT Reviews Aquisition Pack...	10	01-Apr-10	15-Apr-10	95
1.3.6	2CR0P4380R30	Parcel 438, TxDOT Reviews Aquisition Pack...	10	01-Apr-10	15-Apr-10	92
1.3.6	2CR0P3300R40	Parcel 330, Present and Negotiate Offer	20	01-Apr-10	29-Apr-10	67
1.3.6	2CR0P3310R40	Parcel 331, Present and Negotiate Offer	20	01-Apr-10	29-Apr-10	67
1.3.6	2CR0P3370R40	Parcel 337, Present and Negotiate Offer	20	01-Apr-10	29-Apr-10	67
1.3.6	2CR0P3380R40	Parcel 338, Present and Negotiate Offer	20	01-Apr-10	29-Apr-10	67
1.3.6	2CR0P3390R40	Parcel 339, Present and Negotiate Offer	20	01-Apr-10	29-Apr-10	67
1.3.6	2CR0P3400R40	Parcel 340, Present and Negotiate Offer	20	01-Apr-10	29-Apr-10	67
1.3.6	2CR0P3410R40	Parcel 341, Present and Negotiate Offer	20	01-Apr-10	29-Apr-10	67
1.3.6	2CR0P3420R40	Parcel 342, Present and Negotiate Offer	20	01-Apr-10	29-Apr-10	67
1.3.6	2CR0P3430R40	Parcel 343, Present and Negotiate Offer	20	01-Apr-10	29-Apr-10	67
1.3.6	2CR0P3560R40	Parcel 356, Present and Negotiate Offer	20	01-Apr-10	29-Apr-10	67
1.3.6	2CR0P3880R40	Parcel 388, Present and Negotiate Offer	20	01-Apr-10	29-Apr-10	67
1.3.6	2CR0P4080R40	Parcel 408, Present and Negotiate Offer	20	01-Apr-10	29-Apr-10	67
1.3.6	2CR0P4420R40	Parcel 442, Present and Negotiate Offer	20	01-Apr-10	29-Apr-10	67
1.3.6	2CR0P3300R50	Parcel 330, Prepare for Relocation	60	01-Apr-10	24-Jun-10	157
1.3.6	2CR0P3310R50	Parcel 331, Prepare for Relocation	60	01-Apr-10	24-Jun-10	157
1.3.6	2CR0P3370R50	Parcel 337, Prepare for Relocation	60	01-Apr-10	24-Jun-10	157
1.3.6	2CR0P3380R50	Parcel 338, Prepare for Relocation	60	01-Apr-10	24-Jun-10	157
1.3.6	2CR0P3390R50	Parcel 339, Prepare for Relocation	60	01-Apr-10	24-Jun-10	157
1.3.6	2CR0P3400R50	Parcel 340, Prepare for Relocation	60	01-Apr-10	24-Jun-10	157
1.3.6	2CR0P3410R50	Parcel 341, Prepare for Relocation	60	01-Apr-10	24-Jun-10	157
1.3.6	2CR0P3420R50	Parcel 342, Prepare for Relocation	60	01-Apr-10	24-Jun-10	157
1.3.6	2CR0P3430R50	Parcel 343, Prepare for Relocation	60	01-Apr-10	24-Jun-10	157
1.3.6	2CR0P3560R50	Parcel 356, Prepare for Relocation	60	01-Apr-10	24-Jun-10	157
1.3.6	2CR0P3880R50	Parcel 388, Prepare for Relocation	60	01-Apr-10	24-Jun-10	157
1.3.6	2CR0P4080R50	Parcel 408, Prepare for Relocation	60	01-Apr-10	24-Jun-10	157
1.3.6	2CR0P4420R50	Parcel 442, Prepare for Relocation	60	01-Apr-10	24-Jun-10	157
1.3.6	2CR0P2080R40	Parcel 208, Present and Negotiate Offer	20	13-Apr-10	11-May-10	81
1.3.6	2CR0P2090R40	Parcel 209, Present and Negotiate Offer	20	13-Apr-10	11-May-10	93
1.3.6	2CR0P2180R40	Parcel 218, Present and Negotiate Offer	20	13-Apr-10	11-May-10	81
1.3.6	2CR0P2200R40	Parcel 220, Present and Negotiate Offer	20	13-Apr-10	11-May-10	81
1.3.6	2CR0P2340R40	Parcel 234, Present and Negotiate Offer	20	13-Apr-10	11-May-10	81
1.3.6	2CR0P2450R40	Parcel 245, Present and Negotiate Offer	20	13-Apr-10	11-May-10	81
1.3.6	2CR0P2490R40	Parcel 249, Present and Negotiate Offer	20	13-Apr-10	11-May-10	81
1.3.6	2CR0P2550R40	Parcel 255, Present and Negotiate Offer	20	13-Apr-10	11-May-10	81
1.3.6	2CR0P2650R40	Parcel 265, Present and Negotiate Offer	20	13-Apr-10	11-May-10	81
1.3.6	2CR0P2710R40	Parcel 271, Present and Negotiate Offer	20	13-Apr-10	11-May-10	81
1.3.6	2CR0P2750R40	Parcel 275, Present and Negotiate Offer	20	13-Apr-10	11-May-10	81
1.3.6	2CR0P2880R40	Parcel 288, Present and Negotiate Offer	20	13-Apr-10	11-May-10	81
1.3.6	2CR0P2900R40	Parcel 290, Present and Negotiate Offer	20	13-Apr-10	11-May-10	81
1.3.6	2CR0P2080R50	Parcel 208, Prepare for Relocation	60	13-Apr-10	06-Jul-10	171
1.3.6	2CR0P2090R50	Parcel 209, Prepare for Relocation	60	13-Apr-10	06-Jul-10	183
1.3.6	2CR0P2180R50	Parcel 218, Prepare for Relocation	60	13-Apr-10	06-Jul-10	171
1.3.6	2CR0P2200R50	Parcel 220, Prepare for Relocation	60	13-Apr-10	06-Jul-10	171
1.3.6	2CR0P2340R50	Parcel 234, Prepare for Relocation	60	13-Apr-10	06-Jul-10	171

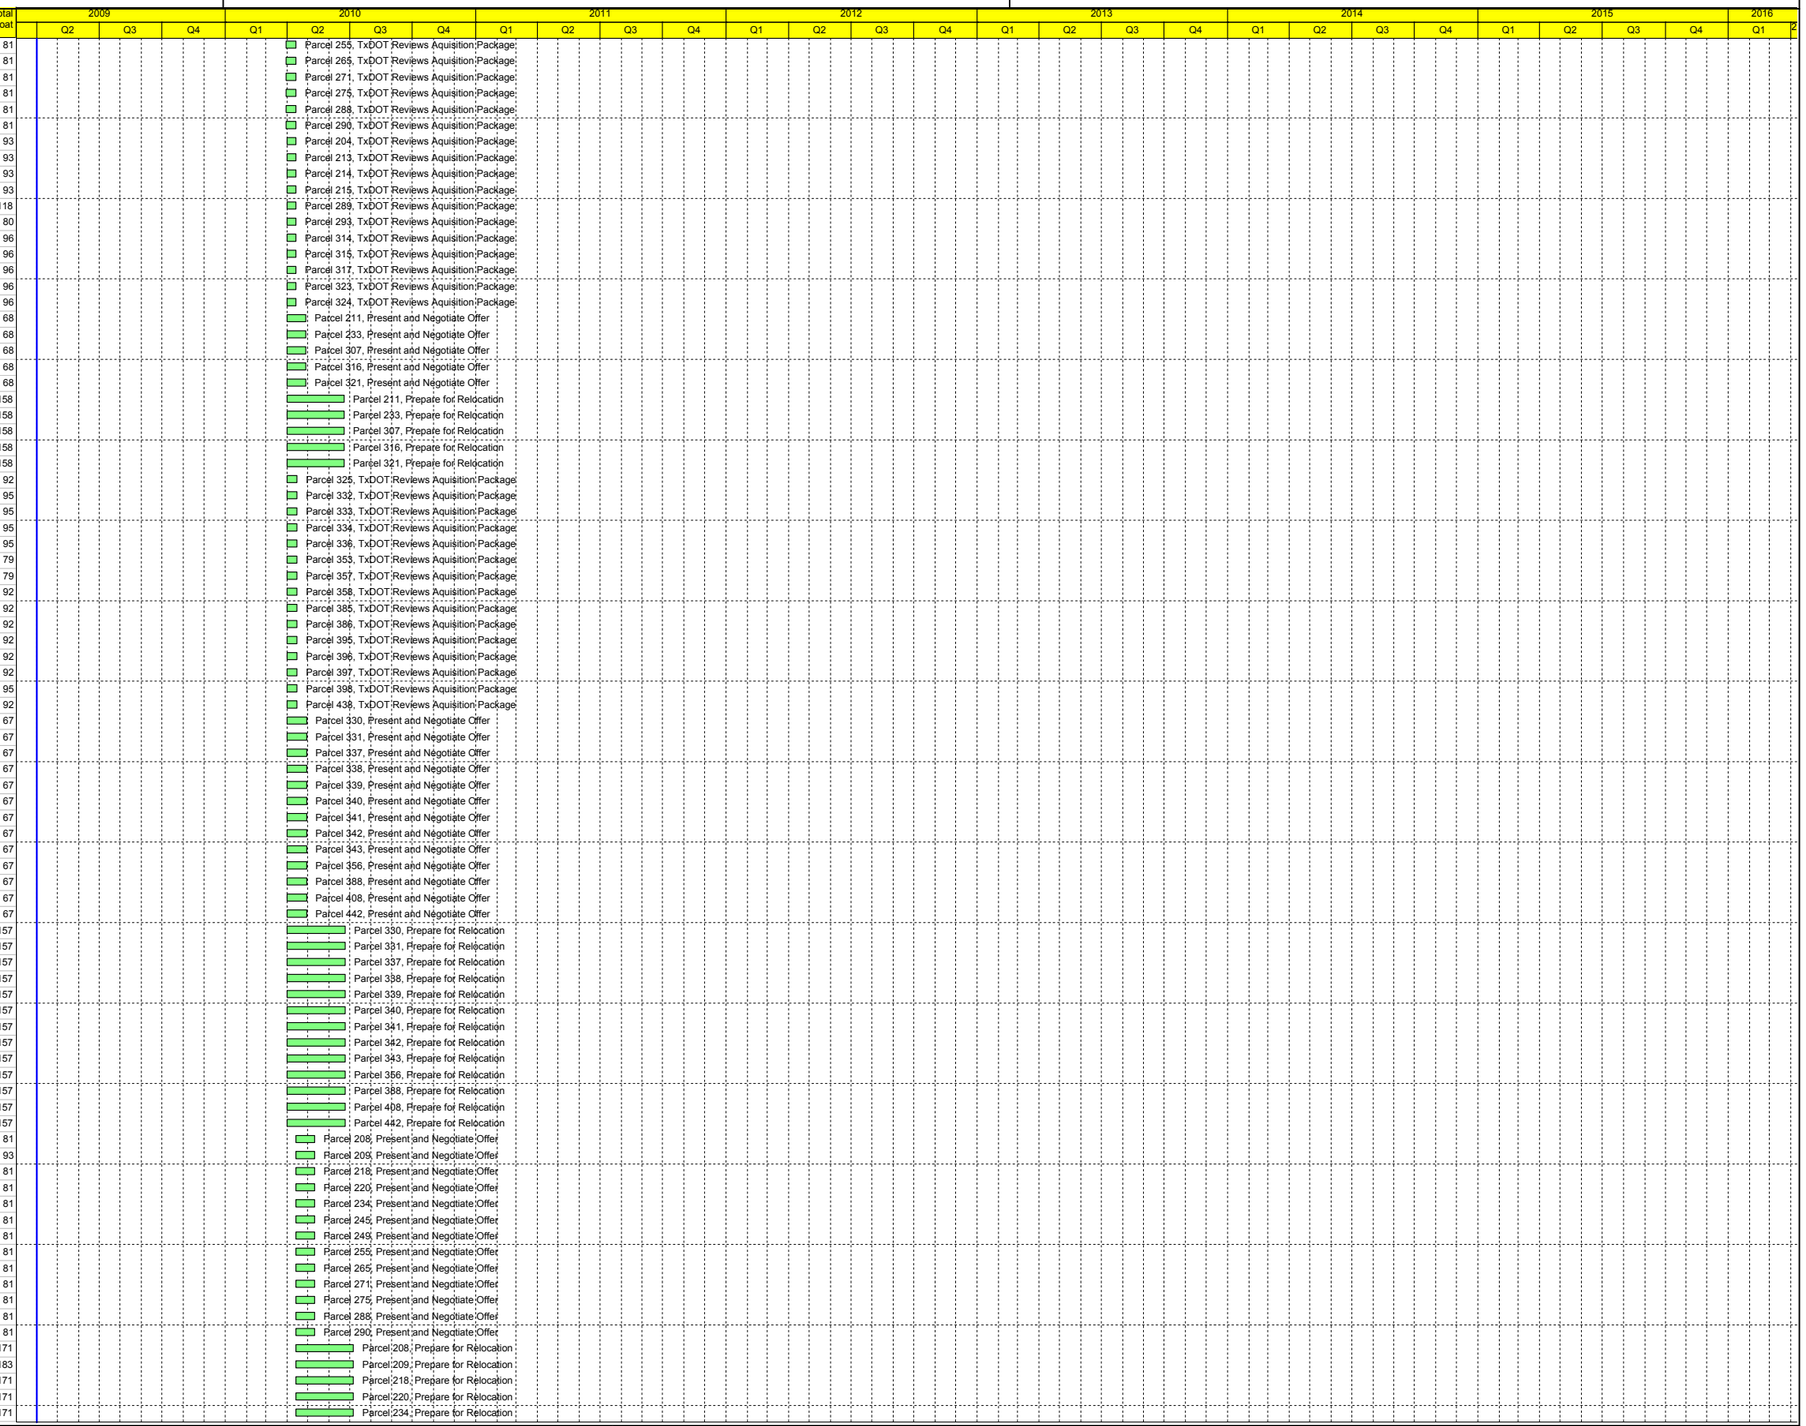

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.3.6	2CR0P2450R50	Parcel 245, Prepare for Relocation	60	13-Apr-10	06-Jul-10	171
1.3.6	2CR0P2490R50	Parcel 249, Prepare for Relocation	60	13-Apr-10	06-Jul-10	171
1.3.6	2CR0P2550R50	Parcel 255, Prepare for Relocation	60	13-Apr-10	06-Jul-10	171
1.3.6	2CR0P2650R50	Parcel 265, Prepare for Relocation	60	13-Apr-10	06-Jul-10	171
1.3.6	2CR0P2710R50	Parcel 271, Prepare for Relocation	60	13-Apr-10	06-Jul-10	171
1.3.6	2CR0P2750R50	Parcel 275, Prepare for Relocation	60	13-Apr-10	06-Jul-10	171
1.3.6	2CR0P2880R50	Parcel 288, Prepare for Relocation	60	13-Apr-10	06-Jul-10	171
1.3.6	2CR0P2900R50	Parcel 290, Prepare for Relocation	60	13-Apr-10	06-Jul-10	171
1.3.6	2CR0P2040R40	Parcel 204, Present and Negotiate Offer	20	14-Apr-10	12-May-10	93
1.3.6	2CR0P2130R40	Parcel 213, Present and Negotiate Offer	20	14-Apr-10	12-May-10	93
1.3.6	2CR0P2140R40	Parcel 214, Present and Negotiate Offer	20	14-Apr-10	12-May-10	93
1.3.6	2CR0P2150R40	Parcel 215, Present and Negotiate Offer	20	14-Apr-10	12-May-10	93
1.3.6	2CR0P2890R40	Parcel 289, Present and Negotiate Offer	20	14-Apr-10	12-May-10	118
1.3.6	2CR0P2930R40	Parcel 293, Present and Negotiate Offer	20	14-Apr-10	12-May-10	80
1.3.6	2CR0P3140R40	Parcel 314, Present and Negotiate Offer	20	14-Apr-10	12-May-10	96
1.3.6	2CR0P3150R40	Parcel 315, Present and Negotiate Offer	20	14-Apr-10	12-May-10	96
1.3.6	2CR0P3170R40	Parcel 317, Present and Negotiate Offer	20	14-Apr-10	12-May-10	96
1.3.6	2CR0P3230R40	Parcel 323, Present and Negotiate Offer	20	14-Apr-10	12-May-10	96
1.3.6	2CR0P3240R40	Parcel 324, Present and Negotiate Offer	20	14-Apr-10	12-May-10	96
1.3.6	2CR0P2040R50	Parcel 204, Prepare for Relocation	60	14-Apr-10	07-Jul-10	183
1.3.6	2CR0P2130R50	Parcel 213, Prepare for Relocation	60	14-Apr-10	07-Jul-10	183
1.3.6	2CR0P2140R50	Parcel 214, Prepare for Relocation	60	14-Apr-10	07-Jul-10	183
1.3.6	2CR0P2150R50	Parcel 215, Prepare for Relocation	60	14-Apr-10	07-Jul-10	183
1.3.6	2CR0P2890R50	Parcel 289, Prepare for Relocation	60	14-Apr-10	07-Jul-10	208
1.3.6	2CR0P2930R50	Parcel 293, Prepare for Relocation	60	14-Apr-10	07-Jul-10	170
1.3.6	2CR0P3140R50	Parcel 314, Prepare for Relocation	60	14-Apr-10	07-Jul-10	186
1.3.6	2CR0P3150R50	Parcel 315, Prepare for Relocation	60	14-Apr-10	07-Jul-10	186
1.3.6	2CR0P3170R50	Parcel 317, Prepare for Relocation	60	14-Apr-10	07-Jul-10	186
1.3.6	2CR0P3230R50	Parcel 323, Prepare for Relocation	60	14-Apr-10	07-Jul-10	186
1.3.6	2CR0P3240R50	Parcel 324, Prepare for Relocation	60	14-Apr-10	07-Jul-10	186
1.3.6	2CR0P3250R40	Parcel 325, Present and Negotiate Offer	20	15-Apr-10	13-May-10	92
1.3.6	2CR0P3320R40	Parcel 332, Present and Negotiate Offer	20	15-Apr-10	13-May-10	95
1.3.6	2CR0P3330R40	Parcel 333, Present and Negotiate Offer	20	15-Apr-10	13-May-10	95
1.3.6	2CR0P3340R40	Parcel 334, Present and Negotiate Offer	20	15-Apr-10	13-May-10	95
1.3.6	2CR0P3360R40	Parcel 336, Present and Negotiate Offer	20	15-Apr-10	13-May-10	95
1.3.6	2CR0P3530R40	Parcel 353, Present and Negotiate Offer	20	15-Apr-10	13-May-10	79
1.3.6	2CR0P3570R40	Parcel 357, Present and Negotiate Offer	20	15-Apr-10	13-May-10	79
1.3.6	2CR0P3580R40	Parcel 358, Present and Negotiate Offer	20	15-Apr-10	13-May-10	92
1.3.6	2CR0P3850R40	Parcel 385, Present and Negotiate Offer	20	15-Apr-10	13-May-10	92
1.3.6	2CR0P3860R40	Parcel 386, Present and Negotiate Offer	20	15-Apr-10	13-May-10	92
1.3.6	2CR0P3950R40	Parcel 395, Present and Negotiate Offer	20	15-Apr-10	13-May-10	92
1.3.6	2CR0P3960R40	Parcel 396, Present and Negotiate Offer	20	15-Apr-10	13-May-10	92
1.3.6	2CR0P3970R40	Parcel 397, Present and Negotiate Offer	20	15-Apr-10	13-May-10	92
1.3.6	2CR0P3980R40	Parcel 398, Present and Negotiate Offer	20	15-Apr-10	13-May-10	95
1.3.6	2CR0P4380R40	Parcel 438, Present and Negotiate Offer	20	15-Apr-10	13-May-10	92
1.3.6	2CR0P3250R50	Parcel 325, Prepare for Relocation	60	15-Apr-10	08-Jul-10	182
1.3.6	2CR0P3320R50	Parcel 332, Prepare for Relocation	60	15-Apr-10	08-Jul-10	185
1.3.6	2CR0P3330R50	Parcel 333, Prepare for Relocation	60	15-Apr-10	08-Jul-10	185
1.3.6	2CR0P3340R50	Parcel 334, Prepare for Relocation	60	15-Apr-10	08-Jul-10	185
1.3.6	2CR0P3360R50	Parcel 336, Prepare for Relocation	60	15-Apr-10	08-Jul-10	185
1.3.6	2CR0P3530R50	Parcel 353, Prepare for Relocation	60	15-Apr-10	08-Jul-10	169
1.3.6	2CR0P3570R50	Parcel 357, Prepare for Relocation	60	15-Apr-10	08-Jul-10	169
1.3.6	2CR0P3580R50	Parcel 358, Prepare for Relocation	60	15-Apr-10	08-Jul-10	182
1.3.6	2CR0P3850R50	Parcel 385, Prepare for Relocation	60	15-Apr-10	08-Jul-10	182
1.3.6	2CR0P3860R50	Parcel 386, Prepare for Relocation	60	15-Apr-10	08-Jul-10	182
1.3.6	2CR0P3950R50	Parcel 395, Prepare for Relocation	60	15-Apr-10	08-Jul-10	182
1.3.6	2CR0P3960R50	Parcel 396, Prepare for Relocation	60	15-Apr-10	08-Jul-10	182
1.3.6	2CR0P3970R50	Parcel 397, Prepare for Relocation	60	15-Apr-10	08-Jul-10	182
1.3.6	2CR0P3980R50	Parcel 398, Prepare for Relocation	60	15-Apr-10	08-Jul-10	185
1.3.6	2CR0P4380R50	Parcel 438, Prepare for Relocation	60	15-Apr-10	08-Jul-10	182
1.3.6	2CR0P2110R60	Parcel 211, Condemnation Process (if requir...	130	28-Apr-10	27-Oct-10	68
1.3.6	2CR0P2330R60	Parcel 233, Condemnation Process (if requir...	130	28-Apr-10	27-Oct-10	68
1.3.6	2CR0P3070R60	Parcel 307, Condemnation Process (if requir...	130	28-Apr-10	27-Oct-10	68
1.3.6	2CR0P3160R60	Parcel 316, Condemnation Process (if requir...	130	28-Apr-10	27-Oct-10	68
1.3.6	2CR0P3210R60	Parcel 321, Condemnation Process (if requir...	130	28-Apr-10	27-Oct-10	68
1.3.6	2CR0P3300R60	Parcel 330, Condemnation Process (if requir...	130	29-Apr-10	28-Oct-10	67
1.3.6	2CR0P3310R60	Parcel 331, Condemnation Process (if requir...	130	29-Apr-10	28-Oct-10	67
1.3.6	2CR0P3370R60	Parcel 337, Condemnation Process (if requir...	130	29-Apr-10	28-Oct-10	67
1.3.6	2CR0P3380R60	Parcel 338, Condemnation Process (if requir...	130	29-Apr-10	28-Oct-10	67
1.3.6	2CR0P3390R60	Parcel 339, Condemnation Process (if requir...	130	29-Apr-10	28-Oct-10	67
1.3.6	2CR0P3400R60	Parcel 340, Condemnation Process (if requir...	130	29-Apr-10	28-Oct-10	67
1.3.6	2CR0P3410R60	Parcel 341, Condemnation Process (if requir...	130	29-Apr-10	28-Oct-10	67
1.3.6	2CR0P3420R60	Parcel 342, Condemnation Process (if requir...	130	29-Apr-10	28-Oct-10	67
1.3.6	2CR0P3430R60	Parcel 343, Condemnation Process (if requir...	130	29-Apr-10	28-Oct-10	67
1.3.6	2CR0P3560R60	Parcel 356, Condemnation Process (if requir...	130	29-Apr-10	28-Oct-10	67
1.3.6	2CR0P3880R60	Parcel 388, Condemnation Process (if requir...	130	29-Apr-10	28-Oct-10	67
1.3.6	2CR0P4080R60	Parcel 408, Condemnation Process (if requir...	130	29-Apr-10	28-Oct-10	67
1.3.6	2CR0P4420R60	Parcel 442, Condemnation Process (if requir...	130	29-Apr-10	28-Oct-10	67
1.3.6	2CR0P2160R30	Parcel 216, TxDOT Reviews Aquisition Pack...	10	10-May...	24-May-10	68
1.3.6	2CR0P2080R60	Parcel 208, Condemnation Process (if requir...	130	11-May...	09-Nov-10	81
1.3.6	2CR0P2090R60	Parcel 209, Condemnation Process (if requir...	130	11-May...	09-Nov-10	93
1.3.6	2CR0P2180R60	Parcel 218, Condemnation Process (if requir...	130	11-May...	09-Nov-10	81
1.3.6	2CR0P2200R60	Parcel 220, Condemnation Process (if requir...	130	11-May...	09-Nov-10	81
1.3.6	2CR0P2340R60	Parcel 234, Condemnation Process (if requir...	130	11-May...	09-Nov-10	81
1.3.6	2CR0P2450R60	Parcel 245, Condemnation Process (if requir...	130	11-May...	09-Nov-10	81
1.3.6	2CR0P2490R60	Parcel 249, Condemnation Process (if requir...	130	11-May...	09-Nov-10	81

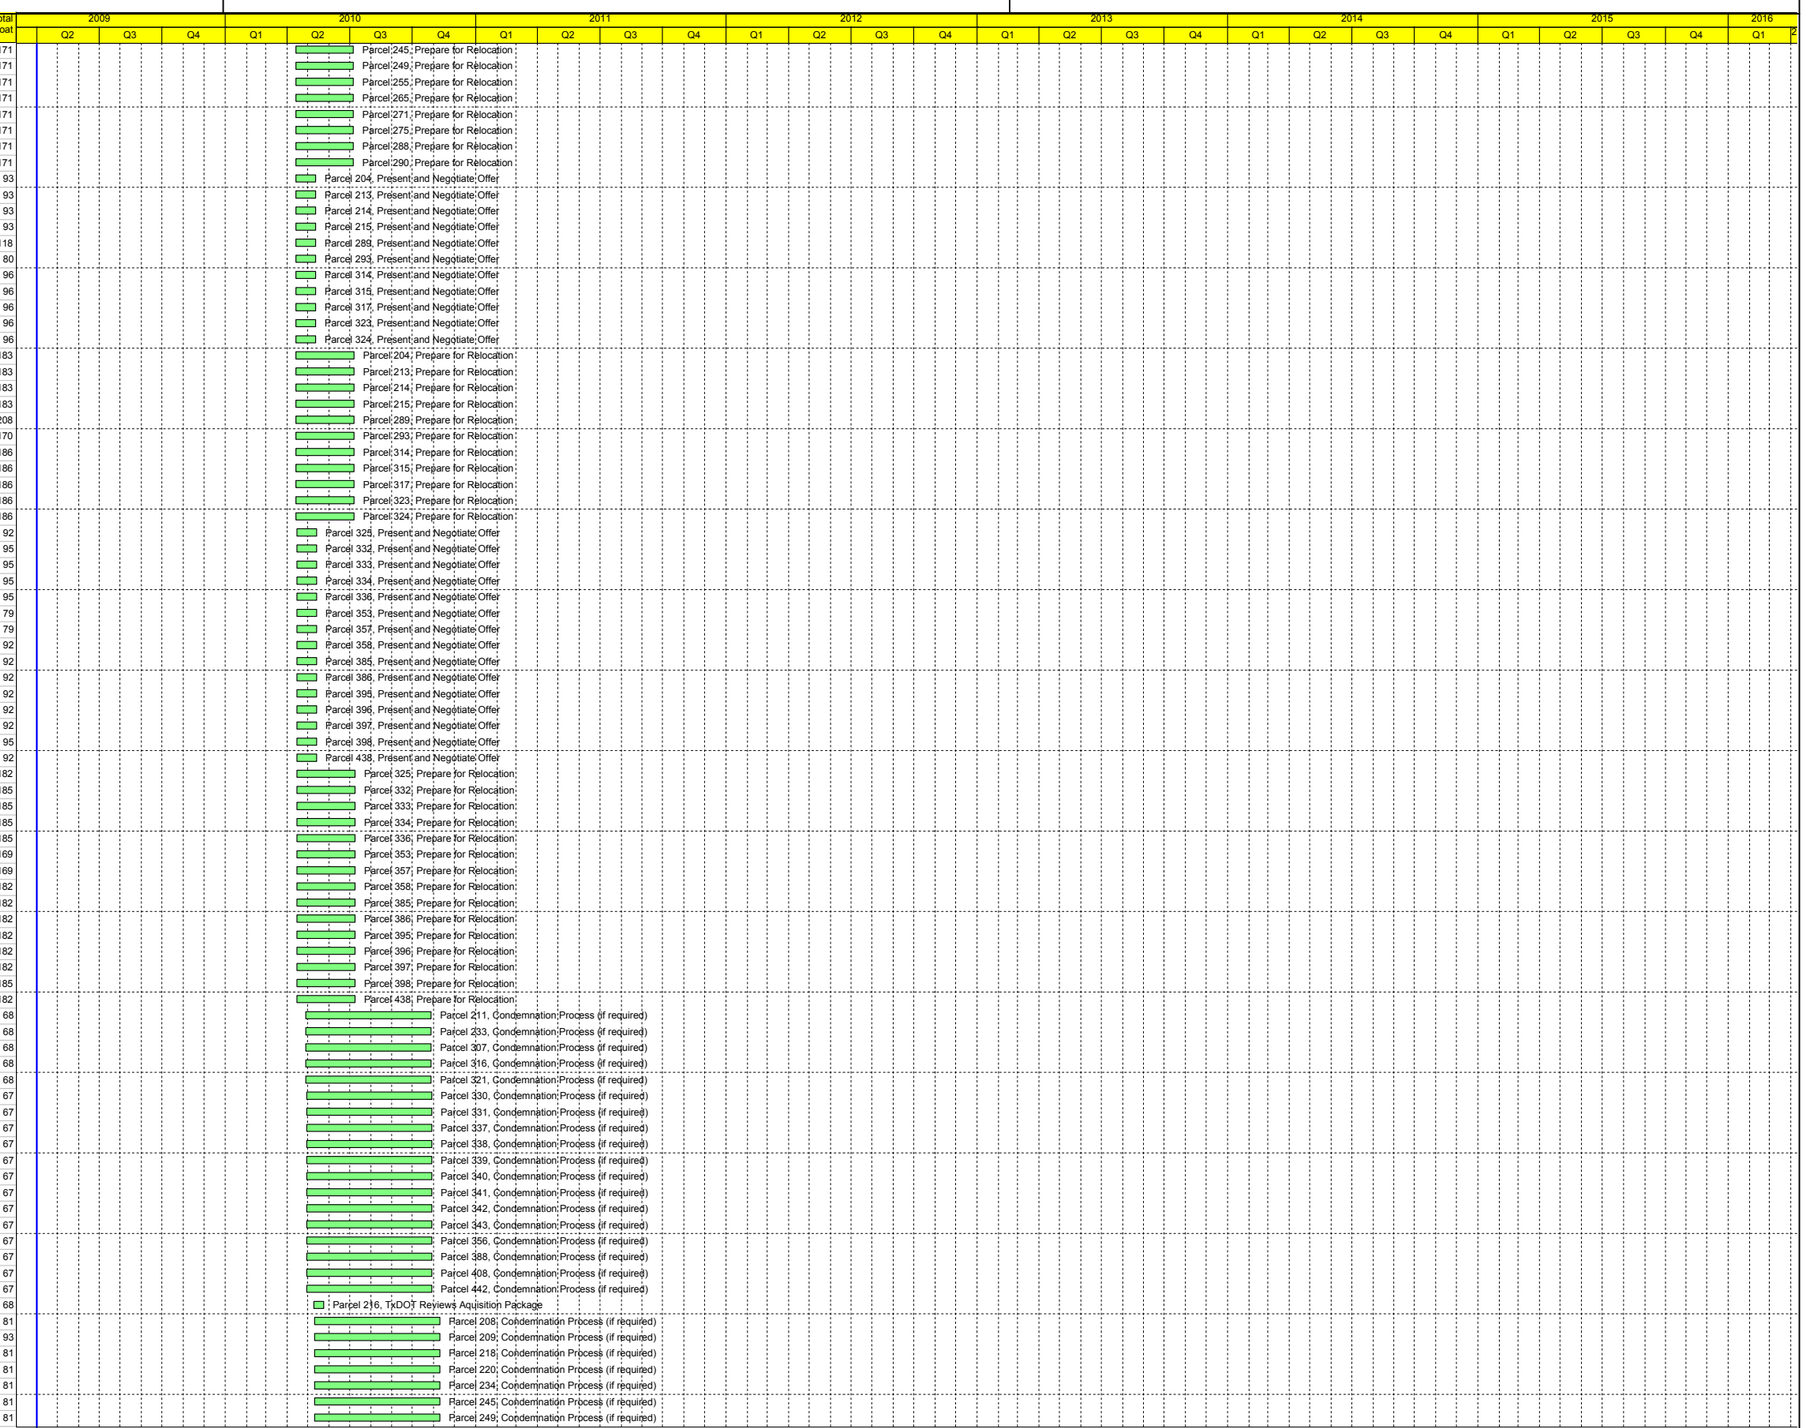

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.3.6	2CR0P2550R60	Parcel 255, Condemnation Process (if requir...	130	11-May...	09-Nov-10	81
1.3.6	2CR0P2650R60	Parcel 265, Condemnation Process (if requir...	130	11-May...	09-Nov-10	81
1.3.6	2CR0P2710R60	Parcel 271, Condemnation Process (if requir...	130	11-May...	09-Nov-10	81
1.3.6	2CR0P2750R60	Parcel 275, Condemnation Process (if requir...	130	11-May...	09-Nov-10	81
1.3.6	2CR0P2880R60	Parcel 288, Condemnation Process (if requir...	130	11-May...	09-Nov-10	81
1.3.6	2CR0P2900R60	Parcel 290, Condemnation Process (if requir...	130	11-May...	09-Nov-10	81
1.3.6	2CR0P2010R30	Parcel 201, TxDOT Reviews Aquisition Pack...	10	12-May...	26-May-10	68
1.3.6	2CR0P2170R30	Parcel 217, TxDOT Reviews Aquisition Pack...	10	12-May...	26-May-10	68
1.3.6	2CR0P2260R30	Parcel 226, TxDOT Reviews Aquisition Pack...	10	12-May...	26-May-10	68
1.3.6	2CR0P2270R30	Parcel 227, TxDOT Reviews Aquisition Pack...	10	12-May...	26-May-10	68
1.3.6	2CR0P2280R30	Parcel 228, TxDOT Reviews Aquisition Pack...	10	12-May...	26-May-10	68
1.3.6	2CR0P2290R30	Parcel 229, TxDOT Reviews Aquisition Pack...	10	12-May...	26-May-10	68
1.3.6	2CR0P2300R30	Parcel 230, TxDOT Reviews Aquisition Pack...	10	12-May...	26-May-10	68
1.3.6	2CR0P2320R30	Parcel 232, TxDOT Reviews Aquisition Pack...	10	12-May...	26-May-10	68
1.3.6	2CR0P3050R30	Parcel 305, TxDOT Reviews Aquisition Pack...	10	12-May...	26-May-10	68
1.3.6	2CR0P3190R30	Parcel 319, TxDOT Reviews Aquisition Pack...	10	12-May...	26-May-10	68
1.3.6	2CR0P3260R30	Parcel 326, TxDOT Reviews Aquisition Pack...	10	12-May...	26-May-10	68
1.3.6	2CR0P3280R30	Parcel 328, TxDOT Reviews Aquisition Pack...	10	12-May...	26-May-10	68
1.3.6	2CR0P3440R30	Parcel 344, TxDOT Reviews Aquisition Pack...	10	12-May...	26-May-10	68
1.3.6	2CR0P3450R30	Parcel 345, TxDOT Reviews Aquisition Pack...	10	12-May...	26-May-10	68
1.3.6	2CR0P3470R30	Parcel 347, TxDOT Reviews Aquisition Pack...	10	12-May...	26-May-10	68
1.3.6	2CR0P3480R30	Parcel 348, TxDOT Reviews Aquisition Pack...	10	12-May...	26-May-10	68
1.3.6	2CR0P3500R30	Parcel 350, TxDOT Reviews Aquisition Pack...	10	12-May...	26-May-10	68
1.3.6	2CR0P3650R30	Parcel 365, TxDOT Reviews Aquisition Pack...	10	12-May...	26-May-10	68
1.3.6	2CR0P3680R30	Parcel 368, TxDOT Reviews Aquisition Pack...	10	12-May...	26-May-10	68
1.3.6	2CR0P3710R30	Parcel 371, TxDOT Reviews Aquisition Pack...	10	12-May...	26-May-10	68
1.3.6	2CR0P3720R30	Parcel 372, TxDOT Reviews Aquisition Pack...	10	12-May...	26-May-10	68
1.3.6	2CR0P3730R30	Parcel 373, TxDOT Reviews Aquisition Pack...	10	12-May...	26-May-10	68
1.3.6	2CR0P3740R30	Parcel 374, TxDOT Reviews Aquisition Pack...	10	12-May...	26-May-10	68
1.3.6	2CR0P3750R30	Parcel 375, TxDOT Reviews Aquisition Pack...	10	12-May...	26-May-10	68
1.3.6	2CR0P3760R30	Parcel 376, TxDOT Reviews Aquisition Pack...	10	12-May...	26-May-10	68
1.3.6	2CR0P3770R30	Parcel 377, TxDOT Reviews Aquisition Pack...	10	12-May...	26-May-10	68
1.3.6	2CR0P3780R30	Parcel 378, TxDOT Reviews Aquisition Pack...	10	12-May...	26-May-10	68
1.3.6	2CR0P3790R30	Parcel 379, TxDOT Reviews Aquisition Pack...	10	12-May...	26-May-10	68
1.3.6	2CR0P3800R30	Parcel 380, TxDOT Reviews Aquisition Pack...	10	12-May...	26-May-10	68
1.3.6	2CR0P3830R30	Parcel 383, TxDOT Reviews Aquisition Pack...	10	12-May...	26-May-10	68
1.3.6	2CR0P4310R30	Parcel 431, TxDOT Reviews Aquisition Pack...	10	12-May...	26-May-10	68
1.3.6	2CR0P4390R30	Parcel 439, TxDOT Reviews Aquisition Pack...	10	12-May...	26-May-10	68
1.3.6	2CR0P4400R30	Parcel 440, TxDOT Reviews Aquisition Pack...	10	12-May...	26-May-10	68
1.3.6	2CR0P4410R30	Parcel 441, TxDOT Reviews Aquisition Pack...	10	12-May...	26-May-10	68
1.3.6	2CR0P2040R60	Parcel 204, Condemnation Process (if requir...	130	12-May...	10-Nov-10	93
1.3.6	2CR0P2130R60	Parcel 213, Condemnation Process (if requir...	130	12-May...	10-Nov-10	93
1.3.6	2CR0P2140R60	Parcel 214, Condemnation Process (if requir...	130	12-May...	10-Nov-10	93
1.3.6	2CR0P2150R60	Parcel 215, Condemnation Process (if requir...	130	12-May...	10-Nov-10	93
1.3.6	2CR0P2890R60	Parcel 289, Condemnation Process (if requir...	130	12-May...	10-Nov-10	118
1.3.6	2CR0P2930R60	Parcel 293, Condemnation Process (if requir...	130	12-May...	10-Nov-10	80
1.3.6	2CR0P3140R60	Parcel 314, Condemnation Process (if requir...	130	12-May...	10-Nov-10	96
1.3.6	2CR0P3150R60	Parcel 315, Condemnation Process (if requir...	130	12-May...	10-Nov-10	96
1.3.6	2CR0P3170R60	Parcel 317, Condemnation Process (if requir...	130	12-May...	10-Nov-10	96
1.3.6	2CR0P3230R60	Parcel 323, Condemnation Process (if requir...	130	12-May...	10-Nov-10	96
1.3.6	2CR0P3240R60	Parcel 324, Condemnation Process (if requir...	130	12-May...	10-Nov-10	96
1.3.6	2CR0P4020R30	Parcel 402, TxDOT Reviews Aquisition Pack...	10	13-May...	27-May-10	67
1.3.6	2CR0P4030R30	Parcel 403, TxDOT Reviews Aquisition Pack...	10	13-May...	27-May-10	67
1.3.6	2CR0P4060R30	Parcel 406, TxDOT Reviews Aquisition Pack...	10	13-May...	27-May-10	67
1.3.6	2CR0P4070R30	Parcel 407, TxDOT Reviews Aquisition Pack...	10	13-May...	27-May-10	67
1.3.6	2CR0P4130R30	Parcel 413, TxDOT Reviews Aquisition Pack...	10	13-May...	27-May-10	67
1.3.6	2CR0P4140R30	Parcel 414, TxDOT Reviews Aquisition Pack...	10	13-May...	27-May-10	67
1.3.6	2CR0P4150R30	Parcel 415, TxDOT Reviews Aquisition Pack...	10	13-May...	27-May-10	67
1.3.6	2CR0P3250R60	Parcel 325, Condemnation Process (if requir...	130	13-May...	11-Nov-10	92
1.3.6	2CR0P3320R60	Parcel 332, Condemnation Process (if requir...	130	13-May...	11-Nov-10	95
1.3.6	2CR0P3330R60	Parcel 333, Condemnation Process (if requir...	130	13-May...	11-Nov-10	95
1.3.6	2CR0P3340R60	Parcel 334, Condemnation Process (if requir...	130	13-May...	11-Nov-10	95
1.3.6	2CR0P3360R60	Parcel 336, Condemnation Process (if requir...	130	13-May...	11-Nov-10	95
1.3.6	2CR0P3530R60	Parcel 353, Condemnation Process (if requir...	130	13-May...	11-Nov-10	79
1.3.6	2CR0P3570R60	Parcel 357, Condemnation Process (if requir...	130	13-May...	11-Nov-10	79
1.3.6	2CR0P3580R60	Parcel 358, Condemnation Process (if requir...	130	13-May...	11-Nov-10	92
1.3.6	2CR0P3850R60	Parcel 385, Condemnation Process (if requir...	130	13-May...	11-Nov-10	92
1.3.6	2CR0P3860R60	Parcel 386, Condemnation Process (if requir...	130	13-May...	11-Nov-10	92
1.3.6	2CR0P3950R60	Parcel 395, Condemnation Process (if requir...	130	13-May...	11-Nov-10	92
1.3.6	2CR0P3960R60	Parcel 396, Condemnation Process (if requir...	130	13-May...	11-Nov-10	92
1.3.6	2CR0P3970R60	Parcel 397, Condemnation Process (if requir...	130	13-May...	11-Nov-10	92
1.3.6	2CR0P3980R60	Parcel 398, Condemnation Process (if requir...	130	13-May...	11-Nov-10	95
1.3.6	2CR0P4380R60	Parcel 438, Condemnation Process (if requir...	130	13-May...	11-Nov-10	92
1.3.6	2CR0P2160R40	Parcel 216, Present and Negotiate Offer	20	24-May...	21-Jun-10	68
1.3.6	2CR0P2160R50	Parcel 216, Prepare for Relocation	60	24-May...	16-Aug-10	158
1.3.6	2CR0P2310R30	Parcel 231, TxDOT Reviews Aquisition Pack...	10	25-May...	08-Jun-10	81
1.3.6	2CR0P2400R30	Parcel 240, TxDOT Reviews Aquisition Pack...	10	25-May...	08-Jun-10	81
1.3.6	2CR0P2410R30	Parcel 241, TxDOT Reviews Aquisition Pack...	10	25-May...	08-Jun-10	81
1.3.6	2CR0P2910R30	Parcel 291, TxDOT Reviews Aquisition Pack...	10	25-May...	08-Jun-10	81
1.3.6	2CR0P2920R30	Parcel 292, TxDOT Reviews Aquisition Pack...	10	25-May...	08-Jun-10	81
1.3.6	2CR0P2990R30	Parcel 299, TxDOT Reviews Aquisition Pack...	10	25-May...	08-Jun-10	81
1.3.6	2CR0P3550R30	Parcel 355, TxDOT Reviews Aquisition Pack...	10	25-May...	08-Jun-10	81
1.3.6	2CR0P3670R30	Parcel 367, TxDOT Reviews Aquisition Pack...	10	25-May...	08-Jun-10	81
1.3.6	2CR0P2020R30	Parcel 202, TxDOT Reviews Aquisition Pack...	10	26-May...	09-Jun-10	96
1.3.6	2CR0P2030R30	Parcel 203, TxDOT Reviews Aquisition Pack...	10	26-May...	09-Jun-10	96
1.3.6	2CR0P2070R30	Parcel 207, TxDOT Reviews Aquisition Pack...	10	26-May...	09-Jun-10	93

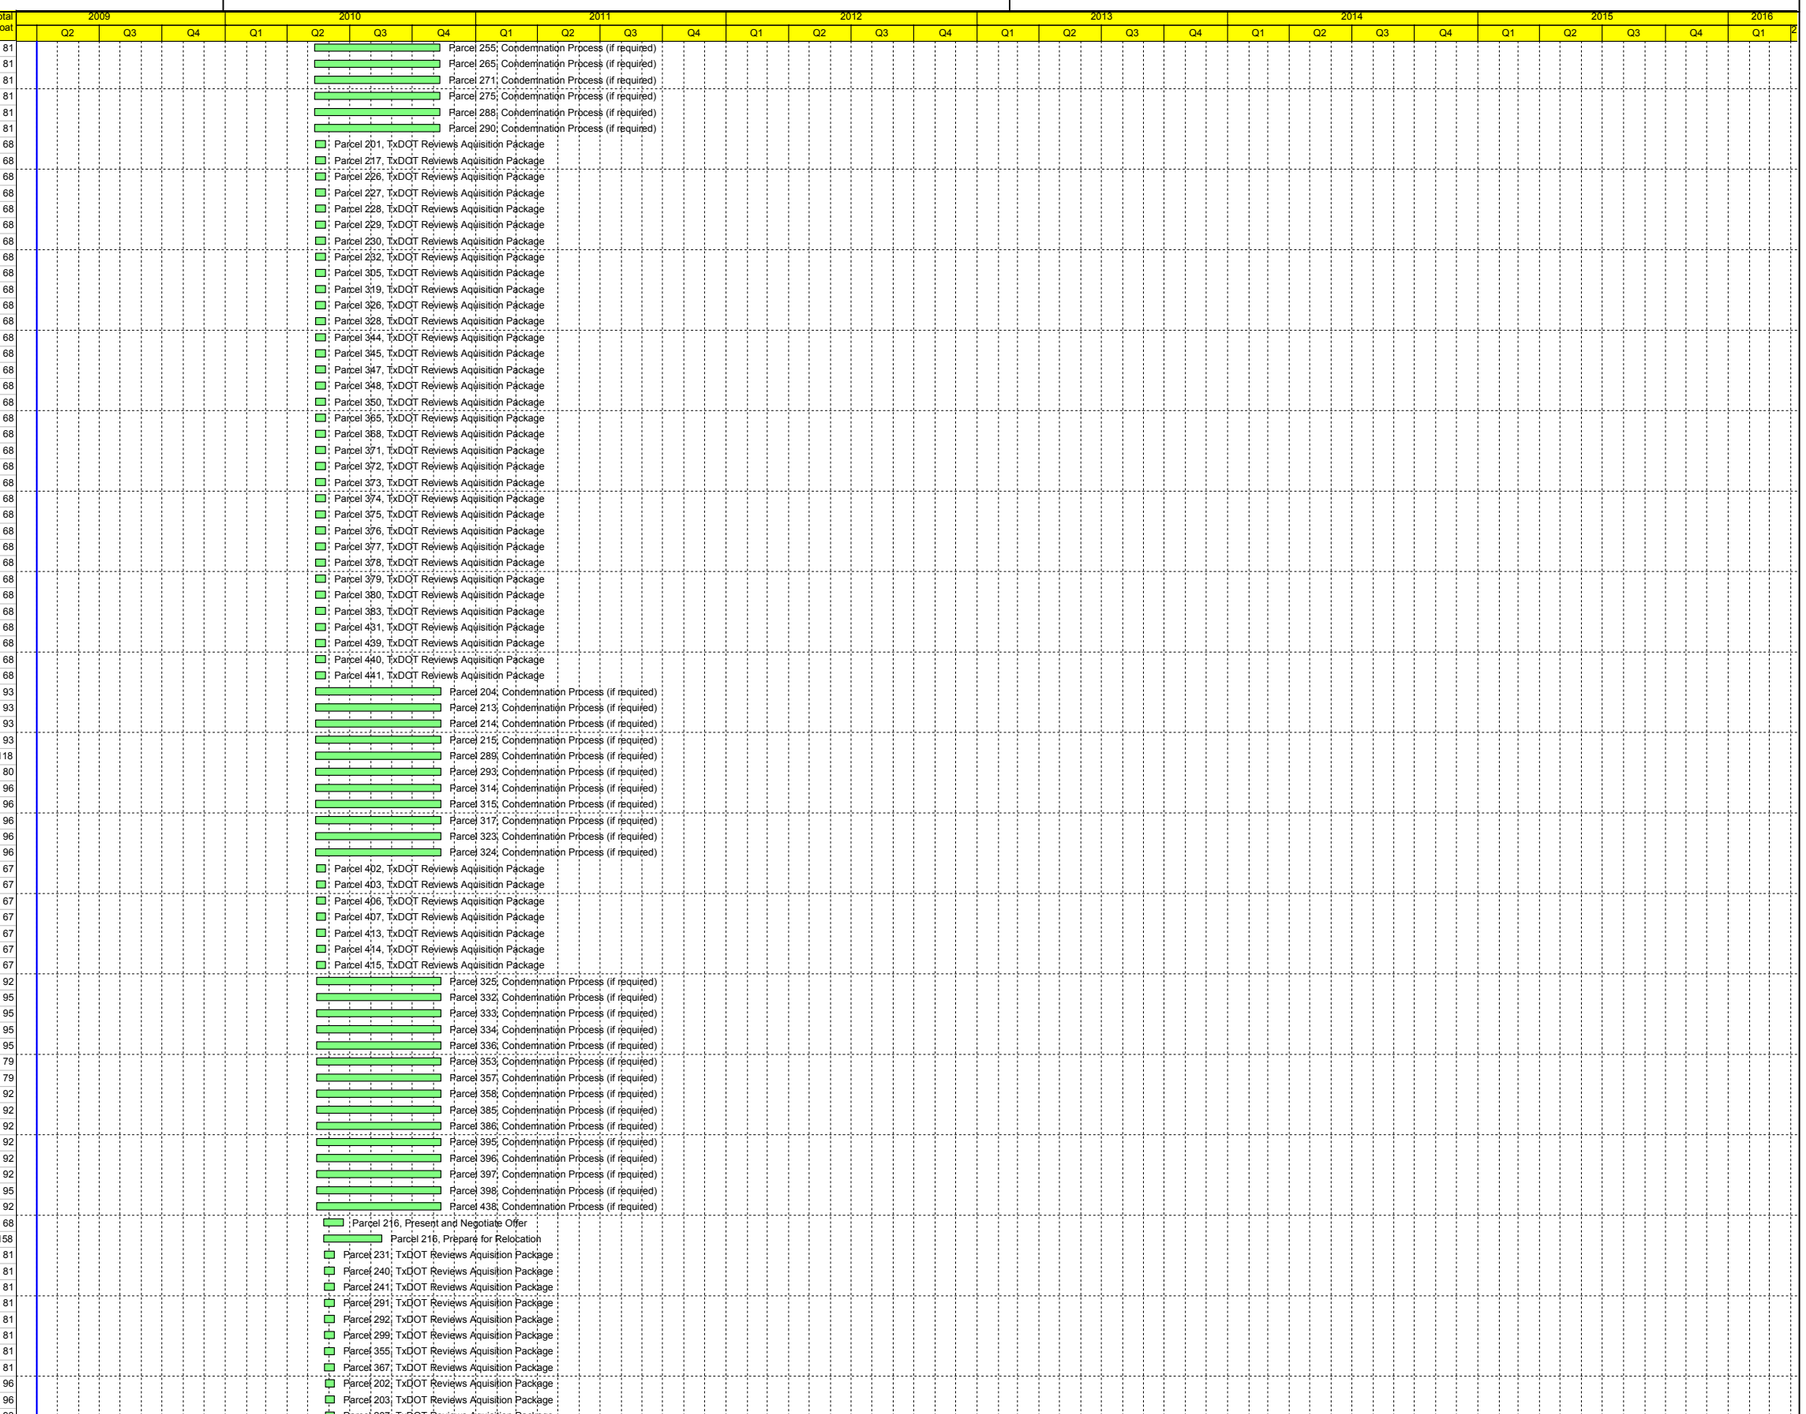

Remaining Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.3.6	2CR0P2250R30	Parcel 225, TxDOT Reviews Aquisition Pack...	10	26-May...	09-Jun-10	80
1.3.6	2CR0P3010R30	Parcel 301, TxDOT Reviews Aquisition Pack...	10	26-May...	09-Jun-10	96
1.3.6	2CR0P3020R30	Parcel 302, TxDOT Reviews Aquisition Pack...	10	26-May...	09-Jun-10	96
1.3.6	2CR0P3040R30	Parcel 304, TxDOT Reviews Aquisition Pack...	10	26-May...	09-Jun-10	80
1.3.6	2CR0P3060R30	Parcel 306, TxDOT Reviews Aquisition Pack...	10	26-May...	09-Jun-10	93
1.3.6	2CR0P3080R30	Parcel 308, TxDOT Reviews Aquisition Pack...	10	26-May...	09-Jun-10	96
1.3.6	2CR0P3180R30	Parcel 318, TxDOT Reviews Aquisition Pack...	10	26-May...	09-Jun-10	96
1.3.6	2CR0P3290R30	Parcel 329, TxDOT Reviews Aquisition Pack...	10	26-May...	09-Jun-10	96
1.3.6	2CR0P3350R30	Parcel 335, TxDOT Reviews Aquisition Pack...	10	26-May...	09-Jun-10	96
1.3.6	2CR0P3490R30	Parcel 349, TxDOT Reviews Aquisition Pack...	10	26-May...	09-Jun-10	93
1.3.6	2CR0P3510R30	Parcel 351, TxDOT Reviews Aquisition Pack...	10	26-May...	09-Jun-10	80
1.3.6	2CR0P3600R30	Parcel 360, TxDOT Reviews Aquisition Pack...	10	26-May...	09-Jun-10	93
1.3.6	2CR0P3610R30	Parcel 361, TxDOT Reviews Aquisition Pack...	10	26-May...	09-Jun-10	93
1.3.6	2CR0P3620R30	Parcel 362, TxDOT Reviews Aquisition Pack...	10	26-May...	09-Jun-10	93
1.3.6	2CR0P3630R30	Parcel 363, TxDOT Reviews Aquisition Pack...	10	26-May...	09-Jun-10	93
1.3.6	2CR0P3640R30	Parcel 364, TxDOT Reviews Aquisition Pack...	10	26-May...	09-Jun-10	93
1.3.6	2CR0P3810R30	Parcel 381, TxDOT Reviews Aquisition Pack...	10	26-May...	09-Jun-10	96
1.3.6	2CR0P3820R30	Parcel 382, TxDOT Reviews Aquisition Pack...	10	26-May...	09-Jun-10	96
1.3.6	2CR0P3840R30	Parcel 384, TxDOT Reviews Aquisition Pack...	10	26-May...	09-Jun-10	96
1.3.6	2CR0P3870R30	Parcel 387, TxDOT Reviews Aquisition Pack...	10	26-May...	09-Jun-10	93
1.3.6	2CR0P4320R30	Parcel 432, TxDOT Reviews Aquisition Pack...	10	26-May...	09-Jun-10	93
1.3.6	2CR0P4330R30	Parcel 433, TxDOT Reviews Aquisition Pack...	10	26-May...	09-Jun-10	93
1.3.6	2CR0P4340R30	Parcel 434, TxDOT Reviews Aquisition Pack...	10	26-May...	09-Jun-10	93
1.3.6	2CR0P4350R30	Parcel 435, TxDOT Reviews Aquisition Pack...	10	26-May...	09-Jun-10	93
1.3.6	2CR0P4360R30	Parcel 436, TxDOT Reviews Aquisition Pack...	10	26-May...	09-Jun-10	93
1.3.6	2CR0P4370R30	Parcel 437, TxDOT Reviews Aquisition Pack...	10	26-May...	09-Jun-10	93
1.3.6	2CR0P2010R40	Parcel 201, Present and Negotiate Offer	20	26-May...	23-Jun-10	68
1.3.6	2CR0P2170R40	Parcel 217, Present and Negotiate Offer	20	26-May...	23-Jun-10	68
1.3.6	2CR0P2260R40	Parcel 226, Present and Negotiate Offer	20	26-May...	23-Jun-10	68
1.3.6	2CR0P2270R40	Parcel 227, Present and Negotiate Offer	20	26-May...	23-Jun-10	68
1.3.6	2CR0P2280R40	Parcel 228, Present and Negotiate Offer	20	26-May...	23-Jun-10	68
1.3.6	2CR0P2290R40	Parcel 229, Present and Negotiate Offer	20	26-May...	23-Jun-10	68
1.3.6	2CR0P2300R40	Parcel 230, Present and Negotiate Offer	20	26-May...	23-Jun-10	68
1.3.6	2CR0P2320R40	Parcel 232, Present and Negotiate Offer	20	26-May...	23-Jun-10	68
1.3.6	2CR0P3050R40	Parcel 305, Present and Negotiate Offer	20	26-May...	23-Jun-10	68
1.3.6	2CR0P3190R40	Parcel 319, Present and Negotiate Offer	20	26-May...	23-Jun-10	68
1.3.6	2CR0P3260R40	Parcel 326, Present and Negotiate Offer	20	26-May...	23-Jun-10	68
1.3.6	2CR0P3280R40	Parcel 328, Present and Negotiate Offer	20	26-May...	23-Jun-10	68
1.3.6	2CR0P3440R40	Parcel 344, Present and Negotiate Offer	20	26-May...	23-Jun-10	68
1.3.6	2CR0P3450R40	Parcel 345, Present and Negotiate Offer	20	26-May...	23-Jun-10	68
1.3.6	2CR0P3470R40	Parcel 347, Present and Negotiate Offer	20	26-May...	23-Jun-10	68
1.3.6	2CR0P3480R40	Parcel 348, Present and Negotiate Offer	20	26-May...	23-Jun-10	68
1.3.6	2CR0P3500R40	Parcel 350, Present and Negotiate Offer	20	26-May...	23-Jun-10	68
1.3.6	2CR0P3650R40	Parcel 365, Present and Negotiate Offer	20	26-May...	23-Jun-10	68
1.3.6	2CR0P3680R40	Parcel 368, Present and Negotiate Offer	20	26-May...	23-Jun-10	68
1.3.6	2CR0P3710R40	Parcel 371, Present and Negotiate Offer	20	26-May...	23-Jun-10	68
1.3.6	2CR0P3720R40	Parcel 372, Present and Negotiate Offer	20	26-May...	23-Jun-10	68
1.3.6	2CR0P3730R40	Parcel 373, Present and Negotiate Offer	20	26-May...	23-Jun-10	68
1.3.6	2CR0P3740R40	Parcel 374, Present and Negotiate Offer	20	26-May...	23-Jun-10	68
1.3.6	2CR0P3750R40	Parcel 375, Present and Negotiate Offer	20	26-May...	23-Jun-10	68
1.3.6	2CR0P3760R40	Parcel 376, Present and Negotiate Offer	20	26-May...	23-Jun-10	68
1.3.6	2CR0P3770R40	Parcel 377, Present and Negotiate Offer	20	26-May...	23-Jun-10	68
1.3.6	2CR0P3780R40	Parcel 378, Present and Negotiate Offer	20	26-May...	23-Jun-10	68
1.3.6	2CR0P3790R40	Parcel 379, Present and Negotiate Offer	20	26-May...	23-Jun-10	68
1.3.6	2CR0P3800R40	Parcel 380, Present and Negotiate Offer	20	26-May...	23-Jun-10	68
1.3.6	2CR0P3830R40	Parcel 383, Present and Negotiate Offer	20	26-May...	23-Jun-10	68
1.3.6	2CR0P4310R40	Parcel 431, Present and Negotiate Offer	20	26-May...	23-Jun-10	68
1.3.6	2CR0P4390R40	Parcel 439, Present and Negotiate Offer	20	26-May...	23-Jun-10	68
1.3.6	2CR0P4400R40	Parcel 440, Present and Negotiate Offer	20	26-May...	23-Jun-10	68
1.3.6	2CR0P4410R40	Parcel 441, Present and Negotiate Offer	20	26-May...	23-Jun-10	68
1.3.6	2CR0P3990R30	Parcel 399, TxDOT Reviews Aquisition Pack...	10	27-May...	10-Jun-10	95
1.3.6	2CR0P4000R30	Parcel 400, TxDOT Reviews Aquisition Pack...	10	27-May...	10-Jun-10	95
1.3.6	2CR0P4040R30	Parcel 404, TxDOT Reviews Aquisition Pack...	10	27-May...	10-Jun-10	92
1.3.6	2CR0P4050R30	Parcel 405, TxDOT Reviews Aquisition Pack...	10	27-May...	10-Jun-10	92
1.3.6	2CR0P4110R30	Parcel 411, TxDOT Reviews Aquisition Pack...	10	27-May...	10-Jun-10	92
1.3.6	2CR0P4120R30	Parcel 412, TxDOT Reviews Aquisition Pack...	10	27-May...	10-Jun-10	92
1.3.6	2CR0P4020R40	Parcel 402, Present and Negotiate Offer	20	27-May...	24-Jun-10	67
1.3.6	2CR0P4030R40	Parcel 403, Present and Negotiate Offer	20	27-May...	24-Jun-10	67
1.3.6	2CR0P4060R40	Parcel 406, Present and Negotiate Offer	20	27-May...	24-Jun-10	67
1.3.6	2CR0P4070R40	Parcel 407, Present and Negotiate Offer	20	27-May...	24-Jun-10	67
1.3.6	2CR0P4130R40	Parcel 413, Present and Negotiate Offer	20	27-May...	24-Jun-10	67
1.3.6	2CR0P4140R40	Parcel 414, Present and Negotiate Offer	20	27-May...	24-Jun-10	67
1.3.6	2CR0P4150R40	Parcel 415, Present and Negotiate Offer	20	27-May...	24-Jun-10	67
1.3.6	2CR0P2350R30	Parcel 235, TxDOT Reviews Aquisition Pack...	10	01-Jun-10	15-Jun-10	68
1.3.6	2CR0P2310R40	Parcel 231, Present and Negotiate Offer	20	08-Jun-10	06-Jul-10	81
1.3.6	2CR0P2400R40	Parcel 240, Present and Negotiate Offer	20	08-Jun-10	06-Jul-10	81
1.3.6	2CR0P2410R40	Parcel 241, Present and Negotiate Offer	20	08-Jun-10	06-Jul-10	81
1.3.6	2CR0P2910R40	Parcel 291, Present and Negotiate Offer	20	08-Jun-10	06-Jul-10	81
1.3.6	2CR0P2920R40	Parcel 292, Present and Negotiate Offer	20	08-Jun-10	06-Jul-10	81
1.3.6	2CR0P2990R40	Parcel 299, Present and Negotiate Offer	20	08-Jun-10	06-Jul-10	81
1.3.6	2CR0P3550R40	Parcel 355, Present and Negotiate Offer	20	08-Jun-10	06-Jul-10	81
1.3.6	2CR0P3670R40	Parcel 367, Present and Negotiate Offer	20	08-Jun-10	06-Jul-10	81
1.3.6	2CR0P2020R40	Parcel 202, Present and Negotiate Offer	20	09-Jun-10	07-Jul-10	96
1.3.6	2CR0P2030R40	Parcel 203, Present and Negotiate Offer	20	09-Jun-10	07-Jul-10	96
1.3.6	2CR0P2070R40	Parcel 207, Present and Negotiate Offer	20	09-Jun-10	07-Jul-10	93
1.3.6	2CR0P2250R40	Parcel 225, Present and Negotiate Offer	20	09-Jun-10	07-Jul-10	80

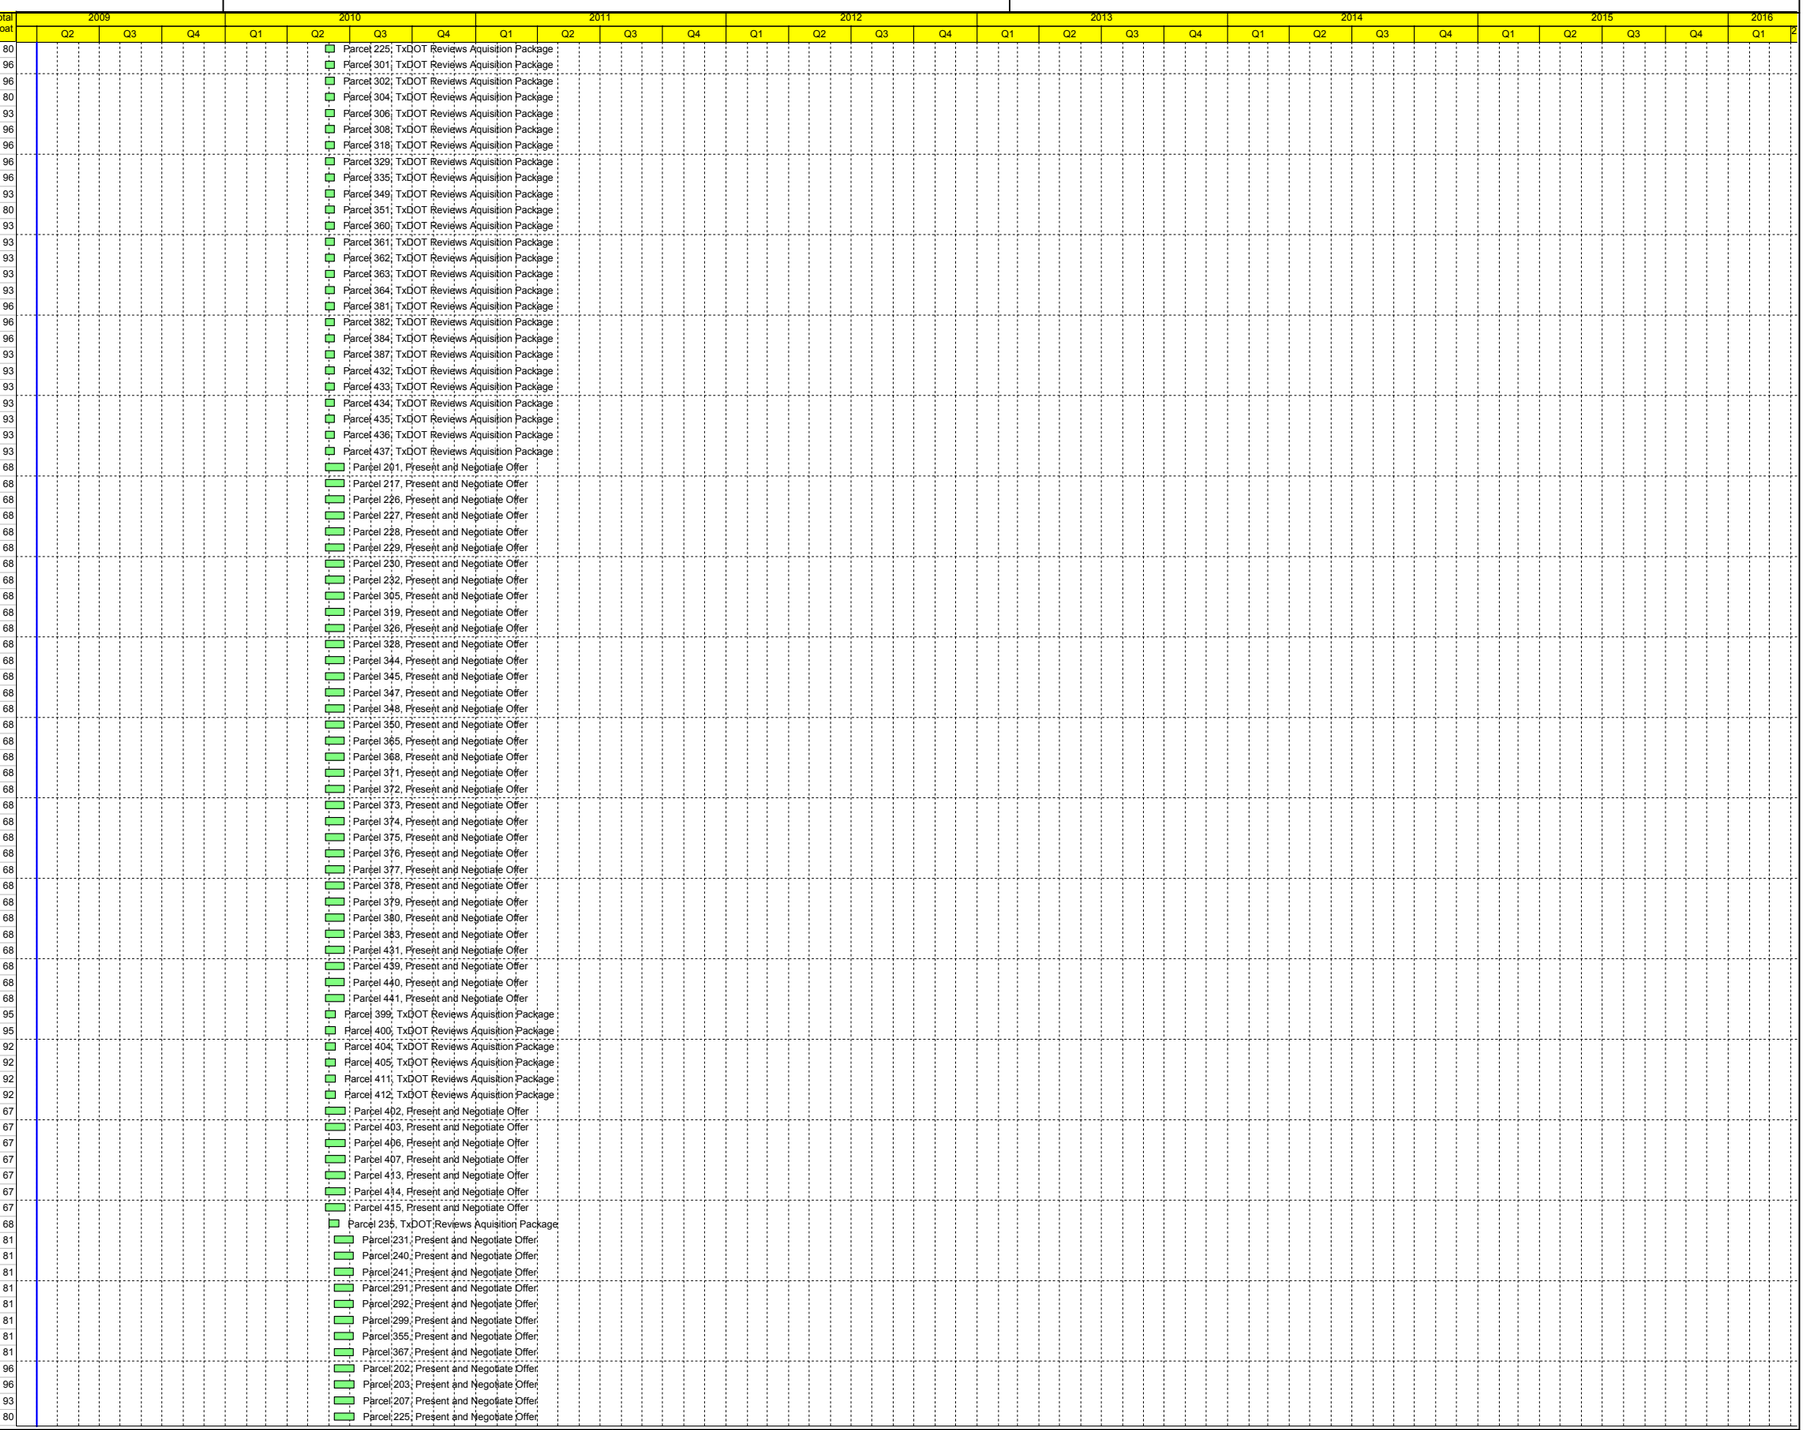

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.3.6	2CR0P3010R40	Parcel 301, Present and Negotiate Offer	20	09-Jun-10	07-Jul-10	96
1.3.6	2CR0P3020R40	Parcel 302, Present and Negotiate Offer	20	09-Jun-10	07-Jul-10	96
1.3.6	2CR0P3040R40	Parcel 304, Present and Negotiate Offer	20	09-Jun-10	07-Jul-10	80
1.3.6	2CR0P3060R40	Parcel 306, Present and Negotiate Offer	20	09-Jun-10	07-Jul-10	93
1.3.6	2CR0P3080R40	Parcel 308, Present and Negotiate Offer	20	09-Jun-10	07-Jul-10	96
1.3.6	2CR0P3180R40	Parcel 318, Present and Negotiate Offer	20	09-Jun-10	07-Jul-10	96
1.3.6	2CR0P3290R40	Parcel 329, Present and Negotiate Offer	20	09-Jun-10	07-Jul-10	96
1.3.6	2CR0P3350R40	Parcel 335, Present and Negotiate Offer	20	09-Jun-10	07-Jul-10	96
1.3.6	2CR0P3490R40	Parcel 349, Present and Negotiate Offer	20	09-Jun-10	07-Jul-10	93
1.3.6	2CR0P3510R40	Parcel 351, Present and Negotiate Offer	20	09-Jun-10	07-Jul-10	80
1.3.6	2CR0P3600R40	Parcel 360, Present and Negotiate Offer	20	09-Jun-10	07-Jul-10	93
1.3.6	2CR0P3610R40	Parcel 361, Present and Negotiate Offer	20	09-Jun-10	07-Jul-10	93
1.3.6	2CR0P3620R40	Parcel 362, Present and Negotiate Offer	20	09-Jun-10	07-Jul-10	93
1.3.6	2CR0P3630R40	Parcel 363, Present and Negotiate Offer	20	09-Jun-10	07-Jul-10	93
1.3.6	2CR0P3640R40	Parcel 364, Present and Negotiate Offer	20	09-Jun-10	07-Jul-10	93
1.3.6	2CR0P3810R40	Parcel 381, Present and Negotiate Offer	20	09-Jun-10	07-Jul-10	96
1.3.6	2CR0P3820R40	Parcel 382, Present and Negotiate Offer	20	09-Jun-10	07-Jul-10	96
1.3.6	2CR0P3840R40	Parcel 384, Present and Negotiate Offer	20	09-Jun-10	07-Jul-10	96
1.3.6	2CR0P3870R40	Parcel 387, Present and Negotiate Offer	20	09-Jun-10	07-Jul-10	93
1.3.6	2CR0P4320R40	Parcel 432, Present and Negotiate Offer	20	09-Jun-10	07-Jul-10	93
1.3.6	2CR0P4330R40	Parcel 433, Present and Negotiate Offer	20	09-Jun-10	07-Jul-10	93
1.3.6	2CR0P4340R40	Parcel 434, Present and Negotiate Offer	20	09-Jun-10	07-Jul-10	93
1.3.6	2CR0P4350R40	Parcel 435, Present and Negotiate Offer	20	09-Jun-10	07-Jul-10	93
1.3.6	2CR0P4360R40	Parcel 436, Present and Negotiate Offer	20	09-Jun-10	07-Jul-10	93
1.3.6	2CR0P4370R40	Parcel 437, Present and Negotiate Offer	20	09-Jun-10	07-Jul-10	93
1.3.6	2CR0P3990R40	Parcel 399, Present and Negotiate Offer	20	10-Jun-10	08-Jul-10	95
1.3.6	2CR0P4000R40	Parcel 400, Present and Negotiate Offer	20	10-Jun-10	08-Jul-10	95
1.3.6	2CR0P4040R40	Parcel 404, Present and Negotiate Offer	20	10-Jun-10	08-Jul-10	92
1.3.6	2CR0P4050R40	Parcel 405, Present and Negotiate Offer	20	10-Jun-10	08-Jul-10	92
1.3.6	2CR0P4110R40	Parcel 411, Present and Negotiate Offer	20	10-Jun-10	08-Jul-10	92
1.3.6	2CR0P4120R40	Parcel 412, Present and Negotiate Offer	20	10-Jun-10	08-Jul-10	92
1.3.6	2CR0P3030R30	Parcel 303, TxDOT Reviews Aquisition Pack...	10	11-Jun-10	25-Jun-10	68
1.3.6	2CR0P2350R40	Parcel 235, Present and Negotiate Offer	20	15-Jun-10	13-Jul-10	68
1.3.6	2CR0P2350R50	Parcel 235, Prepare for Relocation	60	15-Jun-10	07-Sep-10	158
1.3.6	2CR0P2000R30	Parcel 200, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	79
1.3.6	2CR0P2380R30	Parcel 238, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	148
1.3.6	2CR0P2390R30	Parcel 239, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	148
1.3.6	2CR0P2420R30	Parcel 242, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	198
1.3.6	2CR0P2540R30	Parcel 254, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	148
1.3.6	2CR0P2590R30	Parcel 259, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	148
1.3.6	2CR0P2600R30	Parcel 260, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	198
1.3.6	2CR0P3270R30	Parcel 327, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	198
1.3.6	2CR0P3520R30	Parcel 352, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	76
1.3.6	2CR0P3590R30	Parcel 359, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	148
1.3.6	2CR0P3660R30	Parcel 366, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	148
1.3.6	2CR0P3690R30	Parcel 369, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	198
1.3.6	2CR0P3890R30	Parcel 389, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	76
1.3.6	2CR0P3900R30	Parcel 390, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	76
1.3.6	2CR0P3910R30	Parcel 391, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	76
1.3.6	2CR0P3920R30	Parcel 392, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	76
1.3.6	2CR0P3930R30	Parcel 393, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	76
1.3.6	2CR0P3940R30	Parcel 394, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	76
1.3.6	2CR0P4010R30	Parcel 401, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	76
1.3.6	2CR0P4090R30	Parcel 409, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	198
1.3.6	2CR0P4100R30	Parcel 410, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	198
1.3.6	2CR0P4160R30	Parcel 416, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	198
1.3.6	2CR0P4170R30	Parcel 417, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	198
1.3.6	2CR0P4190R30	Parcel 419, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	198
1.3.6	2CR0P4220R30	Parcel 422, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	198
1.3.6	2CR0P4230R30	Parcel 423, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	198
1.3.6	2CR0P4240R30	Parcel 424, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	198
1.3.6	2CR0P4260R30	Parcel 426, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	198
1.3.6	2CR0P4270R30	Parcel 427, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	198
1.3.6	2CR0P4290R30	Parcel 429, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	198
1.3.6	2CR0P4300R30	Parcel 430, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	198
1.3.6	2CR0P4430R30	Parcel 443, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	148
1.3.6	2CR0P4440R30	Parcel 444, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	148
1.3.6	2CR0P4450R30	Parcel 445, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	148
1.3.6	2CR0P4460R30	Parcel 446, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	148
1.3.6	2CR0P4470R30	Parcel 447, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	148
1.3.6	2CR0P4490R30	Parcel 449, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	148
1.3.6	2CR0P4500R30	Parcel 450, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	148
1.3.6	2CR0P4510R30	Parcel 451, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	148
1.3.6	2CR0P2050R30	Parcel 205, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	108
1.3.6	2CR0P2100R30	Parcel 210, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	108
1.3.6	2CR0P2190R30	Parcel 219, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	108
1.3.6	2CR0P2230R30	Parcel 223, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	108
1.3.6	2CR0P2240R30	Parcel 224, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	108
1.3.6	2CR0P2360R30	Parcel 236, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	108
1.3.6	2CR0P2370R30	Parcel 237, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	108
1.3.6	2CR0P2500R30	Parcel 250, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	158
1.3.6	2CR0P2520R30	Parcel 252, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	158
1.3.6	2CR0P2530R30	Parcel 253, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	158
1.3.6	2CR0P2560R30	Parcel 256, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	108
1.3.6	2CR0P2570R30	Parcel 257, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	158
1.3.6	2CR0P2640R30	Parcel 264, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	158

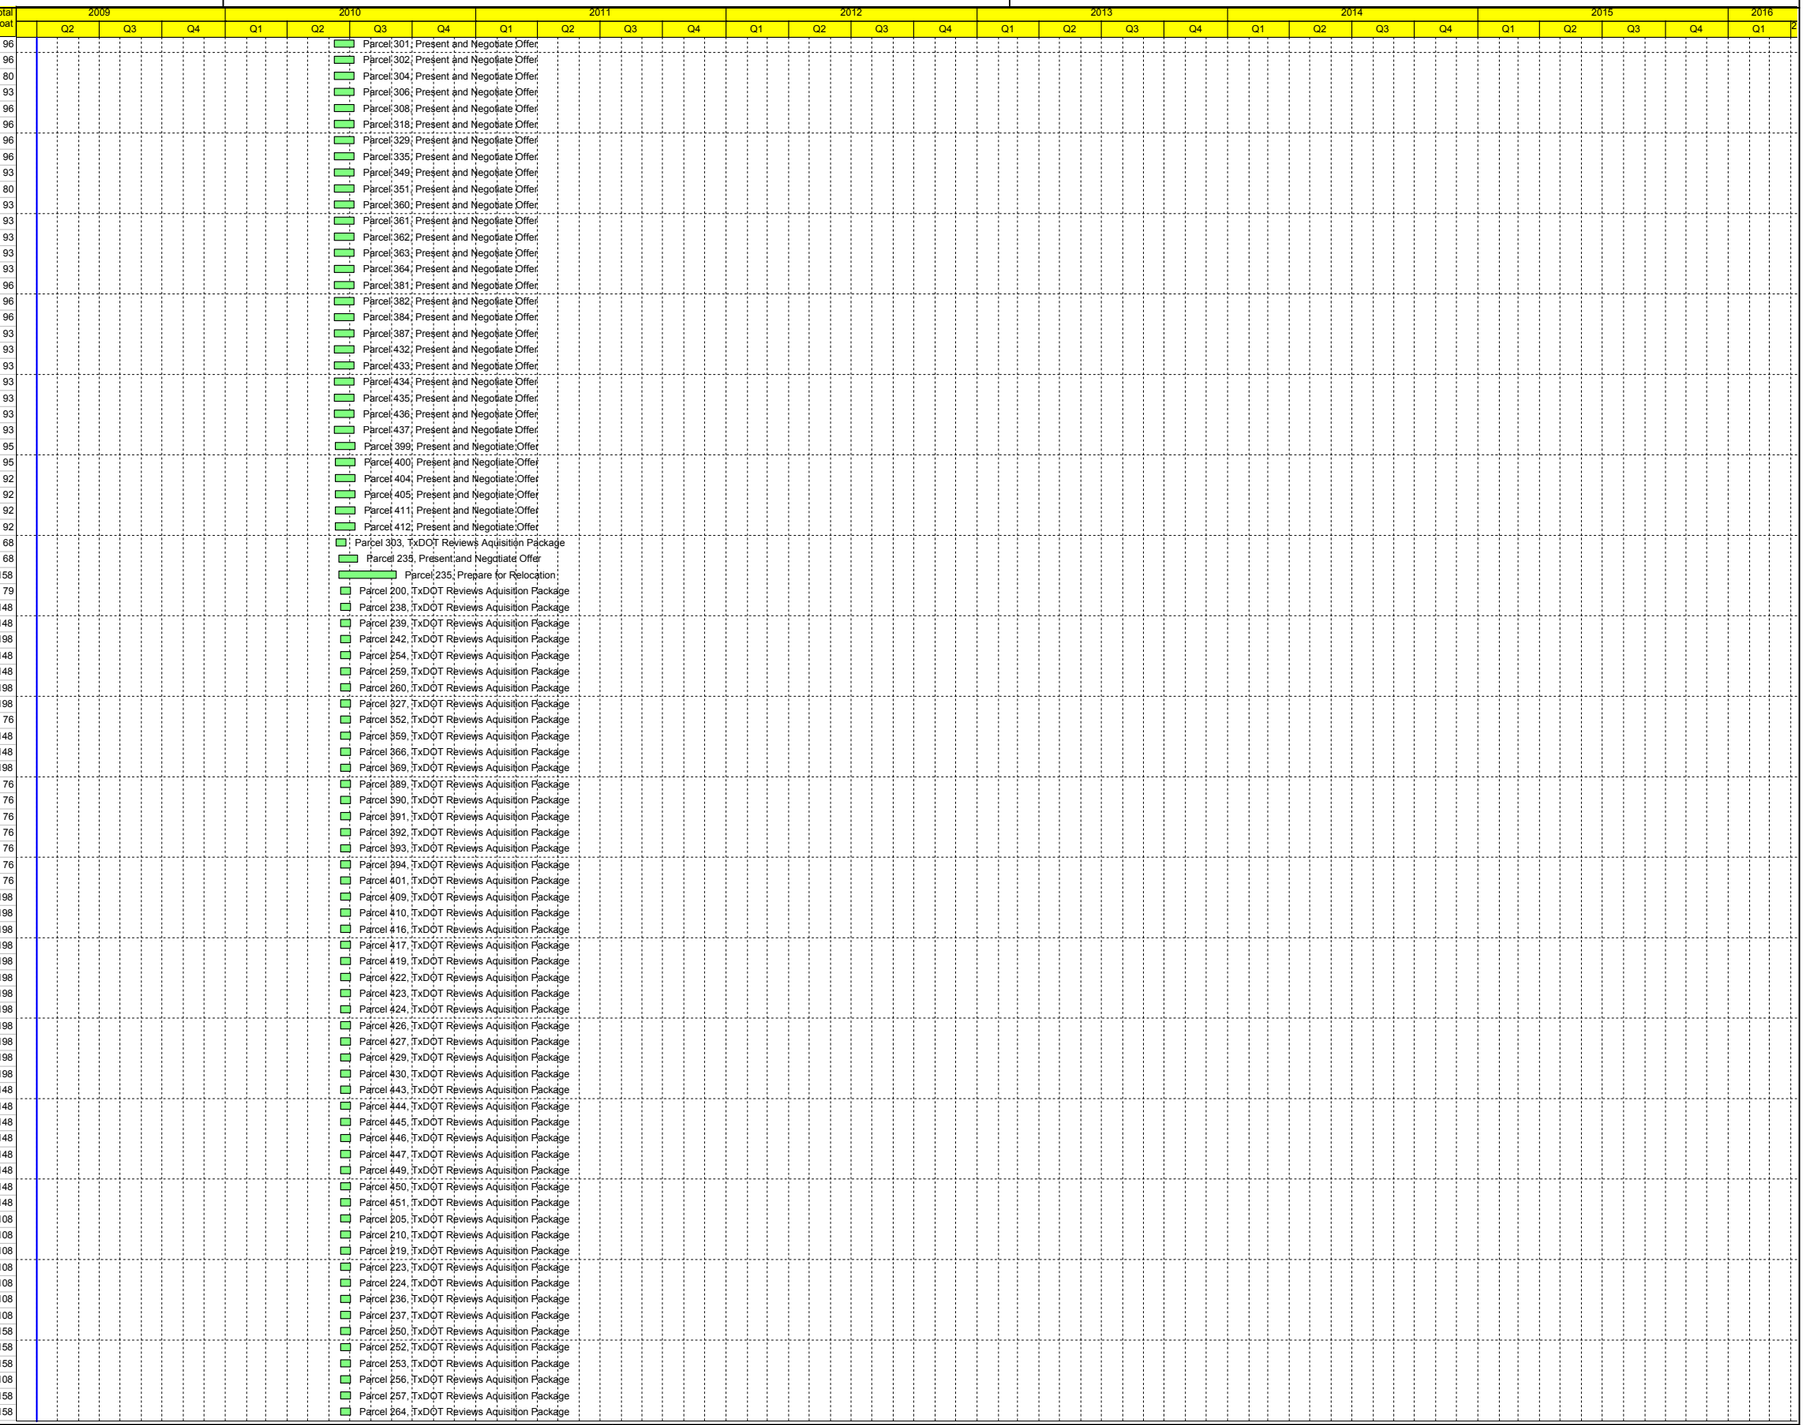

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.3.6	2CR0P2660R30	Parcel 266, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	158
1.3.6	2CR0P2670R30	Parcel 267, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	158
1.3.6	2CR0P2770R30	Parcel 277, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	158
1.3.6	2CR0P2780R30	Parcel 278, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	158
1.3.6	2CR0P2850R30	Parcel 285, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	158
1.3.6	2CR0P5920R30	Parcel 592, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	1108
1.3.6	2CR0P2940R30	Parcel 294, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	108
1.3.6	2CR0P2950R30	Parcel 295, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	108
1.3.6	2CR0P2960R30	Parcel 296, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	108
1.3.6	2CR0P2970R30	Parcel 297, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	108
1.3.6	2CR0P3220R30	Parcel 322, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	108
1.3.6	2CR0P4180R30	Parcel 418, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	158
1.3.6	2CR0P4200R30	Parcel 420, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	158
1.3.6	2CR0P4210R30	Parcel 421, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	158
1.3.6	2CR0P4280R30	Parcel 428, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	158
1.3.6	2CR0P4480R30	Parcel 448, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	108
1.3.6	2CR0P4520R30	Parcel 452, TxDOT Reviews Aquisition Pack...	10	18-Jun-10	02-Jul-10	108
1.3.6	2CR0P2160R60	Parcel 216, Condemnation Process (if requir...	130	21-Jun-10	20-Dec-10	68
1.3.6	2CR0P2010R60	Parcel 201, Condemnation Process (if requir...	130	23-Jun-10	22-Dec-10	68
1.3.6	2CR0P2170R60	Parcel 217, Condemnation Process (if requir...	130	23-Jun-10	22-Dec-10	68
1.3.6	2CR0P2260R60	Parcel 226, Condemnation Process (if requir...	130	23-Jun-10	22-Dec-10	68
1.3.6	2CR0P2270R60	Parcel 227, Condemnation Process (if requir...	130	23-Jun-10	22-Dec-10	68
1.3.6	2CR0P2280R60	Parcel 228, Condemnation Process (if requir...	130	23-Jun-10	22-Dec-10	68
1.3.6	2CR0P2290R60	Parcel 229, Condemnation Process (if requir...	130	23-Jun-10	22-Dec-10	68
1.3.6	2CR0P2300R60	Parcel 230, Condemnation Process (if requir...	130	23-Jun-10	22-Dec-10	68
1.3.6	2CR0P2320R60	Parcel 232, Condemnation Process (if requir...	130	23-Jun-10	22-Dec-10	68
1.3.6	2CR0P3050R60	Parcel 305, Condemnation Process (if requir...	130	23-Jun-10	22-Dec-10	68
1.3.6	2CR0P3190R60	Parcel 319, Condemnation Process (if requir...	130	23-Jun-10	22-Dec-10	68
1.3.6	2CR0P3260R60	Parcel 326, Condemnation Process (if requir...	130	23-Jun-10	22-Dec-10	68
1.3.6	2CR0P3280R60	Parcel 328, Condemnation Process (if requir...	130	23-Jun-10	22-Dec-10	68
1.3.6	2CR0P3440R60	Parcel 344, Condemnation Process (if requir...	130	23-Jun-10	22-Dec-10	68
1.3.6	2CR0P3450R60	Parcel 345, Condemnation Process (if requir...	130	23-Jun-10	22-Dec-10	68
1.3.6	2CR0P3470R60	Parcel 347, Condemnation Process (if requir...	130	23-Jun-10	22-Dec-10	68
1.3.6	2CR0P3480R60	Parcel 348, Condemnation Process (if requir...	130	23-Jun-10	22-Dec-10	68
1.3.6	2CR0P3500R60	Parcel 350, Condemnation Process (if requir...	130	23-Jun-10	22-Dec-10	68
1.3.6	2CR0P3650R60	Parcel 365, Condemnation Process (if requir...	130	23-Jun-10	22-Dec-10	68
1.3.6	2CR0P3680R60	Parcel 368, Condemnation Process (if requir...	130	23-Jun-10	22-Dec-10	68
1.3.6	2CR0P3710R60	Parcel 371, Condemnation Process (if requir...	130	23-Jun-10	22-Dec-10	68
1.3.6	2CR0P3720R60	Parcel 372, Condemnation Process (if requir...	130	23-Jun-10	22-Dec-10	68
1.3.6	2CR0P3730R60	Parcel 373, Condemnation Process (if requir...	130	23-Jun-10	22-Dec-10	68
1.3.6	2CR0P3740R60	Parcel 374, Condemnation Process (if requir...	130	23-Jun-10	22-Dec-10	68
1.3.6	2CR0P3750R60	Parcel 375, Condemnation Process (if requir...	130	23-Jun-10	22-Dec-10	68
1.3.6	2CR0P3760R60	Parcel 376, Condemnation Process (if requir...	130	23-Jun-10	22-Dec-10	68
1.3.6	2CR0P3770R60	Parcel 377, Condemnation Process (if requir...	130	23-Jun-10	22-Dec-10	68
1.3.6	2CR0P3780R60	Parcel 378, Condemnation Process (if requir...	130	23-Jun-10	22-Dec-10	68
1.3.6	2CR0P3790R60	Parcel 379, Condemnation Process (if requir...	130	23-Jun-10	22-Dec-10	68
1.3.6	2CR0P3800R60	Parcel 380, Condemnation Process (if requir...	130	23-Jun-10	22-Dec-10	68
1.3.6	2CR0P3830R60	Parcel 383, Condemnation Process (if requir...	130	23-Jun-10	22-Dec-10	68
1.3.6	2CR0P4310R60	Parcel 431, Condemnation Process (if requir...	130	23-Jun-10	22-Dec-10	68
1.3.6	2CR0P4390R60	Parcel 439, Condemnation Process (if requir...	130	23-Jun-10	22-Dec-10	68
1.3.6	2CR0P4400R60	Parcel 440, Condemnation Process (if requir...	130	23-Jun-10	22-Dec-10	68
1.3.6	2CR0P4410R60	Parcel 441, Condemnation Process (if requir...	130	23-Jun-10	22-Dec-10	68
1.3.6	2CR0P4020R60	Parcel 402, Condemnation Process (if requir...	130	24-Jun-10	23-Dec-10	67
1.3.6	2CR0P4030R60	Parcel 403, Condemnation Process (if requir...	130	24-Jun-10	23-Dec-10	67
1.3.6	2CR0P4060R60	Parcel 406, Condemnation Process (if requir...	130	24-Jun-10	23-Dec-10	67
1.3.6	2CR0P4070R60	Parcel 407, Condemnation Process (if requir...	130	24-Jun-10	23-Dec-10	67
1.3.6	2CR0P4130R60	Parcel 413, Condemnation Process (if requir...	130	24-Jun-10	23-Dec-10	67
1.3.6	2CR0P4140R60	Parcel 414, Condemnation Process (if requir...	130	24-Jun-10	23-Dec-10	67
1.3.6	2CR0P4150R60	Parcel 415, Condemnation Process (if requir...	130	24-Jun-10	23-Dec-10	67
1.3.6	2CR0P3030R40	Parcel 303, Present and Negotiate Offer	20	25-Jun-10	23-Jul-10	68
1.3.6	2CR0P2000R40	Parcel 200, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	79
1.3.6	2CR0P2380R40	Parcel 238, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	148
1.3.6	2CR0P2390R40	Parcel 239, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	148
1.3.6	2CR0P2420R40	Parcel 242, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	198
1.3.6	2CR0P2540R40	Parcel 254, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	148
1.3.6	2CR0P2590R40	Parcel 259, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	148
1.3.6	2CR0P2600R40	Parcel 260, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	198
1.3.6	2CR0P3270R40	Parcel 327, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	198
1.3.6	2CR0P3520R40	Parcel 352, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	76
1.3.6	2CR0P3590R40	Parcel 359, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	148
1.3.6	2CR0P3660R40	Parcel 366, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	148
1.3.6	2CR0P3690R40	Parcel 369, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	198
1.3.6	2CR0P3890R40	Parcel 389, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	76
1.3.6	2CR0P3900R40	Parcel 390, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	76
1.3.6	2CR0P3910R40	Parcel 391, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	76
1.3.6	2CR0P3920R40	Parcel 392, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	76
1.3.6	2CR0P3930R40	Parcel 393, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	76
1.3.6	2CR0P3940R40	Parcel 394, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	76
1.3.6	2CR0P4010R40	Parcel 401, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	76
1.3.6	2CR0P4090R40	Parcel 409, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	198
1.3.6	2CR0P4100R40	Parcel 410, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	198
1.3.6	2CR0P4160R40	Parcel 416, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	198
1.3.6	2CR0P4170R40	Parcel 417, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	198
1.3.6	2CR0P4190R40	Parcel 419, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	198
1.3.6	2CR0P4220R40	Parcel 422, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	198
1.3.6	2CR0P4230R40	Parcel 423, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	198

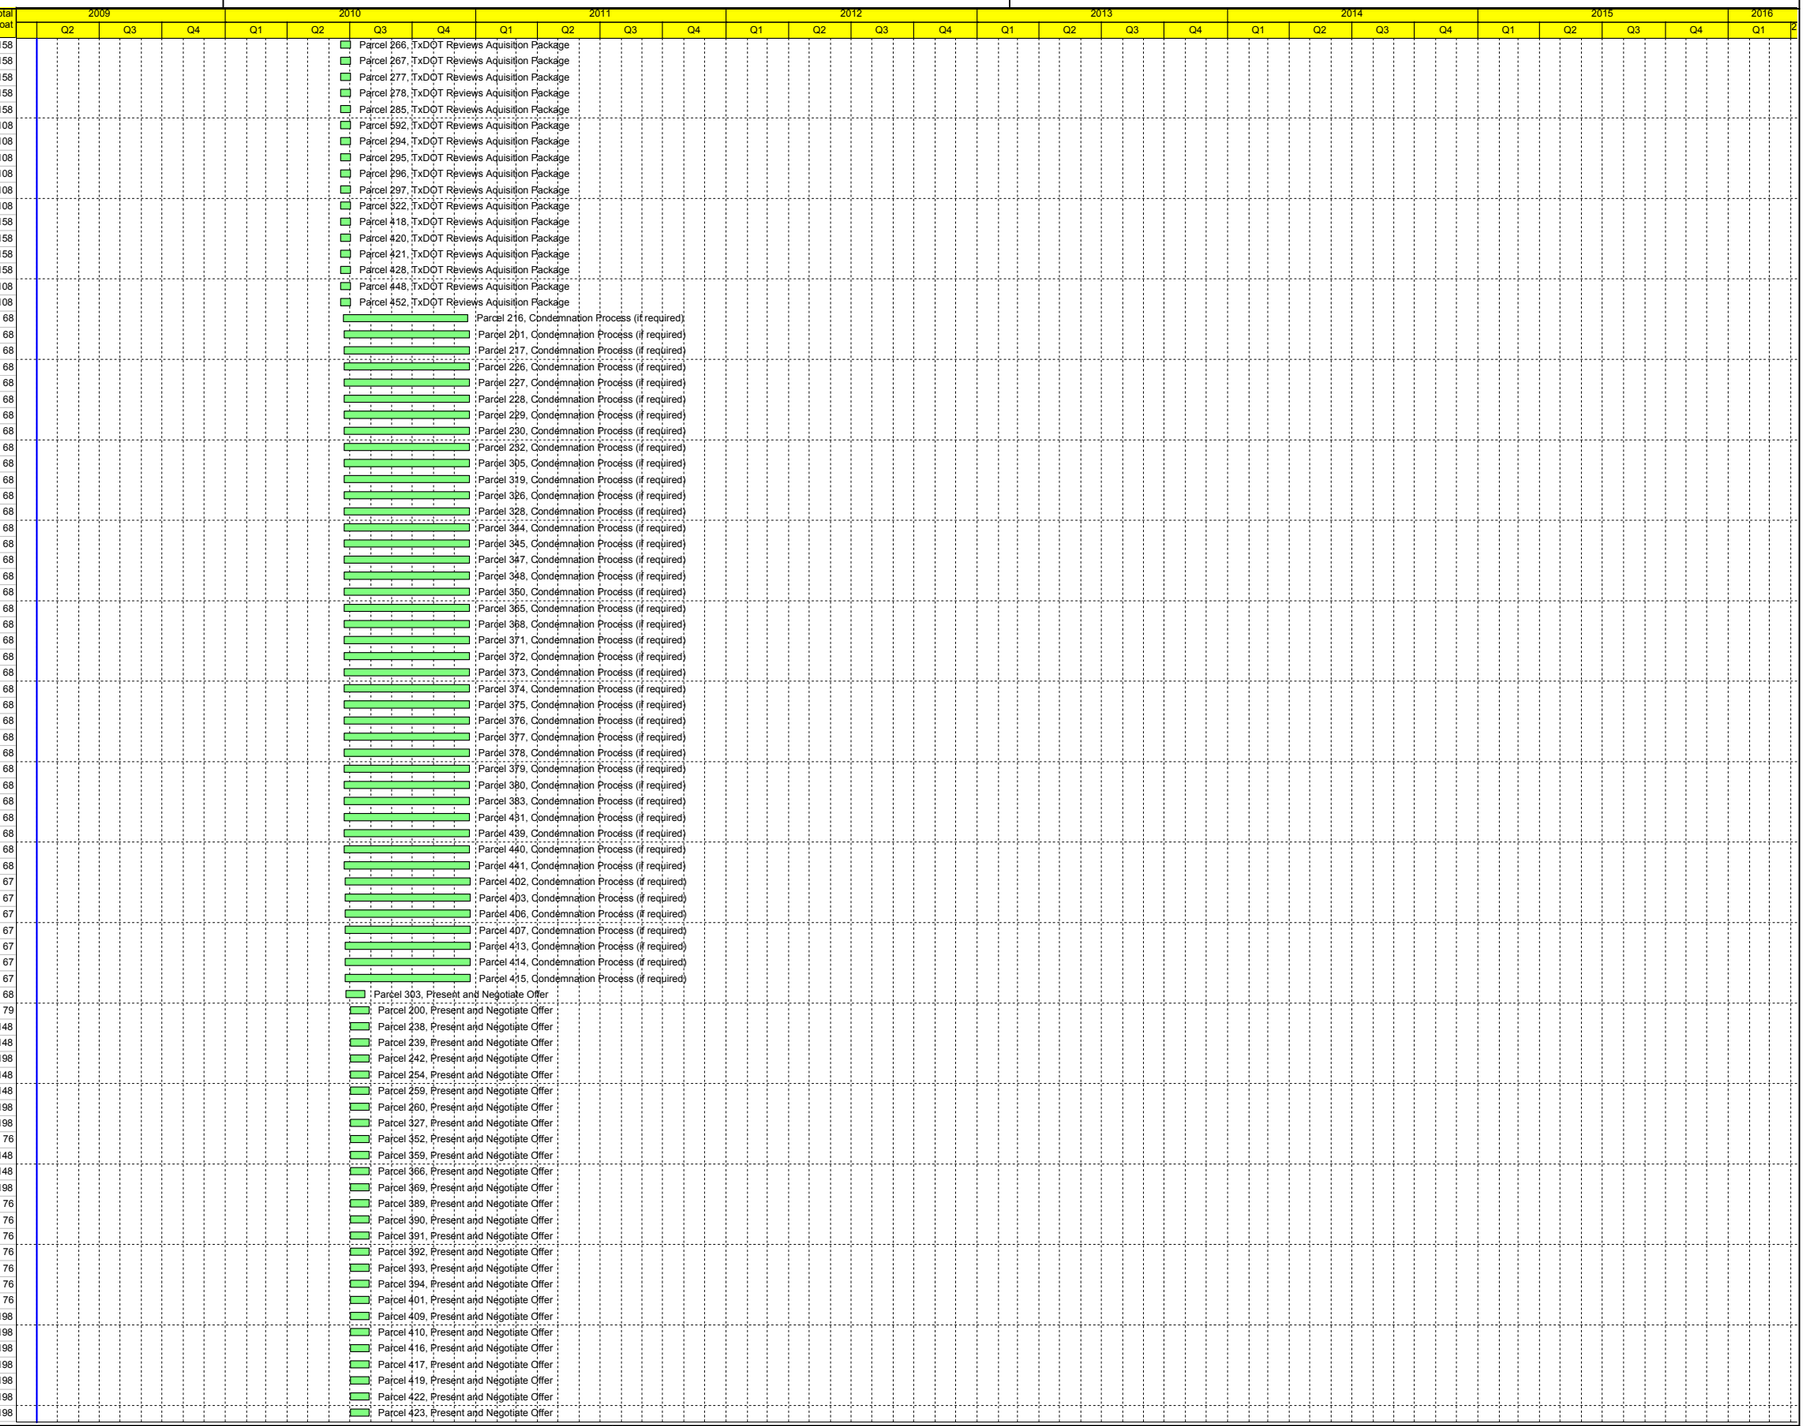

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.3.6	2CR0P4240R40	Parcel 424, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	198
1.3.6	2CR0P4260R40	Parcel 426, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	198
1.3.6	2CR0P4270R40	Parcel 427, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	198
1.3.6	2CR0P4290R40	Parcel 429, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	198
1.3.6	2CR0P4300R40	Parcel 430, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	198
1.3.6	2CR0P4430R40	Parcel 443, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	148
1.3.6	2CR0P4440R40	Parcel 444, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	148
1.3.6	2CR0P4450R40	Parcel 445, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	148
1.3.6	2CR0P4460R40	Parcel 446, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	148
1.3.6	2CR0P4470R40	Parcel 447, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	148
1.3.6	2CR0P4490R40	Parcel 449, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	148
1.3.6	2CR0P4500R40	Parcel 450, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	148
1.3.6	2CR0P4510R40	Parcel 451, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	148
1.3.6	2CR0P2050R40	Parcel 205, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	108
1.3.6	2CR0P2100R40	Parcel 210, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	108
1.3.6	2CR0P2190R40	Parcel 219, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	108
1.3.6	2CR0P2230R40	Parcel 223, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	108
1.3.6	2CR0P2240R40	Parcel 224, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	108
1.3.6	2CR0P2360R40	Parcel 236, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	108
1.3.6	2CR0P2370R40	Parcel 237, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	108
1.3.6	2CR0P2500R40	Parcel 250, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	158
1.3.6	2CR0P2520R40	Parcel 252, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	158
1.3.6	2CR0P2530R40	Parcel 253, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	158
1.3.6	2CR0P2560R40	Parcel 256, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	108
1.3.6	2CR0P2570R40	Parcel 257, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	158
1.3.6	2CR0P2640R40	Parcel 264, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	158
1.3.6	2CR0P2660R40	Parcel 266, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	158
1.3.6	2CR0P2670R40	Parcel 267, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	158
1.3.6	2CR0P2770R40	Parcel 277, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	158
1.3.6	2CR0P2780R40	Parcel 278, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	158
1.3.6	2CR0P2850R40	Parcel 285, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	158
1.3.6	2CR0P5920R40	Parcel 592, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	1108
1.3.6	2CR0P2940R40	Parcel 294, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	108
1.3.6	2CR0P2950R40	Parcel 295, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	108
1.3.6	2CR0P2960R40	Parcel 296, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	108
1.3.6	2CR0P2970R40	Parcel 297, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	108
1.3.6	2CR0P3220R40	Parcel 322, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	108
1.3.6	2CR0P4180R40	Parcel 418, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	158
1.3.6	2CR0P4200R40	Parcel 420, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	158
1.3.6	2CR0P4210R40	Parcel 421, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	158
1.3.6	2CR0P4280R40	Parcel 428, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	158
1.3.6	2CR0P4480R40	Parcel 448, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	108
1.3.6	2CR0P4520R40	Parcel 452, Present and Negotiate Offer	20	02-Jul-10	30-Jul-10	108
1.3.6	2CR0P2050R50	Parcel 205, Prepare for Relocation	60	02-Jul-10	24-Sep-10	198
1.3.6	2CR0P2100R50	Parcel 210, Prepare for Relocation	60	02-Jul-10	24-Sep-10	198
1.3.6	2CR0P2190R50	Parcel 219, Prepare for Relocation	60	02-Jul-10	24-Sep-10	198
1.3.6	2CR0P2230R50	Parcel 223, Prepare for Relocation	60	02-Jul-10	24-Sep-10	198
1.3.6	2CR0P2240R50	Parcel 224, Prepare for Relocation	60	02-Jul-10	24-Sep-10	198
1.3.6	2CR0P2360R50	Parcel 236, Prepare for Relocation	60	02-Jul-10	24-Sep-10	198
1.3.6	2CR0P2370R50	Parcel 237, Prepare for Relocation	60	02-Jul-10	24-Sep-10	198
1.3.6	2CR0P2500R50	Parcel 250, Prepare for Relocation	60	02-Jul-10	24-Sep-10	248
1.3.6	2CR0P2520R50	Parcel 252, Prepare for Relocation	60	02-Jul-10	24-Sep-10	248
1.3.6	2CR0P2530R50	Parcel 253, Prepare for Relocation	60	02-Jul-10	24-Sep-10	248
1.3.6	2CR0P2560R50	Parcel 256, Prepare for Relocation	60	02-Jul-10	24-Sep-10	198
1.3.6	2CR0P2570R50	Parcel 257, Prepare for Relocation	60	02-Jul-10	24-Sep-10	248
1.3.6	2CR0P2640R50	Parcel 264, Prepare for Relocation	60	02-Jul-10	24-Sep-10	248
1.3.6	2CR0P2660R50	Parcel 266, Prepare for Relocation	60	02-Jul-10	24-Sep-10	248
1.3.6	2CR0P2670R50	Parcel 267, Prepare for Relocation	60	02-Jul-10	24-Sep-10	248
1.3.6	2CR0P2770R50	Parcel 277, Prepare for Relocation	60	02-Jul-10	24-Sep-10	248
1.3.6	2CR0P2780R50	Parcel 278, Prepare for Relocation	60	02-Jul-10	24-Sep-10	248
1.3.6	2CR0P2850R50	Parcel 285, Prepare for Relocation	60	02-Jul-10	24-Sep-10	248
1.3.6	2CR0P5920R50	Parcel 592, Prepare for Relocation	60	02-Jul-10	24-Sep-10	1198
1.3.6	2CR0P2940R50	Parcel 294, Prepare for Relocation	60	02-Jul-10	24-Sep-10	198
1.3.6	2CR0P2950R50	Parcel 295, Prepare for Relocation	60	02-Jul-10	24-Sep-10	198
1.3.6	2CR0P2960R50	Parcel 296, Prepare for Relocation	60	02-Jul-10	24-Sep-10	198
1.3.6	2CR0P2970R50	Parcel 297, Prepare for Relocation	60	02-Jul-10	24-Sep-10	198
1.3.6	2CR0P3220R50	Parcel 322, Prepare for Relocation	60	02-Jul-10	24-Sep-10	198
1.3.6	2CR0P4180R50	Parcel 418, Prepare for Relocation	60	02-Jul-10	24-Sep-10	248
1.3.6	2CR0P4200R50	Parcel 420, Prepare for Relocation	60	02-Jul-10	24-Sep-10	248
1.3.6	2CR0P4210R50	Parcel 421, Prepare for Relocation	60	02-Jul-10	24-Sep-10	248
1.3.6	2CR0P4280R50	Parcel 428, Prepare for Relocation	60	02-Jul-10	24-Sep-10	248
1.3.6	2CR0P4480R50	Parcel 448, Prepare for Relocation	60	02-Jul-10	24-Sep-10	198
1.3.6	2CR0P4520R50	Parcel 452, Prepare for Relocation	60	02-Jul-10	24-Sep-10	198
1.3.6	2CR0P2310R60	Parcel 231, Condemnation Process (if requir...	130	06-Jul-10	04-Jan-11	81
1.3.6	2CR0P2400R60	Parcel 240, Condemnation Process (if requir...	130	06-Jul-10	04-Jan-11	81
1.3.6	2CR0P2410R60	Parcel 241, Condemnation Process (if requir...	130	06-Jul-10	04-Jan-11	81
1.3.6	2CR0P2910R60	Parcel 291, Condemnation Process (if requir...	130	06-Jul-10	04-Jan-11	81
1.3.6	2CR0P2920R60	Parcel 292, Condemnation Process (if requir...	130	06-Jul-10	04-Jan-11	81
1.3.6	2CR0P2990R60	Parcel 299, Condemnation Process (if requir...	130	06-Jul-10	04-Jan-11	81
1.3.6	2CR0P3550R60	Parcel 355, Condemnation Process (if requir...	130	06-Jul-10	04-Jan-11	81
1.3.6	2CR0P3670R60	Parcel 367, Condemnation Process (if requir...	130	06-Jul-10	04-Jan-11	81
1.3.6	2CR0P2020R60	Parcel 202, Condemnation Process (if requir...	130	07-Jul-10	05-Jan-11	96
1.3.6	2CR0P2030R60	Parcel 203, Condemnation Process (if requir...	130	07-Jul-10	05-Jan-11	96
1.3.6	2CR0P2070R60	Parcel 207, Condemnation Process (if requir...	130	07-Jul-10	05-Jan-11	93
1.3.6	2CR0P2250R60	Parcel 225, Condemnation Process (if requir...	130	07-Jul-10	05-Jan-11	80
1.3.6	2CR0P3010R60	Parcel 301, Condemnation Process (if requir...	130	07-Jul-10	05-Jan-11	96

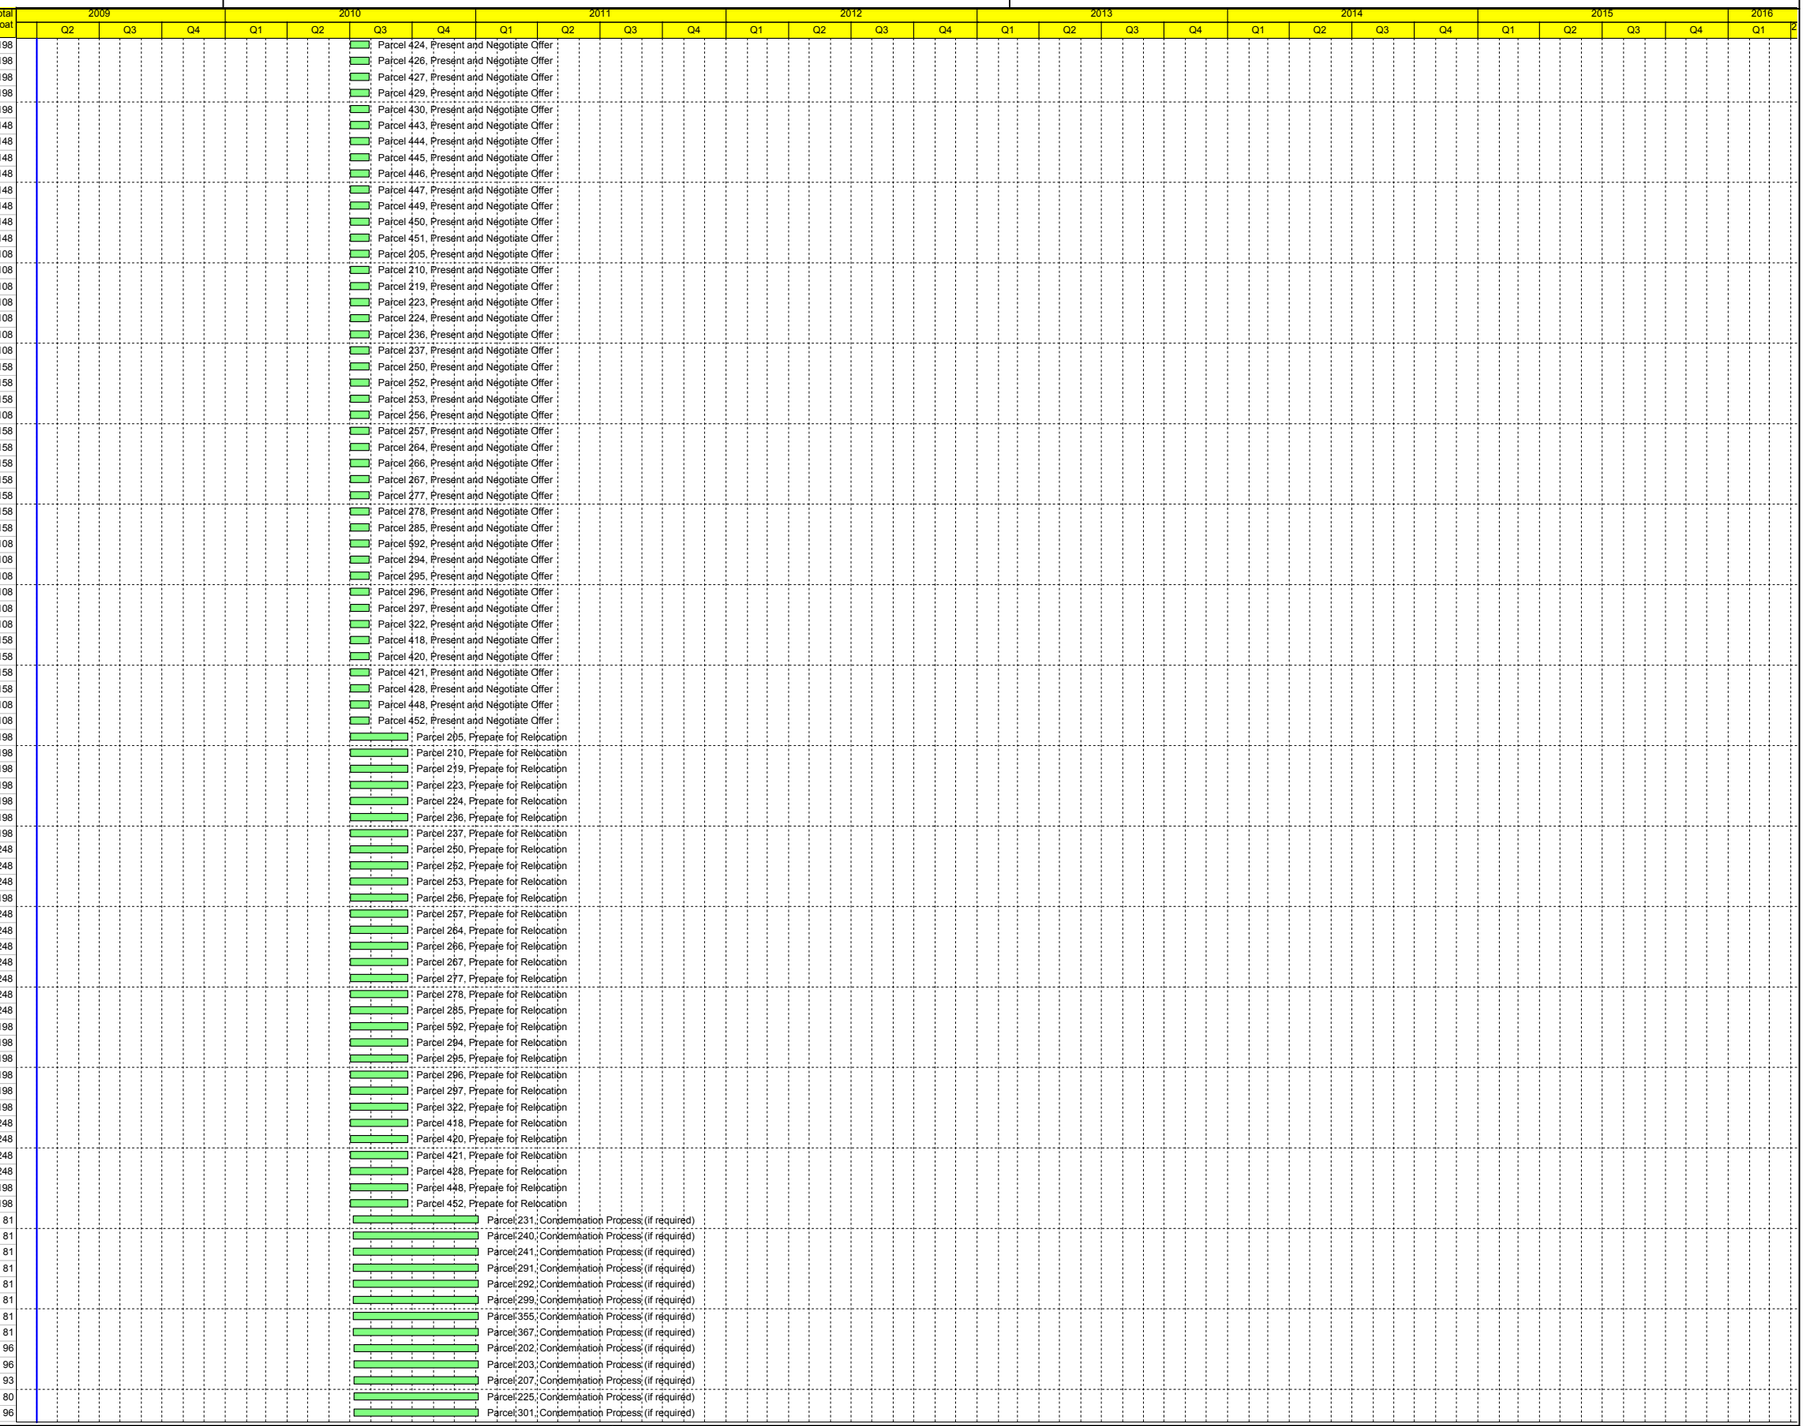

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.3.6	2CR0P3020R60	Parcel 302, Condemnation Process (if requir...	130	07-Jul-10	05-Jan-11	96
1.3.6	2CR0P3040R60	Parcel 304, Condemnation Process (if requir...	130	07-Jul-10	05-Jan-11	80
1.3.6	2CR0P3060R60	Parcel 306, Condemnation Process (if requir...	130	07-Jul-10	05-Jan-11	93
1.3.6	2CR0P3080R60	Parcel 308, Condemnation Process (if requir...	130	07-Jul-10	05-Jan-11	96
1.3.6	2CR0P3180R60	Parcel 318, Condemnation Process (if requir...	130	07-Jul-10	05-Jan-11	96
1.3.6	2CR0P3290R60	Parcel 329, Condemnation Process (if requir...	130	07-Jul-10	05-Jan-11	96
1.3.6	2CR0P3350R60	Parcel 335, Condemnation Process (if requir...	130	07-Jul-10	05-Jan-11	96
1.3.6	2CR0P3490R60	Parcel 349, Condemnation Process (if requir...	130	07-Jul-10	05-Jan-11	93
1.3.6	2CR0P3510R60	Parcel 351, Condemnation Process (if requir...	130	07-Jul-10	05-Jan-11	80
1.3.6	2CR0P3600R60	Parcel 360, Condemnation Process (if requir...	130	07-Jul-10	05-Jan-11	93
1.3.6	2CR0P3610R60	Parcel 361, Condemnation Process (if requir...	130	07-Jul-10	05-Jan-11	93
1.3.6	2CR0P3620R60	Parcel 362, Condemnation Process (if requir...	130	07-Jul-10	05-Jan-11	93
1.3.6	2CR0P3630R60	Parcel 363, Condemnation Process (if requir...	130	07-Jul-10	05-Jan-11	93
1.3.6	2CR0P3640R60	Parcel 364, Condemnation Process (if requir...	130	07-Jul-10	05-Jan-11	93
1.3.6	2CR0P3810R60	Parcel 381, Condemnation Process (if requir...	130	07-Jul-10	05-Jan-11	96
1.3.6	2CR0P3820R60	Parcel 382, Condemnation Process (if requir...	130	07-Jul-10	05-Jan-11	96
1.3.6	2CR0P3840R60	Parcel 384, Condemnation Process (if requir...	130	07-Jul-10	05-Jan-11	96
1.3.6	2CR0P3870R60	Parcel 387, Condemnation Process (if requir...	130	07-Jul-10	05-Jan-11	93
1.3.6	2CR0P4320R60	Parcel 432, Condemnation Process (if requir...	130	07-Jul-10	05-Jan-11	93
1.3.6	2CR0P4330R60	Parcel 433, Condemnation Process (if requir...	130	07-Jul-10	05-Jan-11	93
1.3.6	2CR0P4340R60	Parcel 434, Condemnation Process (if requir...	130	07-Jul-10	05-Jan-11	93
1.3.6	2CR0P4350R60	Parcel 435, Condemnation Process (if requir...	130	07-Jul-10	05-Jan-11	93
1.3.6	2CR0P4360R60	Parcel 436, Condemnation Process (if requir...	130	07-Jul-10	05-Jan-11	93
1.3.6	2CR0P4370R60	Parcel 437, Condemnation Process (if requir...	130	07-Jul-10	05-Jan-11	93
1.3.6	2CR0P3990R60	Parcel 399, Condemnation Process (if requir...	130	08-Jul-10	06-Jan-11	95
1.3.6	2CR0P4000R60	Parcel 400, Condemnation Process (if requir...	130	08-Jul-10	06-Jan-11	95
1.3.6	2CR0P4040R60	Parcel 404, Condemnation Process (if requir...	130	08-Jul-10	06-Jan-11	92
1.3.6	2CR0P4050R60	Parcel 405, Condemnation Process (if requir...	130	08-Jul-10	06-Jan-11	92
1.3.6	2CR0P4110R60	Parcel 411, Condemnation Process (if requir...	130	08-Jul-10	06-Jan-11	92
1.3.6	2CR0P4120R60	Parcel 412, Condemnation Process (if requir...	130	08-Jul-10	06-Jan-11	92
1.3.6	2CR0P2350R60	Parcel 235, Condemnation Process (if requir...	130	13-Jul-10	11-Jan-11	68
1.3.6	2CR0P3030R60	Parcel 303, Condemnation Process (if requir...	130	23-Jul-10	21-Jan-11	68
1.3.6	2CR0P2000R60	Parcel 200, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	79
1.3.6	2CR0P2380R60	Parcel 238, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	148
1.3.6	2CR0P2390R60	Parcel 239, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	148
1.3.6	2CR0P2420R60	Parcel 242, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	198
1.3.6	2CR0P2540R60	Parcel 254, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	148
1.3.6	2CR0P2590R60	Parcel 259, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	148
1.3.6	2CR0P2600R60	Parcel 260, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	198
1.3.6	2CR0P3270R60	Parcel 327, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	198
1.3.6	2CR0P3520R60	Parcel 352, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	76
1.3.6	2CR0P3590R60	Parcel 359, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	148
1.3.6	2CR0P3660R60	Parcel 366, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	148
1.3.6	2CR0P3690R60	Parcel 369, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	198
1.3.6	2CR0P3890R60	Parcel 389, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	76
1.3.6	2CR0P3900R60	Parcel 390, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	76
1.3.6	2CR0P3910R60	Parcel 391, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	76
1.3.6	2CR0P3920R60	Parcel 392, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	76
1.3.6	2CR0P3930R60	Parcel 393, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	76
1.3.6	2CR0P3940R60	Parcel 394, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	76
1.3.6	2CR0P4010R60	Parcel 401, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	76
1.3.6	2CR0P4090R60	Parcel 409, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	198
1.3.6	2CR0P4100R60	Parcel 410, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	198
1.3.6	2CR0P4160R60	Parcel 416, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	198
1.3.6	2CR0P4170R60	Parcel 417, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	198
1.3.6	2CR0P4190R60	Parcel 419, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	198
1.3.6	2CR0P4220R60	Parcel 422, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	198
1.3.6	2CR0P4230R60	Parcel 423, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	198
1.3.6	2CR0P4240R60	Parcel 424, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	198
1.3.6	2CR0P4260R60	Parcel 426, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	198
1.3.6	2CR0P4270R60	Parcel 427, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	198
1.3.6	2CR0P4290R60	Parcel 429, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	198
1.3.6	2CR0P4300R60	Parcel 430, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	198
1.3.6	2CR0P4430R60	Parcel 443, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	148
1.3.6	2CR0P4440R60	Parcel 444, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	148
1.3.6	2CR0P4450R60	Parcel 445, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	148
1.3.6	2CR0P4460R60	Parcel 446, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	148
1.3.6	2CR0P4470R60	Parcel 447, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	148
1.3.6	2CR0P4490R60	Parcel 449, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	148
1.3.6	2CR0P4500R60	Parcel 450, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	148
1.3.6	2CR0P4510R60	Parcel 451, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	148
1.3.6	2CR0P2050R60	Parcel 205, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	108
1.3.6	2CR0P2100R60	Parcel 210, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	108
1.3.6	2CR0P2190R60	Parcel 219, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	108
1.3.6	2CR0P2230R60	Parcel 223, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	108
1.3.6	2CR0P2240R60	Parcel 224, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	108
1.3.6	2CR0P2360R60	Parcel 236, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	108
1.3.6	2CR0P2370R60	Parcel 237, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	108
1.3.6	2CR0P2500R60	Parcel 250, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	158
1.3.6	2CR0P2520R60	Parcel 252, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	158
1.3.6	2CR0P2530R60	Parcel 253, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	158
1.3.6	2CR0P2560R60	Parcel 256, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	108
1.3.6	2CR0P2570R60	Parcel 257, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	158
1.3.6	2CR0P2640R60	Parcel 264, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	158
1.3.6	2CR0P2660R60	Parcel 266, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	158
1.3.6	2CR0P2670R60	Parcel 267, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	158

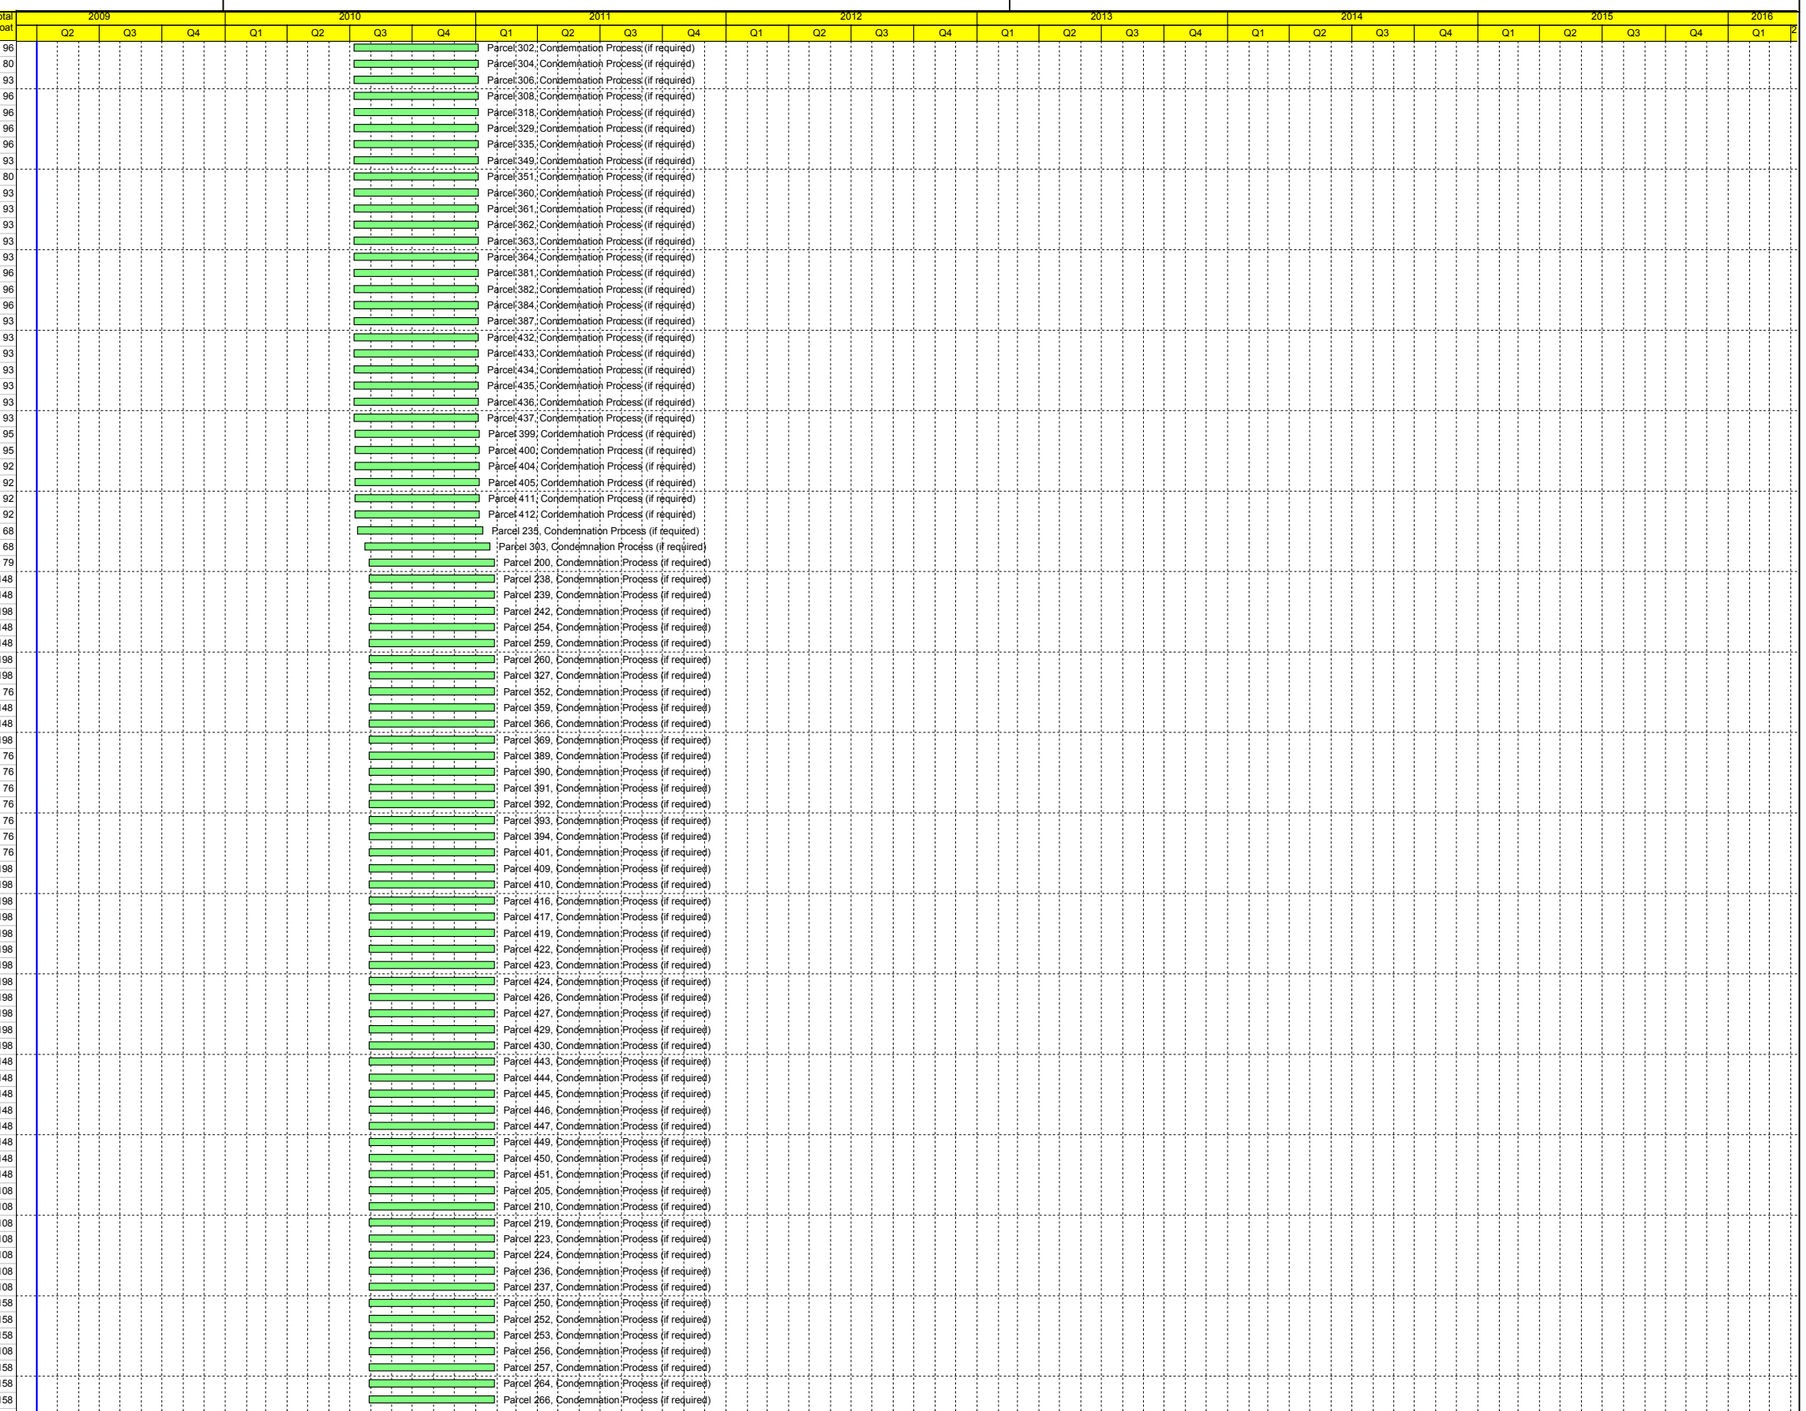

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.3.6	2CR0P2770R60	Parcel 277, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	158
1.3.6	2CR0P2780R60	Parcel 278, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	158
1.3.6	2CR0P2850R60	Parcel 285, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	158
1.3.6	2CR0P5920R60	Parcel 592, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	1108
1.3.6	2CR0P2940R60	Parcel 294, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	108
1.3.6	2CR0P2950R60	Parcel 295, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	108
1.3.6	2CR0P2960R60	Parcel 296, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	108
1.3.6	2CR0P2970R60	Parcel 297, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	108
1.3.6	2CR0P3220R60	Parcel 322, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	108
1.3.6	2CR0P4180R60	Parcel 418, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	158
1.3.6	2CR0P4200R60	Parcel 420, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	158
1.3.6	2CR0P4210R60	Parcel 421, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	158
1.3.6	2CR0P4280R60	Parcel 428, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	158
1.3.6	2CR0P4480R60	Parcel 448, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	108
1.3.6	2CR0P4520R60	Parcel 452, Condemnation Process (if requir...	130	30-Jul-10	28-Jan-11	108
1.3.6	2CR0P2110R70	Parcel 211, Execute Relocation	20	27-Oct-10	24-Nov-10	68
1.3.6	2CR0P2330R70	Parcel 233, Execute Relocation	20	27-Oct-10	24-Nov-10	68
1.3.6	2CR0P3070R70	Parcel 307, Execute Relocation	20	27-Oct-10	24-Nov-10	68
1.3.6	2CR0P3160R70	Parcel 316, Execute Relocation	20	27-Oct-10	24-Nov-10	68
1.3.6	2CR0P3210R70	Parcel 321, Execute Relocation	20	27-Oct-10	24-Nov-10	68
1.3.6	2CR0P3300R70	Parcel 330, Execute Relocation	20	28-Oct-10	25-Nov-10	67
1.3.6	2CR0P3310R70	Parcel 331, Execute Relocation	20	28-Oct-10	25-Nov-10	67
1.3.6	2CR0P3370R70	Parcel 337, Execute Relocation	20	28-Oct-10	25-Nov-10	67
1.3.6	2CR0P3380R70	Parcel 338, Execute Relocation	20	28-Oct-10	25-Nov-10	67
1.3.6	2CR0P3390R70	Parcel 339, Execute Relocation	20	28-Oct-10	25-Nov-10	67
1.3.6	2CR0P3400R70	Parcel 340, Execute Relocation	20	28-Oct-10	25-Nov-10	67
1.3.6	2CR0P3410R70	Parcel 341, Execute Relocation	20	28-Oct-10	25-Nov-10	67
1.3.6	2CR0P3420R70	Parcel 342, Execute Relocation	20	28-Oct-10	25-Nov-10	67
1.3.6	2CR0P3430R70	Parcel 343, Execute Relocation	20	28-Oct-10	25-Nov-10	67
1.3.6	2CR0P3560R70	Parcel 356, Execute Relocation	20	28-Oct-10	25-Nov-10	67
1.3.6	2CR0P3880R70	Parcel 388, Execute Relocation	20	28-Oct-10	25-Nov-10	67
1.3.6	2CR0P4080R70	Parcel 408, Execute Relocation	20	28-Oct-10	25-Nov-10	67
1.3.6	2CR0P4420R70	Parcel 442, Execute Relocation	20	28-Oct-10	25-Nov-10	67
1.3.6	2CR0P2080R70	Parcel 208, Execute Relocation	20	09-Nov-...	07-Dec-10	81
1.3.6	2CR0P2090R70	Parcel 209, Execute Relocation	20	09-Nov-...	07-Dec-10	93
1.3.6	2CR0P2180R70	Parcel 218, Execute Relocation	20	09-Nov-...	07-Dec-10	81
1.3.6	2CR0P2200R70	Parcel 220, Execute Relocation	20	09-Nov-...	07-Dec-10	81
1.3.6	2CR0P2340R70	Parcel 234, Execute Relocation	20	09-Nov-...	07-Dec-10	81
1.3.6	2CR0P2450R70	Parcel 245, Execute Relocation	20	09-Nov-...	07-Dec-10	81
1.3.6	2CR0P2490R70	Parcel 249, Execute Relocation	20	09-Nov-...	07-Dec-10	81
1.3.6	2CR0P2550R70	Parcel 255, Execute Relocation	20	09-Nov-...	07-Dec-10	81
1.3.6	2CR0P2650R70	Parcel 265, Execute Relocation	20	09-Nov-...	07-Dec-10	81
1.3.6	2CR0P2710R70	Parcel 271, Execute Relocation	20	09-Nov-...	07-Dec-10	81
1.3.6	2CR0P2750R70	Parcel 275, Execute Relocation	20	09-Nov-...	07-Dec-10	81
1.3.6	2CR0P2880R70	Parcel 288, Execute Relocation	20	09-Nov-...	07-Dec-10	81
1.3.6	2CR0P2900R70	Parcel 290, Execute Relocation	20	09-Nov-...	07-Dec-10	81
1.3.6	2CR0P2040R70	Parcel 204, Execute Relocation	20	10-Nov-...	08-Dec-10	93
1.3.6	2CR0P2130R70	Parcel 213, Execute Relocation	20	10-Nov-...	08-Dec-10	93
1.3.6	2CR0P2140R70	Parcel 214, Execute Relocation	20	10-Nov-...	08-Dec-10	93
1.3.6	2CR0P2150R70	Parcel 215, Execute Relocation	20	10-Nov-...	08-Dec-10	93
1.3.6	2CR0P2890R70	Parcel 289, Execute Relocation	20	10-Nov-...	08-Dec-10	118
1.3.6	2CR0P2930R70	Parcel 293, Execute Relocation	20	10-Nov-...	08-Dec-10	80
1.3.6	2CR0P3140R70	Parcel 314, Execute Relocation	20	10-Nov-...	08-Dec-10	96
1.3.6	2CR0P3150R70	Parcel 315, Execute Relocation	20	10-Nov-...	08-Dec-10	96
1.3.6	2CR0P3170R70	Parcel 317, Execute Relocation	20	10-Nov-...	08-Dec-10	96
1.3.6	2CR0P3230R70	Parcel 323, Execute Relocation	20	10-Nov-...	08-Dec-10	96
1.3.6	2CR0P3240R70	Parcel 324, Execute Relocation	20	10-Nov-...	08-Dec-10	96
1.3.6	2CR0P3250R70	Parcel 325, Execute Relocation	20	11-Nov-...	09-Dec-10	92
1.3.6	2CR0P3320R70	Parcel 332, Execute Relocation	20	11-Nov-...	09-Dec-10	95
1.3.6	2CR0P3330R70	Parcel 333, Execute Relocation	20	11-Nov-...	09-Dec-10	95
1.3.6	2CR0P3340R70	Parcel 334, Execute Relocation	20	11-Nov-...	09-Dec-10	95
1.3.6	2CR0P3360R70	Parcel 336, Execute Relocation	20	11-Nov-...	09-Dec-10	95
1.3.6	2CR0P3530R70	Parcel 353, Execute Relocation	20	11-Nov-...	09-Dec-10	79
1.3.6	2CR0P3570R70	Parcel 357, Execute Relocation	20	11-Nov-...	09-Dec-10	79
1.3.6	2CR0P3580R70	Parcel 358, Execute Relocation	20	11-Nov-...	09-Dec-10	92
1.3.6	2CR0P3850R70	Parcel 385, Execute Relocation	20	11-Nov-...	09-Dec-10	92
1.3.6	2CR0P3860R70	Parcel 386, Execute Relocation	20	11-Nov-...	09-Dec-10	92
1.3.6	2CR0P3950R70	Parcel 395, Execute Relocation	20	11-Nov-...	09-Dec-10	92
1.3.6	2CR0P3960R70	Parcel 396, Execute Relocation	20	11-Nov-...	09-Dec-10	92
1.3.6	2CR0P3970R70	Parcel 397, Execute Relocation	20	11-Nov-...	09-Dec-10	92
1.3.6	2CR0P3980R70	Parcel 398, Execute Relocation	20	11-Nov-...	09-Dec-10	95
1.3.6	2CR0P4380R70	Parcel 438, Execute Relocation	20	11-Nov-...	09-Dec-10	92
1.3.6	2CR0P2110R80	Parcel 211, Demolish Existing Improvements	20	24-Nov-...	22-Dec-10	68
1.3.6	2CR0P2330R80	Parcel 233, Demolish Existing Improvements	20	24-Nov-...	22-Dec-10	68
1.3.6	2CR0P3070R80	Parcel 307, Demolish Existing Improvements	20	24-Nov-...	22-Dec-10	68
1.3.6	2CR0P3160R80	Parcel 316, Demolish Existing Improvements	20	24-Nov-...	22-Dec-10	68
1.3.6	2CR0P3210R80	Parcel 321, Demolish Existing Improvements	20	24-Nov-...	22-Dec-10	68
1.3.6	2CR0P3300R80	Parcel 330, Demolish Existing Improvements	20	25-Nov-...	23-Dec-10	67
1.3.6	2CR0P3310R80	Parcel 331, Demolish Existing Improvements	20	25-Nov-...	23-Dec-10	67
1.3.6	2CR0P3370R80	Parcel 337, Demolish Existing Improvements	20	25-Nov-...	23-Dec-10	67
1.3.6	2CR0P3380R80	Parcel 338, Demolish Existing Improvements	20	25-Nov-...	23-Dec-10	67
1.3.6	2CR0P3390R80	Parcel 339, Demolish Existing Improvements	20	25-Nov-...	23-Dec-10	67
1.3.6	2CR0P3400R80	Parcel 340, Demolish Existing Improvements	20	25-Nov-...	23-Dec-10	67
1.3.6	2CR0P3410R80	Parcel 341, Demolish Existing Improvements	20	25-Nov-...	23-Dec-10	67
1.3.6	2CR0P3420R80	Parcel 342, Demolish Existing Improvements	20	25-Nov-...	23-Dec-10	67
1.3.6	2CR0P3430R80	Parcel 343, Demolish Existing Improvements	20	25-Nov-...	23-Dec-10	67

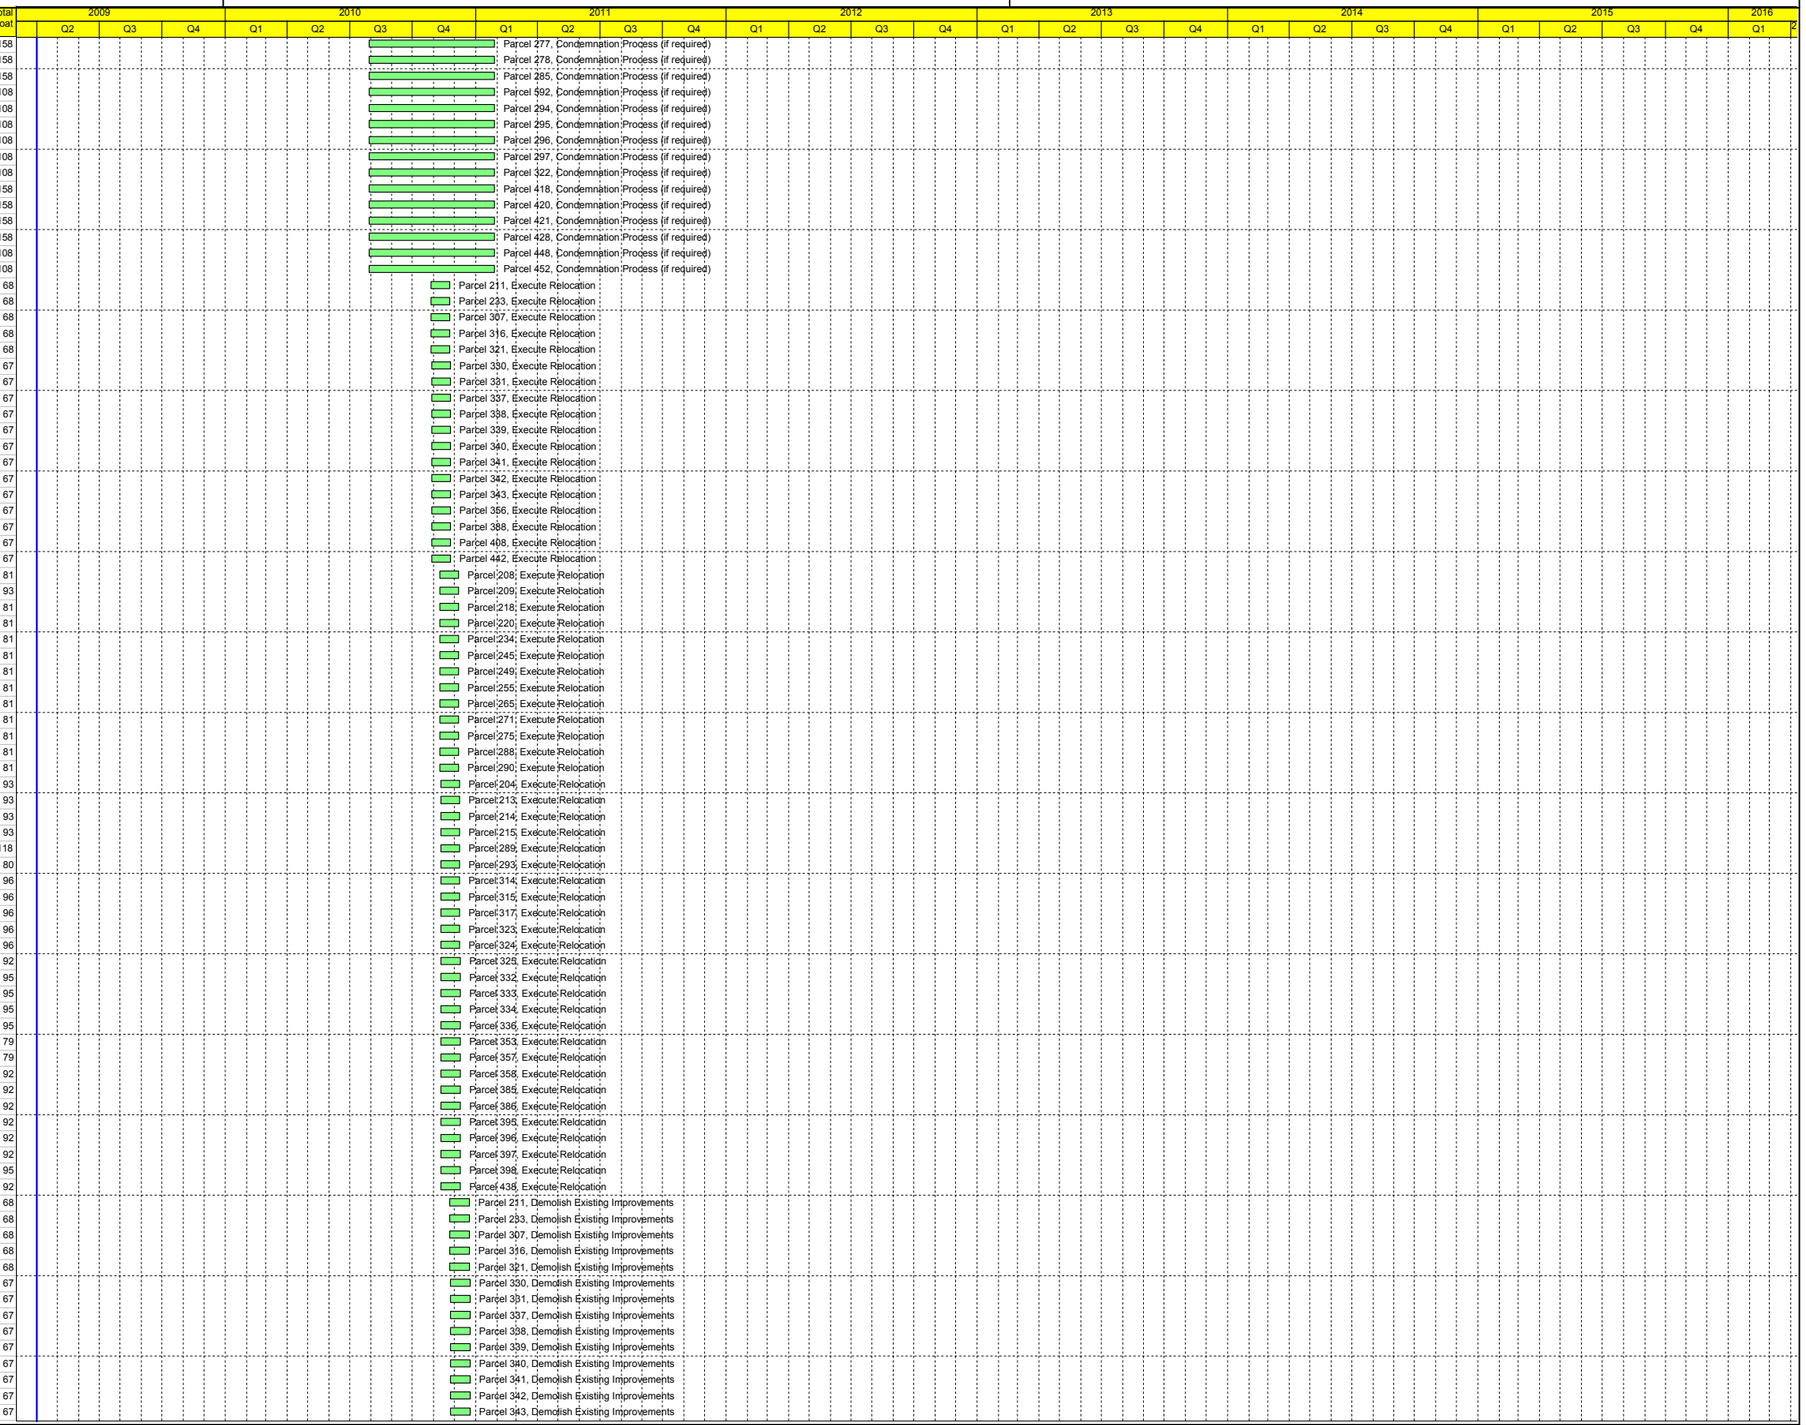

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.3.6	2CR0P3560R80	Parcel 356, Demolish Existing Improvements	20	25-Nov-...	23-Dec-10	67
1.3.6	2CR0P3880R80	Parcel 388, Demolish Existing Improvements	20	25-Nov-...	23-Dec-10	67
1.3.6	2CR0P4080R80	Parcel 408, Demolish Existing Improvements	20	25-Nov-...	23-Dec-10	67
1.3.6	2CR0P4420R80	Parcel 442, Demolish Existing Improvements	20	25-Nov-...	23-Dec-10	67
1.3.6	2CR0P2080R80	Parcel 208, Demolish Existing Improvements	20	07-Dec-...	04-Jan-11	81
1.3.6	2CR0P2090R80	Parcel 209, Demolish Existing Improvements	20	07-Dec-...	04-Jan-11	93
1.3.6	2CR0P2180R80	Parcel 218, Demolish Existing Improvements	20	07-Dec-...	04-Jan-11	81
1.3.6	2CR0P2200R80	Parcel 220, Demolish Existing Improvements	20	07-Dec-...	04-Jan-11	81
1.3.6	2CR0P2340R80	Parcel 234, Demolish Existing Improvements	20	07-Dec-...	04-Jan-11	81
1.3.6	2CR0P2450R80	Parcel 245, Demolish Existing Improvements	20	07-Dec-...	04-Jan-11	81
1.3.6	2CR0P2490R80	Parcel 249, Demolish Existing Improvements	20	07-Dec-...	04-Jan-11	81
1.3.6	2CR0P2550R80	Parcel 255, Demolish Existing Improvements	20	07-Dec-...	04-Jan-11	81
1.3.6	2CR0P2650R80	Parcel 265, Demolish Existing Improvements	20	07-Dec-...	04-Jan-11	81
1.3.6	2CR0P2710R80	Parcel 271, Demolish Existing Improvements	20	07-Dec-...	04-Jan-11	81
1.3.6	2CR0P2750R80	Parcel 275, Demolish Existing Improvements	20	07-Dec-...	04-Jan-11	81
1.3.6	2CR0P2880R80	Parcel 288, Demolish Existing Improvements	20	07-Dec-...	04-Jan-11	81
1.3.6	2CR0P2900R80	Parcel 290, Demolish Existing Improvements	20	07-Dec-...	04-Jan-11	81
1.3.6	2CR0P2040R80	Parcel 204, Demolish Existing Improvements	20	08-Dec-...	05-Jan-11	93
1.3.6	2CR0P2130R80	Parcel 213, Demolish Existing Improvements	20	08-Dec-...	05-Jan-11	93
1.3.6	2CR0P2140R80	Parcel 214, Demolish Existing Improvements	20	08-Dec-...	05-Jan-11	93
1.3.6	2CR0P2150R80	Parcel 215, Demolish Existing Improvements	20	08-Dec-...	05-Jan-11	93
1.3.6	2CR0P2890R80	Parcel 289, Demolish Existing Improvements	20	08-Dec-...	05-Jan-11	118
1.3.6	2CR0P2930R80	Parcel 293, Demolish Existing Improvements	20	08-Dec-...	05-Jan-11	80
1.3.6	2CR0P3140R80	Parcel 314, Demolish Existing Improvements	20	08-Dec-...	05-Jan-11	96
1.3.6	2CR0P3150R80	Parcel 315, Demolish Existing Improvements	20	08-Dec-...	05-Jan-11	96
1.3.6	2CR0P3170R80	Parcel 317, Demolish Existing Improvements	20	08-Dec-...	05-Jan-11	96
1.3.6	2CR0P3230R80	Parcel 323, Demolish Existing Improvements	20	08-Dec-...	05-Jan-11	96
1.3.6	2CR0P3240R80	Parcel 324, Demolish Existing Improvements	20	08-Dec-...	05-Jan-11	96
1.3.6	2CR0P3250R80	Parcel 325, Demolish Existing Improvements	20	09-Dec-...	06-Jan-11	92
1.3.6	2CR0P3320R80	Parcel 332, Demolish Existing Improvements	20	09-Dec-...	06-Jan-11	95
1.3.6	2CR0P3330R80	Parcel 333, Demolish Existing Improvements	20	09-Dec-...	06-Jan-11	95
1.3.6	2CR0P3340R80	Parcel 334, Demolish Existing Improvements	20	09-Dec-...	06-Jan-11	95
1.3.6	2CR0P3360R80	Parcel 336, Demolish Existing Improvements	20	09-Dec-...	06-Jan-11	95
1.3.6	2CR0P3530R80	Parcel 353, Demolish Existing Improvements	20	09-Dec-...	06-Jan-11	79
1.3.6	2CR0P3570R80	Parcel 357, Demolish Existing Improvements	20	09-Dec-...	06-Jan-11	79
1.3.6	2CR0P3580R80	Parcel 358, Demolish Existing Improvements	20	09-Dec-...	06-Jan-11	92
1.3.6	2CR0P3850R80	Parcel 385, Demolish Existing Improvements	20	09-Dec-...	06-Jan-11	92
1.3.6	2CR0P3860R80	Parcel 386, Demolish Existing Improvements	20	09-Dec-...	06-Jan-11	92
1.3.6	2CR0P3950R80	Parcel 395, Demolish Existing Improvements	20	09-Dec-...	06-Jan-11	92
1.3.6	2CR0P3960R80	Parcel 396, Demolish Existing Improvements	20	09-Dec-...	06-Jan-11	92
1.3.6	2CR0P3970R80	Parcel 397, Demolish Existing Improvements	20	09-Dec-...	06-Jan-11	92
1.3.6	2CR0P3980R80	Parcel 398, Demolish Existing Improvements	20	09-Dec-...	06-Jan-11	95
1.3.6	2CR0P4380R80	Parcel 438, Demolish Existing Improvements	20	09-Dec-...	06-Jan-11	92
1.3.6	2CR0P2160R70	Parcel 216, Execute Relocation	20	20-Dec-...	17-Jan-11	68
1.3.6	2CR0P2010R99	Parcel 201, Cleared for Construction	0		22-Dec-10	68
1.3.6	2CR0P2170R99	Parcel 217, Cleared for Construction	0		22-Dec-10	68
1.3.6	2CR0P2260R99	Parcel 226, Cleared for Construction	0		22-Dec-10	68
1.3.6	2CR0P2270R99	Parcel 227, Cleared for Construction	0		22-Dec-10	68
1.3.6	2CR0P2280R99	Parcel 228, Cleared for Construction	0		22-Dec-10	68
1.3.6	2CR0P2290R99	Parcel 229, Cleared for Construction	0		22-Dec-10	68
1.3.6	2CR0P2300R99	Parcel 230, Cleared for Construction	0		22-Dec-10	68
1.3.6	2CR0P2320R99	Parcel 232, Cleared for Construction	0		22-Dec-10	68
1.3.6	2CR0P3050R99	Parcel 305, Cleared for Construction	0		22-Dec-10	68
1.3.6	2CR0P3190R99	Parcel 319, Cleared for Construction	0		22-Dec-10	68
1.3.6	2CR0P3260R99	Parcel 326, Cleared for Construction	0		22-Dec-10	68
1.3.6	2CR0P3280R99	Parcel 328, Cleared for Construction	0		22-Dec-10	68
1.3.6	2CR0P3440R99	Parcel 344, Cleared for Construction	0		22-Dec-10	68
1.3.6	2CR0P3450R99	Parcel 345, Cleared for Construction	0		22-Dec-10	68
1.3.6	2CR0P3470R99	Parcel 347, Cleared for Construction	0		22-Dec-10	68
1.3.6	2CR0P3480R99	Parcel 348, Cleared for Construction	0		22-Dec-10	68
1.3.6	2CR0P3500R99	Parcel 350, Cleared for Construction	0		22-Dec-10	68
1.3.6	2CR0P3650R99	Parcel 365, Cleared for Construction	0		22-Dec-10	68
1.3.6	2CR0P3680R99	Parcel 368, Cleared for Construction	0		22-Dec-10	68
1.3.6	2CR0P3710R99	Parcel 371, Cleared for Construction	0		22-Dec-10	68
1.3.6	2CR0P3720R99	Parcel 372, Cleared for Construction	0		22-Dec-10	68
1.3.6	2CR0P3730R99	Parcel 373, Cleared for Construction	0		22-Dec-10	68
1.3.6	2CR0P3740R99	Parcel 374, Cleared for Construction	0		22-Dec-10	68
1.3.6	2CR0P3750R99	Parcel 375, Cleared for Construction	0		22-Dec-10	68
1.3.6	2CR0P3760R99	Parcel 376, Cleared for Construction	0		22-Dec-10	68
1.3.6	2CR0P3770R99	Parcel 377, Cleared for Construction	0		22-Dec-10	68
1.3.6	2CR0P3780R99	Parcel 378, Cleared for Construction	0		22-Dec-10	68
1.3.6	2CR0P3790R99	Parcel 379, Cleared for Construction	0		22-Dec-10	68
1.3.6	2CR0P3800R99	Parcel 380, Cleared for Construction	0		22-Dec-10	68
1.3.6	2CR0P3830R99	Parcel 383, Cleared for Construction	0		22-Dec-10	68
1.3.6	2CR0P4310R99	Parcel 431, Cleared for Construction	0		22-Dec-10	68
1.3.6	2CR0P4390R99	Parcel 439, Cleared for Construction	0		22-Dec-10	68
1.3.6	2CR0P4400R99	Parcel 440, Cleared for Construction	0		22-Dec-10	68
1.3.6	2CR0P4410R99	Parcel 441, Cleared for Construction	0		22-Dec-10	68
1.3.6	2CR0P2110R99	Parcel 211, Cleared for Construction	0		22-Dec-10	68
1.3.6	2CR0P2330R99	Parcel 233, Cleared for Construction	0		22-Dec-10	68
1.3.6	2CR0P3070R99	Parcel 307, Cleared for Construction	0		22-Dec-10	68
1.3.6	2CR0P3160R99	Parcel 316, Cleared for Construction	0		22-Dec-10	68
1.3.6	2CR0P3210R99	Parcel 321, Cleared for Construction	0		22-Dec-10	68
1.3.6	2CR0P4020R99	Parcel 402, Cleared for Construction	0		23-Dec-10	67
1.3.6	2CR0P4030R99	Parcel 403, Cleared for Construction	0		23-Dec-10	67
1.3.6	2CR0P4060R99	Parcel 406, Cleared for Construction	0		23-Dec-10	67

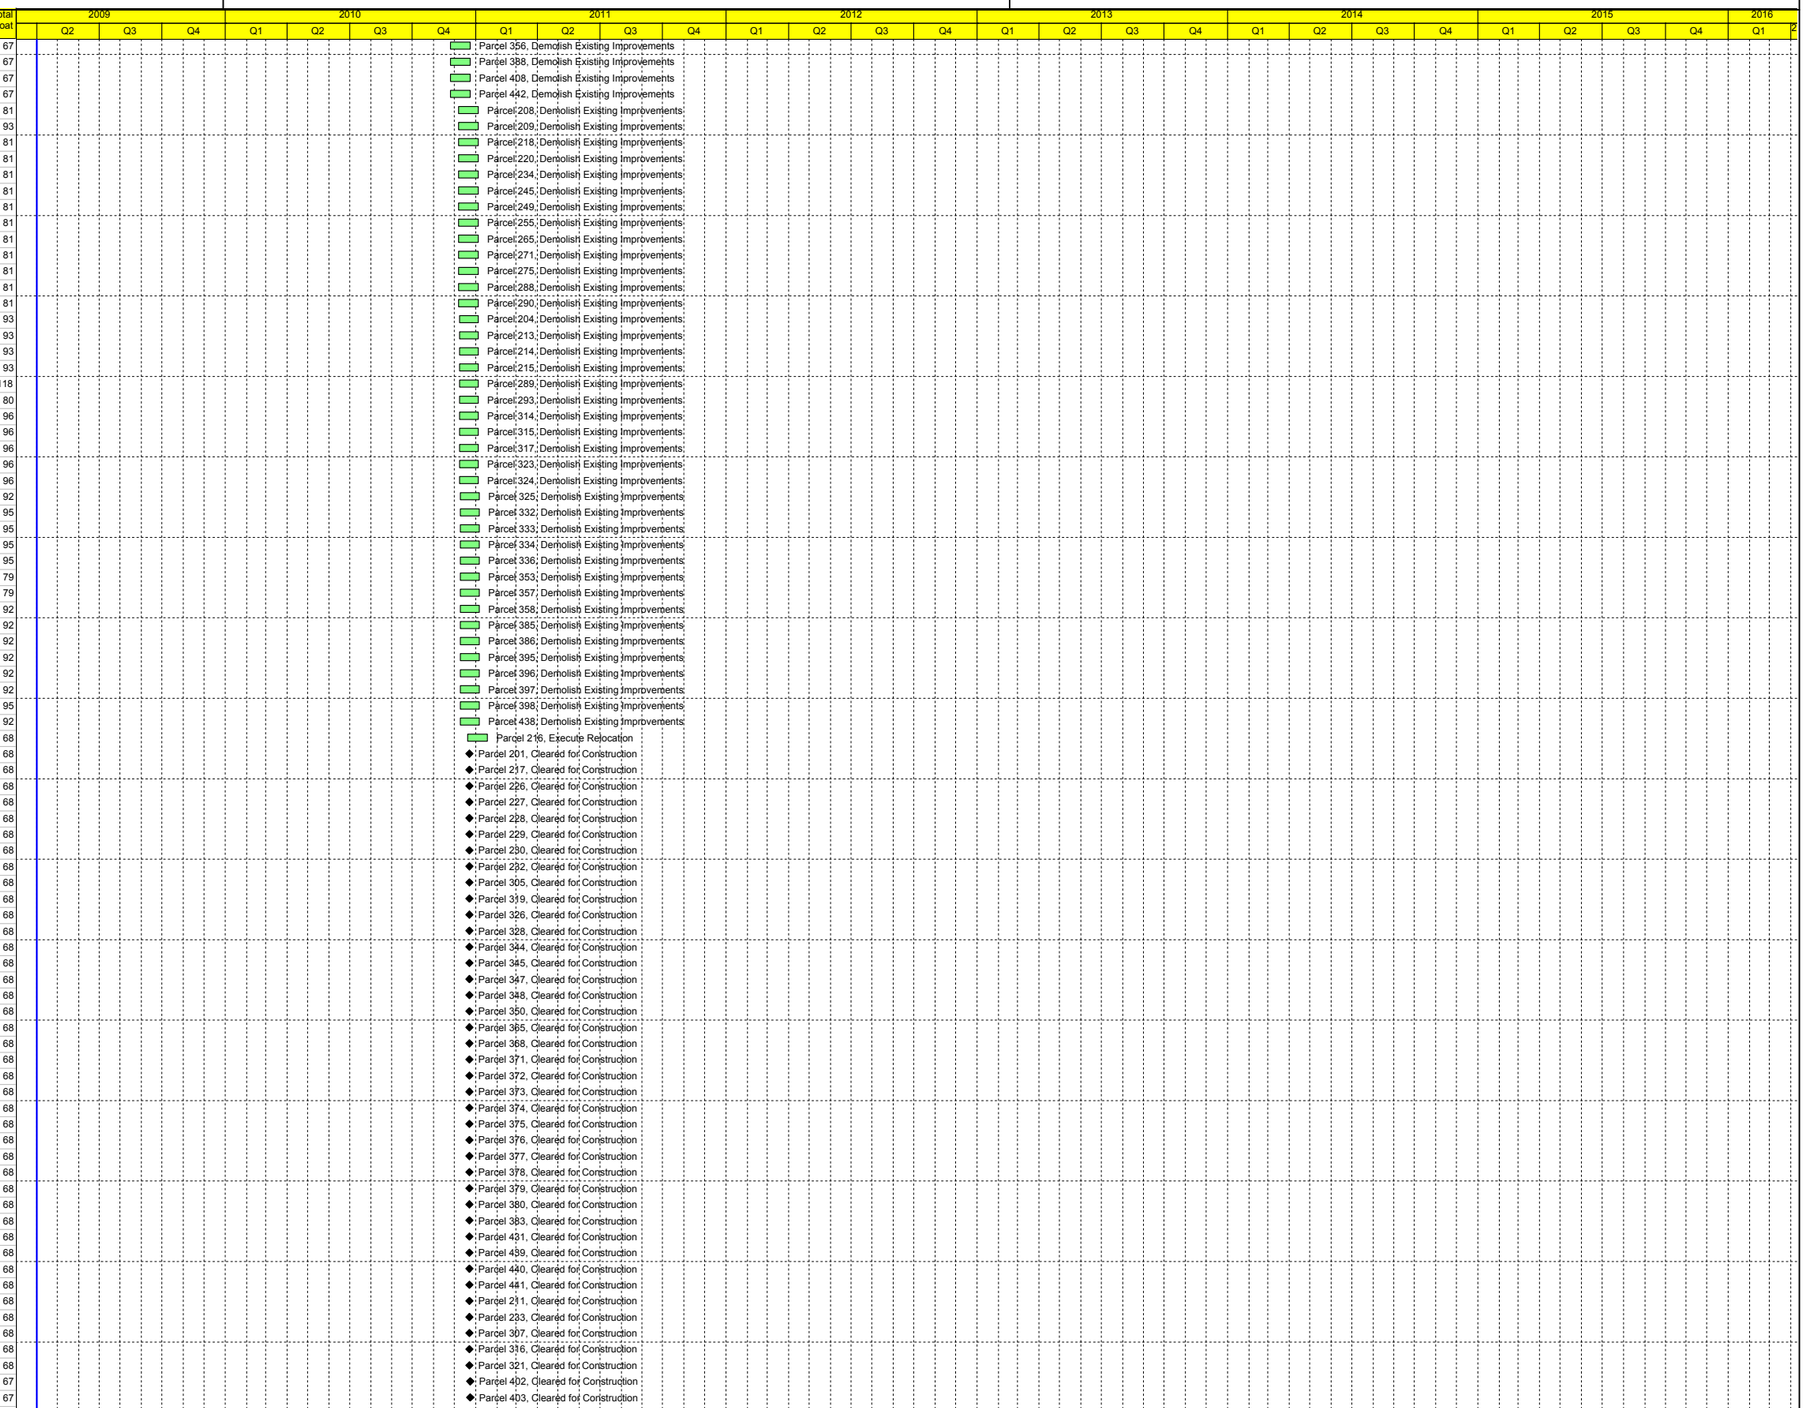

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.3.6	2CR0P4070R99	Parcel 407, Cleared for Construction	0		23-Dec-10	67
1.3.6	2CR0P4130R99	Parcel 413, Cleared for Construction	0		23-Dec-10	67
1.3.6	2CR0P4140R99	Parcel 414, Cleared for Construction	0		23-Dec-10	67
1.3.6	2CR0P4150R99	Parcel 415, Cleared for Construction	0		23-Dec-10	67
1.3.6	2CR0P3300R99	Parcel 330, Cleared for Construction	0		23-Dec-10	67
1.3.6	2CR0P3310R99	Parcel 331, Cleared for Construction	0		23-Dec-10	67
1.3.6	2CR0P3370R99	Parcel 337, Cleared for Construction	0		23-Dec-10	67
1.3.6	2CR0P3380R99	Parcel 338, Cleared for Construction	0		23-Dec-10	67
1.3.6	2CR0P3390R99	Parcel 339, Cleared for Construction	0		23-Dec-10	67
1.3.6	2CR0P3400R99	Parcel 340, Cleared for Construction	0		23-Dec-10	67
1.3.6	2CR0P3410R99	Parcel 341, Cleared for Construction	0		23-Dec-10	67
1.3.6	2CR0P3420R99	Parcel 342, Cleared for Construction	0		23-Dec-10	67
1.3.6	2CR0P3430R99	Parcel 343, Cleared for Construction	0		23-Dec-10	67
1.3.6	2CR0P3560R99	Parcel 356, Cleared for Construction	0		23-Dec-10	67
1.3.6	2CR0P3880R99	Parcel 388, Cleared for Construction	0		23-Dec-10	67
1.3.6	2CR0P4080R99	Parcel 408, Cleared for Construction	0		23-Dec-10	67
1.3.6	2CR0P4420R99	Parcel 442, Cleared for Construction	0		23-Dec-10	67
1.3.6	2CR0P2310R99	Parcel 231, Cleared for Construction	0		04-Jan-11	81
1.3.6	2CR0P2400R99	Parcel 240, Cleared for Construction	0		04-Jan-11	81
1.3.6	2CR0P2410R99	Parcel 241, Cleared for Construction	0		04-Jan-11	81
1.3.6	2CR0P2910R99	Parcel 291, Cleared for Construction	0		04-Jan-11	81
1.3.6	2CR0P2920R99	Parcel 292, Cleared for Construction	0		04-Jan-11	81
1.3.6	2CR0P2990R99	Parcel 299, Cleared for Construction	0		04-Jan-11	81
1.3.6	2CR0P3550R99	Parcel 355, Cleared for Construction	0		04-Jan-11	81
1.3.6	2CR0P3670R99	Parcel 367, Cleared for Construction	0		04-Jan-11	81
1.3.6	2CR0P2080R99	Parcel 208, Cleared for Construction	0		04-Jan-11	81
1.3.6	2CR0P2090R99	Parcel 209, Cleared for Construction	0		04-Jan-11	93
1.3.6	2CR0P2180R99	Parcel 218, Cleared for Construction	0		04-Jan-11	81
1.3.6	2CR0P2200R99	Parcel 220, Cleared for Construction	0		04-Jan-11	81
1.3.6	2CR0P2340R99	Parcel 234, Cleared for Construction	0		04-Jan-11	81
1.3.6	2CR0P2450R99	Parcel 245, Cleared for Construction	0		04-Jan-11	81
1.3.6	2CR0P2490R99	Parcel 249, Cleared for Construction	0		04-Jan-11	81
1.3.6	2CR0P2550R99	Parcel 255, Cleared for Construction	0		04-Jan-11	81
1.3.6	2CR0P2650R99	Parcel 265, Cleared for Construction	0		04-Jan-11	81
1.3.6	2CR0P2710R99	Parcel 271, Cleared for Construction	0		04-Jan-11	81
1.3.6	2CR0P2750R99	Parcel 275, Cleared for Construction	0		04-Jan-11	81
1.3.6	2CR0P2880R99	Parcel 288, Cleared for Construction	0		04-Jan-11	81
1.3.6	2CR0P2900R99	Parcel 290, Cleared for Construction	0		04-Jan-11	81
1.3.6	2CR0P2020R99	Parcel 202, Cleared for Construction	0		05-Jan-11	96
1.3.6	2CR0P2030R99	Parcel 203, Cleared for Construction	0		05-Jan-11	96
1.3.6	2CR0P2070R99	Parcel 207, Cleared for Construction	0		05-Jan-11	93
1.3.6	2CR0P2250R99	Parcel 225, Cleared for Construction	0		05-Jan-11	80
1.3.6	2CR0P3010R99	Parcel 301, Cleared for Construction	0		05-Jan-11	96
1.3.6	2CR0P3020R99	Parcel 302, Cleared for Construction	0		05-Jan-11	96
1.3.6	2CR0P3040R99	Parcel 304, Cleared for Construction	0		05-Jan-11	80
1.3.6	2CR0P3060R99	Parcel 306, Cleared for Construction	0		05-Jan-11	93
1.3.6	2CR0P3080R99	Parcel 308, Cleared for Construction	0		05-Jan-11	96
1.3.6	2CR0P3180R99	Parcel 318, Cleared for Construction	0		05-Jan-11	96
1.3.6	2CR0P3290R99	Parcel 329, Cleared for Construction	0		05-Jan-11	96
1.3.6	2CR0P3350R99	Parcel 335, Cleared for Construction	0		05-Jan-11	96
1.3.6	2CR0P3490R99	Parcel 349, Cleared for Construction	0		05-Jan-11	93
1.3.6	2CR0P3510R99	Parcel 351, Cleared for Construction	0		05-Jan-11	80
1.3.6	2CR0P3600R99	Parcel 360, Cleared for Construction	0		05-Jan-11	93
1.3.6	2CR0P3610R99	Parcel 361, Cleared for Construction	0		05-Jan-11	93
1.3.6	2CR0P3620R99	Parcel 362, Cleared for Construction	0		05-Jan-11	93
1.3.6	2CR0P3630R99	Parcel 363, Cleared for Construction	0		05-Jan-11	93
1.3.6	2CR0P3640R99	Parcel 364, Cleared for Construction	0		05-Jan-11	93
1.3.6	2CR0P3810R99	Parcel 381, Cleared for Construction	0		05-Jan-11	96
1.3.6	2CR0P3820R99	Parcel 382, Cleared for Construction	0		05-Jan-11	96
1.3.6	2CR0P3840R99	Parcel 384, Cleared for Construction	0		05-Jan-11	96
1.3.6	2CR0P3870R99	Parcel 387, Cleared for Construction	0		05-Jan-11	93
1.3.6	2CR0P4320R99	Parcel 432, Cleared for Construction	0		05-Jan-11	93
1.3.6	2CR0P4330R99	Parcel 433, Cleared for Construction	0		05-Jan-11	93
1.3.6	2CR0P4340R99	Parcel 434, Cleared for Construction	0		05-Jan-11	93
1.3.6	2CR0P4350R99	Parcel 435, Cleared for Construction	0		05-Jan-11	93
1.3.6	2CR0P4360R99	Parcel 436, Cleared for Construction	0		05-Jan-11	93
1.3.6	2CR0P4370R99	Parcel 437, Cleared for Construction	0		05-Jan-11	93
1.3.6	2CR0P2040R99	Parcel 204, Cleared for Construction	0		05-Jan-11	93
1.3.6	2CR0P2130R99	Parcel 213, Cleared for Construction	0		05-Jan-11	93
1.3.6	2CR0P2140R99	Parcel 214, Cleared for Construction	0		05-Jan-11	93
1.3.6	2CR0P2150R99	Parcel 215, Cleared for Construction	0		05-Jan-11	93
1.3.6	2CR0P2890R99	Parcel 289, Cleared for Construction	0		05-Jan-11	118
1.3.6	2CR0P2930R99	Parcel 293, Cleared for Construction	0		05-Jan-11	80
1.3.6	2CR0P3140R99	Parcel 314, Cleared for Construction	0		05-Jan-11	96
1.3.6	2CR0P3150R99	Parcel 315, Cleared for Construction	0		05-Jan-11	96
1.3.6	2CR0P3170R99	Parcel 317, Cleared for Construction	0		05-Jan-11	96
1.3.6	2CR0P3230R99	Parcel 323, Cleared for Construction	0		05-Jan-11	96
1.3.6	2CR0P3240R99	Parcel 324, Cleared for Construction	0		05-Jan-11	96
1.3.6	2CR0P3990R99	Parcel 399, Cleared for Construction	0		06-Jan-11	95
1.3.6	2CR0P4000R99	Parcel 400, Cleared for Construction	0		06-Jan-11	95
1.3.6	2CR0P4040R99	Parcel 404, Cleared for Construction	0		06-Jan-11	92
1.3.6	2CR0P4050R99	Parcel 405, Cleared for Construction	0		06-Jan-11	92
1.3.6	2CR0P4110R99	Parcel 411, Cleared for Construction	0		06-Jan-11	92
1.3.6	2CR0P4120R99	Parcel 412, Cleared for Construction	0		06-Jan-11	92
1.3.6	2CR0P3250R99	Parcel 325, Cleared for Construction	0		06-Jan-11	92
1.3.6	2CR0P3320R99	Parcel 332, Cleared for Construction	0		06-Jan-11	95

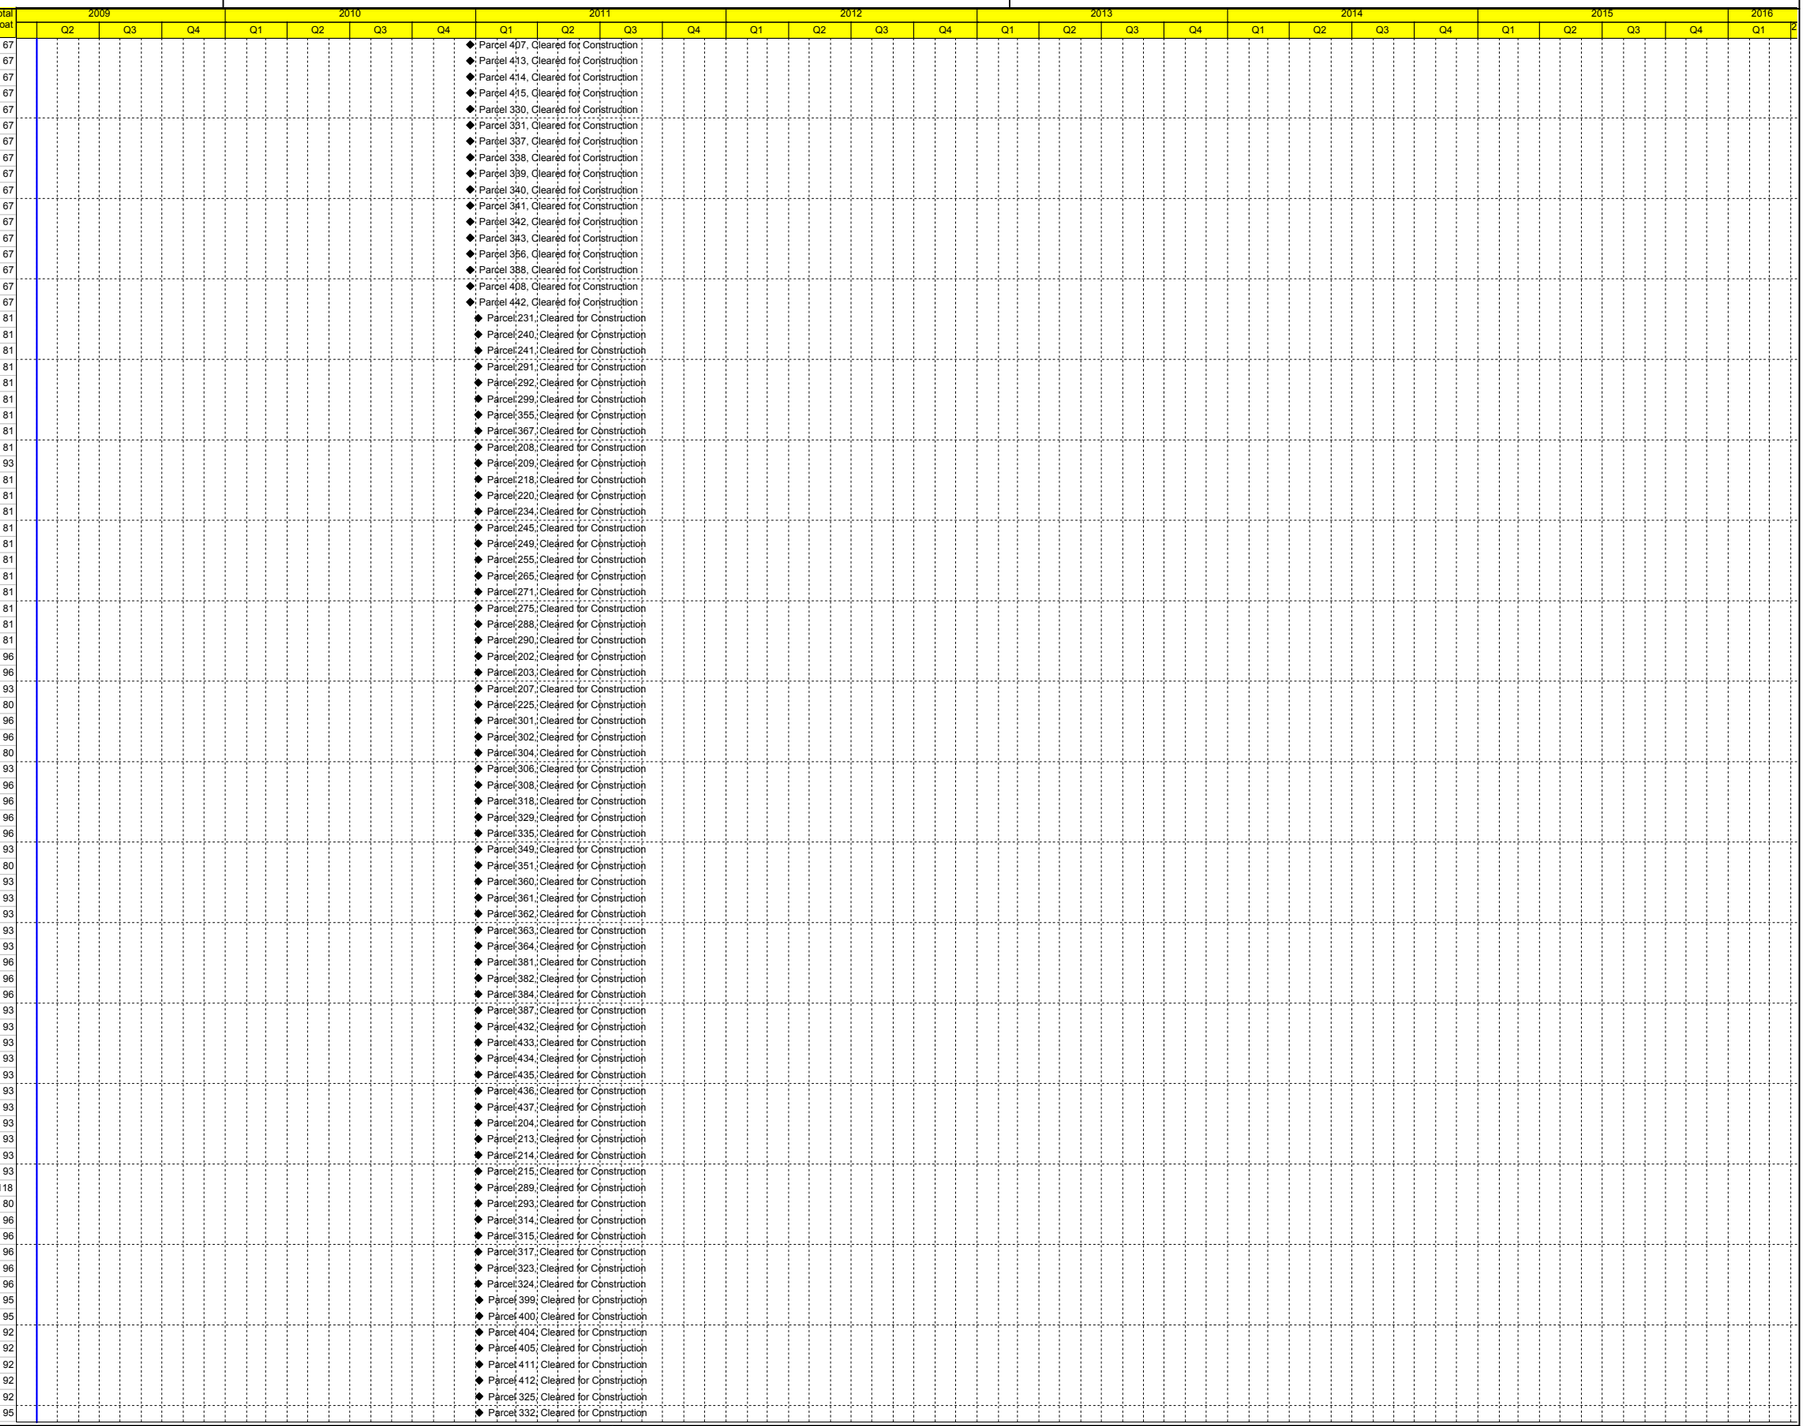

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.3.6	2CR0P3330R99	Parcel 333, Cleared for Construction	0		06-Jan-11	95
1.3.6	2CR0P3340R99	Parcel 334, Cleared for Construction	0		06-Jan-11	95
1.3.6	2CR0P3360R99	Parcel 336, Cleared for Construction	0		06-Jan-11	95
1.3.6	2CR0P3530R99	Parcel 353, Cleared for Construction	0		06-Jan-11	79
1.3.6	2CR0P3570R99	Parcel 357, Cleared for Construction	0		06-Jan-11	79
1.3.6	2CR0P3580R99	Parcel 358, Cleared for Construction	0		06-Jan-11	92
1.3.6	2CR0P3850R99	Parcel 385, Cleared for Construction	0		06-Jan-11	92
1.3.6	2CR0P3860R99	Parcel 386, Cleared for Construction	0		06-Jan-11	92
1.3.6	2CR0P3950R99	Parcel 395, Cleared for Construction	0		06-Jan-11	92
1.3.6	2CR0P3960R99	Parcel 396, Cleared for Construction	0		06-Jan-11	92
1.3.6	2CR0P3970R99	Parcel 397, Cleared for Construction	0		06-Jan-11	92
1.3.6	2CR0P3980R99	Parcel 398, Cleared for Construction	0		06-Jan-11	95
1.3.6	2CR0P4380R99	Parcel 438, Cleared for Construction	0		06-Jan-11	92
1.3.6	2CR0P2350R70	Parcel 235, Execute Relocation	20	11-Jan-11	08-Feb-11	68
1.3.6	2CR0P2160R80	Parcel 216, Demolish Existing Improvements	20	17-Jan-11	14-Feb-11	68
1.3.6	2CR0P3030R99	Parcel 303, Cleared for Construction	0		21-Jan-11	68
1.3.6	2CR0P2000R99	Parcel 200, Cleared for Construction	0		28-Jan-11	79
1.3.6	2CR0P2380R99	Parcel 238, Cleared for Construction	0		28-Jan-11	148
1.3.6	2CR0P2390R99	Parcel 239, Cleared for Construction	0		28-Jan-11	148
1.3.6	2CR0P2420R99	Parcel 242, Cleared for Construction	0		28-Jan-11	198
1.3.6	2CR0P2540R99	Parcel 254, Cleared for Construction	0		28-Jan-11	148
1.3.6	2CR0P2590R99	Parcel 259, Cleared for Construction	0		28-Jan-11	148
1.3.6	2CR0P2600R99	Parcel 260, Cleared for Construction	0		28-Jan-11	198
1.3.6	2CR0P3270R99	Parcel 327, Cleared for Construction	0		28-Jan-11	198
1.3.6	2CR0P3520R99	Parcel 352, Cleared for Construction	0		28-Jan-11	76
1.3.6	2CR0P3590R99	Parcel 359, Cleared for Construction	0		28-Jan-11	148
1.3.6	2CR0P3660R99	Parcel 366, Cleared for Construction	0		28-Jan-11	148
1.3.6	2CR0P3690R99	Parcel 369, Cleared for Construction	0		28-Jan-11	198
1.3.6	2CR0P3890R99	Parcel 389, Cleared for Construction	0		28-Jan-11	76
1.3.6	2CR0P3900R99	Parcel 390, Cleared for Construction	0		28-Jan-11	76
1.3.6	2CR0P3910R99	Parcel 391, Cleared for Construction	0		28-Jan-11	76
1.3.6	2CR0P3920R99	Parcel 392, Cleared for Construction	0		28-Jan-11	76
1.3.6	2CR0P3930R99	Parcel 393, Cleared for Construction	0		28-Jan-11	76
1.3.6	2CR0P3940R99	Parcel 394, Cleared for Construction	0		28-Jan-11	76
1.3.6	2CR0P4010R99	Parcel 401, Cleared for Construction	0		28-Jan-11	76
1.3.6	2CR0P4090R99	Parcel 409, Cleared for Construction	0		28-Jan-11	198
1.3.6	2CR0P4100R99	Parcel 410, Cleared for Construction	0		28-Jan-11	198
1.3.6	2CR0P4160R99	Parcel 416, Cleared for Construction	0		28-Jan-11	198
1.3.6	2CR0P4170R99	Parcel 417, Cleared for Construction	0		28-Jan-11	198
1.3.6	2CR0P4190R99	Parcel 419, Cleared for Construction	0		28-Jan-11	198
1.3.6	2CR0P4220R99	Parcel 422, Cleared for Construction	0		28-Jan-11	198
1.3.6	2CR0P4230R99	Parcel 423, Cleared for Construction	0		28-Jan-11	198
1.3.6	2CR0P4240R99	Parcel 424, Cleared for Construction	0		28-Jan-11	198
1.3.6	2CR0P4260R99	Parcel 426, Cleared for Construction	0		28-Jan-11	198
1.3.6	2CR0P4270R99	Parcel 427, Cleared for Construction	0		28-Jan-11	198
1.3.6	2CR0P4290R99	Parcel 429, Cleared for Construction	0		28-Jan-11	198
1.3.6	2CR0P4300R99	Parcel 430, Cleared for Construction	0		28-Jan-11	198
1.3.6	2CR0P4430R99	Parcel 443, Cleared for Construction	0		28-Jan-11	148
1.3.6	2CR0P4440R99	Parcel 444, Cleared for Construction	0		28-Jan-11	148
1.3.6	2CR0P4450R99	Parcel 445, Cleared for Construction	0		28-Jan-11	148
1.3.6	2CR0P4460R99	Parcel 446, Cleared for Construction	0		28-Jan-11	148
1.3.6	2CR0P4470R99	Parcel 447, Cleared for Construction	0		28-Jan-11	148
1.3.6	2CR0P4490R99	Parcel 449, Cleared for Construction	0		28-Jan-11	148
1.3.6	2CR0P4500R99	Parcel 450, Cleared for Construction	0		28-Jan-11	148
1.3.6	2CR0P4510R99	Parcel 451, Cleared for Construction	0		28-Jan-11	148
1.3.6	2CR0P2050R70	Parcel 205, Execute Relocation	20	28-Jan-11	25-Feb-11	108
1.3.6	2CR0P2100R70	Parcel 210, Execute Relocation	20	28-Jan-11	25-Feb-11	108
1.3.6	2CR0P2190R70	Parcel 219, Execute Relocation	20	28-Jan-11	25-Feb-11	108
1.3.6	2CR0P2230R70	Parcel 223, Execute Relocation	20	28-Jan-11	25-Feb-11	108
1.3.6	2CR0P2240R70	Parcel 224, Execute Relocation	20	28-Jan-11	25-Feb-11	108
1.3.6	2CR0P2360R70	Parcel 236, Execute Relocation	20	28-Jan-11	25-Feb-11	108
1.3.6	2CR0P2370R70	Parcel 237, Execute Relocation	20	28-Jan-11	25-Feb-11	108
1.3.6	2CR0P2500R70	Parcel 250, Execute Relocation	20	28-Jan-11	25-Feb-11	158
1.3.6	2CR0P2520R70	Parcel 252, Execute Relocation	20	28-Jan-11	25-Feb-11	158
1.3.6	2CR0P2530R70	Parcel 253, Execute Relocation	20	28-Jan-11	25-Feb-11	158
1.3.6	2CR0P2560R70	Parcel 256, Execute Relocation	20	28-Jan-11	25-Feb-11	108
1.3.6	2CR0P2570R70	Parcel 257, Execute Relocation	20	28-Jan-11	25-Feb-11	158
1.3.6	2CR0P2640R70	Parcel 264, Execute Relocation	20	28-Jan-11	25-Feb-11	158
1.3.6	2CR0P2660R70	Parcel 266, Execute Relocation	20	28-Jan-11	25-Feb-11	158
1.3.6	2CR0P2670R70	Parcel 267, Execute Relocation	20	28-Jan-11	25-Feb-11	158
1.3.6	2CR0P2770R70	Parcel 277, Execute Relocation	20	28-Jan-11	25-Feb-11	158
1.3.6	2CR0P2780R70	Parcel 278, Execute Relocation	20	28-Jan-11	25-Feb-11	158
1.3.6	2CR0P2850R70	Parcel 285, Execute Relocation	20	28-Jan-11	25-Feb-11	158
1.3.6	2CR0P5920R70	Parcel 592, Execute Relocation	20	28-Jan-11	25-Feb-11	1108
1.3.6	2CR0P2940R70	Parcel 294, Execute Relocation	20	28-Jan-11	25-Feb-11	108
1.3.6	2CR0P2950R70	Parcel 295, Execute Relocation	20	28-Jan-11	25-Feb-11	108
1.3.6	2CR0P2960R70	Parcel 296, Execute Relocation	20	28-Jan-11	25-Feb-11	108
1.3.6	2CR0P2970R70	Parcel 297, Execute Relocation	20	28-Jan-11	25-Feb-11	108
1.3.6	2CR0P3220R70	Parcel 322, Execute Relocation	20	28-Jan-11	25-Feb-11	108
1.3.6	2CR0P4180R70	Parcel 418, Execute Relocation	20	28-Jan-11	25-Feb-11	158
1.3.6	2CR0P4200R70	Parcel 420, Execute Relocation	20	28-Jan-11	25-Feb-11	158
1.3.6	2CR0P4210R70	Parcel 421, Execute Relocation	20	28-Jan-11	25-Feb-11	158
1.3.6	2CR0P4280R70	Parcel 428, Execute Relocation	20	28-Jan-11	25-Feb-11	158
1.3.6	2CR0P4480R70	Parcel 448, Execute Relocation	20	28-Jan-11	25-Feb-11	108
1.3.6	2CR0P4520R70	Parcel 452, Execute Relocation	20	28-Jan-11	25-Feb-11	108
1.3.6	2CR0P2350R80	Parcel 235, Demolish Existing Improvements	20	08-Feb-11	08-Mar-11	68

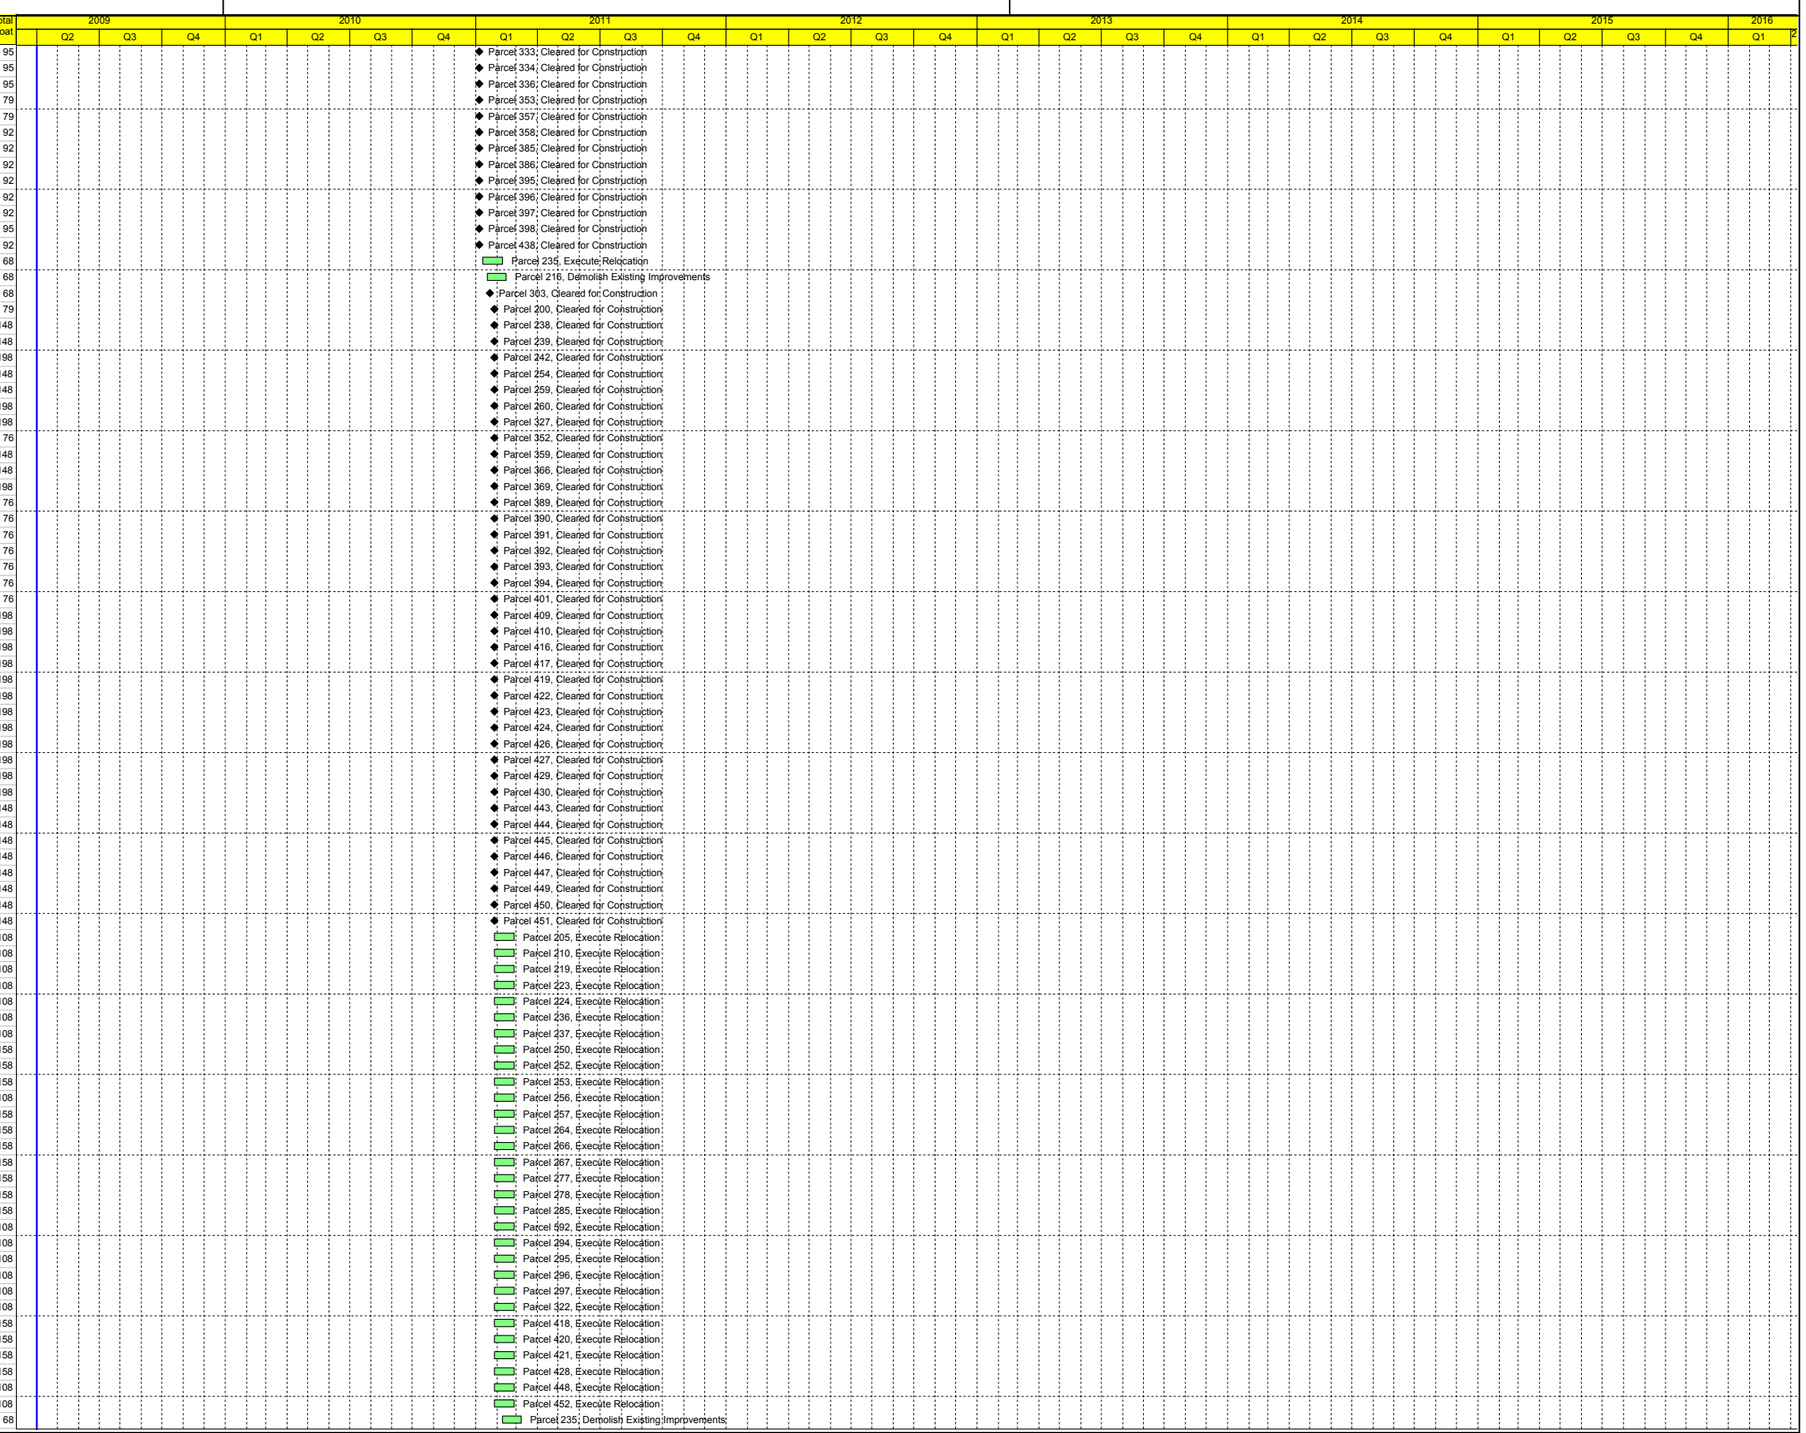

Remaining Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.3.6	2CR0P2160R99	Parcel 216, Cleared for Construction	0		14-Feb-11	68
1.3.6	2CR0P2050R80	Parcel 205, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	108
1.3.6	2CR0P2100R80	Parcel 210, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	108
1.3.6	2CR0P2190R80	Parcel 219, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	108
1.3.6	2CR0P2230R80	Parcel 223, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	108
1.3.6	2CR0P2240R80	Parcel 224, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	108
1.3.6	2CR0P2360R80	Parcel 236, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	108
1.3.6	2CR0P2370R80	Parcel 237, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	108
1.3.6	2CR0P2500R80	Parcel 250, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	158
1.3.6	2CR0P2520R80	Parcel 252, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	158
1.3.6	2CR0P2530R80	Parcel 253, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	158
1.3.6	2CR0P2560R80	Parcel 256, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	108
1.3.6	2CR0P2570R80	Parcel 257, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	158
1.3.6	2CR0P2640R80	Parcel 264, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	158
1.3.6	2CR0P2660R80	Parcel 266, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	158
1.3.6	2CR0P2670R80	Parcel 267, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	158
1.3.6	2CR0P2770R80	Parcel 277, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	158
1.3.6	2CR0P2780R80	Parcel 278, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	158
1.3.6	2CR0P2850R80	Parcel 285, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	158
1.3.6	2CR0P5920R80	Parcel 592, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	1108
1.3.6	2CR0P2940R80	Parcel 294, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	108
1.3.6	2CR0P2950R80	Parcel 295, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	108
1.3.6	2CR0P2960R80	Parcel 296, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	108
1.3.6	2CR0P2970R80	Parcel 297, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	108
1.3.6	2CR0P3220R80	Parcel 322, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	108
1.3.6	2CR0P4180R80	Parcel 418, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	158
1.3.6	2CR0P4200R80	Parcel 420, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	158
1.3.6	2CR0P4210R80	Parcel 421, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	158
1.3.6	2CR0P4280R80	Parcel 428, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	158
1.3.6	2CR0P4480R80	Parcel 448, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	108
1.3.6	2CR0P4520R80	Parcel 452, Demolish Existing Improvements	20	25-Feb-11	25-Mar-11	108
1.3.6	2CR0P2350R99	Parcel 235, Cleared for Construction	0		08-Mar-11	68
1.3.6	2CR0P2050R99	Parcel 205, Cleared for Construction	0		25-Mar-11	108
1.3.6	2CR0P2100R99	Parcel 210, Cleared for Construction	0		25-Mar-11	108
1.3.6	2CR0P2190R99	Parcel 219, Cleared for Construction	0		25-Mar-11	108
1.3.6	2CR0P2230R99	Parcel 223, Cleared for Construction	0		25-Mar-11	108
1.3.6	2CR0P2240R99	Parcel 224, Cleared for Construction	0		25-Mar-11	108
1.3.6	2CR0P2360R99	Parcel 236, Cleared for Construction	0		25-Mar-11	108
1.3.6	2CR0P2370R99	Parcel 237, Cleared for Construction	0		25-Mar-11	108
1.3.6	2CR0P2500R99	Parcel 250, Cleared for Construction	0		25-Mar-11	158
1.3.6	2CR0P2520R99	Parcel 252, Cleared for Construction	0		25-Mar-11	158
1.3.6	2CR0P2530R99	Parcel 253, Cleared for Construction	0		25-Mar-11	158
1.3.6	2CR0P2560R99	Parcel 256, Cleared for Construction	0		25-Mar-11	108
1.3.6	2CR0P2570R99	Parcel 257, Cleared for Construction	0		25-Mar-11	158
1.3.6	2CR0P2640R99	Parcel 264, Cleared for Construction	0		25-Mar-11	158
1.3.6	2CR0P2660R99	Parcel 266, Cleared for Construction	0		25-Mar-11	158
1.3.6	2CR0P2670R99	Parcel 267, Cleared for Construction	0		25-Mar-11	158
1.3.6	2CR0P2770R99	Parcel 277, Cleared for Construction	0		25-Mar-11	158
1.3.6	2CR0P2780R99	Parcel 278, Cleared for Construction	0		25-Mar-11	158
1.3.6	2CR0P2850R99	Parcel 285, Cleared for Construction	0		25-Mar-11	158
1.3.6	2CR0P2940R99	Parcel 294, Cleared for Construction	0		25-Mar-11	108
1.3.6	2CR0P2950R99	Parcel 295, Cleared for Construction	0		25-Mar-11	108
1.3.6	2CR0P2960R99	Parcel 296, Cleared for Construction	0		25-Mar-11	108
1.3.6	2CR0P2970R99	Parcel 297, Cleared for Construction	0		25-Mar-11	108
1.3.6	2CR0P3220R99	Parcel 322, Cleared for Construction	0		25-Mar-11	108
1.3.6	2CR0P4180R99	Parcel 418, Cleared for Construction	0		25-Mar-11	158
1.3.6	2CR0P4200R99	Parcel 420, Cleared for Construction	0		25-Mar-11	158
1.3.6	2CR0P4210R99	Parcel 421, Cleared for Construction	0		25-Mar-11	158
1.3.6	2CR0P4280R99	Parcel 428, Cleared for Construction	0		25-Mar-11	158
1.3.6	2CR0P4480R99	Parcel 448, Cleared for Construction	0		25-Mar-11	108
1.3.6	2CR0P4520R99	Parcel 452, Cleared for Construction	0		25-Mar-11	108
UTILITY RELOCATIONS			406	19-Mar-10	10-Oct-11	534
1.4.C	2C6UC00UAA	Prep Assembly, Seg 2C Cable, Charter (Opt 6)	20	19-Mar-10	16-Apr-10	303
1.4.C1	2C6UC01UAA	Prep Assembly, Seg 2C Cable, Comcast (Op...	20	19-Mar-10	16-Apr-10	299
1.4.WW3	2C6UWW3UAA	Prep Assembly, Seg 2C Wastewater, TRA (O...	20	19-Mar-10	16-Apr-10	865
1.4.T8	2C6UT08UAA	Prep Assembly, Seg 2C Comm, Verizon (Opt...	20	19-Mar-10	16-Apr-10	295
1.4.WW4	2C6UWW4UAA	Prep Assembly, Seg 2C Wastewater, N. Rich...	20	19-Mar-10	16-Apr-10	834
1.4.W5	2C6UW05UAA	Prep Assembly, Seg 2C Water, N. Richland ...	23	19-Mar-10	21-Apr-10	276
1.4.WW2	2C6UWW2UAA	Prep Assembly, Seg 2C Wastewater, Hurst (...	25	19-Mar-10	23-Apr-10	265
1.4.E1	2C6UE01UAA	Prep Assembly, Seg 2C Electric, TXU (Opt 6)	34	19-Mar-10	06-May-10	260
1.4.WW1	2C6UWW1UAA	Prep Assembly, Seg 2C Wastewater, Bedfor...	53	19-Mar-10	02-Jun-10	203
1.4.G2	2C6UG02UAA	Prep Assembly, Seg 2C Gas, Atmos (Opt 6)	61	19-Mar-10	14-Jun-10	249
1.4.W3	2C6UW03UAA	Prep Assembly, Seg 2C Water Hurst (Opt 6)	74	19-Mar-10	01-Jul-10	204
1.4.T1	2C6UT01UAA	Prep Assembly, Seg 2C Comm, AT&T (Opt 6)	79	19-Mar-10	08-Jul-10	237
1.4.W1	2C6UW01UAA	Prep Assembly, Seg 2C Water, Bedford (Opt 6)	103	19-Mar-10	11-Aug-10	188
1.4.C	2C6UC00TX	TxDOT Review, Seg 2C Cable, Charter (Opt 6)	10	16-Apr-10	30-Apr-10	303
1.4.C1	2C6UC01TX	TxDOT Review, Seg 2C Cable, Comcast (Op...	10	16-Apr-10	30-Apr-10	299
1.4.WW3	2C6UWW3TX	TxDOT Review, Seg 2C Wastewater, TRA (O...	10	16-Apr-10	30-Apr-10	865
1.4.T8	2C6UT08TX	TxDOT Review, Seg 2C Comm, Verizon (Opt 6)	10	16-Apr-10	30-Apr-10	295
1.4.WW4	2C6UWW4TX	TxDOT Review, Seg 2C Wastewater, N. Rich...	10	16-Apr-10	30-Apr-10	834
1.4.W5	2C6UW05TX	TxDOT Review, Seg 2C Water, N. Richland ...	10	21-Apr-10	05-May-10	276
1.4.WW2	2C6UWW2TX	TxDOT Review, Seg 2C Wastewater, Hurst (...	10	23-Apr-10	07-May-10	265
1.4.WW3	2C6UWW3	Seg 2C, Relocate Wastewater, TRA (Opt 6)	45	30-Apr-10	02-Jul-10	865
1.4.E1	2C6UE01TX	TxDOT Review, Seg 2C Electric, TXU (Opt 6)	10	06-May...	20-May-10	260
1.4.WW1	2C6UWW1TX	TxDOT Review, Seg 2C Wastewater, Bedfor...	10	02-Jun-10	16-Jun-10	203
1.4.G2	2C6UG02TX	TxDOT Review, Seg 2C Gas, Atmos (Opt 6)	10	14-Jun-10	28-Jun-10	249

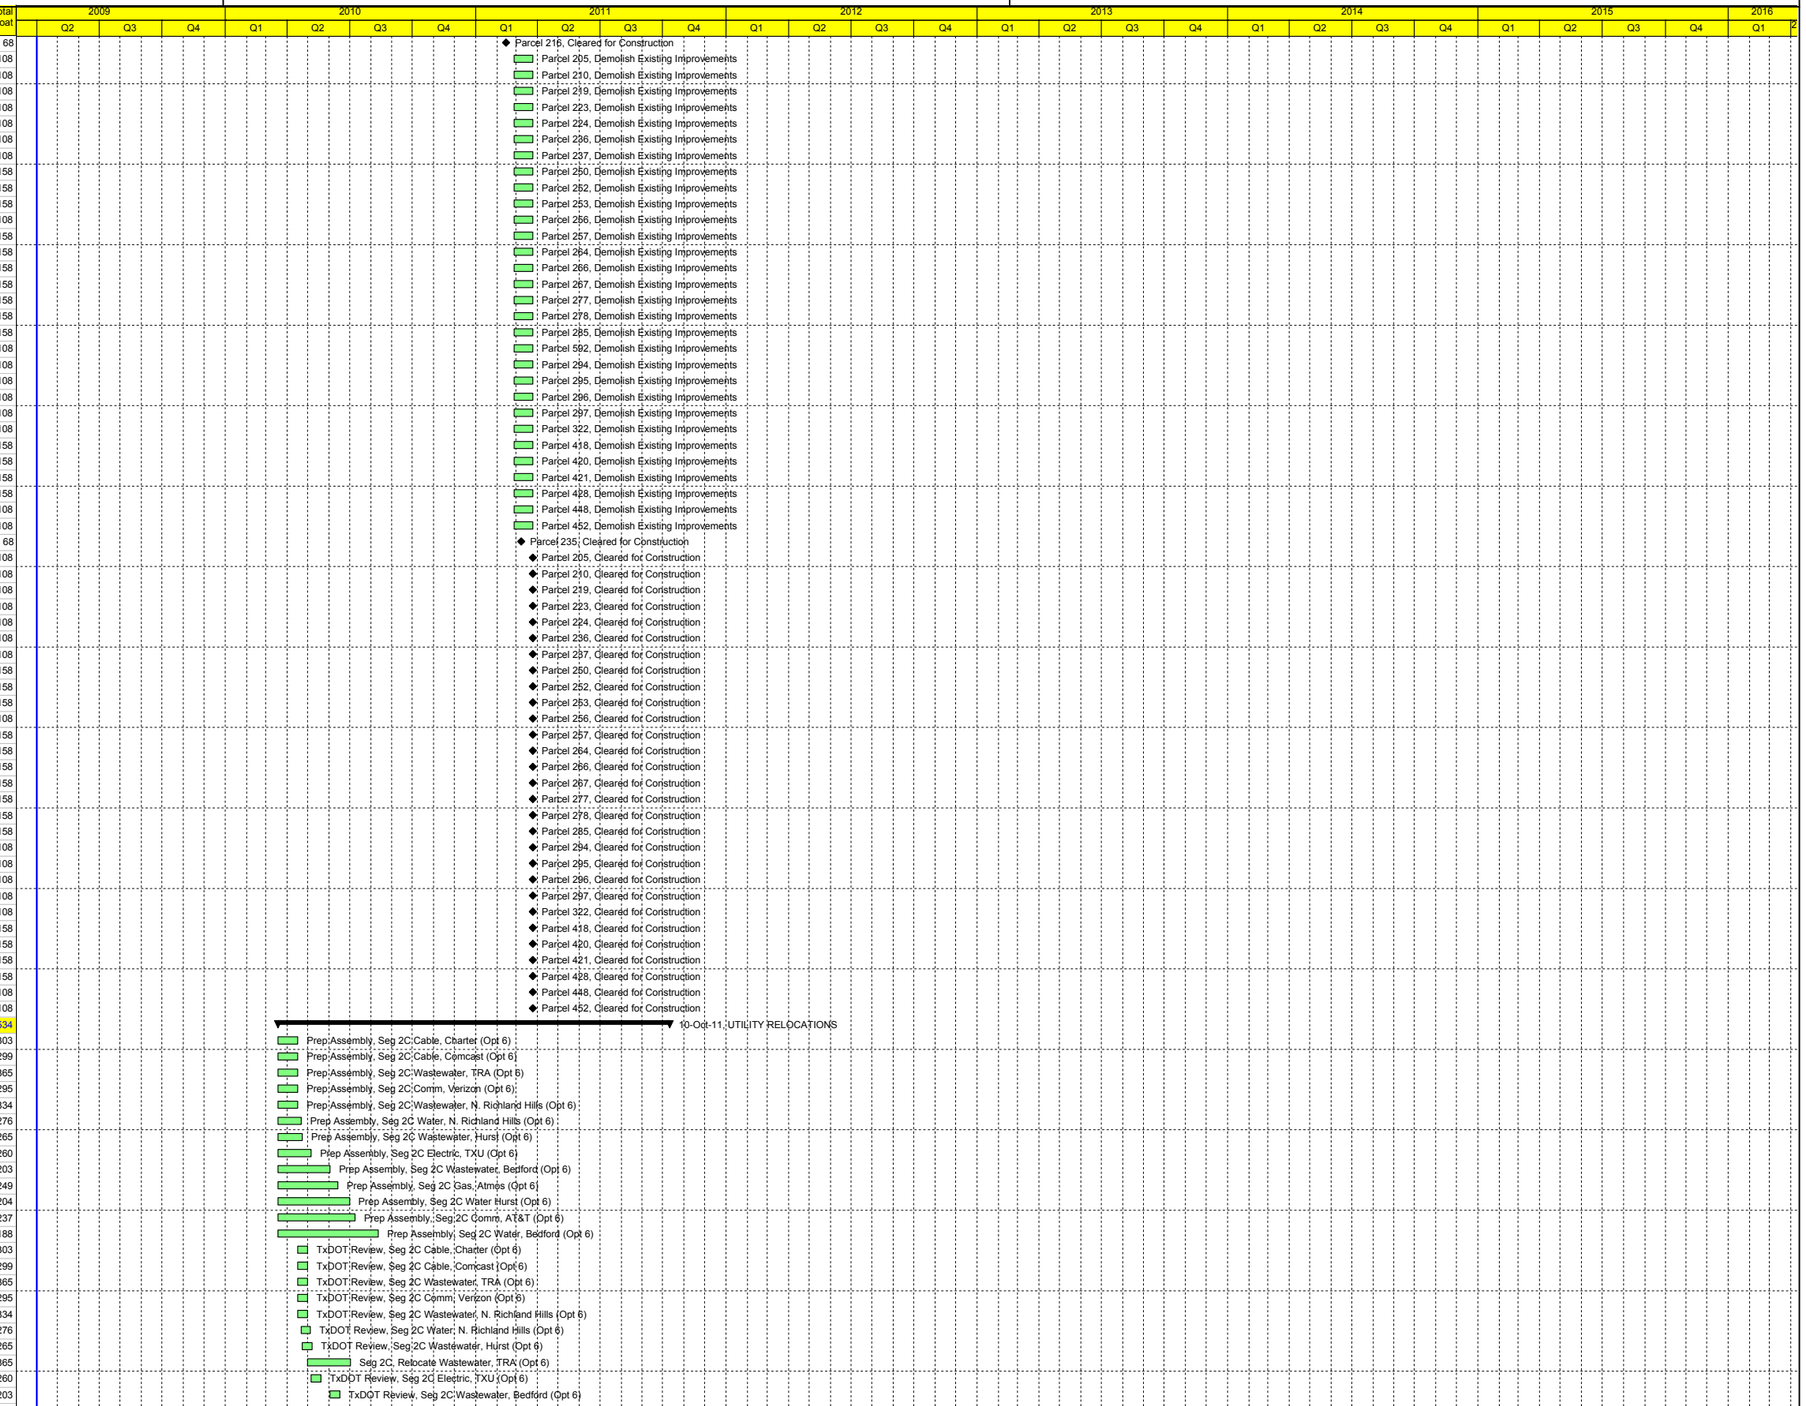

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.4.W3	2C6UW03TX	TxDOT Review, Seg 2C Water Hurst (Opt 6)	10	01-Jul-10	15-Jul-10	204
1.4.T1	2C6UT01TX	TxDOT Review, Seg 2C Comm, AT&T (Opt 6)	10	08-Jul-10	22-Jul-10	237
1.4.W1	2C6UW01TX	TxDOT Review, Seg 2C Water, Bedford (Opt 6)	10	11-Aug-...	25-Aug-10	188
1.4.C	2C6UC00	Seg 2C, Relocate Cable, Charter (Opt 6)	40	23-Dec-...	17-Feb-11	134
1.4.WW1	2C6UWW1	Seg 2C, Relocate Wastewater, Bedford (Opt ...	132	23-Dec-...	27-Jun-11	67
1.4.WW2	2C6UWW2	Seg 2C, Relocate Wastewater, Hurst (Opt 6)	123	04-Jan-11	24-Jun-11	93
1.4.WW4	2C6UWW4	Seg 2C, Relocate Wastewater, N. Richland ...	76	05-Jan-11	21-Apr-11	656
1.4.T1	2C6UT01	Seg 2C, Relocate Comm, AT&T (Opt 6) (2 cr...	197	06-Jan-11	10-Oct-11	117
1.4.C1	2C6UC01	Seg 2C, Relocate Cable, Comcast (Opt 6)	44	21-Jan-11	24-Mar-11	109
1.4.W3	2C6UW03	Seg 2C, Relocate Water Hurst (Opt 6) (2 cre...	185	21-Jan-11	07-Oct-11	68
1.4.T8	2C6UT08	Seg 2C, Relocate Comm, Verizon (Opt 6)	48	28-Jan-11	06-Apr-11	100
1.4.W5	2C6UW05	Seg 2C, Relocate Water, N. Richland Hills (O...	114	28-Jan-11	07-Jul-11	84
1.4.W1	2C6UW01	Seg 2C, Relocate Water, Bedford (Opt 6) (3 ...	172	28-Jan-11	27-Sep-11	76
1.4.E1	2C6UE01	Seg 2C, Relocate Electric, TXU (Opt 6)	169	14-Feb-11	07-Oct-11	68
1.4.G2	2C6UG02	Seg 2C, Relocate Gas, Atmos (Opt 6) (2 crews)	153	08-Mar-11	07-Oct-11	68
CONSTRUCTION MILESTONES			1018	23-May...	16-Apr-15	49
1.5	2C00EF60000001	START EB Frontage Roads - US 183	0	23-May...		67
1.5	2C00WF600000...	START WB Frontage Roads - Subsegment C	0	24-Jun-11		93
1.5	2C00XU60000001	START Crossroad Underpasses - Subsegme...	0	27-Jun-11		773
1.5	2C00SF60000001	START SB Frontage Roads - SH 121	0	07-Oct-11		150
1.5	2C00EG60000001	START EB General Purpose Lanes - Subseg...	0	10-Oct-11		132
1.5	2C00RP60000001	START Ramps - Subsegment C	0	10-Oct-11		164
1.5	2C00WG60000...	START WB General Purpose Lanes - Subse...	0	10-Oct-11		160
1.5	2C00XR60000001	START Crossroad Overpasses - Subsegment C	0	10-Oct-11		852
1.5	2C00SG60000001	START SB General Purpose Lanes - SH 121	0	30-Dec-...		150
1.5	2C00SF60099999	FINISH SB Frontage Roads - SH 121	0		24-Feb-12	868
1.5	2C00XR60099999	FINISH Crossroad Overpasses - Subsegmen...	0		19-Mar-12	852
1.5	2C00NG60000001	START NB General Purpose Lanes - SH 121	0	30-May...		157
1.5	2C00EF60099999	FINISH EB Frontage Roads - US 183	0		19-Sep-12	720
1.5	2C00WF600999...	FINISH WB Frontage Roads - Subsegment C	0		17-Oct-12	700
1.5	2C00NG60099999	FINISH NB General Purpose Lanes - SH 121	0		26-Feb-13	606
1.5	2C00ML60000001	START Managed Lanes - Subsegment C	0	24-Jul-13		67
1.5	2C00SG60099999	FINISH SB General Purpose Lanes - SH 121	0		03-Apr-14	319
1.5	2C00EG60099999	FINISH EB General Purpose Lanes - Subseg...	0		05-Aug-14	231
1.5	2C00RP60099999	FINISH Ramps - Subsegment C	0		08-Sep-14	207
1.5	2C00XU60099999	FINISH Crossroad Underpasses - Subsegme...	0		12-Dec-14	138
1.5	2C00WG60099...	FINISH WB General Purpose Lanes - Subse...	0		04-Mar-15	80
1.5	2C00ML60099999	FINISH Managed Lanes - Subsegment C	0		16-Apr-15	49
CONSTRUCTION PHASE 1			367	23-May...	17-Oct-12	700
1.5	2C10EF60000001	Area EF6, PH 1, Start	0	23-May...		67
1.5.2.6	2C10EF60050600	Area EF6, PH 1, Place Temp Erosion Control	53	23-May...	04-Aug-11	67
1.5.7.6	2C10EF60090010	Area EF6, PH 1, Install Noise Walls (2 crews)	34	30-May...	15-Jul-11	81
1.5.2.6	2C10EF60010410	Area EF6, PH 1, Rem Conc Pavement	23	17-Jun-11	20-Jul-11	81
1.5	2C10WF600000...	Area WF6, PH 1, Start	0	24-Jun-11		93
1.5.2.6	2C10WF600506...	Area WF6, PH 1, Place Temp Erosion Control	53	24-Jun-11	07-Sep-11	93
1.5	2C10XU60000001	Area XU6, PH 1, Start	0	27-Jun-11		879
1.5.2.6	2C10XU60050600	Area XU6, PH 1, Place Temp Erosion Control	13	27-Jun-11	14-Jul-11	879
1.5.7.6	2C10WF600900...	Area WF6, PH 1, Install Noise Walls	68	01-Jul-11	05-Oct-11	98
1.5.2.6	2C10XU60010410	Area XU6, PH 1, Rem Conc Pavement	3	14-Jul-11	19-Jul-11	879
1.5.3.6	2C10XU60046420	Area XU6, PH 1, Install Medium RCP	6	19-Jul-11	27-Jul-11	894
1.5.8.6	2C10XU60062899	Area XU6, PH 1, Install Elec Service for ITS/...	15	19-Jul-11	09-Aug-11	973
1.5.2.6	2C10XU60026010	Area XU6, PH 1, Lime Treat Subgrade	38	19-Jul-11	09-Sep-11	879
1.5.8.6	2C10XU60061899	Area XU6, PH 1, Install ITS Duct Bank	3	27-Jul-11	01-Aug-11	979
1.5.3.6	2C10XU60046410	Area XU6, PH 1, Install Small RCP	10	27-Jul-11	10-Aug-11	894
1.5.2.6	2C10WF600104...	Area WF6, PH 1, Rem Conc Pavement	23	29-Jul-11	31-Aug-11	98
1.5.4.6	2C10WF600423...	Area WF6, PH 1, Install Cut Wall, Stage 1	110	29-Jul-11	30-Dec-11	102
1.5.3.6	2C10EF60046220	Area EF6, PH 1, Install Medium CBC	19	04-Aug-...	31-Aug-11	70
1.5.4.6	2C10EF60042320	Area EF6, PH 1, Install Cut Wall, Stage 1 (2 ...	108	04-Aug-...	03-Jan-12	67
1.5.3.6	2C10XU60046510	Area XU6, PH 1, Install MHs and Inlets	7	10-Aug-...	19-Aug-11	894
1.5.4.6	2C10WF600423...	Area WF6, PH 1, Install Fill Wall Complete	21	18-Aug-...	16-Sep-11	219
1.5.2.6	2C10WF600132...	Area WF6, PH 1, Place Embankment (2 crews)	71	18-Aug-...	25-Nov-11	110
1.5.2.6	2C10WF600110...	Area WF6, PH 1, Excavate Cut Areas (2 crews)	101	18-Aug-...	06-Jan-12	102
1.5.2.6	2C10EF60013210	Area EF6, PH 1, Place Embankment (2 crews)	71	22-Aug-...	29-Nov-11	97
1.5.2.6	2C10EF60011010	Area EF6, PH 1, Excavate Cut Areas (2 crews)	101	22-Aug-...	10-Jan-12	67
1.5.4.6	2C10EF60042325	Area EF6, PH 1, Install Cut Wall, Stage 2 (2 ...	162	29-Aug-...	11-Apr-12	128
1.5.3.6	2C10EF60046210	Area EF6, PH 1, Install Small CBC	13	31-Aug-...	19-Sep-11	148
1.5.3.6	2C10EF60046420	Area EF6, PH 1, Install Medium RCP	100	31-Aug-...	18-Jan-12	70
1.5.3.6	2C10WF600462...	Area WF6, PH 1, Install Medium CBC	19	07-Sep-...	04-Oct-11	93
1.5.2.6	2C10XU60024710	Area XU6, PH 1, Place Flexible Base	14	09-Sep-...	29-Sep-11	879
1.5.2.6	2C10EF60026010	Area EF6, PH 1, Lime Treat Subgrade	97	12-Sep-...	25-Jan-12	132
1.5.2.6	2C10WF600260...	Area WF6, PH 1, Lime Treat Subgrade	92	14-Sep-...	20-Jan-12	134
1.5.4.6	2C10WF600423...	Area WF6, PH 1, Install Cut Wall, Stage 2 (2 ...	83	27-Sep-...	20-Jan-12	181
1.5.2.6	2C10XU60052910	Area XU6, PH 1, Place Curb & Gutter	4	29-Sep-...	05-Oct-11	879
1.5.3.6	2C10WF600462...	Area WF6, PH 1, Install Small CBC	13	04-Oct-11	21-Oct-11	137
1.5.3.6	2C10WF600464...	Area WF6, PH 1, Install Medium RCP (2 crews)	55	04-Oct-11	20-Dec-11	93
1.5.2.6	2C10XU60034011	Area XU6, PH 1, Place HMA Base	20	05-Oct-11	02-Nov-11	879
1.5	2C10SF60000001	Area SF6, PH 1, Start	0	07-Oct-11		150
1.5.2.6	2C10SF60050600	Area SF6, PH 1, Place Temp Erosion Control	12	07-Oct-11	25-Oct-11	150
1.5	2C10EG60000001	Area EG6, PH 1, Start	0	10-Oct-11		911
1.5	2C10RP60000001	Area RP6, PH 1, Start	0	10-Oct-11		813
1.5	2C10WG60000...	Area WG6, PH 1, Start	0	10-Oct-11		882
1.5	2C10XR60000001	Area XR6, PH 1, Start	0	10-Oct-11		852
1.5.2.6	2C10RP60010410	Area RP6, PH 1, Rem Conc Pavement	4	10-Oct-11	14-Oct-11	813
1.5.2.6	2C10WG60050...	Area WG6, PH 1, Place Temp Erosion Control	5	10-Oct-11	17-Oct-11	882
1.5.2.6	2C10XR60050600	Area XR6, PH 1, Place Temp Erosion Control	6	10-Oct-11	18-Oct-11	860
1.5.4.6	2C10EG60042320	Area EG6, PH 1, Install Cut Wall, Stage 1	15	10-Oct-11	31-Oct-11	911

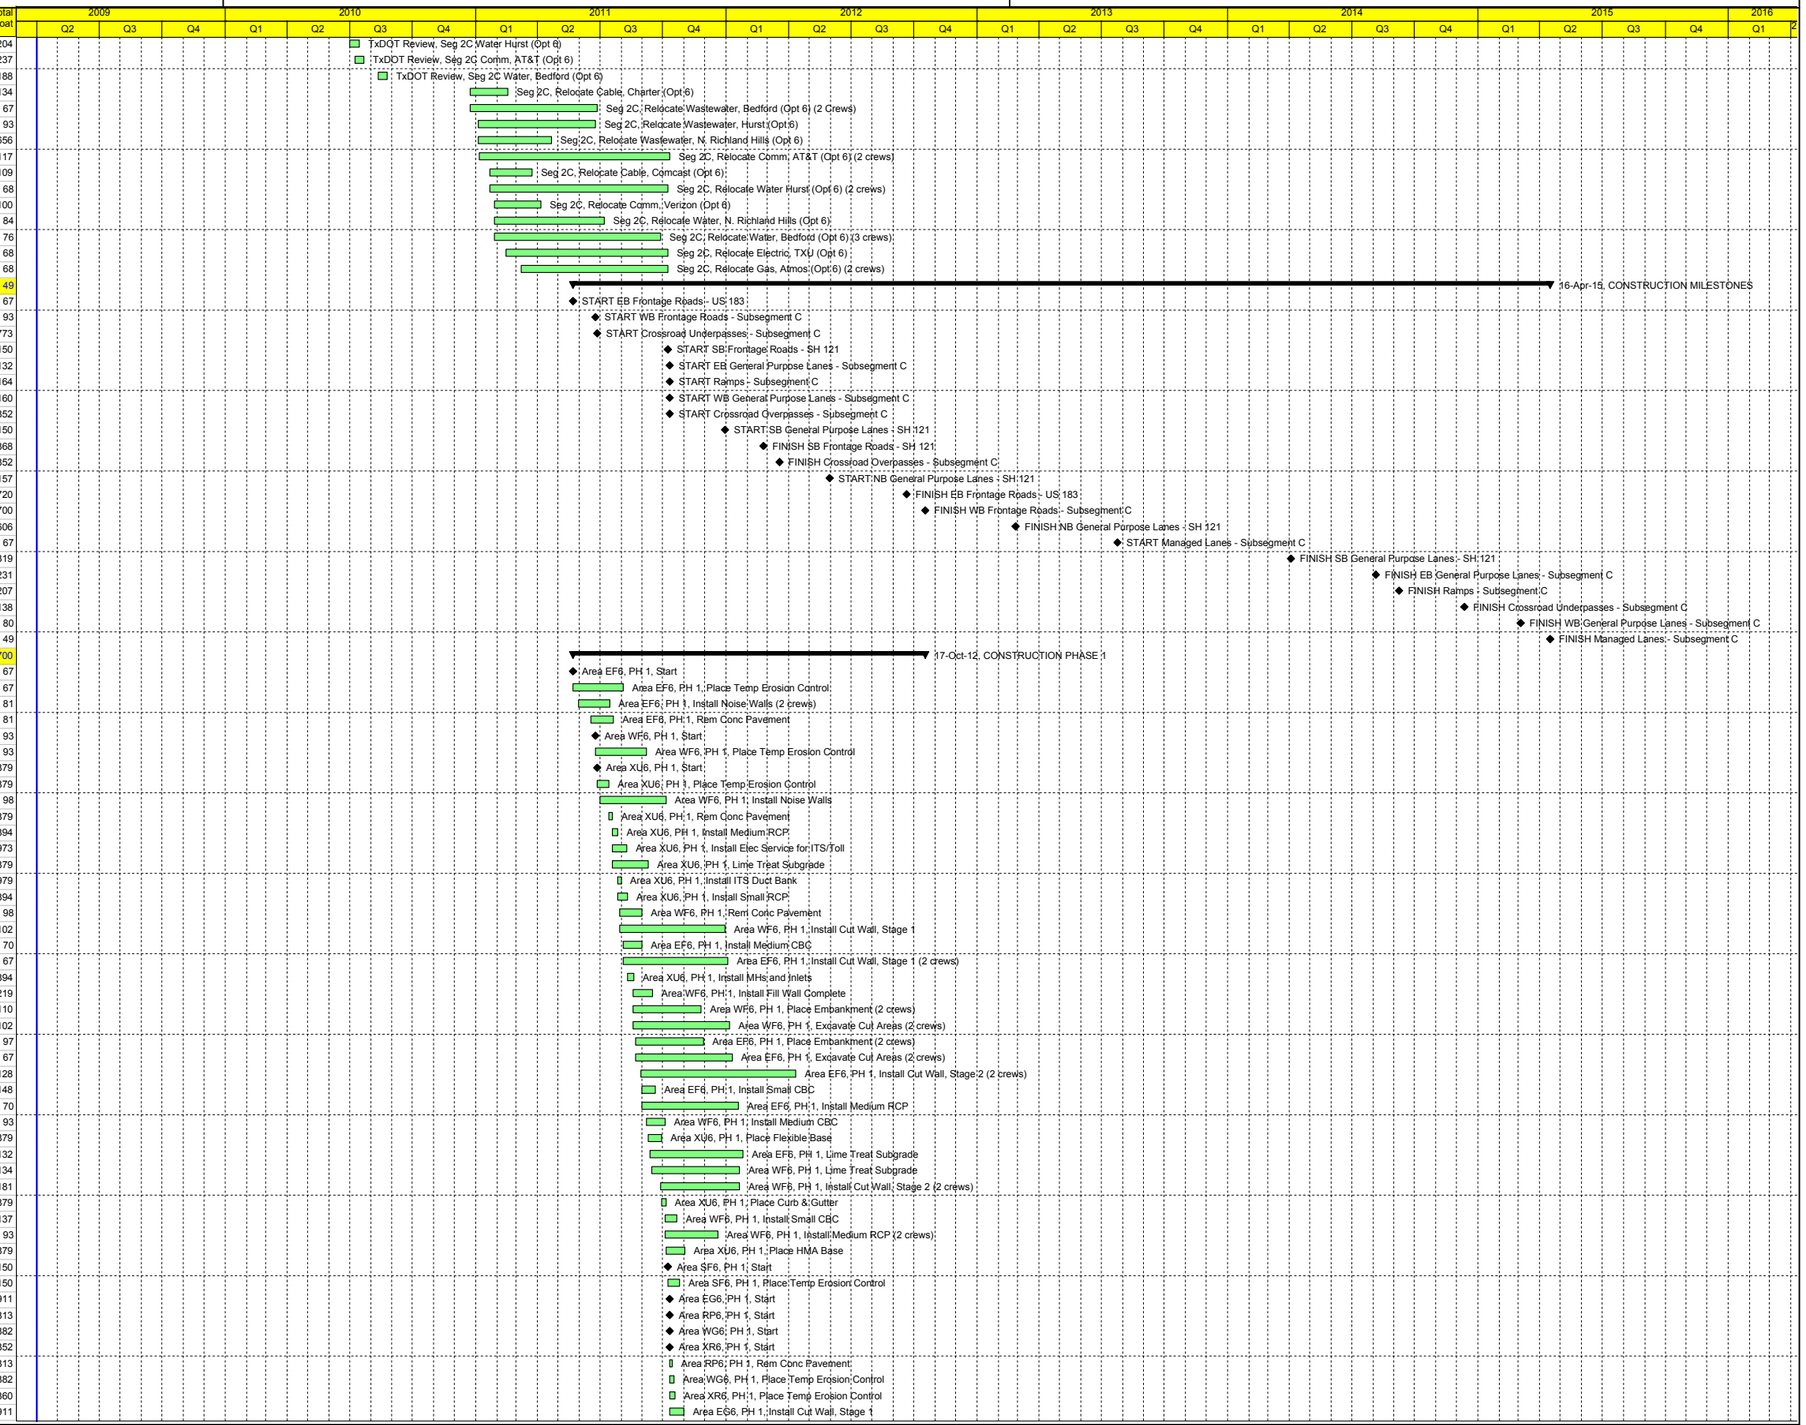

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.5.3.6	2C10RP60046220	Area RP6, PH 1, Install Medium CBC	2	14-Oct-11	18-Oct-11	861
1.5.2.6	2C10RP60013210	Area RP6, PH 1, Place Embankment	23	14-Oct-11	16-Nov-11	822
1.5.2.6	2C10RP60011010	Area RP6, PH 1, Excavate Cut Areas	32	14-Oct-11	29-Nov-11	813
1.5.2.6	2C10WG60054...	Area WG6, PH 1, Rem MBGF	1	17-Oct-11	18-Oct-11	884
1.5.2.6	2C10WG60060...	Area WG6, PH 1, Rem Light Poles	1	17-Oct-11	18-Oct-11	884
1.5.2.6	2C10WG60063...	Area WG6, PH 1, Rem Overhead Sign Supp...	3	17-Oct-11	20-Oct-11	882
1.5.3.6	2C10RP60046210	Area RP6, PH 1, Install Small CBC	1	18-Oct-11	19-Oct-11	861
1.5.2.6	2C10XR60010410	Area XR6, PH 1, Rem Conc Pavement	2	18-Oct-11	20-Oct-11	860
1.5.3.6	2C10RP60046420	Area RP6, PH 1, Install Medium RCP	3	19-Oct-11	24-Oct-11	861
1.5.2.6	2C10WG60010...	Area WG6, PH 1, Rem Concrete Barrier	2	20-Oct-11	24-Oct-11	882
1.5.3.6	2C10XR60046420	Area XR6, PH 1, Install Medium RCP	3	20-Oct-11	25-Oct-11	867
1.5.8.6	2C10XR60062899	Area XR6, PH 1, Install Elec Service for ITS/...	13	20-Oct-11	08-Nov-11	925
1.5.2.6	2C10XR60026010	Area XR6, PH 1, Lime Treat Subgrade	19	20-Oct-11	16-Nov-11	860
1.5.2.6	2C10WG60010...	Area WG6, PH 1, Rem Conc Pavement	1	24-Oct-11	25-Oct-11	882
1.5.4.6	2C10WG60042...	Area WG6, PH 1, Install Fill Wall Complete	3	25-Oct-11	28-Oct-11	888
1.5.8.6	2C10XR60061899	Area XR6, PH 1, Install ITS Duct Bank	3	25-Oct-11	28-Oct-11	932
1.5.3.6	2C10WG60046...	Area WG6, PH 1, Install Large CBC	4	25-Oct-11	31-Oct-11	908
1.5.3.6	2C10XR60046410	Area XR6, PH 1, Install Small RCP	5	25-Oct-11	01-Nov-11	867
1.5.2.6	2C10WG60013...	Area WG6, PH 1, Place Embankment	7	25-Oct-11	03-Nov-11	884
1.5.7.6	2C10SF60090010	Area SF6, PH 1, Install Noise Walls	8	25-Oct-11	04-Nov-11	150
1.5.2.6	2C10WG60011...	Area WG6, PH 1, Excavate Cut Areas	9	25-Oct-11	07-Nov-11	882
1.5.3.6	2C10WG60046...	Area WG6, PH 1, Install Medium CBC	2	31-Oct-11	02-Nov-11	908
1.5.4.6	2C10EG60042310	Area EG6, PH 1, Install Fill Wall Complete	9	31-Oct-11	11-Nov-11	920
1.5.4.6	2C10EG60042325	Area EG6, PH 1, Install Cut Wall, Stage 2	22	31-Oct-11	30-Nov-11	911
1.5.3.6	2C10XR60046510	Area XR6, PH 1, Install MHs and Inlets	4	01-Nov-...	07-Nov-11	867
1.5.3.6	2C10WG60046...	Area WG6, PH 1, Install Small CBC	2	02-Nov-...	04-Nov-11	908
1.5.9.6	2C10XU60066200	Area XU6, PH 1, Place Temp Marking & Sign...	2	02-Nov-...	04-Nov-11	948
1.5.7.6	2C10XU60061020	Area XU6, PH 1, Install Rdwy Illumination	15	02-Nov-...	23-Nov-11	912
1.5.7.6	2C10XU60068010	Area XU6, PH 1, Install Traffic Signal Systems	71	02-Nov-...	09-Feb-12	879
1.5.3.6	2C10WG60046...	Area WG6, PH 1, Install Medium RCP	1	04-Nov-...	07-Nov-11	908
1.5.2.6	2C10SF60010410	Area SF6, PH 1, Rem Conc Pavement	3	04-Nov-...	09-Nov-11	150
1.5.8.6	2C10WG60061...	Area WG6, PH 1, Install ITS Duct Bank	1	07-Nov-...	08-Nov-11	927
1.5.3.6	2C10WG60046...	Area WG6, PH 1, Install Small RCP	1	07-Nov-...	08-Nov-11	908
1.5.2.6	2C10WG60026...	Area WG6, PH 1, Lime Treat Subgrade	29	07-Nov-...	16-Dec-11	882
1.5.3.6	2C10WG60046...	Area WG6, PH 1, Install MHs and Inlets	2	08-Nov-...	10-Nov-11	908
1.5.8.6	2C10WG60041...	Area WG6, PH 1, Install ITS Structures & Equip	4	08-Nov-...	14-Nov-11	927
1.5.3.6	2C10SF60046220	Area SF6, PH 1, Install Medium CBC	3	09-Nov-...	14-Nov-11	156
1.5.2.6	2C10SF60013210	Area SF6, PH 1, Place Embankment	15	09-Nov-...	30-Nov-11	157
1.5.2.6	2C10SF60011010	Area SF6, PH 1, Excavate Cut Areas	22	09-Nov-...	09-Dec-11	150
1.5.4.6	2C10EG60042315	Area EG6, PH 1, Install Moment Slabs	4	11-Nov-...	17-Nov-11	920
1.5.3.6	2C10SF60046210	Area SF6, PH 1, Install Small CBC	2	14-Nov-...	16-Nov-11	156
1.5.2.6	2C10XR60024710	Area XR6, PH 1, Place Flexible Base	7	16-Nov-...	25-Nov-11	860
1.5.3.6	2C10SF60046420	Area SF6, PH 1, Install Medium RCP	12	16-Nov-...	02-Dec-11	156
1.5.2.6	2C10XU60034610	Area XU6, PH 1, Place SMA Surface	21	23-Nov-...	22-Dec-11	912
1.5.2.6	2C10XR60052910	Area XR6, PH 1, Place Curb & Gutter	2	25-Nov-...	29-Nov-11	860
1.5.3.6	2C10RP60046410	Area RP6, PH 1, Install Small RCP	4	29-Nov-...	05-Dec-11	835
1.5.2.6	2C10XR60034011	Area XR6, PH 1, Place HMA Base	10	29-Nov-...	13-Dec-11	860
1.5.2.6	2C10RP60026010	Area RP6, PH 1, Lime Treat Subgrade	31	29-Nov-...	11-Jan-12	813
1.5.9.6	2C10EG60050820	Area EG6, PH 1, Const Temp Detour	10	30-Nov-...	14-Dec-11	911
1.5.3.6	2C10RP60046510	Area RP6, PH 1, Install MHs and Inlets	5	05-Dec-...	12-Dec-11	835
1.5.3.6	2C10SF60046410	Area SF6, PH 1, Install Small RCP	5	09-Dec-...	16-Dec-11	151
1.5.8.6	2C10SF60061899	Area SF6, PH 1, Install ITS Duct Bank	8	09-Dec-...	21-Dec-11	166
1.5.2.6	2C10SF60026010	Area SF6, PH 1, Lime Treat Subgrade	11	09-Dec-...	26-Dec-11	150
1.5.9.6	2C10XR60066200	Area XR6, PH 1, Place Temp Marking & Sign...	1	13-Dec-...	14-Dec-11	920
1.5.7.6	2C10XR60061020	Area XR6, PH 1, Install Rdwy Illumination	9	13-Dec-...	26-Dec-11	900
1.5.7.6	2C10XR60068010	Area XR6, PH 1, Install Traffic Signal Systems	61	13-Dec-...	07-Mar-12	860
1.5.9.6	2C10EG60051200	Area EG6, PH 1, Place Temp Conc Barrier	9	14-Dec-...	27-Dec-11	911
1.5.4.6	2C10WG60042...	Area WG6, PH 1, Install Moment Slabs	2	16-Dec-...	20-Dec-11	885
1.5.3.6	2C10SF60046510	Area SF6, PH 1, Install MHs and Inlets	5	16-Dec-...	23-Dec-11	151
1.5.2.6	2C10WG60024...	Area WG6, PH 1, Place Flexible Base	5	16-Dec-...	23-Dec-11	882
1.5.3.6	2C10WF600464...	Area WF6, PH 1, Install Small RCP	42	20-Dec-...	16-Feb-12	93
1.5.7.6	2C10XU60066610	Area XU6, PH 1, Install Perm Markings	2	22-Dec-...	26-Dec-11	912
1.5.3.6	2C10WF600465...	Area WF6, PH 1, Install MHs and Inlets	44	22-Dec-...	22-Feb-12	93
1.5.2.6	2C10WG60053...	Area WG6, PH 1, Place Sidewalks & Drivew...	5	23-Dec-...	30-Dec-11	899
1.5.2.6	2C10WG60034...	Area WG6, PH 1, Place HMA Base	8	23-Dec-...	04-Jan-12	882
1.5.2.6	2C10SF60024710	Area SF6, PH 1, Place Flexible Base	4	26-Dec-...	30-Dec-11	150
1.5.2.6	2C10XR60034610	Area XR6, PH 1, Place SMA Surface	11	26-Dec-...	10-Jan-12	900
1.5	2C10EG60099999	Area EG6, PH 1, Finish	0		27-Dec-11	911
1.5.2.6	2C10SF60052910	Area SF6, PH 1, Place Curb & Gutter	3	30-Dec-...	04-Jan-12	150
1.5.9.6	2C10WG60051...	Area WG6, PH 1, Place Temp Conc Barrier	2	04-Jan-12	06-Jan-12	902
1.5.2.6	2C10WG60045...	Area WG6, PH 1, Place Conc Rail (Ret Wall)	3	04-Jan-12	09-Jan-12	894
1.5.2.6	2C10SF60034011	Area SF6, PH 1, Place HMA Base	6	04-Jan-12	12-Jan-12	150
1.5.2.6	2C10SF60053110	Area SF6, PH 1, Place Sidewalks & Driveways	8	04-Jan-12	16-Jan-12	170
1.5.7.6	2C10WG60065...	Area WG6, PH 1, Install OH Sign Structures	8	04-Jan-12	16-Jan-12	882
1.5.9.6	2C10WG60066...	Area WG6, PH 1, Place Temp Marking & Sig...	1	06-Jan-12	09-Jan-12	902
1.5.8.6	2C10WF600618...	Area WF6, PH 1, Install ITS Duct Bank	70	06-Jan-12	13-Apr-12	102
1.5.2.6	2C10WG60054...	Area WG6, PH 1, Install MBGF	6	09-Jan-12	17-Jan-12	894
1.5.7.6	2C10XR60066610	Area XR6, PH 1, Install Perm Markings	1	10-Jan-12	11-Jan-12	900
1.5.3.6	2C10EF60046410	Area EF6, PH 1, Install Small RCP	42	10-Jan-12	08-Mar-12	67
1.5.2.6	2C10RP60024710	Area RP6, PH 1, Place Flexible Base	6	11-Jan-12	19-Jan-12	813
1.5.9.6	2C10SF60066200	Area SF6, PH 1, Place Temp Marking & Sign...	1	12-Jan-12	13-Jan-12	180
1.5.2.6	2C10SF60045010	Area SF6, PH 1, Place Conc Rail (Ret Wall)	7	12-Jan-12	23-Jan-12	173
1.5.7.6	2C10SF60061020	Area SF6, PH 1, Install Rdwy Illumination	14	12-Jan-12	01-Feb-12	150
1.5.3.6	2C10EF60046510	Area EF6, PH 1, Install MHs and Inlets	44	12-Jan-12	14-Mar-12	67
1.5.7.6	2C10WG60061...	Area WG6, PH 1, Install Rdwy Illumination	6	16-Jan-12	24-Jan-12	882
1.5.2.6	2C10WG60054...	Area WG6, PH 1, Install Attenuators	1	17-Jan-12	18-Jan-12	894

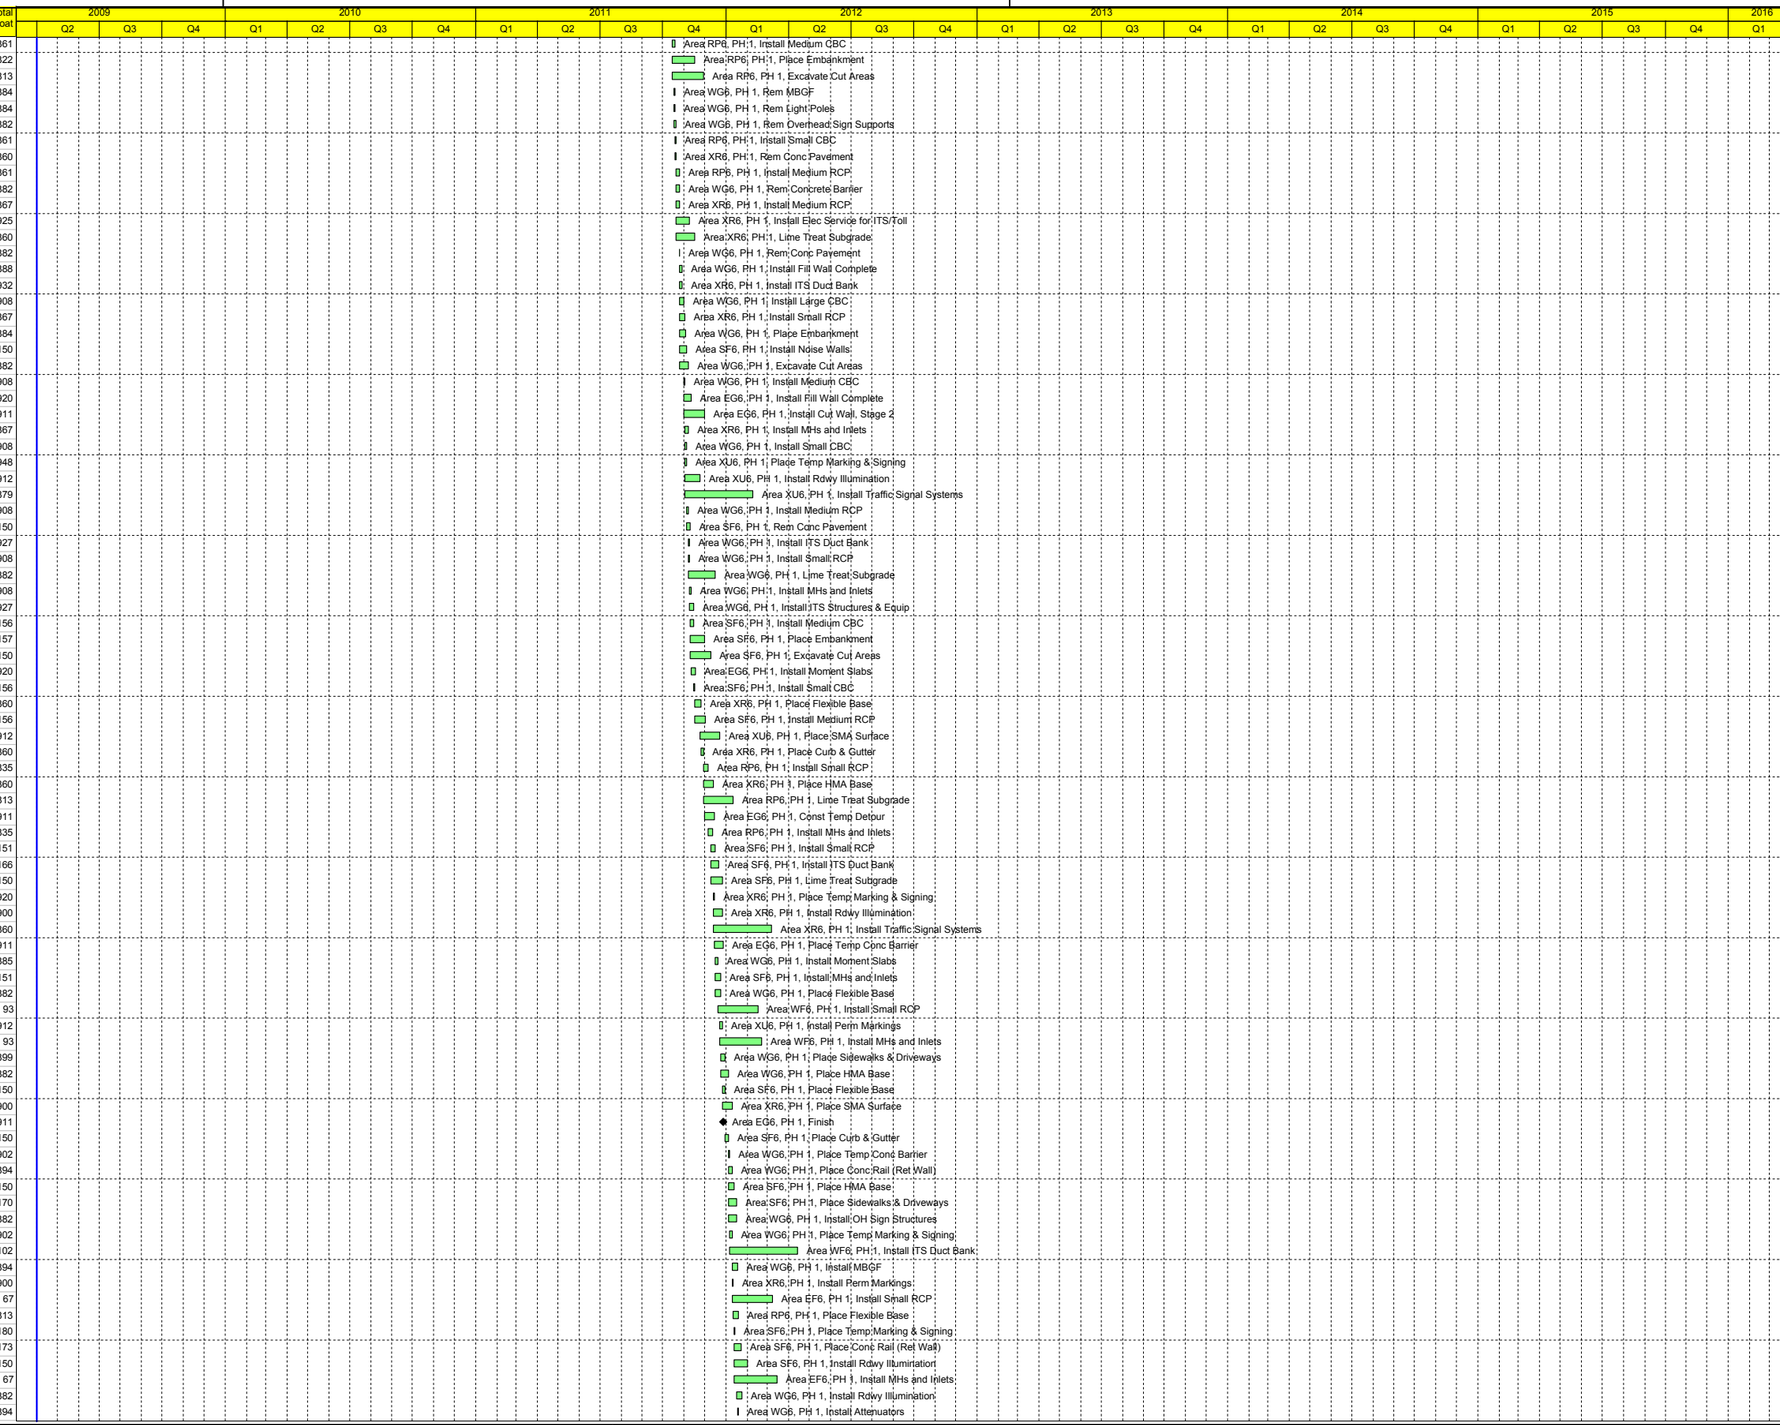

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.5.8.6	2C10EF60061899	Area EF6, PH 1, Install ITS Duct Bank	74	18-Jan-12	01-May-12	70
1.5.2.6	2C10RP60052910	Area RP6, PH 1, Place Curb & Gutter	5	19-Jan-12	26-Jan-12	813
1.5.4.6	2C10WF600423...	Area WF6, PH 1, Install Moment Slabs	10	20-Jan-12	03-Feb-12	171
1.5.7.6	2C10WG60064...	Area WG6, PH 1, Install Small Signs	1	24-Jan-12	25-Jan-12	890
1.5.2.6	2C10WG60034...	Area WG6, PH 1, Place SMA Surface	8	24-Jan-12	03-Feb-12	882
1.5.2.6	2C10RP60034012	Area RP6, PH 1, Place HMA Base	9	26-Jan-12	08-Feb-12	813
1.5.2.6	2C10SF60043210	Area SF6, PH 1, Place Conc RipRap	8	01-Feb-12	13-Feb-12	150
1.5.7.6	2C10WG60066...	Area WG6, PH 1, Install Perm Markings	1	03-Feb-12	06-Feb-12	882
1.5	2C10WG60099...	Area WG6, PH 1, Finish	0		06-Feb-12	882
1.5.2.6	2C10RP60045010	Area RP6, PH 1, Place Conc Rail (Ret Wall)	10	08-Feb-12	22-Feb-12	869
1.5.7.6	2C10RP60065010	Area RP6, PH 1, Install OH Sign Structures	25	08-Feb-12	14-Mar-12	813
1.5	2C10XU60099999	Area XU6, PH 1, Finish	0		09-Feb-12	879
1.5.2.6	2C10SF60016010	Area SF6, PH 1, Place Topsoil	2	13-Feb-12	15-Feb-12	150
1.5.7.6	2C10SF60064410	Area SF6, PH 1, Install Small Signs	1	15-Feb-12	16-Feb-12	155
1.5.2.6	2C10SF60034610	Area SF6, PH 1, Place SMA Surface	6	15-Feb-12	23-Feb-12	150
1.5.6.6	2C10SF60016410	Area SF6, PH 1, Place Seeding and Sodding	1	16-Feb-12	17-Feb-12	155
1.5.2.6	2C10WF600247...	Area WF6, PH 1, Place Flexible Base	33	22-Feb-12	09-Apr-12	93
1.5.7.6	2C10SF60066610	Area SF6, PH 1, Install Perm Markings	1	23-Feb-12	24-Feb-12	150
1.5	2C10SF60099999	Area SF6, PH 1, Finish	0		24-Feb-12	150
1.5.7.6	2C10RP60061020	Area RP6, PH 1, Install Rdwy Illumination	20	14-Mar-12	11-Apr-12	813
1.5.2.6	2C10EF60024710	Area EF6, PH 1, Place Flexible Base	35	14-Mar-12	02-May-12	67
1.5	2C10XR60099999	Area XR6, PH 1, Finish	0		19-Mar-12	852
1.5.2.6	2C10WF600529...	Area WF6, PH 1, Place Curb & Gutter	28	19-Mar-12	26-Apr-12	93
1.5.2.6	2C10WF600450...	Area WF6, PH 1, Place Conc Rail (Ret Wall)	58	23-Mar-12	13-Jun-12	144
1.5.2.6	2C10WF600340...	Area WF6, PH 1, Place HMA Base	49	29-Mar-12	06-Jun-12	132
1.5.2.6	2C10EF60052910	Area EF6, PH 1, Place Curb & Gutter	28	04-Apr-12	14-May-12	67
1.5.2.6	2C10EF60045010	Area EF6, PH 1, Place Conc Rail (Ret Wall)	61	10-Apr-12	04-Jul-12	83
1.5.2.6	2C10RP60043210	Area RP6, PH 1, Place Conc RipRap	12	11-Apr-12	27-Apr-12	813
1.5.2.6	2C10EF60034011	Area EF6, PH 1, Place HMA Base	52	16-Apr-12	27-Jun-12	83
1.5.2.6	2C10EF60034610	Area EF6, PH 1, Place SMA Surface	55	25-Apr-12	11-Jul-12	113
1.5.2.6	2C10WF600531...	Area WF6, PH 1, Place Sidewalks & Driveways	68	26-Apr-12	31-Jul-12	125
1.5.7.6	2C10WF600610...	Area WF6, PH 1, Install Rdwy Illumination	95	26-Apr-12	06-Sep-12	93
1.5.2.6	2C10RP60034610	Area RP6, PH 1, Place SMA Surface	9	27-Apr-12	10-May-12	813
1.5.2.6	2C10EF60043210	Area EF6, PH 1, Place Conc RipRap	74	04-May...	16-Aug-12	67
1.5.7.6	2C10RP60066610	Area RP6, PH 1, Install Perm Markings	1	10-May...	11-May-12	813
1.5	2C10RP60099999	Area RP6, PH 1, Finish	0		11-May-12	813
1.5.7.6	2C10EF60061020	Area EF6, PH 1, Install Rdwy Illumination (2 ...	63	14-May...	09-Aug-12	67
1.5.2.6	2C10EF60053110	Area EF6, PH 1, Place Sidewalks & Driveways	68	14-May...	16-Aug-12	67
1.5.2.6	2C10WF600432...	Area WF6, PH 1, Place Conc RipRap	74	01-Jun-12	13-Sep-12	93
1.5.9.6	2C10WF600662...	Area WF6, PH 1, Place Temp Marking & Sig...	3	06-Jun-12	11-Jun-12	185
1.5.2.6	2C10WF600346...	Area WF6, PH 1, Place SMA Surface	52	06-Jun-12	17-Aug-12	132
1.5.9.6	2C10EF60066200	Area EF6, PH 1, Place Temp Marking & Sign...	3	27-Jun-12	02-Jul-12	124
1.5.7.6	2C10EF60066610	Area EF6, PH 1, Install Perm Markings	4	11-Jul-12	17-Jul-12	113
1.5.2.6	2C10EF60016010	Area EF6, PH 1, Place Topsoil	15	16-Aug-...	06-Sep-12	67
1.5.7.6	2C10WF600666...	Area WF6, PH 1, Install Perm Markings	4	17-Aug-...	23-Aug-12	132
1.5.7.6	2C10EF60064410	Area EF6, PH 1, Install Small Signs	2	06-Sep-...	10-Sep-12	67
1.5.6.6	2C10EF60016410	Area EF6, PH 1, Place Seeding and Sodding	7	10-Sep-...	19-Sep-12	67
1.5.2.6	2C10WF600160...	Area WF6, PH 1, Place Topsoil	15	13-Sep-...	04-Oct-12	93
1.5	2C10EF60099999	Area EF6, PH 1, Finish	0		19-Sep-12	67
1.5.7.6	2C10WF600644...	Area WF6, PH 1, Install Small Signs	2	04-Oct-12	08-Oct-12	93
1.5.6.6	2C10WF600164...	Area WF6, PH 1, Place Seeding and Sodding	7	08-Oct-12	17-Oct-12	93
1.5	2C10WF600999...	Area WF6, PH 1, Finish	0		17-Oct-12	93
1.5.4.6.1.108	2C10B108000001	BR 108, PH 1, Start	0	10-Oct-11		919
1.5.4.6.1.108	2C10B108041600	BR 108, PH 1, Install Drill Shafts	6	10-Oct-11	18-Oct-11	919
1.5.4.6.1.108	2C10B108042040	BR 108, PH 1, Install Abutments	2	18-Oct-11	20-Oct-11	933
1.5.4.6.1.108	2C10B108042010	BR 108, PH 1, Install Footings	8	18-Oct-11	28-Oct-11	919
1.5.4.6.1.108	2C10B108042020	BR 108, PH 1, Install Columns	4	28-Oct-11	03-Nov-11	919
1.5.4.6.1.108	2C10B108042030	BR 108, PH 1, Install Bent Caps	4	03-Nov-...	09-Nov-11	919
1.5.4.6.1.108	2C10B108042510	BR 108, PH 1, Install Conc Beams	2	09-Nov-...	11-Nov-11	919
1.5.4.6.1.108	2C10B108045410	BR 108, PH 1, Install Exp Joints	1	11-Nov-...	14-Nov-11	919
1.5.4.6.1.108	2C10B108042210	BR 108, PH 1, Install Deck Slab	10	14-Nov-...	28-Nov-11	919
1.5.4.6.1.108	2C10B108042050	BR 108, PH 1, Install Apprch Slabs	4	28-Nov-...	02-Dec-11	925
1.5.4.6.1.108	2C10B108045020	BR 108, PH 1, Install Conc Rail	3	12-Dec-...	15-Dec-11	919
1.5.4.6.1.108	2C10B108099999	BR 108, PH 1, Finish	0		15-Dec-11	919
1.5.4.6.1.109	2C10B109000001	BR 109, PH 1, Start	0	10-Oct-11		834
1.5.4.6.1.109	2C10B109041600	BR 109, PH 1, Install Drill Shafts	27	10-Oct-11	16-Nov-11	834
1.5.4.6.1.109	2C10B109042010	BR 109, PH 1, Install Footings	47	17-Oct-11	21-Dec-11	834
1.5.4.6.1.109	2C10B109042020	BR 109, PH 1, Install Columns	56	24-Oct-11	10-Jan-12	834
1.5.4.6.1.109	2C10B109042040	BR 109, PH 1, Install Abutments	2	16-Nov-...	18-Nov-11	837
1.5.4.6.1.109	2C10B109042510	BR 109, PH 1, Install Conc Beams	9	23-Nov-...	06-Dec-11	834
1.5.4.6.1.109	2C10B109042030	BR 109, PH 1, Install Bent Caps	39	23-Nov-...	17-Jan-12	834
1.5.4.6.1.109	2C10B109042210	BR 109, PH 1, Install Deck Slab	73	30-Nov-...	12-Mar-12	834
1.5.4.6.1.109	2C10B109044210	BR 109, PH 1, Install Plate Girders	16	02-Jan-12	24-Jan-12	858
1.5.4.6.1.109	2C10B109042050	BR 109, PH 1, Install Apprch Slabs	5	12-Mar-12	19-Mar-12	839
1.5.4.6.1.109	2C10B109045020	BR 109, PH 1, Install Conc Rail	13	26-Mar-12	12-Apr-12	834
1.5.4.6.1.109	2C10B109099999	BR 109, PH 1, Finish	0		12-Apr-12	834
1.5.4.6.1.112	2C10B112000001	BR 112, PH 1, Start	0	10-Oct-11		900
1.5.4.6.1.112	2C10B112049610	BR 112, PH 1, Demo Extg Bridge	13	10-Oct-11	27-Oct-11	900
1.5.4.6.1.112	2C10B112041600	BR 112, PH 1, Install Drill Shafts	6	27-Oct-11	04-Nov-11	900
1.5.4.6.1.112	2C10B112042020	BR 112, PH 1, Install Columns	2	04-Nov-...	08-Nov-11	902
1.5.4.6.1.112	2C10B112042040	BR 112, PH 1, Install Abutments	7	04-Nov-...	15-Nov-11	900
1.5.4.6.1.112	2C10B112042030	BR 112, PH 1, Install Bent Caps	3	08-Nov-...	11-Nov-11	902
1.5.4.6.1.112	2C10B112042510	BR 112, PH 1, Install Conc Beams	2	15-Nov-...	17-Nov-11	900
1.5.4.6.1.112	2C10B112045410	BR 112, PH 1, Install Exp Joints	2	17-Nov-...	21-Nov-11	900
1.5.4.6.1.112	2C10B112042210	BR 112, PH 1, Install Deck Slab	17	21-Nov-...	14-Dec-11	900
1.5.4.6.1.112	2C10B112042050	BR 112, PH 1, Install Apprch Slabs	18	14-Dec-...	09-Jan-12	900

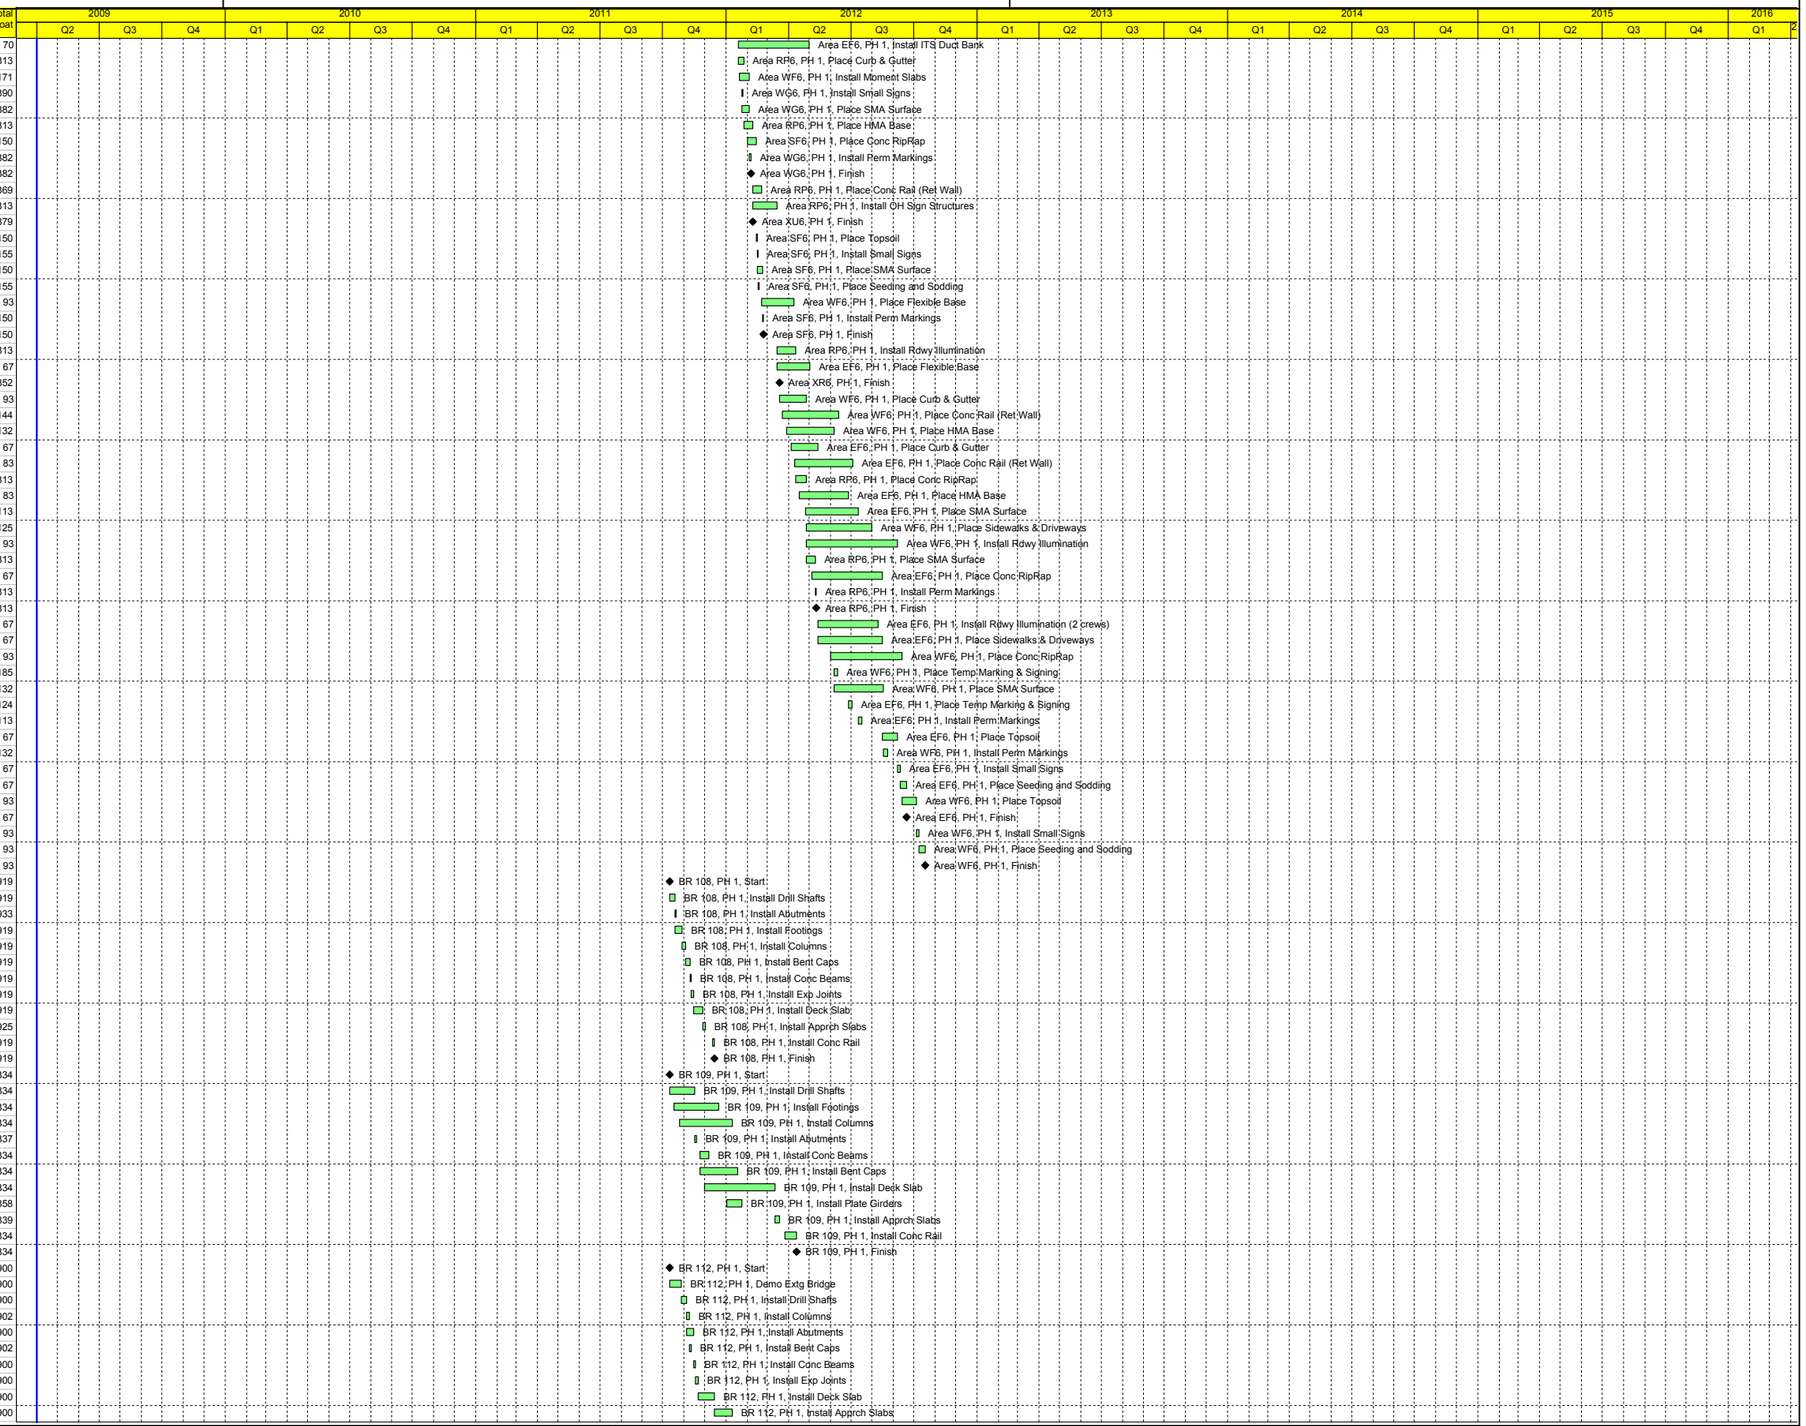

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.5.4.6.1.112	2C10B112045020	BR 112, PH 1, Install Conc Rail	2	09-Jan-12	11-Jan-12	900
1.5.4.6.1.112	2C10B112099999	BR 112, PH 1, Finish	0		11-Jan-12	900
1.5.4.6.1.118	2C10B118000001	BR 118, PH 1, Start	0	10-Oct-11		852
1.5.4.6.1.118	2C10B118049610	BR 118, PH 1, Demo Extg Bridge	14	10-Oct-11	28-Oct-11	852
1.5.4.6.1.118	2C10B118041600	BR 118, PH 1, Install Drill Shafts	11	28-Oct-11	14-Nov-11	852
1.5.4.6.1.118	2C10B118042020	BR 118, PH 1, Install Columns	4	14-Nov-...	18-Nov-11	854
1.5.4.6.1.118	2C10B118042040	BR 118, PH 1, Install Abutments	14	14-Nov-...	02-Dec-11	852
1.5.4.6.1.118	2C10B118042030	BR 118, PH 1, Install Bent Caps	8	18-Nov-...	30-Nov-11	854
1.5.4.6.1.118	2C10B118042510	BR 118, PH 1, Install Conc Beams	5	02-Dec-...	09-Dec-11	852
1.5.4.6.1.118	2C10B118042210	BR 118, PH 1, Install Deck Slab	49	09-Dec-...	16-Feb-12	852
1.5.4.6.1.118	2C10B118042050	BR 118, PH 1, Install Apprch Slabs	20	16-Feb-12	15-Mar-12	852
1.5.4.6.1.118	2C10B118045020	BR 118, PH 1, Install Conc Rail	2	15-Mar-12	19-Mar-12	852
1.5.4.6.1.118	2C10B118099999	BR 118, PH 1, Finish	0		19-Mar-12	852
1.5.4.6.1.138	2C10B138000001	BR 138, PH 1, Start	0	10-Oct-11		869
1.5.4.6.1.138	2C10B138049610	BR 138, PH 1, Demo Extg Bridge	16	10-Oct-11	01-Nov-11	869
1.5.4.6.1.138	2C10B138041600	BR 138, PH 1, Install Drill Shafts	5	01-Nov-...	08-Nov-11	869
1.5.4.6.1.138	2C10B138042020	BR 138, PH 1, Install Columns	2	08-Nov-...	10-Nov-11	876
1.5.4.6.1.138	2C10B138042040	BR 138, PH 1, Install Abutments	12	08-Nov-...	24-Nov-11	869
1.5.4.6.1.138	2C10B138042030	BR 138, PH 1, Install Bent Caps	3	10-Nov-...	15-Nov-11	876
1.5.4.6.1.138	2C10B138042510	BR 138, PH 1, Install Conc Beams	3	24-Nov-...	29-Nov-11	869
1.5.4.6.1.138	2C10B138045410	BR 138, PH 1, Install Exp Joints	3	29-Nov-...	02-Dec-11	869
1.5.4.6.1.138	2C10B138042210	BR 138, PH 1, Install Deck Slab	23	02-Dec-...	04-Jan-12	869
1.5.4.6.1.138	2C10B138042050	BR 138, PH 1, Install Apprch Slabs	34	04-Jan-12	21-Feb-12	869
1.5.4.6.1.138	2C10B138045020	BR 138, PH 1, Install Conc Rail	2	21-Feb-12	23-Feb-12	869
1.5.4.6.1.138	2C10B138099999	BR 138, PH 1, Finish	0		23-Feb-12	869
1.5.4.6.1.139	2C10B139000001	BR 139, PH 1, Start	0	10-Oct-11		862
1.5.4.6.1.139	2C10B139049610	BR 139, PH 1, Demo Extg Bridge	16	10-Oct-11	01-Nov-11	862
1.5.4.6.1.139	2C10B139041600	BR 139, PH 1, Install Drill Shafts	4	01-Nov-...	07-Nov-11	862
1.5.4.6.1.139	2C10B139042020	BR 139, PH 1, Install Columns	3	07-Nov-...	10-Nov-11	867
1.5.4.6.1.139	2C10B139042040	BR 139, PH 1, Install Abutments	13	07-Nov-...	24-Nov-11	862
1.5.4.6.1.139	2C10B139042030	BR 139, PH 1, Install Bent Caps	5	10-Nov-...	17-Nov-11	867
1.5.4.6.1.139	2C10B139042510	BR 139, PH 1, Install Conc Beams	4	24-Nov-...	30-Nov-11	862
1.5.4.6.1.139	2C10B139045410	BR 139, PH 1, Install Exp Joints	3	30-Nov-...	05-Dec-11	862
1.5.4.6.1.139	2C10B139042210	BR 139, PH 1, Install Deck Slab	31	05-Dec-...	17-Jan-12	862
1.5.4.6.1.139	2C10B139042050	BR 139, PH 1, Install Apprch Slabs	32	17-Jan-12	01-Mar-12	862
1.5.4.6.1.139	2C10B139045020	BR 139, PH 1, Install Conc Rail	2	01-Mar-12	05-Mar-12	862
1.5.4.6.1.139	2C10B139099999	BR 139, PH 1, Finish	0		05-Mar-12	862
1.5.4.6.1.142	2C10B142000001	BR 142, PH 1, Start	0	10-Oct-11		941
1.5.4.6.1.142	2C10B142049610	BR 142, PH 1, Demo Extg Bridge	3	10-Oct-11	13-Oct-11	941
1.5.4.6.1.142	2C10B142041600	BR 142, PH 1, Install Drill Shafts	2	13-Oct-11	17-Oct-11	941
1.5.4.6.1.142	2C10B142042020	BR 142, PH 1, Install Columns	1	17-Oct-11	18-Oct-11	941
1.5.4.6.1.142	2C10B142042040	BR 142, PH 1, Install Abutments	2	17-Oct-11	19-Oct-11	941
1.5.4.6.1.142	2C10B142042030	BR 142, PH 1, Install Bent Caps	1	18-Oct-11	19-Oct-11	941
1.5.4.6.1.142	2C10B142042510	BR 142, PH 1, Install Conc Beams	1	19-Oct-11	20-Oct-11	941
1.5.4.6.1.142	2C10B142045410	BR 142, PH 1, Install Exp Joints	1	20-Oct-11	21-Oct-11	941
1.5.4.6.1.142	2C10B142042210	BR 142, PH 1, Install Deck Slab	4	21-Oct-11	27-Oct-11	941
1.5.4.6.1.142	2C10B142042050	BR 142, PH 1, Install Apprch Slabs	3	27-Oct-11	01-Nov-11	948
1.5.4.6.1.142	2C10B142045020	BR 142, PH 1, Install Conc Rail	3	10-Nov-...	15-Nov-11	941
1.5.4.6.1.142	2C10B142099999	BR 142, PH 1, Finish	0		15-Nov-11	941
1.5	2C100000000001	START PHASE 1, SUBSEGMENT 2C	0	23-May...		67
1.5	2C100000099999	FINISH PHASE 1, SUBSEGMENT 2C	0		17-Oct-12	700
CONSTRUCTION PHASE 2			305	02-Nov-...	02-Jan-13	645
1.5	2C20EG60000001	Area EG6, PH 2, Start	0	02-Nov-...		115
1.5.2.6	2C20EG60060010	Area EG6, PH 2, Rem Light Poles	4	02-Nov-...	08-Nov-11	139
1.5.2.6	2C20EG60054210	Area EG6, PH 2, Rem MBGF	6	02-Nov-...	10-Nov-11	137
1.5.2.6	2C20EG60063010	Area EG6, PH 2, Rem Overhead Sign Supports	28	02-Nov-...	12-Dec-11	115
1.5.2.6	2C20EG60050600	Area EG6, PH 2, Place Temp Erosion Control	28	02-Nov-...	12-Dec-11	115
1.5.3.6	2C20EG60046230	Area EG6, PH 2, Install Large CBC	38	21-Nov-...	12-Jan-12	144
1.5.2.6	2C20EG60010430	Area EG6, PH 2, Rem Concrete Barrier	15	12-Dec-...	02-Jan-12	115
1.5	2C20SG60000001	Area SG6, PH 2, Start	0	30-Dec-...		150
1.5.2.6	2C20SG60060010	Area SG6, PH 2, Rem Light Poles	3	30-Dec-...	04-Jan-12	159
1.5.2.6	2C20SG60054210	Area SG6, PH 2, Rem MBGF	4	30-Dec-...	05-Jan-12	158
1.5.2.6	2C20SG60063010	Area SG6, PH 2, Rem Overhead Sign Supports	8	30-Dec-...	11-Jan-12	154
1.5.2.6	2C20SG60050600	Area SG6, PH 2, Place Temp Erosion Control	16	30-Dec-...	23-Jan-12	150
1.5.2.6	2C20EG60010410	Area EG6, PH 2, Rem Conc Pavement	12	02-Jan-12	18-Jan-12	115
1.5	2C20WG60000...	Area WG6, PH 2, Start	0	11-Jan-12		93
1.5.2.6	2C20WG60054...	Area WG6, PH 2, Rem MBGF	2	11-Jan-12	13-Jan-12	898
1.5.2.6	2C20WG60060...	Area WG6, PH 2, Rem Light Poles	2	11-Jan-12	13-Jan-12	898
1.5.2.6	2C20WG60010...	Area WG6, PH 2, Rem Concrete Barrier	4	11-Jan-12	17-Jan-12	99
1.5.2.6	2C20WG60063...	Area WG6, PH 2, Rem Overhead Sign Supp...	6	11-Jan-12	19-Jan-12	894
1.5.2.6	2C20SG60010430	Area SG6, PH 2, Rem Concrete Barrier	9	11-Jan-12	24-Jan-12	154
1.5.2.6	2C20WG60050...	Area WG6, PH 2, Place Temp Erosion Control	10	11-Jan-12	25-Jan-12	93
1.5.3.6	2C20EG60046220	Area EG6, PH 2, Install Medium CBC	20	12-Jan-12	09-Feb-12	144
1.5.2.6	2C20EG60013210	Area EG6, PH 2, Place Embankment (2 Crews)	36	18-Jan-12	08-Mar-12	127
1.5.4.6	2C20EG60042310	Area EG6, PH 2, Install Fill Wall Complete	36	18-Jan-12	08-Mar-12	186
1.5.2.6	2C20EG60011010	Area EG6, PH 2, Excavate Cut Areas (2 Crews)	51	18-Jan-12	29-Mar-12	115
1.5.9.6	2C20EG60040390	Area EG6, PH 2, Construct Temp Walls/Shor...	54	18-Jan-12	03-Apr-12	168
1.5.2.6	2C20SG60010410	Area SG6, PH 2, Rem Conc Pavement	7	23-Jan-12	01-Feb-12	150
1.5.2.6	2C20WG60010...	Area WG6, PH 2, Rem Conc Pavement	4	25-Jan-12	31-Jan-12	93
1.5.3.6	2C20WG60046...	Area WG6, PH 2, Install Large CBC	11	25-Jan-12	09-Feb-12	186
1.5.4.6	2C20WG60042...	Area WG6, PH 2, Install Cut Wall, Stage 1	40	31-Jan-12	27-Mar-12	93
1.5.3.6	2C20SG60046230	Area SG6, PH 2, Install Large CBC	23	01-Feb-12	05-Mar-12	186
1.5.2.6	2C20SG60013210	Area SG6, PH 2, Place Embankment	42	01-Feb-12	30-Mar-12	150
1.5.2.6	2C20SG60011010	Area SG6, PH 2, Excavate Cut Areas	60	01-Feb-12	25-Apr-12	150
1.5.2.6	2C20EG60026010	Area EG6, PH 2, Lime Treat Subgrade (3 cre...	95	01-Feb-12	13-Jun-12	127
1.5.2.6	2C20SG60026010	Area SG6, PH 2, Lime Treat Subgrade (2 cre...	97	08-Feb-12	22-Jun-12	150

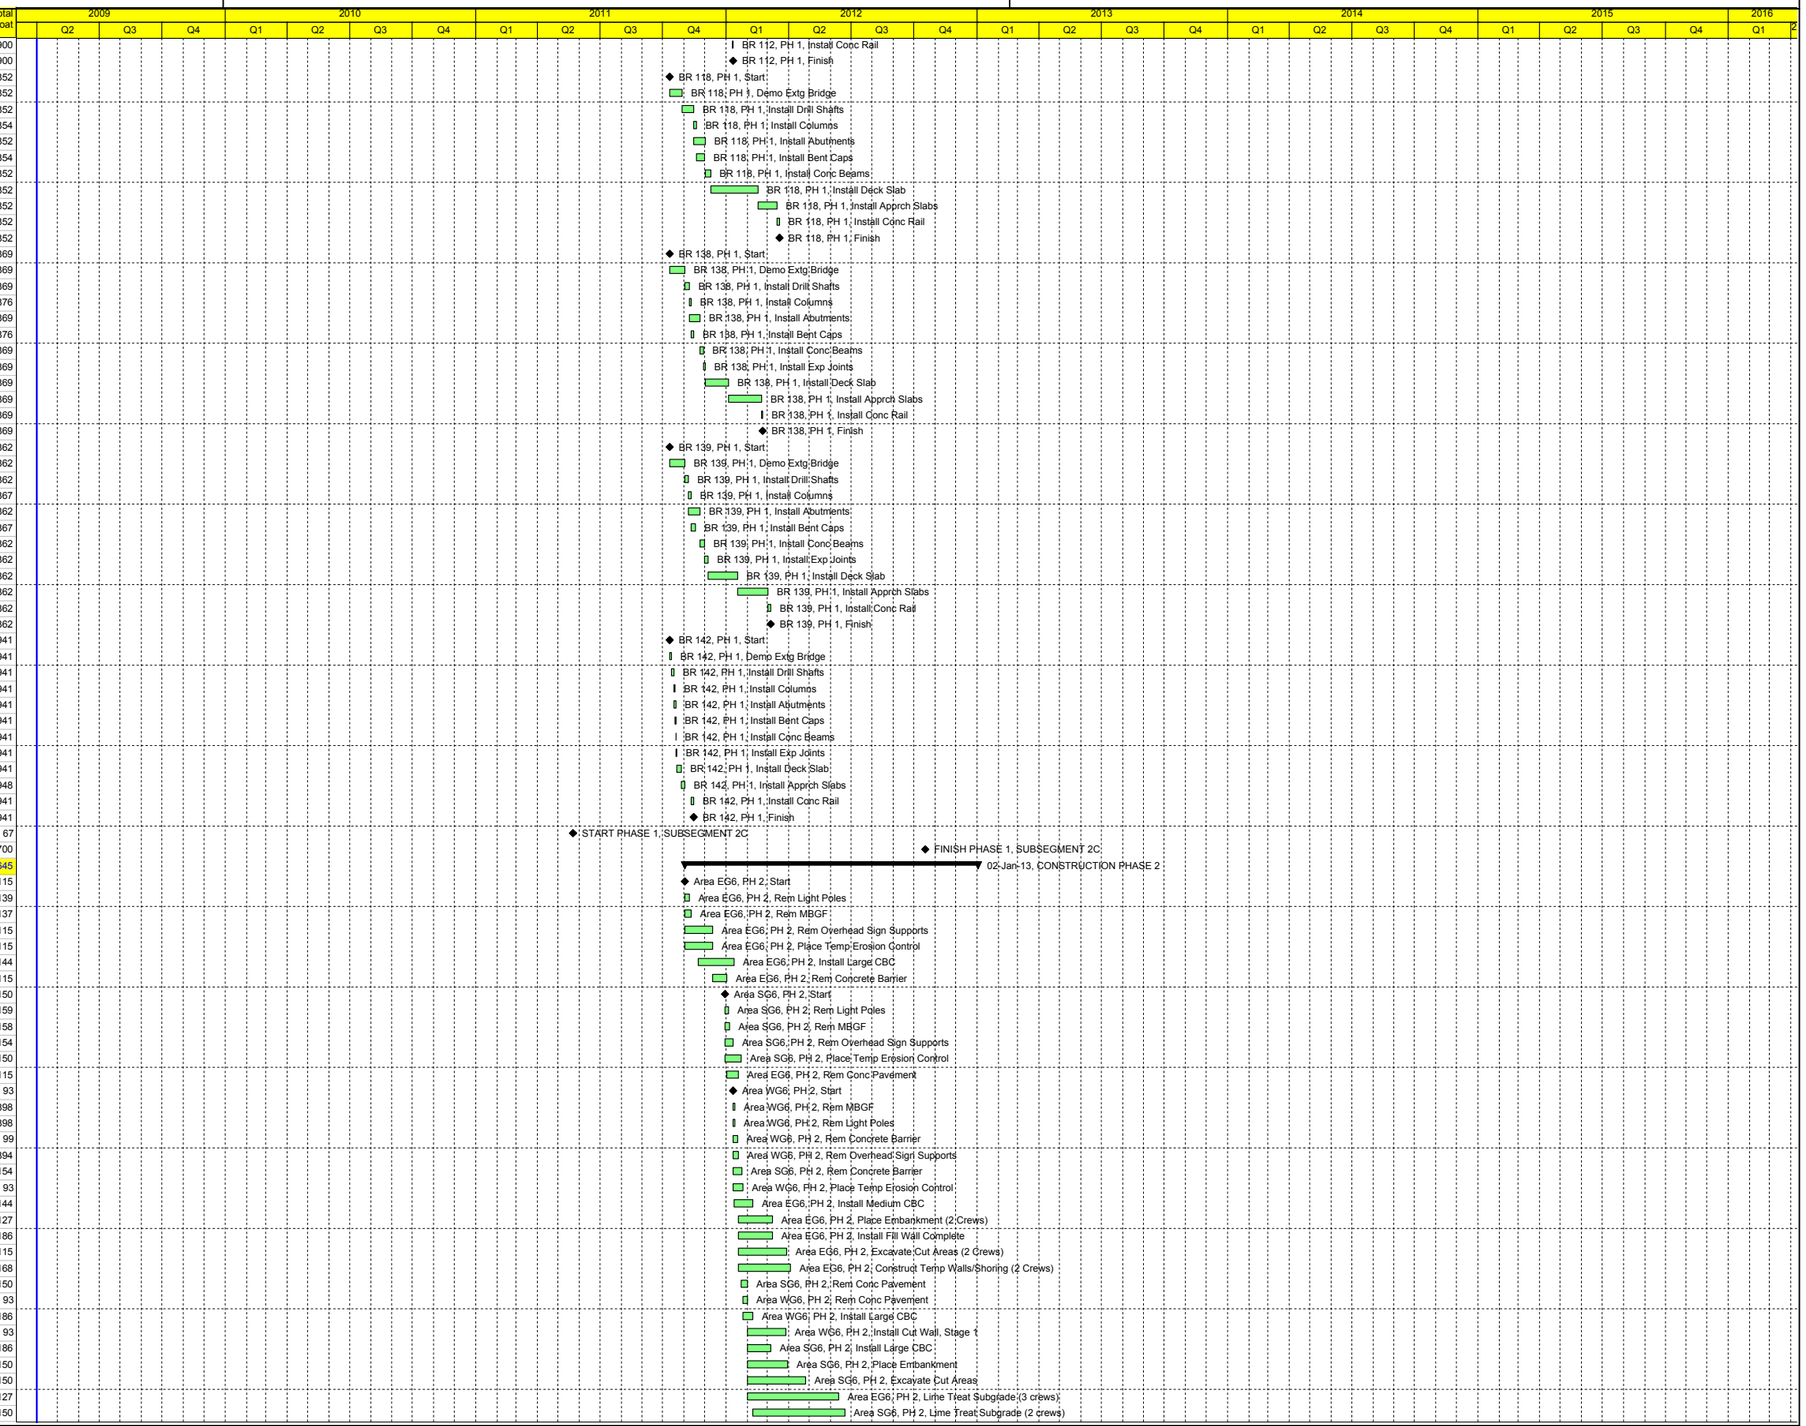

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.5.3.6	2C20EG60046420	Area EG6, PH 2, Install Medium RCP	6	09-Feb-12	17-Feb-12	144
1.5.3.6	2C20WG60046...	Area WG6, PH 2, Install Medium CBC	6	09-Feb-12	17-Feb-12	186
1.5.3.6	2C20EG60046210	Area EG6, PH 2, Install Small CBC	18	09-Feb-12	06-Mar-12	186
1.5.3.6	2C20WG60046...	Area WG6, PH 2, Install Medium RCP	2	17-Feb-12	21-Feb-12	189
1.5.3.6	2C20WG60046...	Area WG6, PH 2, Install Small CBC	5	17-Feb-12	24-Feb-12	186
1.5	2C20RP60000001	Area RP6, PH 2, Start	0	22-Feb-12		67
1.5.2.6	2C20RP60010410	Area RP6, PH 2, Rem Conc Pavement	13	22-Feb-12	12-Mar-12	67
1.5.4.6	2C20WG60042...	Area WG6, PH 2, Install Fill Wall Complete	12	23-Feb-12	12-Mar-12	169
1.5.9.6	2C20WG60040...	Area WG6, PH 2, Construct Temp Walls/Sho...	15	23-Feb-12	15-Mar-12	166
1.5.2.6	2C20WG60013...	Area WG6, PH 2, Place Embankment	20	23-Feb-12	22-Mar-12	93
1.5.2.6	2C20WG60011...	Area WG6, PH 2, Excavate Cut Areas	28	23-Feb-12	03-Apr-12	93
1.5.4.6	2C20WG60042...	Area WG6, PH 2, Install Cut Wall, Stage 2	60	01-Mar-12	24-May-12	148
1.5.2.6	2C20WG60026...	Area WG6, PH 2, Lime Treat Subgrade	88	01-Mar-12	03-Jul-12	93
1.5.3.6	2C20SG60046220	Area SG6, PH 2, Install Medium CBC	12	05-Mar-12	21-Mar-12	186
1.5.3.6	2C20RP60046220	Area RP6, PH 2, Install Medium CBC	6	12-Mar-12	20-Mar-12	160
1.5.4.6	2C20RP60042320	Area RP6, PH 2, Install Cut Wall, Stage 1 (2 ...	55	12-Mar-12	28-May-12	67
1.5.2.6	2C20RP60013210	Area RP6, PH 2, Place Embankment	76	12-Mar-12	26-Jun-12	93
1.5.4.6	2C20RP60042310	Area RP6, PH 2, Install Fill Wall Complete (3...	90	12-Mar-12	16-Jul-12	93
1.5.2.6	2C20RP60011010	Area RP6, PH 2, Excavate Cut Areas	108	12-Mar-12	09-Aug-12	67
1.5.4.6	2C20RP60042325	Area RP6, PH 2, Install Cut Wall, Stage 2 (2 ...	82	19-Mar-12	11-Jul-12	131
1.5.3.6	2C20RP60046210	Area RP6, PH 2, Install Small CBC	3	20-Mar-12	23-Mar-12	166
1.5.3.6	2C20RP60046420	Area RP6, PH 2, Install Medium RCP	9	20-Mar-12	02-Apr-12	160
1.5.3.6	2C20SG60046420	Area SG6, PH 2, Install Medium RCP	4	21-Mar-12	27-Mar-12	193
1.5.3.6	2C20SG60046210	Area SG6, PH 2, Install Small CBC	11	21-Mar-12	05-Apr-12	186
1.5.8.6	2C20EG60061899	Area EG6, PH 2, Install ITS Duct Bank	6	29-Mar-12	06-Apr-12	115
1.5.3.6	2C20EG60046410	Area EG6, PH 2, Install Small RCP	10	29-Mar-12	12-Apr-12	169
1.5.3.6	2C20EG60046510	Area EG6, PH 2, Install MHs and Inlets	12	29-Mar-12	16-Apr-12	169
1.5.2.6	2C20EG60024710	Area EG6, PH 2, Place Flexible Base	57	02-Apr-12	20-Jun-12	127
1.5.8.6	2C20WG60061...	Area WG6, PH 2, Install ITS Duct Bank	2	03-Apr-12	05-Apr-12	190
1.5.3.6	2C20WG60046...	Area WG6, PH 2, Install Small RCP	3	03-Apr-12	06-Apr-12	159
1.5.3.6	2C20WG60046...	Area WG6, PH 2, Install MHs and Inlets	4	03-Apr-12	09-Apr-12	159
1.5.8.6	2C20WG60041...	Area WG6, PH 2, Install ITS Structures & Equip	15	05-Apr-12	26-Apr-12	190
1.5.8.6	2C20EG60041699	Area EG6, PH 2, Install ITS Structures & Equip	47	06-Apr-12	12-Jun-12	115
1.5.2.6	2C20EG60034012	Area EG6, PH 2, Place HMA Base	85	09-Apr-12	06-Aug-12	140
1.5.8.6	2C20SG60061899	Area SG6, PH 2, Install ITS Duct Bank	1	25-Apr-12	26-Apr-12	184
1.5.3.6	2C20SG60046410	Area SG6, PH 2, Install Small RCP	6	25-Apr-12	03-May-12	172
1.5.3.6	2C20SG60046510	Area SG6, PH 2, Install MHs and Inlets	7	25-Apr-12	04-May-12	172
1.5.7.6	2C20SG60061320	Area SG6, PH 2, Install High Mast Illumination	14	25-Apr-12	15-May-12	224
1.5.8.6	2C20SG60041699	Area SG6, PH 2, Install ITS Structures & Equip	4	26-Apr-12	02-May-12	184
1.5.7.6	2C20SG60061020	Area SG6, PH 2, Install Rdwy Illumination	38	04-May...	27-Jun-12	193
1.5.7.6	2C20EG60065010	Area EG6, PH 2, Install OH Sign Structures	81	04-May...	27-Aug-12	140
1.5.4.6	2C20RP60042315	Area RP6, PH 2, Install Moment Slabs	89	04-May...	06-Sep-12	90
1.5.2.6	2C20SG60024710	Area SG6, PH 2, Place Flexible Base	34	11-May...	28-Jun-12	167
1.5.2.6	2C20SG60034012	Area SG6, PH 2, Place HMA Base	51	18-May...	30-Jul-12	167
1.5	2C20NG60000001	Area NG6, PH 2, Start	0	30-May...		157
1.5.2.6	2C20NG60050600	Area NG6, PH 2, Place Temp Erosion Control	4	30-May...	05-Jun-12	157
1.5.2.6	2C20SG60053110	Area SG6, PH 2, Place Sidewalks & Driveways	32	31-May...	16-Jul-12	180
1.5.2.6	2C20NG60054210	Area NG6, PH 2, Rem MBGF	1	05-Jun-12	06-Jun-12	159
1.5.2.6	2C20NG60060010	Area NG6, PH 2, Rem Light Poles	1	05-Jun-12	06-Jun-12	159
1.5.2.6	2C20NG60063010	Area NG6, PH 2, Rem Overhead Sign Supports	3	05-Jun-12	08-Jun-12	157
1.5.2.6	2C20EG60054010	Area EG6, PH 2, Install MBGF	68	06-Jun-12	10-Sep-12	140
1.5.4.6	2C20EG60042315	Area EG6, PH 2, Install Moment Slabs	14	07-Jun-12	27-Jun-12	163
1.5.2.6	2C20NG60010430	Area NG6, PH 2, Rem Concrete Barrier	1	08-Jun-12	11-Jun-12	157
1.5.2.6	2C20NG60010410	Area NG6, PH 2, Rem Conc Pavement	1	11-Jun-12	12-Jun-12	157
1.5.2.6	2C20SG60054010	Area SG6, PH 2, Install MBGF	41	11-Jun-12	07-Aug-12	167
1.5.4.6	2C20NG60042310	Area NG6, PH 2, Install Fill Wall Complete	2	12-Jun-12	14-Jun-12	162
1.5.3.6	2C20NG60046230	Area NG6, PH 2, Install Large CBC	3	12-Jun-12	15-Jun-12	175
1.5.2.6	2C20NG60013210	Area NG6, PH 2, Place Embankment	5	12-Jun-12	19-Jun-12	159
1.5.2.6	2C20NG60011010	Area NG6, PH 2, Excavate Cut Areas	7	12-Jun-12	21-Jun-12	157
1.5.2.6	2C20RP60026010	Area RP6, PH 2, Lime Treat Subgrade (2 cre...	52	12-Jun-12	23-Aug-12	75
1.5.2.6	2C20EG60034610	Area EG6, PH 2, Place SMA Surface	91	12-Jun-12	17-Oct-12	115
1.5.3.6	2C20NG60046220	Area NG6, PH 2, Install Medium CBC	2	15-Jun-12	19-Jun-12	175
1.5.3.6	2C20NG60046210	Area NG6, PH 2, Install Small CBC	2	19-Jun-12	21-Jun-12	175
1.5.2.6	2C20SG60034610	Area SG6, PH 2, Place SMA Surface	54	19-Jun-12	03-Sep-12	150
1.5.7.6	2C20EG60061020	Area EG6, PH 2, Install Rdwy Illumination	63	20-Jun-12	17-Sep-12	127
1.5.3.6	2C20NG60046420	Area NG6, PH 2, Install Medium RCP	1	21-Jun-12	22-Jun-12	175
1.5.7.6	2C20NG60061320	Area NG6, PH 2, Install High Mast Illumination	14	21-Jun-12	11-Jul-12	185
1.5.2.6	2C20NG60026010	Area NG6, PH 2, Lime Treat Subgrade	21	21-Jun-12	20-Jul-12	157
1.5.3.6	2C20NG60046410	Area NG6, PH 2, Install Small RCP	1	22-Jun-12	25-Jun-12	175
1.5.7.6	2C20SG60065010	Area SG6, PH 2, Install OH Sign Structures	46	22-Jun-12	27-Aug-12	150
1.5.3.6	2C20NG60046510	Area NG6, PH 2, Install MHs and Inlets	1	25-Jun-12	26-Jun-12	175
1.5.2.6	2C20WG60024...	Area WG6, PH 2, Place Flexible Base	16	25-Jun-12	17-Jul-12	93
1.5.2.6	2C20EG60045010	Area EG6, PH 2, Place Conc Rail (Ret Wall)	31	29-Jun-12	13-Aug-12	140
1.5.4.6	2C20WG60042...	Area WG6, PH 2, Install Moment Slabs	5	03-Jul-12	10-Jul-12	110
1.5.2.6	2C20WG60034...	Area WG6, PH 2, Place HMA Base	23	09-Jul-12	09-Aug-12	93
1.5.2.6	2C20WG60053...	Area WG6, PH 2, Place Sidewalks & Drivew...	15	17-Jul-12	07-Aug-12	108
1.5.4.6	2C20NG60042315	Area NG6, PH 2, Install Moment Slabs	1	20-Jul-12	23-Jul-12	160
1.5.2.6	2C20NG60024710	Area NG6, PH 2, Place Flexible Base	4	20-Jul-12	26-Jul-12	157
1.5.2.6	2C20NG60053110	Area NG6, PH 2, Place Sidewalks & Driveways	4	26-Jul-12	01-Aug-12	170
1.5.2.6	2C20NG60034012	Area NG6, PH 2, Place HMA Base	6	26-Jul-12	03-Aug-12	157
1.5.9.6	2C20SG60066200	Area SG6, PH 2, Place Temp Marking & Sig...	6	30-Jul-12	07-Aug-12	173
1.5.9.6	2C20NG60066200	Area NG6, PH 2, Place Temp Marking & Sig...	1	03-Aug-...	06-Aug-12	174
1.5.2.6	2C20NG60045010	Area NG6, PH 2, Place Conc Rail (Ret Wall)	2	03-Aug-...	07-Aug-12	167
1.5.7.6	2C20NG60065010	Area NG6, PH 2, Install OH Sign Structures	7	03-Aug-...	14-Aug-12	157
1.5.9.6	2C20EG60050820	Area EG6, PH 2, Const Temp Detour	10	06-Aug-...	20-Aug-12	145
1.5.2.6	2C20SG60054510	Area SG6, PH 2, Install Attenuators	2	07-Aug-...	09-Aug-12	167

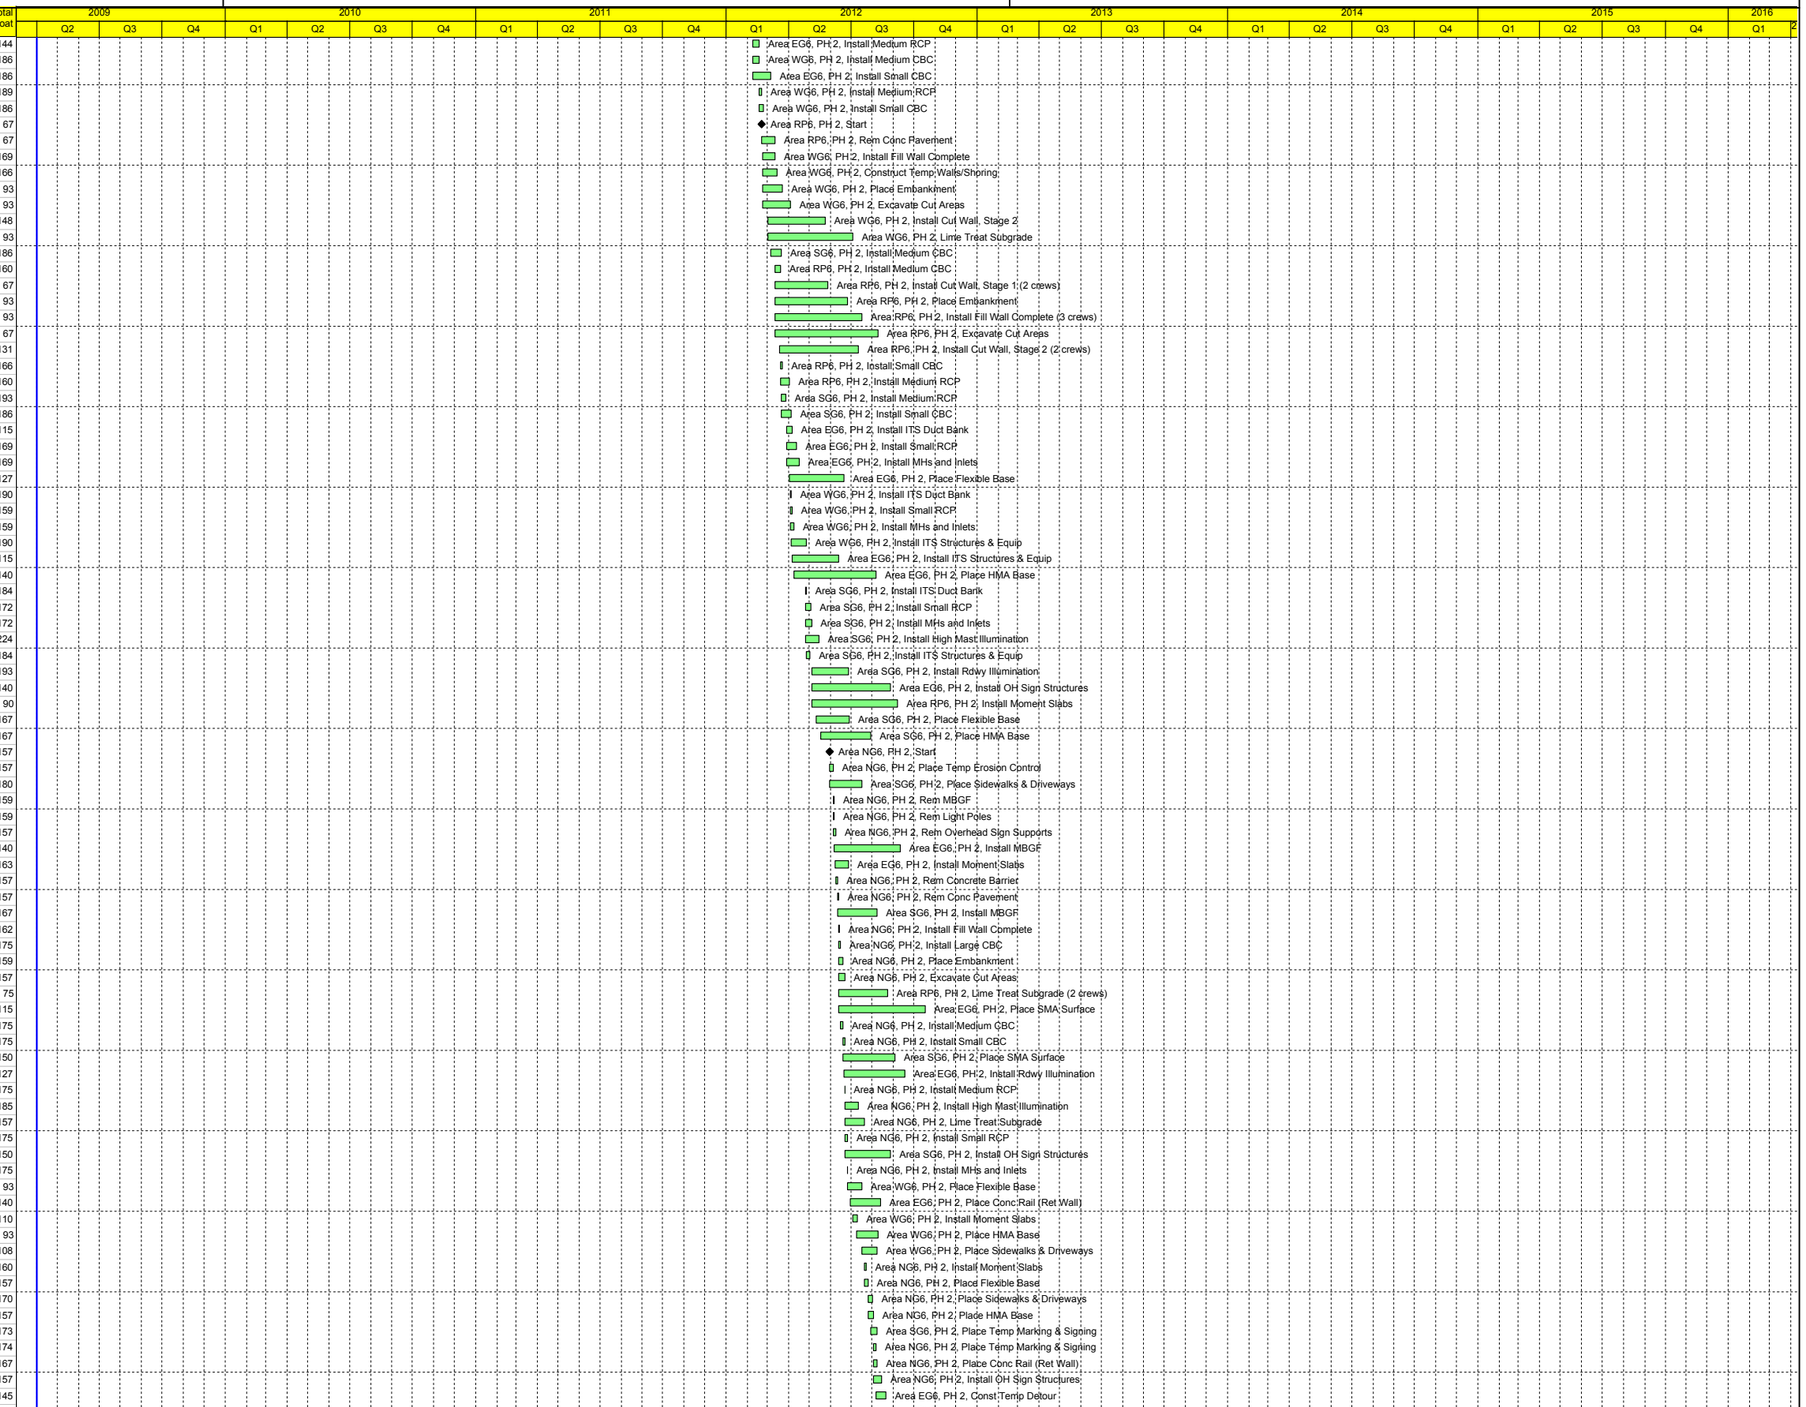

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.5.2.6	2C20NG60054010	Area NG6, PH 2, Install MBGF	5	07-Aug-...	14-Aug-12	167
1.5.2.6	2C20WG60034...	Area WG6, PH 2, Place SMA Surface	25	07-Aug-...	11-Sep-12	108
1.5.2.6	2C20WG60045...	Area WG6, PH 2, Place Conc Rail (Ret Wall)	9	09-Aug-...	22-Aug-12	102
1.5.3.6	2C20RP60046410	Area RP6, PH 2, Install Small RCP	11	09-Aug-...	24-Aug-12	67
1.5.9.6	2C20WG60050...	Area WG6, PH 2, Const Temp Detour	20	09-Aug-...	06-Sep-12	95
1.5.7.6	2C20WG60065...	Area WG6, PH 2, Install OH Sign Structures	22	09-Aug-...	10-Sep-12	93
1.5.7.6	2C20RP60065010	Area RP6, PH 2, Install OH Sign Structures	84	09-Aug-...	05-Dec-12	77
1.5.2.6	2C20RP60024710	Area RP6, PH 2, Place Flexible Base	19	10-Aug-...	06-Sep-12	75
1.5.7.6	2C20NG60061020	Area NG6, PH 2, Install Rdwy Illumination	4	14-Aug-...	20-Aug-12	157
1.5.7.6	2C20NG60064410	Area NG6, PH 2, Install Small Signs	1	20-Aug-...	21-Aug-12	163
1.5.2.6	2C20NG60034610	Area NG6, PH 2, Place SMA Surface	6	20-Aug-...	28-Aug-12	157
1.5.9.6	2C20EG60051200	Area EG6, PH 2, Place Temp Conc Barrier	9	20-Aug-...	31-Aug-12	145
1.5.2.6	2C20WG60054...	Area WG6, PH 2, Install MBGF	19	22-Aug-...	18-Sep-12	102
1.5.3.6	2C20RP60046510	Area RP6, PH 2, Install MHs and Inlets	17	24-Aug-...	18-Sep-12	67
1.5.7.6	2C20SG60064410	Area SG6, PH 2, Install Small Signs	1	27-Aug-...	28-Aug-12	158
1.5.7.6	2C20NG60066610	Area NG6, PH 2, Install Perm Markings	1	28-Aug-...	29-Aug-12	157
1.5	2C20NG60099999	Area NG6, PH 2, Finish	0		29-Aug-12	157
1.5.9.6	2C20EG60066200	Area EG6, PH 2, Place Temp Marking & Sig...	10	31-Aug-...	14-Sep-12	145
1.5.7.6	2C20SG60066610	Area SG6, PH 2, Install Perm Markings	4	03-Sep-...	07-Sep-12	150
1.5.7.6	2C20RP60061020	Area RP6, PH 2, Install Rdwy Illumination	67	05-Sep-...	07-Dec-12	75
1.5.9.6	2C20WG60051...	Area WG6, PH 2, Place Temp Conc Barrier	15	06-Sep-...	27-Sep-12	95
1.5	2C20SG60099999	Area SG6, PH 2, Finish	0		07-Sep-12	150
1.5.2.6	2C20EG60054510	Area EG6, PH 2, Install Attenuators	2	10-Sep-...	12-Sep-12	140
1.5.7.6	2C20WG60061...	Area WG6, PH 2, Install Rdwy Illumination	17	10-Sep-...	03-Oct-12	93
1.5.7.6	2C20EG60064410	Area EG6, PH 2, Install Small Signs	1	17-Sep-...	18-Sep-12	143
1.5.2.6	2C20WG60054...	Area WG6, PH 2, Install Attenuators	1	18-Sep-...	19-Sep-12	102
1.5.2.6	2C20RP60052910	Area RP6, PH 2, Place Curb & Gutter	15	18-Sep-...	09-Oct-12	67
1.5.7.6	2C20WG60066...	Area WG6, PH 2, Install Perm Markings	2	19-Sep-...	21-Sep-12	102
1.5.9.6	2C20WG60066...	Area WG6, PH 2, Place Temp Marking & Sig...	3	27-Sep-...	02-Oct-12	95
1.5.7.6	2C20WG60064...	Area WG6, PH 2, Install Small Signs	1	03-Oct-12	04-Oct-12	93
1.5	2C20WG60099...	Area WG6, PH 2, Finish	0		04-Oct-12	93
1.5.2.6	2C20RP60034012	Area RP6, PH 2, Place HMA Base	28	09-Oct-12	16-Nov-12	67
1.5.2.6	2C20RP60045010	Area RP6, PH 2, Place Conc Rail (Ret Wall)	33	09-Oct-12	23-Nov-12	75
1.5.7.6	2C20EG60066610	Area EG6, PH 2, Install Perm Markings	7	17-Oct-12	26-Oct-12	115
1.5	2C20EG60099999	Area EG6, PH 2, Finish	0		26-Oct-12	115
1.5.2.6	2C20RP60043210	Area RP6, PH 2, Place Conc RipRap	39	29-Oct-12	21-Dec-12	75
1.5.9.6	2C20RP60050820	Area RP6, PH 2, Const Temp Detour	9	16-Nov-...	29-Nov-12	88
1.5.2.6	2C20RP60034610	Area RP6, PH 2, Place SMA Surface	30	16-Nov-...	28-Dec-12	67
1.5.9.6	2C20RP60051200	Area RP6, PH 2, Place Temp Conc Barrier	3	29-Nov-...	04-Dec-12	88
1.5.7.6	2C20RP60066610	Area RP6, PH 2, Install Perm Markings	3	28-Dec-...	02-Jan-13	67
1.5	2C20RP60099999	Area RP6, PH 2, Finish	0		02-Jan-13	67
1.5.4.6.1.106	2C20B106000001	BR 106, PH 2, Start	0	22-Feb-12		195
1.5.4.6.1.106	2C20B106041600	BR 106, PH 2, Install Drill Shafts	16	22-Feb-12	15-Mar-12	195
1.5.4.6.1.106	2C20B106042040	BR 106, PH 2, Install Abutments	4	29-Feb-12	06-Mar-12	217
1.5.4.6.1.106	2C20B106042010	BR 106, PH 2, Install Footings	26	29-Feb-12	05-Apr-12	195
1.5.4.6.1.106	2C20B106042020	BR 106, PH 2, Install Columns	21	14-Mar-12	12-Apr-12	195
1.5.4.6.1.106	2C20B106042030	BR 106, PH 2, Install Bent Caps	32	21-Mar-12	04-May-12	195
1.5.4.6.1.106	2C20B106042510	BR 106, PH 2, Install Conc Beams	6	04-Apr-12	12-Apr-12	195
1.5.4.6.1.106	2C20B106042210	BR 106, PH 2, Install Deck Slab	45	11-Apr-12	13-Jun-12	195
1.5.4.6.1.106	2C20B106042050	BR 106, PH 2, Install Apprch Slabs	9	13-Jun-12	26-Jun-12	196
1.5.4.6.1.106	2C20B106045020	BR 106, PH 2, Install Conc Rail	6	27-Jun-12	05-Jul-12	195
1.5.4.6.1.106	2C20B106099999	BR 106, PH 2, Finish	0		05-Jul-12	196
1.5.4.6.1.107	2C20B107000001	BR 107, PH 2, Start	0	04-May...		213
1.5.4.6.1.107	2C20B107044210	BR 107, PH 2, Install Plate Girders	5	04-May...	11-May-12	213
1.5.4.6.1.107	2C20B107042210	BR 107, PH 2, Install Deck Slab	5	13-Jun-12	20-Jun-12	196
1.5.4.6.1.107	2C20B107045020	BR 107, PH 2, Install Conc Rail	1	05-Jul-12	06-Jul-12	195
1.5.4.6.1.107	2C20B107099999	BR 107, PH 2, Finish	0		06-Jul-12	195
1.5.4.6.1.110	2C20B110000001	BR 110, PH 2, Start	0	02-Nov-...		279
1.5.4.6.1.110	2C20B110049610	BR 110, PH 2, Demo Extg Bridge	33	02-Nov-...	19-Dec-11	279
1.5.4.6.1.110	2C20B110041600	BR 110, PH 2, Install Drill Shafts	7	19-Dec-...	28-Dec-11	279
1.5.4.6.1.110	2C20B110042020	BR 110, PH 2, Install Columns	4	28-Dec-...	03-Jan-12	279
1.5.4.6.1.110	2C20B110042040	BR 110, PH 2, Install Abutments	8	28-Dec-...	09-Jan-12	279
1.5.4.6.1.110	2C20B110042030	BR 110, PH 2, Install Bent Caps	4	03-Jan-12	09-Jan-12	279
1.5.4.6.1.110	2C20B110042510	BR 110, PH 2, Install Conc Beams	2	09-Jan-12	11-Jan-12	279
1.5.4.6.1.110	2C20B110045410	BR 110, PH 2, Install Exp Joints	2	11-Jan-12	13-Jan-12	279
1.5.4.6.1.110	2C20B110042210	BR 110, PH 2, Install Deck Slab	19	13-Jan-12	09-Feb-12	279
1.5.4.6.1.110	2C20B110042050	BR 110, PH 2, Install Apprch Slabs	20	09-Feb-12	08-Mar-12	279
1.5.4.6.1.110	2C20B110045020	BR 110, PH 2, Install Conc Rail	2	08-Mar-12	12-Mar-12	279
1.5.4.6.1.110	2C20B110099999	BR 110, PH 2, Finish	0		12-Mar-12	279
1.5.4.6.1.116	2C20B116000001	BR 116, PH 2, Start	0	11-Jan-12		227
1.5.4.6.1.116	2C20B116041600	BR 116, PH 2, Install Drill Shafts	6	11-Jan-12	19-Jan-12	227
1.5.4.6.1.116	2C20B116042020	BR 116, PH 2, Install Columns	2	19-Jan-12	23-Jan-12	230
1.5.4.6.1.116	2C20B116042040	BR 116, PH 2, Install Abutments	8	19-Jan-12	31-Jan-12	227
1.5.4.6.1.116	2C20B116042030	BR 116, PH 2, Install Bent Caps	3	23-Jan-12	26-Jan-12	230
1.5.4.6.1.116	2C20B116042510	BR 116, PH 2, Install Conc Beams	2	31-Jan-12	02-Feb-12	227
1.5.4.6.1.116	2C20B116045410	BR 116, PH 2, Install Exp Joints	2	02-Feb-12	06-Feb-12	227
1.5.4.6.1.116	2C20B116042210	BR 116, PH 2, Install Deck Slab	18	06-Feb-12	01-Mar-12	227
1.5.4.6.1.116	2C20B116042050	BR 116, PH 2, Install Apprch Slabs	19	01-Mar-12	28-Mar-12	227
1.5.4.6.1.116	2C20B116045020	BR 116, PH 2, Install Conc Rail	2	28-Mar-12	30-Mar-12	227
1.5.4.6.1.116	2C20B116099999	BR 116, PH 2, Finish	0		30-Mar-12	227
1.5.4.6.1.120	2C20B120000001	BR 120, PH 2, Start	0	22-Feb-12		238
1.5.4.6.1.120	2C20B120041600	BR 120, PH 2, Install Drill Shafts	3	22-Feb-12	27-Feb-12	238
1.5.4.6.1.120	2C20B120042040	BR 120, PH 2, Install Abutments	5	27-Feb-12	05-Mar-12	253
1.5.4.6.1.120	2C20B120042010	BR 120, PH 2, Install Footings	9	27-Feb-12	09-Mar-12	238
1.5.4.6.1.120	2C20B120042020	BR 120, PH 2, Install Columns	4	09-Mar-12	15-Mar-12	238
1.5.4.6.1.120	2C20B120042030	BR 120, PH 2, Install Bent Caps	7	15-Mar-12	26-Mar-12	238

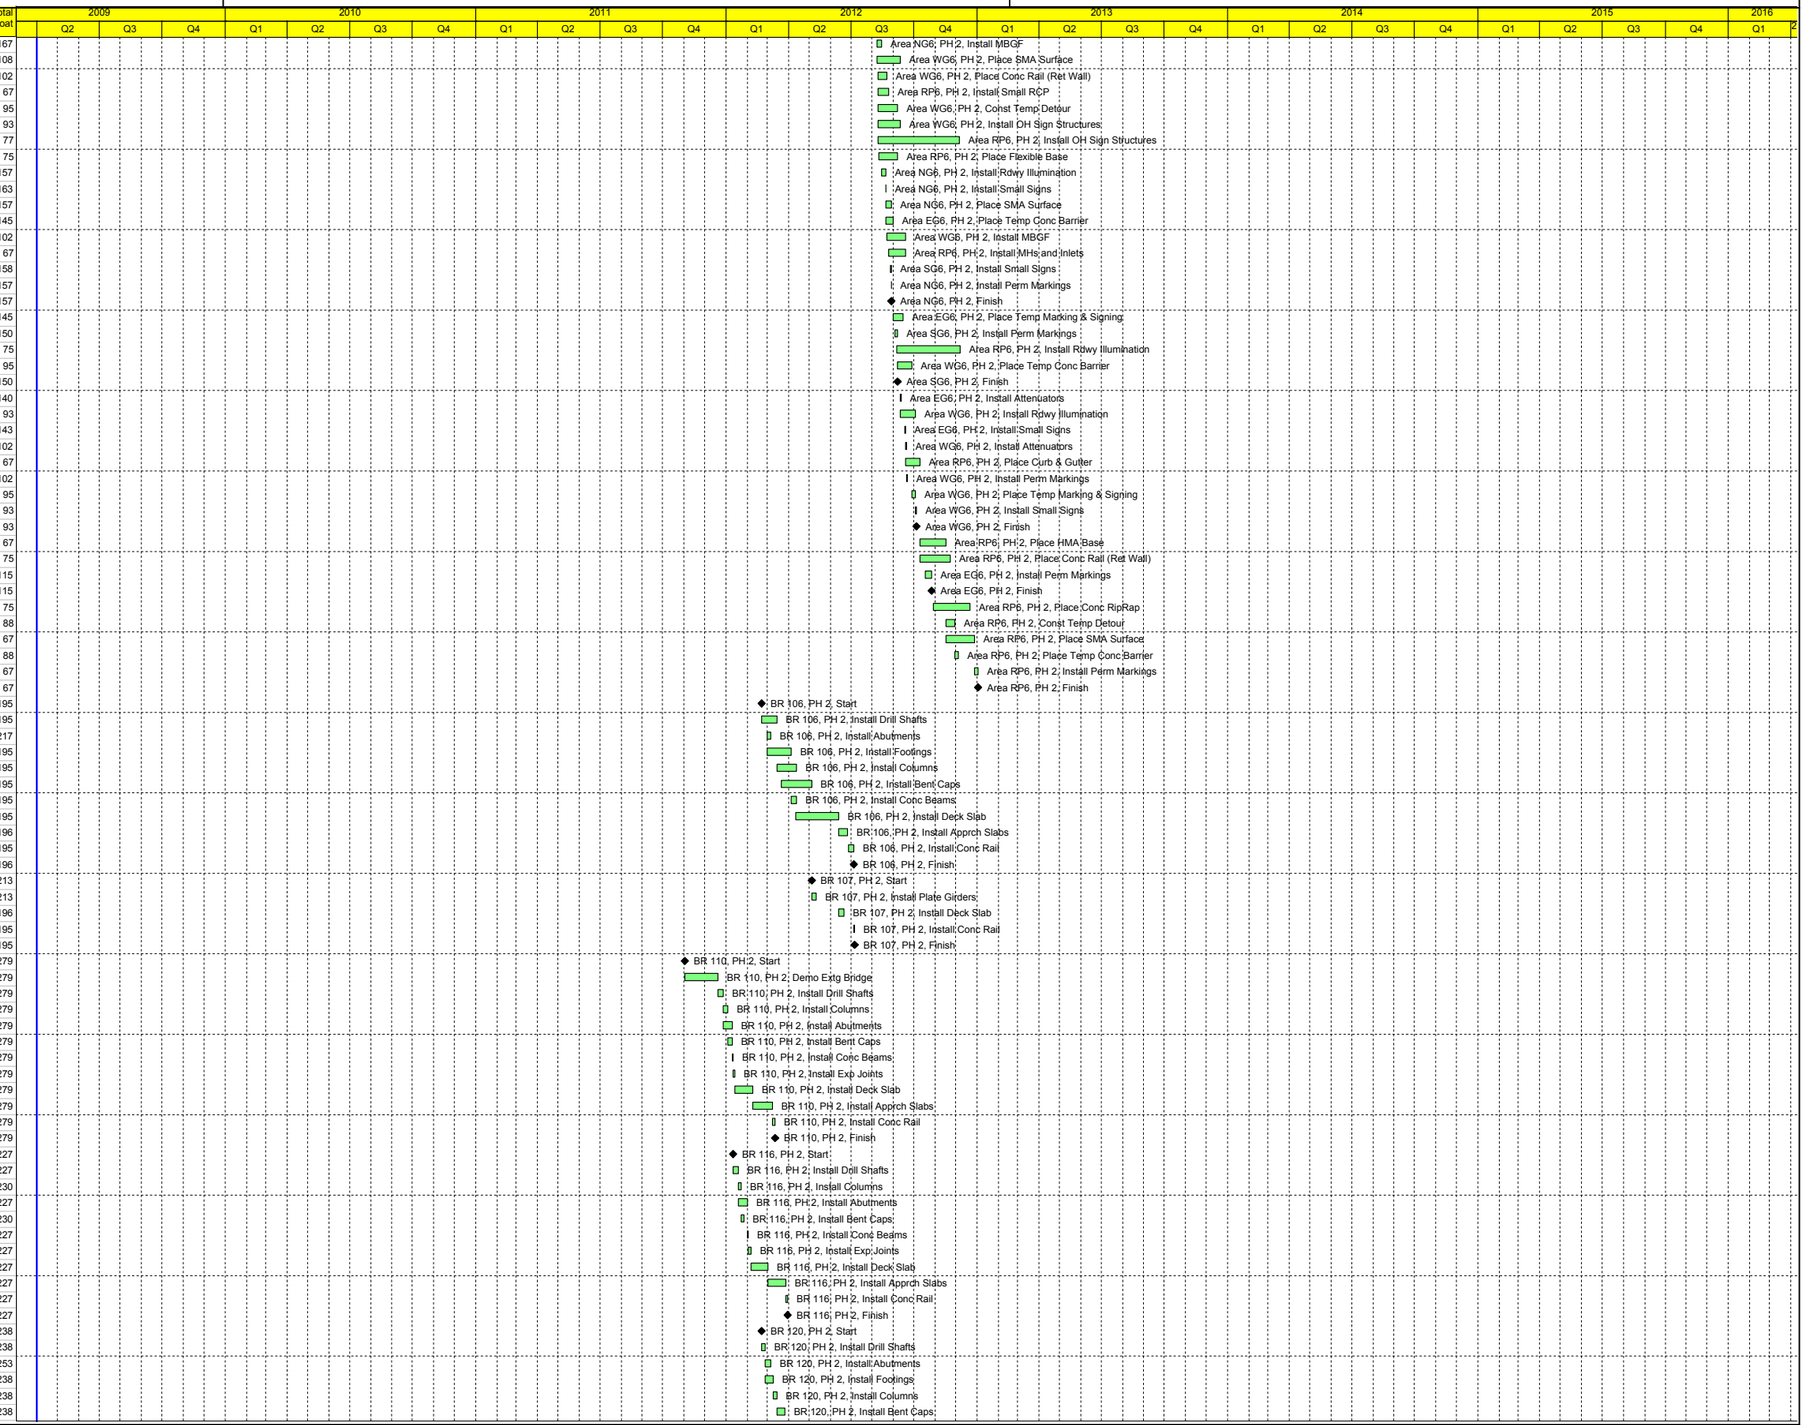

Remaining Level of Effort | Remaining Work | Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.5.4.6.1.120	2C20B120042510	BR 120, PH 2, Install Conc Beams	2	26-Mar-12	28-Mar-12	238
1.5.4.6.1.120	2C20B120045410	BR 120, PH 2, Install Exp Joints	2	28-Mar-12	30-Mar-12	238
1.5.4.6.1.120	2C20B120042210	BR 120, PH 2, Install Deck Slab	14	30-Mar-12	19-Apr-12	238
1.5.4.6.1.120	2C20B120042050	BR 120, PH 2, Install Apprch Slabs	10	19-Apr-12	03-May-12	238
1.5.4.6.1.120	2C20B120045020	BR 120, PH 2, Install Conc Rail	3	03-May...	08-May-12	238
1.5.4.6.1.120	2C20B120099999	BR 120, PH 2, Finish	0		08-May-12	238
1.5.4.6.1.121	2C20B121000001	BR 121, PH 2, Start	0	22-Feb-12		187
1.5.4.6.1.121	2C20B121041600	BR 121, PH 2, Install Drill Shafts	6	22-Feb-12	01-Mar-12	187
1.5.4.6.1.121	2C20B121042040	BR 121, PH 2, Install Abutments	3	01-Mar-12	06-Mar-12	215
1.5.4.6.1.121	2C20B121042010	BR 121, PH 2, Install Footings	7	01-Mar-12	12-Mar-12	187
1.5.4.6.1.121	2C20B121042020	BR 121, PH 2, Install Columns	9	12-Mar-12	23-Mar-12	187
1.5.4.6.1.121	2C20B121042030	BR 121, PH 2, Install Bent Caps	15	23-Mar-12	13-Apr-12	187
1.5.4.6.1.121	2C20B121042510	BR 121, PH 2, Install Conc Beams	6	13-Apr-12	23-Apr-12	187
1.5.4.6.1.121	2C20B121045410	BR 121, PH 2, Install Exp Joints	2	23-Apr-12	25-Apr-12	187
1.5.4.6.1.121	2C20B121042210	BR 121, PH 2, Install Deck Slab	42	25-Apr-12	22-Jun-12	187
1.5.4.6.1.121	2C20B121042050	BR 121, PH 2, Install Apprch Slabs	5	22-Jun-12	29-Jun-12	192
1.5.4.6.1.121	2C20B121045020	BR 121, PH 2, Install Conc Rail	8	06-Jul-12	18-Jul-12	187
1.5.4.6.1.121	2C20B121099999	BR 121, PH 2, Finish	0		18-Jul-12	187
1.5.4.6.1.122	2C20B122000001	BR 122, PH 2, Start	0	22-Feb-12		138
1.5.4.6.1.122	2C20B122041600	BR 122, PH 2, Install Drill Shafts	8	22-Feb-12	05-Mar-12	138
1.5.4.6.1.122	2C20B122042040	BR 122, PH 2, Install Abutments	4	05-Mar-12	09-Mar-12	222
1.5.4.6.1.122	2C20B122042010	BR 122, PH 2, Install Footings	32	05-Mar-12	18-Apr-12	138
1.5.4.6.1.122	2C20B122042020	BR 122, PH 2, Install Columns	24	18-Apr-12	22-May-12	138
1.5.4.6.1.122	2C20B122042030	BR 122, PH 2, Install Bent Caps	32	22-May...	05-Jul-12	138
1.5.4.6.1.122	2C20B122042510	BR 122, PH 2, Install Conc Beams	5	05-Jul-12	12-Jul-12	138
1.5.4.6.1.122	2C20B122045410	BR 122, PH 2, Install Exp Joints	2	12-Jul-12	16-Jul-12	138
1.5.4.6.1.122	2C20B122042210	BR 122, PH 2, Install Deck Slab	34	16-Jul-12	31-Aug-12	138
1.5.4.6.1.122	2C20B122042050	BR 122, PH 2, Install Apprch Slabs	8	31-Aug-...	12-Sep-12	140
1.5.4.6.1.122	2C20B122045020	BR 122, PH 2, Install Conc Rail	7	14-Sep-...	25-Sep-12	138
1.5.4.6.1.122	2C20B122099999	BR 122, PH 2, Finish	0		25-Sep-12	138
1.5.4.6.1.124	2C20B124000001	BR 124, PH 2, Start	0	11-Jan-12		182
1.5.4.6.1.124	2C20B124049610	BR 124, PH 2, Demo Extg Bridge	33	11-Jan-12	27-Feb-12	182
1.5.4.6.1.124	2C20B124041600	BR 124, PH 2, Install Drill Shafts	4	27-Feb-12	02-Mar-12	182
1.5.4.6.1.124	2C20B124042020	BR 124, PH 2, Install Columns	3	02-Mar-12	07-Mar-12	183
1.5.4.6.1.124	2C20B124042040	BR 124, PH 2, Install Abutments	8	02-Mar-12	14-Mar-12	182
1.5.4.6.1.124	2C20B124042030	BR 124, PH 2, Install Bent Caps	4	07-Mar-12	13-Mar-12	183
1.5.4.6.1.124	2C20B124042510	BR 124, PH 2, Install Conc Beams	3	14-Mar-12	19-Mar-12	182
1.5.4.6.1.124	2C20B124045410	BR 124, PH 2, Install Exp Joints	2	19-Mar-12	21-Mar-12	182
1.5.4.6.1.124	2C20B124042210	BR 124, PH 2, Install Deck Slab	19	21-Mar-12	17-Apr-12	182
1.5.4.6.1.124	2C20B124042050	BR 124, PH 2, Install Apprch Slabs	31	17-Apr-12	30-May-12	182
1.5.4.6.1.124	2C20B124045020	BR 124, PH 2, Install Conc Rail	2	30-May...	01-Jun-12	182
1.5.4.6.1.124	2C20B124099999	BR 124, PH 2, Finish	0		01-Jun-12	182
1.5.4.6.1.127	2C20B127000001	BR 127, PH 2, Start	0	02-Nov-...		265
1.5.4.6.1.127	2C20B127049610	BR 127, PH 2, Demo Extg Bridge	33	02-Nov-...	19-Dec-11	265
1.5.4.6.1.127	2C20B127041600	BR 127, PH 2, Install Drill Shafts	8	19-Dec-...	29-Dec-11	265
1.5.4.6.1.127	2C20B127042020	BR 127, PH 2, Install Columns	3	29-Dec-...	03-Jan-12	267
1.5.4.6.1.127	2C20B127042040	BR 127, PH 2, Install Abutments	9	29-Dec-...	11-Jan-12	265
1.5.4.6.1.127	2C20B127042030	BR 127, PH 2, Install Bent Caps	4	03-Jan-12	09-Jan-12	267
1.5.4.6.1.127	2C20B127042510	BR 127, PH 2, Install Conc Beams	4	11-Jan-12	17-Jan-12	265
1.5.4.6.1.127	2C20B127045410	BR 127, PH 2, Install Exp Joints	2	17-Jan-12	19-Jan-12	265
1.5.4.6.1.127	2C20B127042210	BR 127, PH 2, Install Deck Slab	26	19-Jan-12	24-Feb-12	265
1.5.4.6.1.127	2C20B127042050	BR 127, PH 2, Install Apprch Slabs	23	24-Feb-12	28-Mar-12	265
1.5.4.6.1.127	2C20B127045020	BR 127, PH 2, Install Conc Rail	2	28-Mar-12	30-Mar-12	265
1.5.4.6.1.127	2C20B127099999	BR 127, PH 2, Finish	0		30-Mar-12	265
1.5.4.6.1.130	2C20B130000001	BR 130, PH 2, Start	0	02-Nov-...		276
1.5.4.6.1.130	2C20B130049610	BR 130, PH 2, Demo Extg Bridge	33	02-Nov-...	19-Dec-11	276
1.5.4.6.1.130	2C20B130041600	BR 130, PH 2, Install Drill Shafts	6	19-Dec-...	27-Dec-11	276
1.5.4.6.1.130	2C20B130042020	BR 130, PH 2, Install Columns	3	27-Dec-...	30-Dec-11	277
1.5.4.6.1.130	2C20B130042040	BR 130, PH 2, Install Abutments	8	27-Dec-...	06-Jan-12	276
1.5.4.6.1.130	2C20B130042030	BR 130, PH 2, Install Bent Caps	4	30-Dec-...	05-Jan-12	277
1.5.4.6.1.130	2C20B130042510	BR 130, PH 2, Install Conc Beams	3	06-Jan-12	11-Jan-12	276
1.5.4.6.1.130	2C20B130045410	BR 130, PH 2, Install Exp Joints	2	11-Jan-12	13-Jan-12	276
1.5.4.6.1.130	2C20B130042210	BR 130, PH 2, Install Deck Slab	21	13-Jan-12	13-Feb-12	276
1.5.4.6.1.130	2C20B130042050	BR 130, PH 2, Install Apprch Slabs	21	13-Feb-12	13-Mar-12	276
1.5.4.6.1.130	2C20B130045020	BR 130, PH 2, Install Conc Rail	2	13-Mar-12	15-Mar-12	276
1.5.4.6.1.130	2C20B130099999	BR 130, PH 2, Finish	0		15-Mar-12	276
1.5.4.6.1.133	2C20B133000001	BR 133, PH 2, Start	0	22-Feb-12		166
1.5.4.6.1.133	2C20B133049610	BR 133, PH 2, Demo Extg Bridge	19	22-Feb-12	20-Mar-12	166
1.5.4.6.1.133	2C20B133041600	BR 133, PH 2, Install Drill Shafts	6	20-Mar-12	28-Mar-12	166
1.5.4.6.1.133	2C20B133042040	BR 133, PH 2, Install Abutments	6	28-Mar-12	05-Apr-12	195
1.5.4.6.1.133	2C20B133042010	BR 133, PH 2, Install Footings	29	28-Mar-12	08-May-12	166
1.5.4.6.1.133	2C20B133042050	BR 133, PH 2, Install Apprch Slabs	14	05-Apr-12	25-Apr-12	241
1.5.4.6.1.133	2C20B133042020	BR 133, PH 2, Install Columns	22	13-Apr-12	15-May-12	166
1.5.4.6.1.133	2C20B133042030	BR 133, PH 2, Install Bent Caps	59	20-Apr-12	12-Jul-12	166
1.5.4.6.1.133	2C20B133042510	BR 133, PH 2, Install Conc Beams	7	04-May...	15-May-12	174
1.5.4.6.1.133	2C20B133042210	BR 133, PH 2, Install Deck Slab	53	21-May...	02-Aug-12	166
1.5.4.6.1.133	2C20B133045020	BR 133, PH 2, Install Conc Rail	6	08-Aug-...	16-Aug-12	166
1.5.4.6.1.133	2C20B133099999	BR 133, PH 2, Finish	0		16-Aug-12	166
1.5.4.6.1.141	2C20B141000001	BR 141, PH 2, Start	0	22-Feb-12		241
1.5.4.6.1.141	2C20B141041600	BR 141, PH 2, Install Drill Shafts	3	22-Feb-12	27-Feb-12	241
1.5.4.6.1.141	2C20B141042040	BR 141, PH 2, Install Abutments	2	27-Feb-12	29-Feb-12	254
1.5.4.6.1.141	2C20B141042010	BR 141, PH 2, Install Footings	8	27-Feb-12	08-Mar-12	241
1.5.4.6.1.141	2C20B141042020	BR 141, PH 2, Install Columns	3	08-Mar-12	13-Mar-12	241
1.5.4.6.1.141	2C20B141042030	BR 141, PH 2, Install Bent Caps	4	13-Mar-12	19-Mar-12	241
1.5.4.6.1.141	2C20B141042510	BR 141, PH 2, Install Conc Beams	3	19-Mar-12	22-Mar-12	241
1.5.4.6.1.141	2C20B141045410	BR 141, PH 2, Install Exp Joints	1	22-Mar-12	23-Mar-12	241

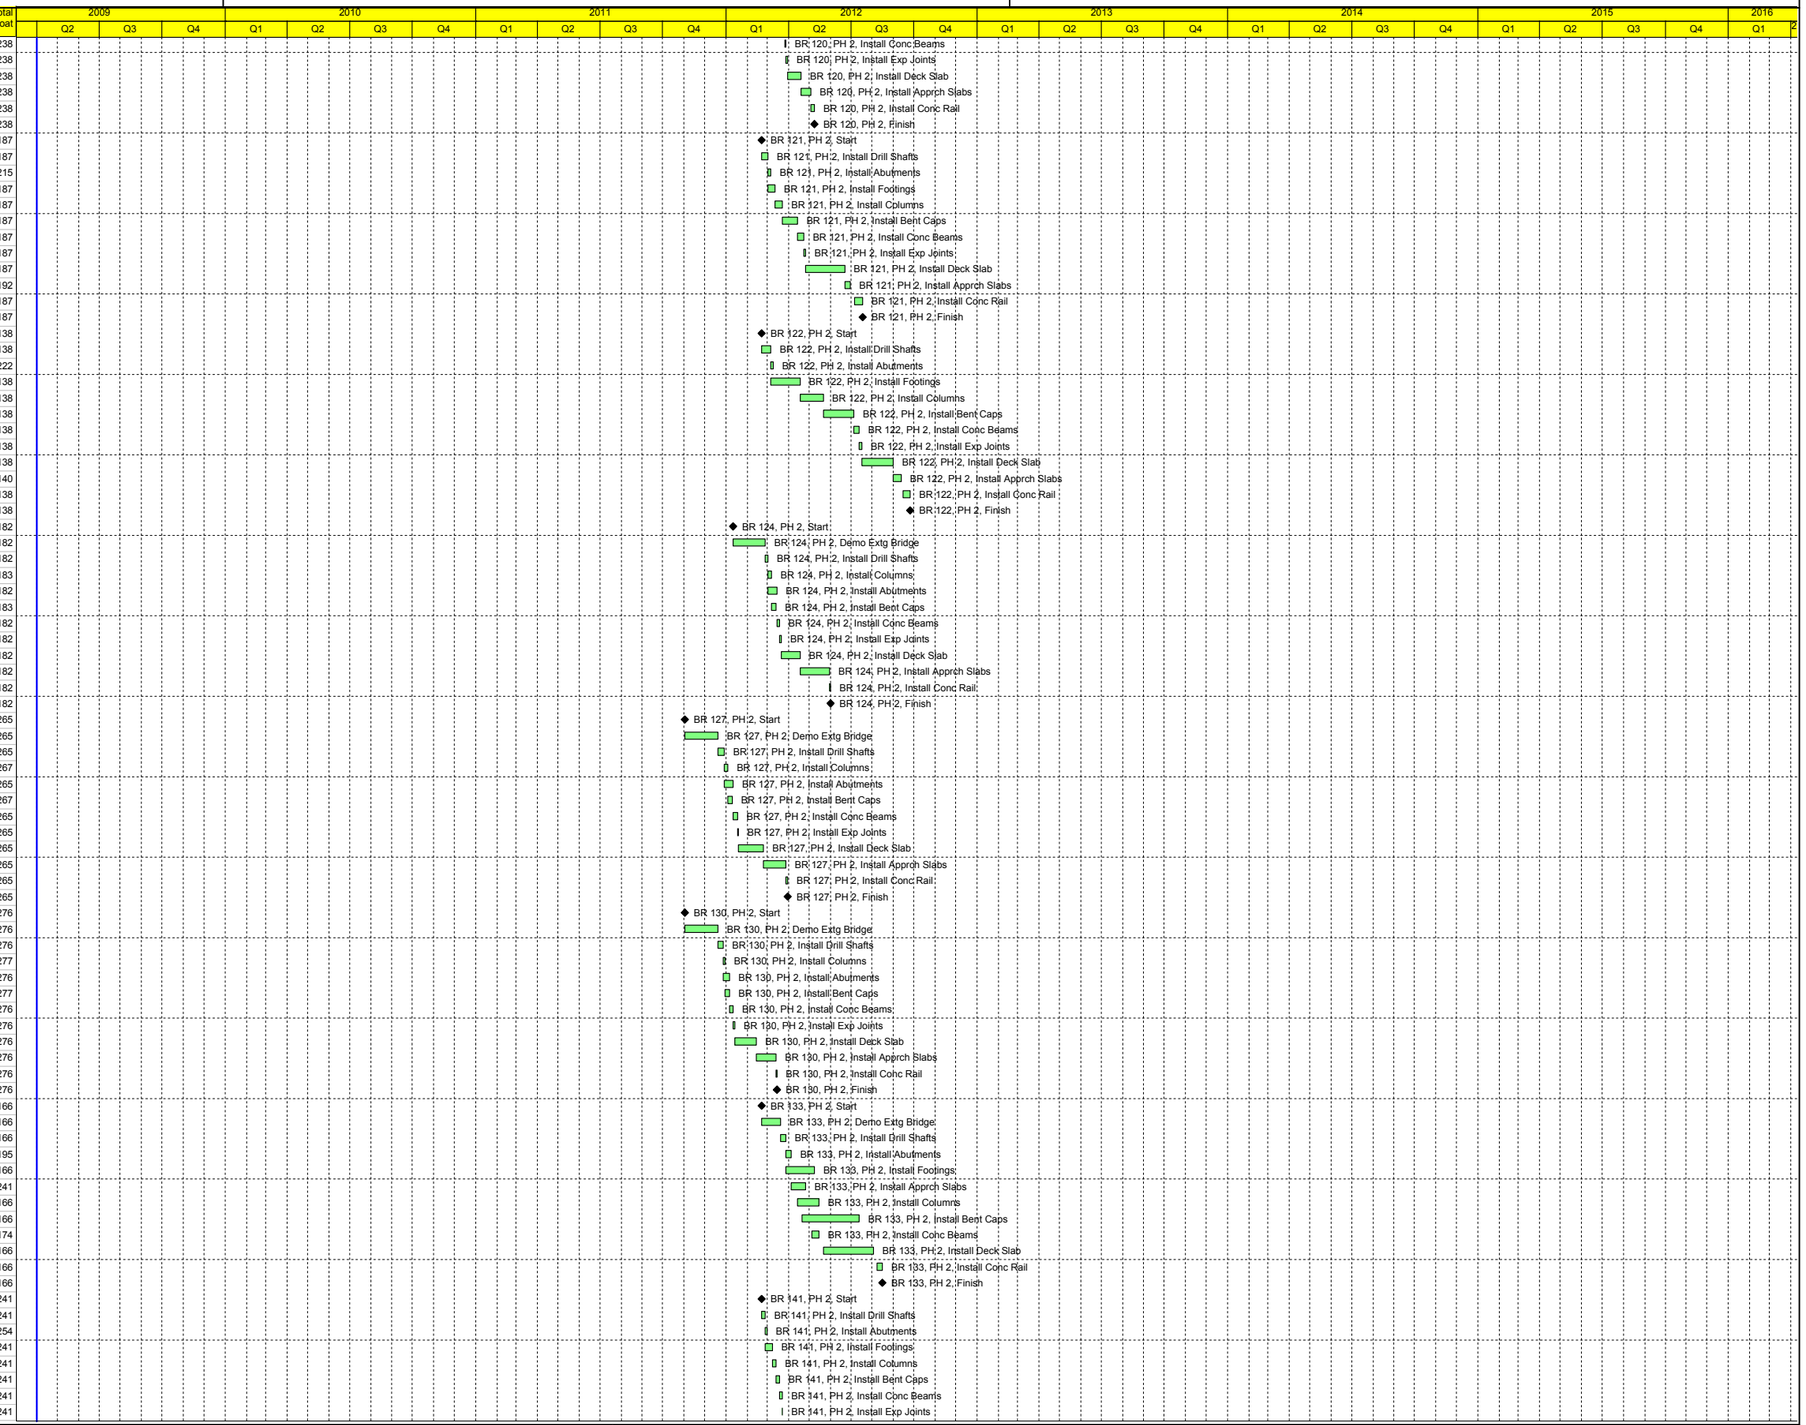

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.5.4.6.1.141	2C20B141042210	BR 141, PH 2, Install Deck Slab	15	23-Mar-12	13-Apr-12	241
1.5.4.6.1.141	2C20B141042050	BR 141, PH 2, Install Apprch Slabs	5	13-Apr-12	20-Apr-12	246
1.5.4.6.1.141	2C20B141045020	BR 141, PH 2, Install Conc Rail	4	27-Apr-12	03-May-12	241
1.5.4.6.1.141	2C20B141099999	BR 141, PH 2, Finish	0		03-May-12	241
1.5	2C200000000001	START PHASE 2, SUBSEGMENT 2C	0	17-Oct-12		700
1.5	2C200000099999	FINISH PHASE 2, SUBSEGMENT 2C	0		02-Jan-13	67
CONSTRUCTION PHASE 3			209	04-Oct-12	24-Jul-13	67
1.5	2C30WG60000...	Area WG6, PH 3, Start	0	04-Oct-12		93
1.5.2.6	2C30WG60060...	Area WG6, PH 3, Rem Light Poles	4	04-Oct-12	10-Oct-12	114
1.5.2.6	2C30WG60054...	Area WG6, PH 3, Rem MBGF	6	04-Oct-12	12-Oct-12	112
1.5.2.6	2C30WG60050...	Area WG6, PH 3, Place Temp Erosion Control	12	04-Oct-12	22-Oct-12	93
1.5.2.6	2C30WG60063...	Area WG6, PH 3, Rem Overhead Sign Supp...	18	04-Oct-12	30-Oct-12	112
1.5.2.6	2C30WG60010...	Area WG6, PH 3, Rem Concrete Barrier	14	12-Oct-12	01-Nov-12	112
1.5.2.6	2C30WG60010...	Area WG6, PH 3, Rem Conc Pavement	11	22-Oct-12	06-Nov-12	111
1.5.3.6	2C30WG60046...	Area WG6, PH 3, Install Large CBC	34	22-Oct-12	07-Dec-12	93
1.5.4.6	2C30WG60042...	Area WG6, PH 3, Install Cut Wall, Stage 1 (2...	43	22-Oct-12	20-Dec-12	104
1.5.2.6	2C30WG60013...	Area WG6, PH 3, Place Embankment (2 Cre...	32	01-Nov-...	17-Dec-12	104
1.5.2.6	2C30WG60011...	Area WG6, PH 3, Excavate Cut Areas (2 Cre...	45	01-Nov-...	03-Jan-13	104
1.5.9.6	2C30WG60040...	Area WG6, PH 3, Construct Temp Walls/Sho...	45	01-Nov-...	03-Jan-13	107
1.5.4.6	2C30WG60042...	Area WG6, PH 3, Install Fill Wall Complete (...	75	01-Nov-...	14-Feb-13	104
1.5.4.6	2C30WG60042...	Area WG6, PH 3, Install Cut Wall, Stage 2 (2...	71	08-Nov-...	15-Feb-13	113
1.5.2.6	2C30WG60026...	Area WG6, PH 3, Lime Treat Subgrade (3 cr...	72	13-Nov-...	21-Feb-13	104
1.5.3.6	2C30WG60046...	Area WG6, PH 3, Install Medium CBC	18	07-Dec-...	02-Jan-13	93
1.5.4.6	2C30WG60042...	Area WG6, PH 3, Install Moment Slabs	56	12-Dec-...	28-Feb-13	131
1.5.2.6	2C30WG60024...	Area WG6, PH 3, Place Flexible Base	51	19-Dec-...	28-Feb-13	104
1.5.2.6	2C30WG60034...	Area WG6, PH 3, Place HMA Base	65	26-Dec-...	27-Mar-13	117
1.5	2C30EG60000001	Area EG6, PH 3, Start	0	02-Jan-13		68
1.5	2C30RP60000001	Area RP6, PH 3, Start	0	02-Jan-13		67
1.5	2C30NG60000001	Area NG6, PH 3, Start	0	02-Jan-13		173
1.5	2C30SG60000001	Area SG6, PH 3, Start	0	02-Jan-13		210
1.5.4.6	2C30SG60042310	Area SG6, PH 3, Install Fill Wall Complete	1	02-Jan-13	03-Jan-13	210
1.5.2.6	2C30NG60050600	Area NG6, PH 3, Place Temp Erosion Control	2	02-Jan-13	04-Jan-13	173
1.5.2.6	2C30RP60010410	Area RP6, PH 3, Rem Conc Pavement	4	02-Jan-13	08-Jan-13	67
1.5.3.6	2C30WG60046...	Area WG6, PH 3, Install Small CBC	15	02-Jan-13	23-Jan-13	93
1.5.2.6	2C30EG60050600	Area EG6, PH 3, Place Temp Erosion Control	24	02-Jan-13	05-Feb-13	68
1.5.2.6	2C30WG60034...	Area WG6, PH 3, Place SMA Surface	74	02-Jan-13	16-Apr-13	132
1.5.4.6	2C30SG60042315	Area SG6, PH 3, Install Moment Slabs	1	03-Jan-13	04-Jan-13	210
1.5	2C30SG60099999	Area SG6, PH 3, Finish	0		04-Jan-13	210
1.5.2.6	2C30NG60054210	Area NG6, PH 3, Rem MBGF	1	04-Jan-13	07-Jan-13	174
1.5.2.6	2C30NG60060010	Area NG6, PH 3, Rem Light Poles	1	04-Jan-13	07-Jan-13	174
1.5.2.6	2C30NG60063010	Area NG6, PH 3, Rem Overhead Sign Supports	2	04-Jan-13	08-Jan-13	173
1.5.2.6	2C30WG60053...	Area WG6, PH 3, Place Sidewalks & Drivew...	48	07-Jan-13	14-Mar-13	150
1.5.2.6	2C30NG60010430	Area NG6, PH 3, Rem Concrete Barrier	1	08-Jan-13	09-Jan-13	173
1.5.3.6	2C30RP60046220	Area RP6, PH 3, Install Medium CBC	2	08-Jan-13	10-Jan-13	159
1.5.4.6	2C30RP60042320	Area RP6, PH 3, Install Cut Wall, Stage 1 (3 ...	33	08-Jan-13	22-Feb-13	67
1.5.2.6	2C30NG60010410	Area NG6, PH 3, Rem Conc Pavement	1	09-Jan-13	10-Jan-13	173
1.5.3.6	2C30RP60046210	Area RP6, PH 3, Install Small CBC	1	10-Jan-13	11-Jan-13	159
1.5.4.6	2C30NG60042310	Area NG6, PH 3, Install Fill Wall Complete	1	10-Jan-13	11-Jan-13	176
1.5.3.6	2C30NG60046230	Area NG6, PH 3, Install Large CBC	2	10-Jan-13	14-Jan-13	182
1.5.2.6	2C30NG60013210	Area NG6, PH 3, Place Embankment	3	10-Jan-13	15-Jan-13	174
1.5.2.6	2C30NG60011010	Area NG6, PH 3, Excavate Cut Areas	4	10-Jan-13	16-Jan-13	173
1.5.3.6	2C30RP60046420	Area RP6, PH 3, Install Medium RCP	3	11-Jan-13	16-Jan-13	159
1.5.3.6	2C30NG60046220	Area NG6, PH 3, Install Medium CBC	1	14-Jan-13	15-Jan-13	182
1.5.3.6	2C30NG60046210	Area NG6, PH 3, Install Small CBC	1	15-Jan-13	16-Jan-13	182
1.5.3.6	2C30NG60046420	Area NG6, PH 3, Install Medium RCP	1	16-Jan-13	17-Jan-13	182
1.5.7.6	2C30NG60061320	Area NG6, PH 3, Install High Mast Illumination	8	16-Jan-13	28-Jan-13	189
1.5.2.6	2C30NG60026010	Area NG6, PH 3, Lime Treat Subgrade	12	16-Jan-13	01-Feb-13	173
1.5.3.6	2C30NG60046410	Area NG6, PH 3, Install Small RCP	1	17-Jan-13	18-Jan-13	182
1.5.3.6	2C30NG60046510	Area NG6, PH 3, Install MHs and Inlets	1	18-Jan-13	21-Jan-13	182
1.5.2.6	2C30WG60054...	Area WG6, PH 3, Install MBGF	61	22-Jan-13	17-Apr-13	129
1.5.3.6	2C30WG60046...	Area WG6, PH 3, Install Medium RCP	5	23-Jan-13	30-Jan-13	93
1.5.8.6	2C30WG60061...	Area WG6, PH 3, Install ITS Duct Bank	5	30-Jan-13	06-Feb-13	93
1.5.3.6	2C30WG60046...	Area WG6, PH 3, Install Small RCP	9	30-Jan-13	12-Feb-13	109
1.5.3.6	2C30WG60046...	Area WG6, PH 3, Install MHs and Inlets	11	30-Jan-13	14-Feb-13	109
1.5.4.6	2C30NG60042315	Area NG6, PH 3, Install Moment Slabs	1	01-Feb-13	04-Feb-13	174
1.5.2.6	2C30NG60024710	Area NG6, PH 3, Place Flexible Base	2	01-Feb-13	05-Feb-13	173
1.5.2.6	2C30EG60060010	Area EG6, PH 3, Rem Light Poles	2	05-Feb-13	07-Feb-13	75
1.5.2.6	2C30NG60053110	Area NG6, PH 3, Place Sidewalks & Driveways	2	05-Feb-13	07-Feb-13	181
1.5.2.6	2C30EG60054210	Area EG6, PH 3, Rem MBGF	3	05-Feb-13	08-Feb-13	74
1.5.2.6	2C30NG60034012	Area NG6, PH 3, Place HMA Base	3	05-Feb-13	08-Feb-13	173
1.5.2.6	2C30EG60063010	Area EG6, PH 3, Rem Overhead Sign Supports	9	05-Feb-13	18-Feb-13	68
1.5.8.6	2C30WG60041...	Area WG6, PH 3, Install ITS Structures & Equip	38	06-Feb-13	01-Apr-13	93
1.5.9.6	2C30NG60066200	Area NG6, PH 3, Place Temp Marking & Sig...	1	08-Feb-13	11-Feb-13	184
1.5.2.6	2C30NG60045010	Area NG6, PH 3, Place Conc Rail (Ret Wall)	2	08-Feb-13	12-Feb-13	179
1.5.7.6	2C30NG60065010	Area NG6, PH 3, Install OH Sign Structures	4	08-Feb-13	14-Feb-13	173
1.5.2.6	2C30NG60054010	Area NG6, PH 3, Install MBGF	3	12-Feb-13	15-Feb-13	179
1.5.7.6	2C30NG60061020	Area NG6, PH 3, Install Rdwy Illumination	3	14-Feb-13	19-Feb-13	173
1.5.4.6	2C30RP60042325	Area RP6, PH 3, Install Cut Wall, Stage 2 (3 ...	43	14-Feb-13	16-Apr-13	115
1.5.7.6	2C30WG60065...	Area WG6, PH 3, Install OH Sign Structures	67	15-Feb-13	21-May-13	113
1.5.2.6	2C30EG60010430	Area EG6, PH 3, Rem Concrete Barrier	7	18-Feb-13	27-Feb-13	68
1.5.7.6	2C30NG60064410	Area NG6, PH 3, Install Small Signs	1	19-Feb-13	20-Feb-13	177
1.5.2.6	2C30NG60034610	Area NG6, PH 3, Place SMA Surface	4	19-Feb-13	25-Feb-13	173
1.5.9.6	2C30RP60040390	Area RP6, PH 3, Construct Temp Walls/Shori...	10	22-Feb-13	08-Mar-13	90
1.5.2.6	2C30RP60013210	Area RP6, PH 3, Place Embankment	22	22-Feb-13	26-Mar-13	67
1.5.2.6	2C30WG60045...	Area WG6, PH 3, Place Conc Rail (Ret Wall)	28	22-Feb-13	03-Apr-13	129
1.5.2.6	2C30RP60011010	Area RP6, PH 3, Excavate Cut Areas	32	22-Feb-13	09-Apr-13	67

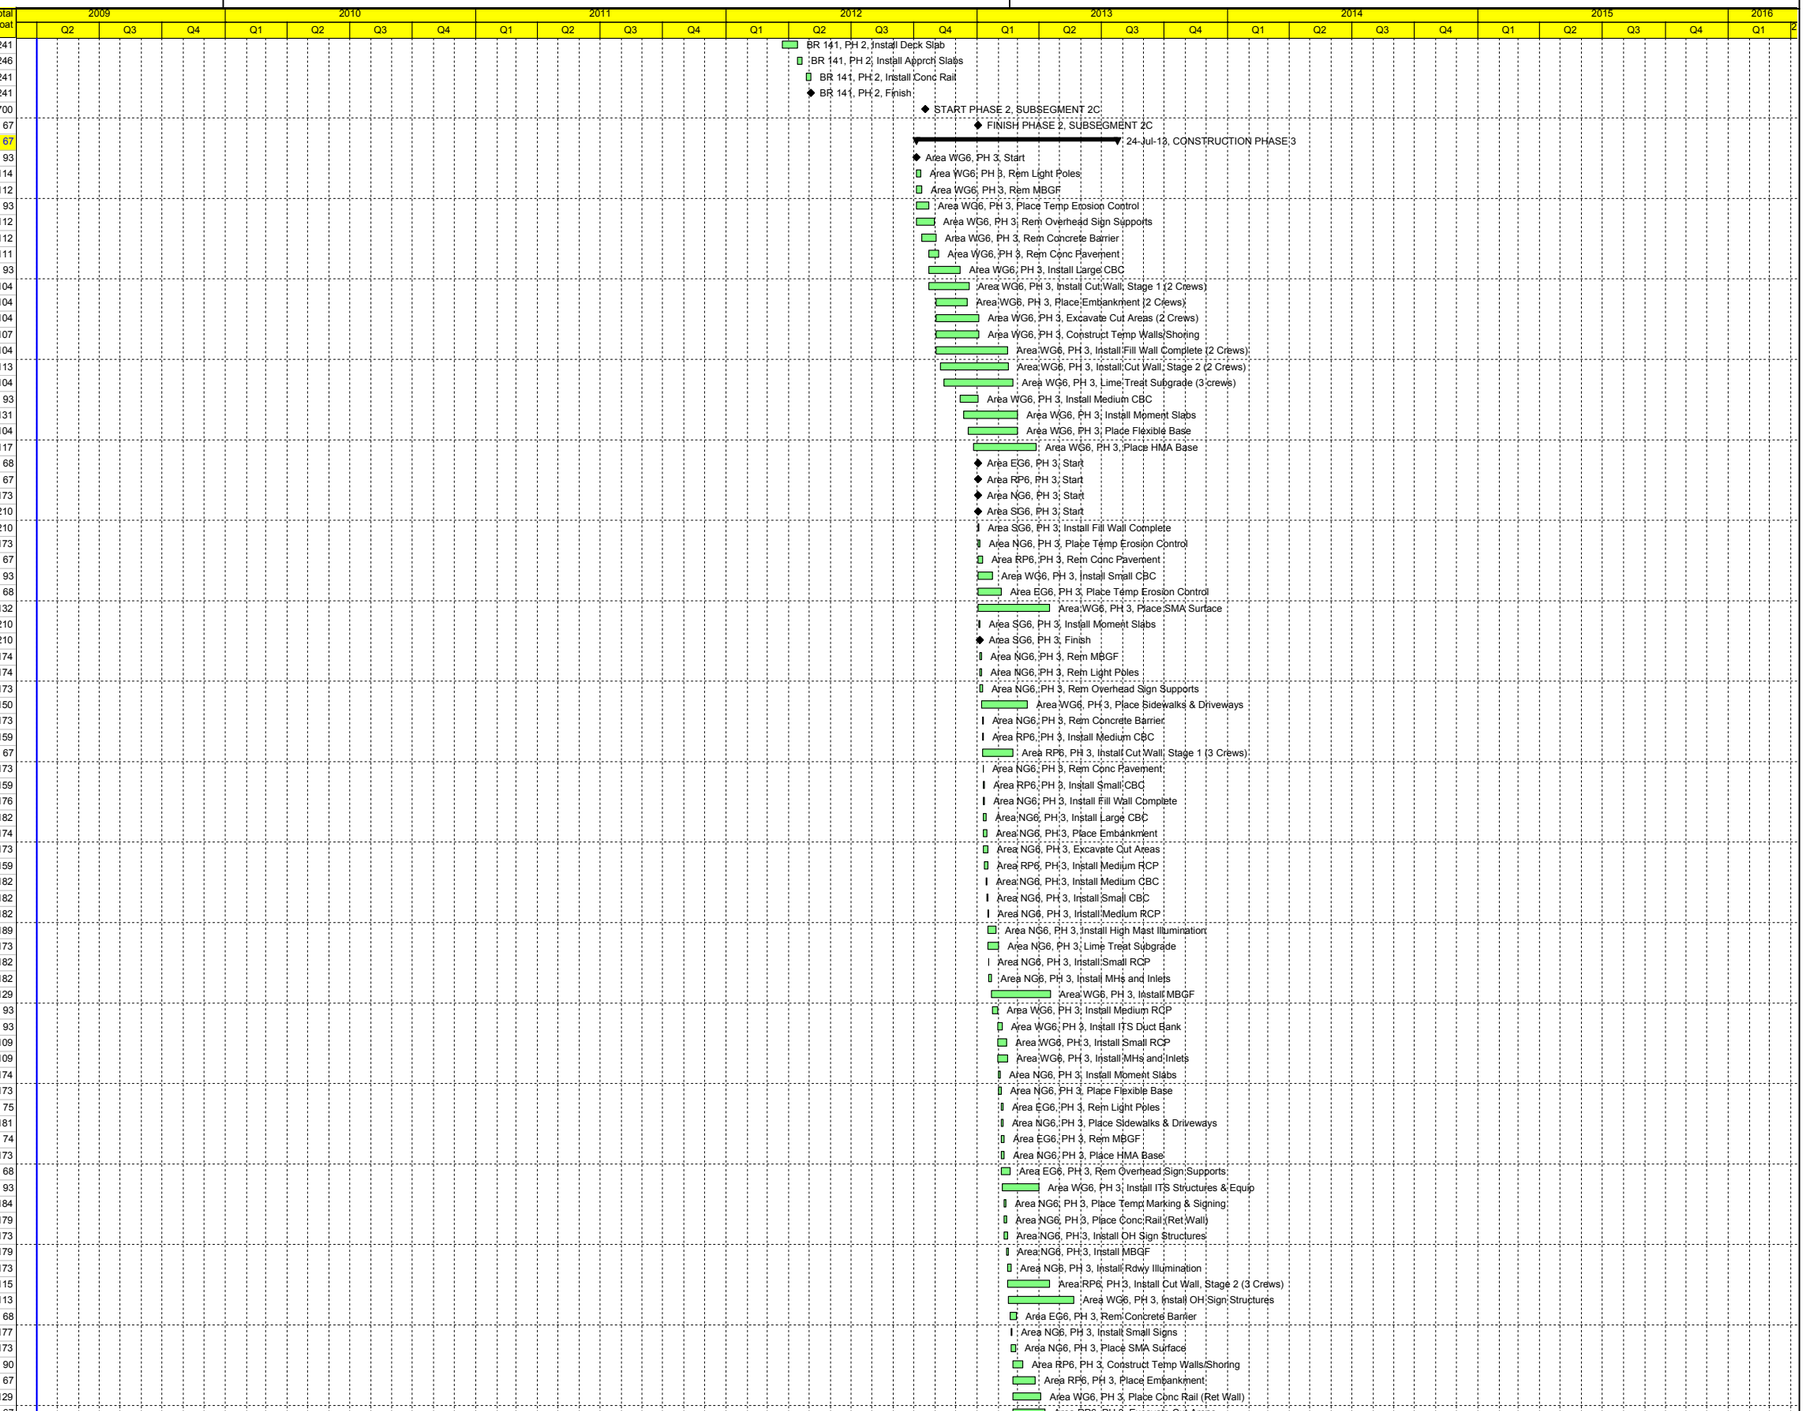

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.5.4.6	2C30RP60042310	Area RP6, PH 3, Install Fill Wall Complete (2...	33	22-Feb-13	10-Apr-13	67
1.5.7.6	2C30NG60066610	Area NG6, PH 3, Install Perm Markings	1	25-Feb-13	26-Feb-13	173
1.5	2C30NG60099999	Area NG6, PH 3, Finish	0		26-Feb-13	173
1.5.2.6	2C30EG60010410	Area EG6, PH 3, Rem Conc Pavement	5	27-Feb-13	06-Mar-13	68
1.5.9.6	2C30WG60050...	Area WG6, PH 3, Const Temp Detour	52	28-Feb-13	13-May-13	104
1.5.4.6	2C30EG60042310	Area EG6, PH 3, Install Fill Wall Complete	4	06-Mar-13	12-Mar-13	111
1.5.9.6	2C30EG60040390	Area EG6, PH 3, Construct Temp Walls/Shor...	16	06-Mar-13	28-Mar-13	99
1.5.3.6	2C30EG60046230	Area EG6, PH 3, Install Large CBC	17	06-Mar-13	29-Mar-13	72
1.5.2.6	2C30EG60013210	Area EG6, PH 3, Place Embankment	31	06-Mar-13	18-Apr-13	68
1.5.2.6	2C30EG60011010	Area EG6, PH 3, Excavate Cut Areas	38	06-Mar-13	29-Apr-13	68
1.5.2.6	2C30EG60026010	Area EG6, PH 3, Lime Treat Subgrade (3 Cr...	47	13-Mar-13	17-May-13	68
1.5.3.6	2C30EG60046220	Area EG6, PH 3, Install Medium CBC	9	29-Mar-13	11-Apr-13	72
1.5.7.6	2C30WG60064...	Area WG6, PH 3, Install Small Signs	1	01-Apr-13	02-Apr-13	148
1.5.7.6	2C30WG60061...	Area WG6, PH 3, Install Rdwy Illumination	56	01-Apr-13	18-Jun-13	93
1.5.3.6	2C30RP60046410	Area RP6, PH 3, Install Small RCP	4	09-Apr-13	15-Apr-13	100
1.5.7.6	2C30RP60061020	Area RP6, PH 3, Install Rdwy Illumination	20	09-Apr-13	07-May-13	101
1.5.2.6	2C30RP60026010	Area RP6, PH 3, Lime Treat Subgrade	30	10-Apr-13	22-May-13	67
1.5.3.6	2C30EG60046210	Area EG6, PH 3, Install Small CBC	8	11-Apr-13	23-Apr-13	72
1.5.3.6	2C30RP60046510	Area RP6, PH 3, Install MHs and Inlets	5	15-Apr-13	22-Apr-13	100
1.5.2.6	2C30WG60054...	Area WG6, PH 3, Install Attenuators	2	17-Apr-13	19-Apr-13	129
1.5.9.6	2C30WG60051...	Area WG6, PH 3, Place Temp Conc Barrier	17	18-Apr-13	13-May-13	104
1.5.2.6	2C30EG60024710	Area EG6, PH 3, Place Flexible Base	25	19-Apr-13	24-May-13	68
1.5.3.6	2C30EG60046420	Area EG6, PH 3, Install Medium RCP	3	23-Apr-13	26-Apr-13	72
1.5.2.6	2C30EG60034012	Area EG6, PH 3, Place HMA Base	38	26-Apr-13	19-Jun-13	68
1.5.8.6	2C30EG60061899	Area EG6, PH 3, Install ITS Duct Bank	4	29-Apr-13	03-May-13	96
1.5.3.6	2C30EG60046410	Area EG6, PH 3, Install Small RCP	5	29-Apr-13	06-May-13	71
1.5.8.6	2C30EG60041699	Area EG6, PH 3, Install ITS Structures & Equip	28	03-May...	12-Jun-13	96
1.5.3.6	2C30EG60046510	Area EG6, PH 3, Install MHs and Inlets	6	06-May...	14-May-13	71
1.5.2.6	2C30RP60043210	Area RP6, PH 3, Place Conc RipRap	12	07-May...	23-May-13	101
1.5.9.6	2C30WG60066...	Area WG6, PH 3, Place Temp Marking & Sig...	9	13-May...	24-May-13	104
1.5.4.6	2C30EG60042315	Area EG6, PH 3, Install Moment Slabs	2	17-May...	21-May-13	84
1.5.2.6	2C30EG60034610	Area EG6, PH 3, Place SMA Surface	40	21-May...	16-Jul-13	70
1.5.2.6	2C30RP60024710	Area RP6, PH 3, Place Flexible Base	6	22-May...	30-May-13	78
1.5.4.6	2C30RP60042315	Area RP6, PH 3, Install Moment Slabs	22	22-May...	21-Jun-13	67
1.5.7.6	2C30WG60066...	Area WG6, PH 3, Install Perm Markings	6	24-May...	03-Jun-13	104
1.5.2.6	2C30EG60053110	Area EG6, PH 3, Place Sidewalks & Driveways	24	24-May...	27-Jun-13	85
1.5.7.6	2C30EG60065010	Area EG6, PH 3, Install OH Sign Structures	36	27-May...	16-Jul-13	72
1.5.2.6	2C30RP60052910	Area RP6, PH 3, Place Curb & Gutter	5	30-May...	06-Jun-13	78
1.5.2.6	2C30EG60054010	Area EG6, PH 3, Install MBGF	30	04-Jun-13	16-Jul-13	68
1.5.2.6	2C30RP60034610	Area RP6, PH 3, Place SMA Surface	9	06-Jun-13	19-Jun-13	91
1.5.7.6	2C30EG60061020	Area EG6, PH 3, Install Rdwy Illumination	28	06-Jun-13	16-Jul-13	72
1.5	2C30WG60099...	Area WG6, PH 3, Finish	0		18-Jun-13	93
1.5.9.6	2C30EG60066200	Area EG6, PH 3, Place Temp Marking & Sig...	5	19-Jun-13	26-Jun-13	87
1.5.2.6	2C30EG60045010	Area EG6, PH 3, Place Conc Rail (Ret Wall)	14	19-Jun-13	09-Jul-13	68
1.5.7.6	2C30RP60065010	Area RP6, PH 3, Install OH Sign Structures	24	20-Jun-13	24-Jul-13	67
1.5.10.6	2C30RP60041698	Area RP6, PH 3, Install Tolling Systems	2	21-Jun-13	25-Jun-13	88
1.5.2.6	2C30RP60034012	Area RP6, PH 3, Place HMA Base	8	21-Jun-13	03-Jul-13	67
1.5.9.6	2C30RP60050820	Area RP6, PH 3, Const Temp Detour	8	03-Jul-13	15-Jul-13	71
1.5.2.6	2C30RP60045010	Area RP6, PH 3, Place Conc Rail (Ret Wall)	10	03-Jul-13	17-Jul-13	67
1.5.9.6	2C30RP60051200	Area RP6, PH 3, Place Temp Conc Barrier	3	15-Jul-13	18-Jul-13	71
1.5.7.6	2C30EG60064410	Area EG6, PH 3, Install Small Signs	1	16-Jul-13	17-Jul-13	72
1.5.2.6	2C30EG60054510	Area EG6, PH 3, Install Attenuators	2	16-Jul-13	18-Jul-13	68
1.5.7.6	2C30RP60066610	Area RP6, PH 3, Install Perm Markings	1	17-Jul-13	18-Jul-13	71
1.5.7.6	2C30EG60066610	Area EG6, PH 3, Install Perm Markings	3	18-Jul-13	23-Jul-13	68
1.5	2C30EG60099999	Area EG6, PH 3, Finish	0		23-Jul-13	68
1.5	2C30RP60099999	Area RP6, PH 3, Finish	0		24-Jul-13	67
1.5.4.6.1.109	2C30B109000001	BR 109, PH 3, Start	0	02-Jan-13		131
1.5.4.6.1.109	2C30B109041600	BR 109, PH 3, Install Drill Shafts	7	02-Jan-13	11-Jan-13	131
1.5.4.6.1.109	2C30B109042040	BR 109, PH 3, Install Abutments	1	11-Jan-13	14-Jan-13	166
1.5.4.6.1.109	2C30B109042010	BR 109, PH 3, Install Footings	12	11-Jan-13	29-Jan-13	131
1.5.4.6.1.109	2C30B109042020	BR 109, PH 3, Install Columns	14	29-Jan-13	18-Feb-13	131
1.5.4.6.1.109	2C30B109042030	BR 109, PH 3, Install Bent Caps	10	18-Feb-13	04-Mar-13	131
1.5.4.6.1.109	2C30B109042510	BR 109, PH 3, Install Conc Beams	3	04-Mar-13	07-Mar-13	132
1.5.4.6.1.109	2C30B109044210	BR 109, PH 3, Install Plate Girders	4	04-Mar-13	08-Mar-13	131
1.5.4.6.1.109	2C30B109045410	BR 109, PH 3, Install Exp Joints	1	08-Mar-13	11-Mar-13	131
1.5.4.6.1.109	2C30B109042210	BR 109, PH 3, Install Deck Slab	19	11-Mar-13	05-Apr-13	131
1.5.4.6.1.109	2C30B109042050	BR 109, PH 3, Install Apprch Slabs	2	05-Apr-13	09-Apr-13	139
1.5.4.6.1.109	2C30B109045020	BR 109, PH 3, Install Conc Rail	4	19-Apr-13	25-Apr-13	131
1.5.4.6.1.109	2C30B109099999	BR 109, PH 3, Finish	0		25-Apr-13	131
1.5.4.6.1.111	2C30B111000001	BR 111, PH 3, Start	0	04-Oct-12		203
1.5.4.6.1.111	2C30B111041600	BR 111, PH 3, Install Drill Shafts	8	04-Oct-12	16-Oct-12	203
1.5.4.6.1.111	2C30B111042020	BR 111, PH 3, Install Columns	3	16-Oct-12	19-Oct-12	205
1.5.4.6.1.111	2C30B111042040	BR 111, PH 3, Install Abutments	9	16-Oct-12	29-Oct-12	203
1.5.4.6.1.111	2C30B111042030	BR 111, PH 3, Install Bent Caps	4	19-Oct-12	25-Oct-12	205
1.5.4.6.1.111	2C30B111042510	BR 111, PH 3, Install Conc Beams	4	29-Oct-12	02-Nov-12	203
1.5.4.6.1.111	2C30B111045410	BR 111, PH 3, Install Exp Joints	2	02-Nov-...	06-Nov-12	203
1.5.4.6.1.111	2C30B111042210	BR 111, PH 3, Install Deck Slab	25	06-Nov-...	11-Dec-12	203
1.5.4.6.1.111	2C30B111042050	BR 111, PH 3, Install Apprch Slabs	23	11-Dec-...	11-Jan-13	203
1.5.4.6.1.111	2C30B111045020	BR 111, PH 3, Install Conc Rail	2	11-Jan-13	15-Jan-13	203
1.5.4.6.1.111	2C30B111099999	BR 111, PH 3, Finish	0		15-Jan-13	203
1.5.4.6.1.113	2C30B113000001	BR 113, PH 3, Start	0	02-Jan-13		129
1.5.4.6.1.113	2C30B113049610	BR 113, PH 3, Demo Extg Bridge	25	02-Jan-13	06-Feb-13	129
1.5.4.6.1.113	2C30B113041600	BR 113, PH 3, Install Drill Shafts	6	06-Feb-13	14-Feb-13	129
1.5.4.6.1.113	2C30B113042020	BR 113, PH 3, Install Columns	2	14-Feb-13	18-Feb-13	132
1.5.4.6.1.113	2C30B113042040	BR 113, PH 3, Install Abutments	8	14-Feb-13	26-Feb-13	129
1.5.4.6.1.113	2C30B113042030	BR 113, PH 3, Install Bent Caps	3	18-Feb-13	21-Feb-13	132

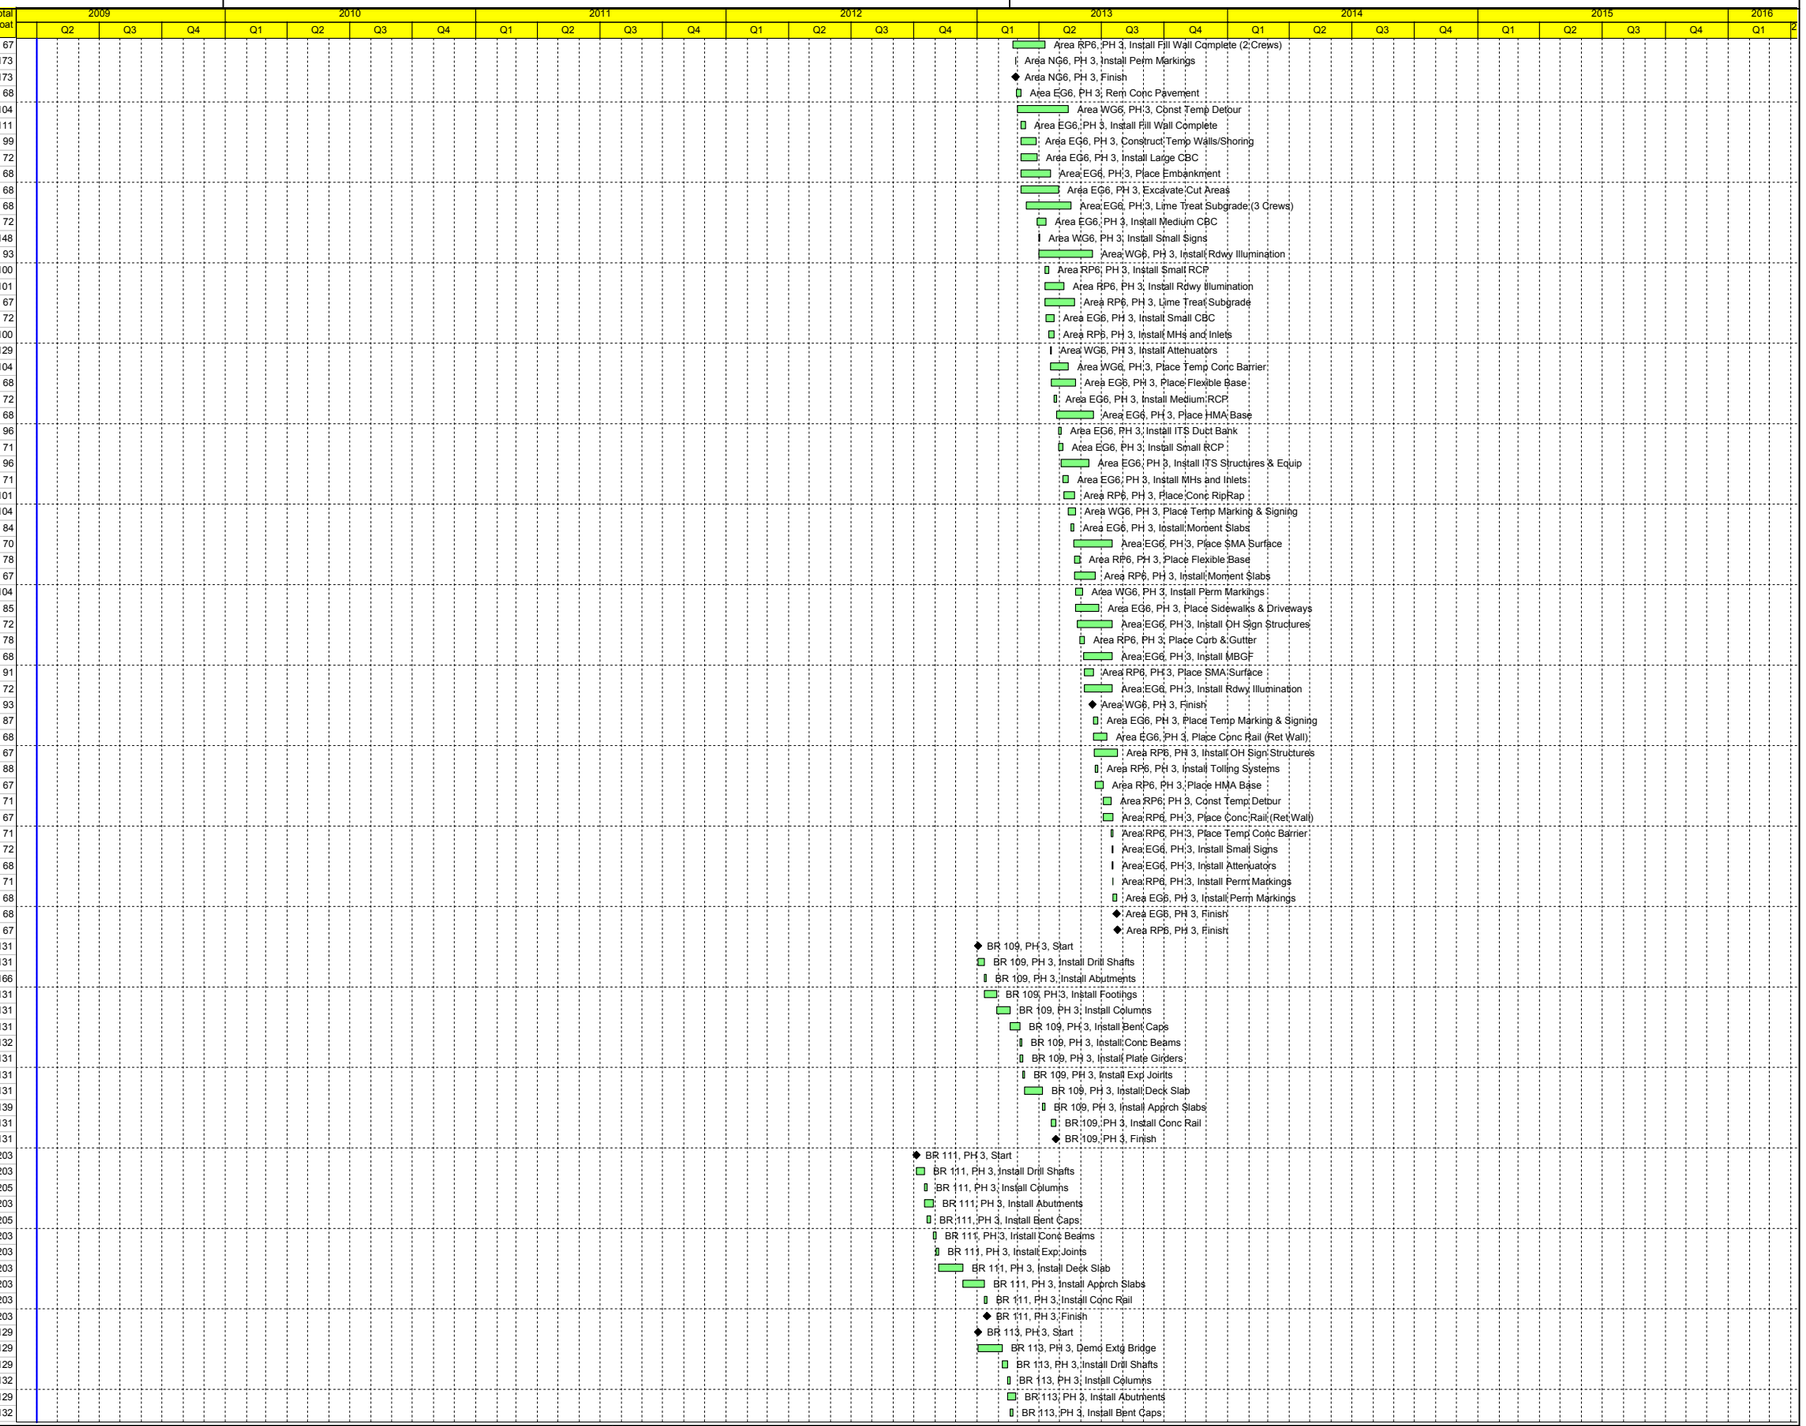

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.5.4.6.1.113	2C30B113042510	BR 113, PH 3, Install Conc Beams	2	26-Feb-13	28-Feb-13	129
1.5.4.6.1.113	2C30B113045410	BR 113, PH 3, Install Exp Joints	2	28-Feb-13	04-Mar-13	129
1.5.4.6.1.113	2C30B113042210	BR 113, PH 3, Install Deck Slab	19	04-Mar-13	29-Mar-13	129
1.5.4.6.1.113	2C30B113042050	BR 113, PH 3, Install Apprch Slabs	19	29-Mar-13	25-Apr-13	129
1.5.4.6.1.113	2C30B113045020	BR 113, PH 3, Install Conc Rail	2	25-Apr-13	29-Apr-13	129
1.5.4.6.1.113	2C30B113099999	BR 113, PH 3, Finish	0		29-Apr-13	129
1.5.4.6.1.123	2C30B123000001	BR 123, PH 3, Start	0	02-Jan-13		104
1.5.4.6.1.123	2C30B123041600	BR 123, PH 3, Install Drill Shafts	6	02-Jan-13	10-Jan-13	104
1.5.4.6.1.123	2C30B123042010	BR 123, PH 3, Install Footings	10	10-Jan-13	24-Jan-13	104
1.5.4.6.1.123	2C30B123042020	BR 123, PH 3, Install Columns	14	24-Jan-13	13-Feb-13	104
1.5.4.6.1.123	2C30B123042030	BR 123, PH 3, Install Bent Caps	10	13-Feb-13	27-Feb-13	104
1.5.4.6.1.123	2C30B123042510	BR 123, PH 3, Install Conc Beams	6	27-Feb-13	07-Mar-13	104
1.5.4.6.1.123	2C30B123045410	BR 123, PH 3, Install Exp Joints	1	07-Mar-13	08-Mar-13	104
1.5.4.6.1.123	2C30B123042210	BR 123, PH 3, Install Deck Slab	42	08-Mar-13	07-May-13	104
1.5.4.6.1.123	2C30B123045020	BR 123, PH 3, Install Conc Rail	9	21-May...	03-Jun-13	104
1.5.4.6.1.123	2C30B123099999	BR 123, PH 3, Finish	0		03-Jun-13	104
1.5.4.6.1.126	2C30B126000001	BR 126, PH 3, Start	0	04-Oct-12		206
1.5.4.6.1.126	2C30B126041600	BR 126, PH 3, Install Drill Shafts	4	04-Oct-12	10-Oct-12	206
1.5.4.6.1.126	2C30B126042020	BR 126, PH 3, Install Columns	3	10-Oct-12	15-Oct-12	207
1.5.4.6.1.126	2C30B126042040	BR 126, PH 3, Install Abutments	8	10-Oct-12	22-Oct-12	206
1.5.4.6.1.126	2C30B126042030	BR 126, PH 3, Install Bent Caps	4	15-Oct-12	19-Oct-12	207
1.5.4.6.1.126	2C30B126042510	BR 126, PH 3, Install Conc Beams	3	22-Oct-12	25-Oct-12	206
1.5.4.6.1.126	2C30B126045410	BR 126, PH 3, Install Exp Joints	3	25-Oct-12	30-Oct-12	206
1.5.4.6.1.126	2C30B126042210	BR 126, PH 3, Install Deck Slab	20	30-Oct-12	27-Nov-12	206
1.5.4.6.1.126	2C30B126042050	BR 126, PH 3, Install Apprch Slabs	30	27-Nov-...	08-Jan-13	206
1.5.4.6.1.126	2C30B126045020	BR 126, PH 3, Install Conc Rail	2	08-Jan-13	10-Jan-13	206
1.5.4.6.1.126	2C30B126099999	BR 126, PH 3, Finish	0		10-Jan-13	206
1.5.4.6.1.129	2C30B129000001	BR 129, PH 3, Start	0	04-Oct-12		202
1.5.4.6.1.129	2C30B129041600	BR 129, PH 3, Install Drill Shafts	8	04-Oct-12	16-Oct-12	202
1.5.4.6.1.129	2C30B129042020	BR 129, PH 3, Install Columns	3	16-Oct-12	19-Oct-12	204
1.5.4.6.1.129	2C30B129042040	BR 129, PH 3, Install Abutments	9	16-Oct-12	29-Oct-12	202
1.5.4.6.1.129	2C30B129042030	BR 129, PH 3, Install Bent Caps	4	19-Oct-12	25-Oct-12	204
1.5.4.6.1.129	2C30B129042510	BR 129, PH 3, Install Conc Beams	4	29-Oct-12	02-Nov-12	202
1.5.4.6.1.129	2C30B129045410	BR 129, PH 3, Install Exp Joints	2	02-Nov-...	06-Nov-12	202
1.5.4.6.1.129	2C30B129042210	BR 129, PH 3, Install Deck Slab	26	06-Nov-...	12-Dec-12	202
1.5.4.6.1.129	2C30B129042050	BR 129, PH 3, Install Apprch Slabs	23	12-Dec-...	14-Jan-13	202
1.5.4.6.1.129	2C30B129045020	BR 129, PH 3, Install Conc Rail	2	14-Jan-13	16-Jan-13	202
1.5.4.6.1.129	2C30B129099999	BR 129, PH 3, Finish	0		16-Jan-13	202
1.5.4.6.1.132	2C30B132000001	BR 132, PH 3, Start	0	04-Oct-12		206
1.5.4.6.1.132	2C30B132041600	BR 132, PH 3, Install Drill Shafts	7	04-Oct-12	15-Oct-12	206
1.5.4.6.1.132	2C30B132042020	BR 132, PH 3, Install Columns	3	15-Oct-12	18-Oct-12	208
1.5.4.6.1.132	2C30B132042040	BR 132, PH 3, Install Abutments	9	15-Oct-12	26-Oct-12	206
1.5.4.6.1.132	2C30B132042030	BR 132, PH 3, Install Bent Caps	4	18-Oct-12	24-Oct-12	208
1.5.4.6.1.132	2C30B132042510	BR 132, PH 3, Install Conc Beams	3	26-Oct-12	31-Oct-12	206
1.5.4.6.1.132	2C30B132045410	BR 132, PH 3, Install Exp Joints	2	31-Oct-12	02-Nov-12	206
1.5.4.6.1.132	2C30B132042210	BR 132, PH 3, Install Deck Slab	24	02-Nov-...	06-Dec-12	206
1.5.4.6.1.132	2C30B132042050	BR 132, PH 3, Install Apprch Slabs	23	06-Dec-...	08-Jan-13	206
1.5.4.6.1.132	2C30B132045020	BR 132, PH 3, Install Conc Rail	2	08-Jan-13	10-Jan-13	206
1.5.4.6.1.132	2C30B132099999	BR 132, PH 3, Finish	0		10-Jan-13	206
1.5.4.6.1.136	2C30B136000001	BR 136, PH 3, Start	0	02-Jan-13		152
1.5.4.6.1.136	2C30B136041600	BR 136, PH 3, Install Drill Shafts	2	02-Jan-13	04-Jan-13	152
1.5.4.6.1.136	2C30B136042040	BR 136, PH 3, Install Abutments	5	04-Jan-13	11-Jan-13	169
1.5.4.6.1.136	2C30B136042010	BR 136, PH 3, Install Footings	7	04-Jan-13	15-Jan-13	152
1.5.4.6.1.136	2C30B136042020	BR 136, PH 3, Install Columns	5	15-Jan-13	22-Jan-13	152
1.5.4.6.1.136	2C30B136042030	BR 136, PH 3, Install Bent Caps	10	22-Jan-13	05-Feb-13	152
1.5.4.6.1.136	2C30B136042510	BR 136, PH 3, Install Conc Beams	3	05-Feb-13	08-Feb-13	152
1.5.4.6.1.136	2C30B136045410	BR 136, PH 3, Install Exp Joints	2	08-Feb-13	12-Feb-13	152
1.5.4.6.1.136	2C30B136042210	BR 136, PH 3, Install Deck Slab	16	12-Feb-13	06-Mar-13	152
1.5.4.6.1.136	2C30B136042050	BR 136, PH 3, Install Apprch Slabs	13	06-Mar-13	25-Mar-13	152
1.5.4.6.1.136	2C30B136045020	BR 136, PH 3, Install Conc Rail	2	25-Mar-13	27-Mar-13	152
1.5.4.6.1.136	2C30B136099999	BR 136, PH 3, Finish	0		27-Mar-13	152
1.5.4.6.1.140	2C30B140000001	BR 140, PH 3, Start	0	02-Jan-13		155
1.5.4.6.1.140	2C30B140041600	BR 140, PH 3, Install Drill Shafts	3	02-Jan-13	07-Jan-13	155
1.5.4.6.1.140	2C30B140042040	BR 140, PH 3, Install Abutments	2	07-Jan-13	09-Jan-13	184
1.5.4.6.1.140	2C30B140042010	BR 140, PH 3, Install Footings	11	07-Jan-13	22-Jan-13	155
1.5.4.6.1.140	2C30B140042020	BR 140, PH 3, Install Columns	7	22-Jan-13	31-Jan-13	155
1.5.4.6.1.140	2C30B140042030	BR 140, PH 3, Install Bent Caps	13	31-Jan-13	19-Feb-13	155
1.5.4.6.1.140	2C30B140042510	BR 140, PH 3, Install Conc Beams	2	19-Feb-13	21-Feb-13	155
1.5.4.6.1.140	2C30B140045410	BR 140, PH 3, Install Exp Joints	1	21-Feb-13	22-Feb-13	155
1.5.4.6.1.140	2C30B140042210	BR 140, PH 3, Install Deck Slab	8	22-Feb-13	06-Mar-13	155
1.5.4.6.1.140	2C30B140042050	BR 140, PH 3, Install Apprch Slabs	4	06-Mar-13	12-Mar-13	161
1.5.4.6.1.140	2C30B140045020	BR 140, PH 3, Install Conc Rail	2	20-Mar-13	22-Mar-13	155
1.5.4.6.1.140	2C30B140099999	BR 140, PH 3, Finish	0		22-Mar-13	155
1.5	2C300000000001	START PHASE 3, SUBSEGMENT 2C	0	02-Jan-13		67
1.5	2C300000099999	FINISH PHASE 3, SUBSEGMENT 2C	0		24-Jul-13	67
CONSTRUCTION PHASE 4A			606	19-Dec-...	16-Apr-15	49
1.5	2C4AEG60000001	Area EG6, PH 4A, Start	0	24-Jul-13		111
1.5	2C4ALA60000001	Area LA6, PH 4A, Start	0	24-Jul-13		259
1.5	2C4ARP60000001	Area RP6, PH 4A, Start	0	24-Jul-13		95
1.5	2C4AML60000001	Area ML6, PH 4A, Start	0	24-Jul-13		67
1.5	2C4AXC60000001	Area XC6, PH 4A, Start	0	24-Jul-13		218
1.5	2C4ASG60000001	Area SG6, PH 4A, Start	0	24-Jul-13		122
1.5	2C4AWG60000...	Area WG6, PH 4A, Start	0	24-Jul-13		131
1.5	2C4AXU60000001	Area XU6, PH 4A, Start	0	24-Jul-13		231
1.5.2.6	2C4AXU60050600	Area XU6, PH 4A, Place Temp Erosion Control	6	24-Jul-13	01-Aug-13	231
1.5.2.6	2C4ARP60010410	Area RP6, PH 4A, Rem Conc Pavement	7	24-Jul-13	02-Aug-13	95

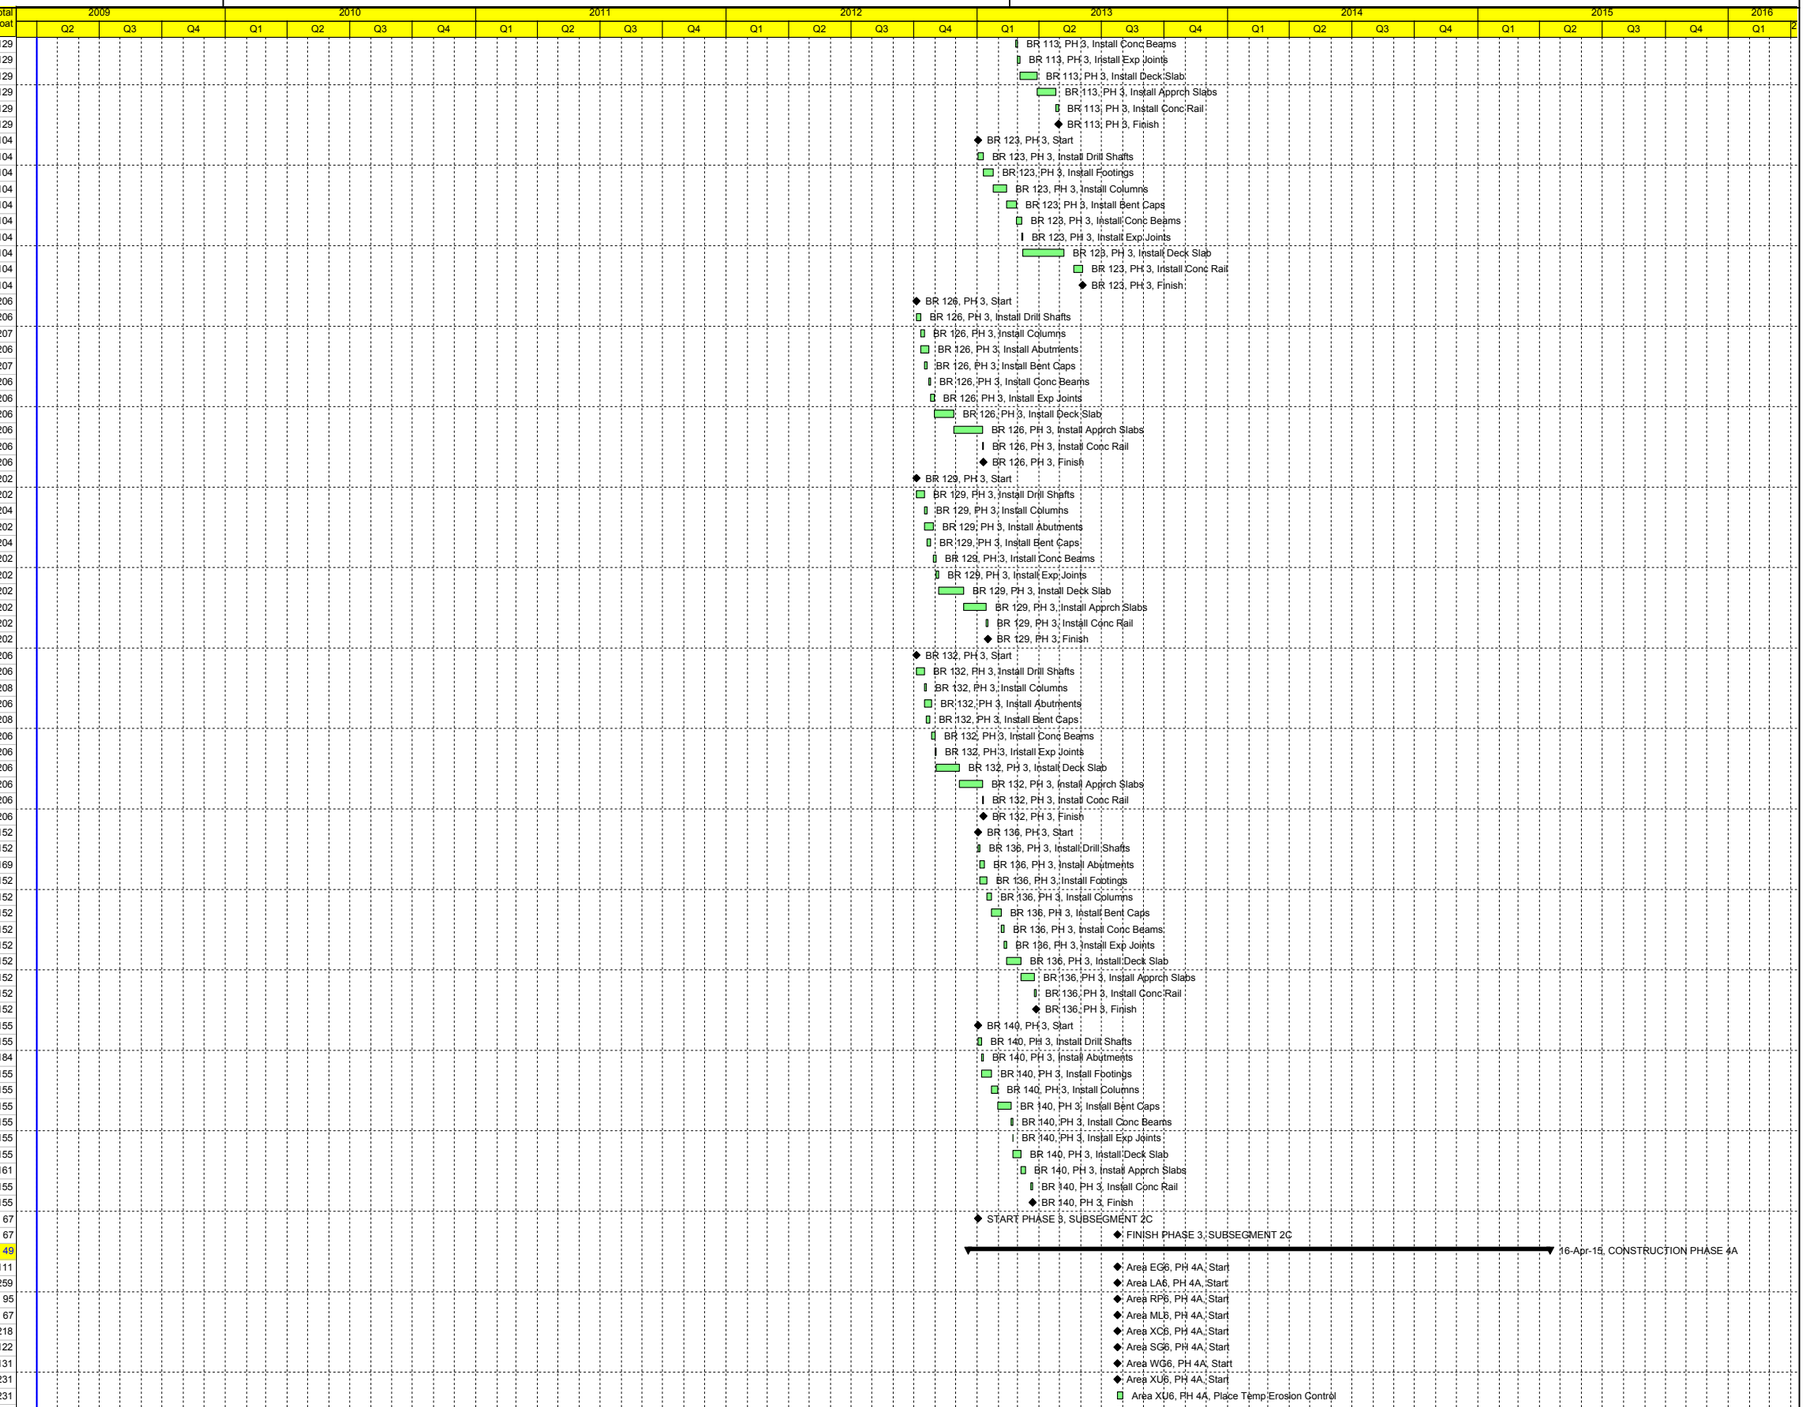

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.5.2.6	2C4AWG60050...	Area WG6, PH 4A, Place Temp Erosion Cont...	10	24-Jul-13	07-Aug-13	131
1.5.2.6	2C4AEG60050600	Area EG6, PH 4A, Place Temp Erosion Control	11	24-Jul-13	08-Aug-13	111
1.5.2.6	2C4ASG60050600	Area SG6, PH 4A, Place Temp Erosion Control	17	24-Jul-13	16-Aug-13	122
1.5.3.6	2C4AML60046220	Area ML6, PH 4A, Install Medium CBC	21	24-Jul-13	22-Aug-13	71
1.5.4.6	2C4AML60042310	Area ML6, PH 4A, Install Fill Wall Complete	27	24-Jul-13	30-Aug-13	116
1.5.2.6	2C4ALA60016010	Area LA6, PH 4A, Place Topsoil	31	24-Jul-13	05-Sep-13	259
1.5.8.6	2C4AXC60061899	Area XC6, PH 4A, Install ITS Duct Bank	41	24-Jul-13	19-Sep-13	218
1.5.2.6	2C4AML60013210	Area ML6, PH 4A, Place Embankment (2 Cre...	46	24-Jul-13	26-Sep-13	80
1.5.2.6	2C4AML60011010	Area ML6, PH 4A, Excavate Cut Areas (2 Cr...	59	24-Jul-13	15-Oct-13	67
1.5.2.6	2C4AML60026010	Area ML6, PH 4A, Lime Treat Subgrade (3 C...	77	31-Jul-13	15-Nov-13	71
1.5.2.6	2C4AXU60010410	Area XU6, PH 4A, Rem Conc Pavement	2	01-Aug-...	05-Aug-13	231
1.5.3.6	2C4ARP60046220	Area RP6, PH 4A, Install Medium CBC	3	02-Aug-...	07-Aug-13	122
1.5.2.6	2C4ARP60013210	Area RP6, PH 4A, Place Embankment (2 Cre...	21	02-Aug-...	02-Sep-13	95
1.5.2.6	2C4ARP60011010	Area RP6, PH 4A, Excavate Cut Areas (2 Cr...	30	02-Aug-...	13-Sep-13	95
1.5.3.6	2C4AXU60046420	Area XU6, PH 4A, Install Medium RCP	3	05-Aug-...	08-Aug-13	235
1.5.8.6	2C4AXU60062899	Area XU6, PH 4A, Install Elec Service for ITS...	7	05-Aug-...	14-Aug-13	271
1.5.2.6	2C4AXU60026010	Area XU6, PH 4A, Lime Treat Subgrade	16	05-Aug-...	27-Aug-13	231
1.5.2.6	2C4AWG60060...	Area WG6, PH 4A, Rem Light Poles	1	07-Aug-...	08-Aug-13	134
1.5.3.6	2C4ARP60046210	Area RP6, PH 4A, Install Small CBC	2	07-Aug-...	09-Aug-13	122
1.5.2.6	2C4AWG60054...	Area WG6, PH 4A, Rem MBGF	2	07-Aug-...	09-Aug-13	133
1.5.2.6	2C4AWG60063...	Area WG6, PH 4A, Rem Overhead Sign Sup...	4	07-Aug-...	13-Aug-13	131
1.5.2.6	2C4AEG60060010	Area EG6, PH 4A, Rem Light Poles	1	08-Aug-...	09-Aug-13	115
1.5.2.6	2C4AEG60054210	Area EG6, PH 4A, Rem MBGF	2	08-Aug-...	12-Aug-13	114
1.5.8.6	2C4AXU60061899	Area XU6, PH 4A, Install ITS Duct Bank	2	08-Aug-...	12-Aug-13	273
1.5.2.6	2C4AEG60063010	Area EG6, PH 4A, Rem Overhead Sign Supp...	5	08-Aug-...	15-Aug-13	111
1.5.3.6	2C4AXU60046410	Area XU6, PH 4A, Install Small RCP	5	08-Aug-...	15-Aug-13	235
1.5.3.6	2C4ARP60046420	Area RP6, PH 4A, Install Medium RCP	5	09-Aug-...	16-Aug-13	122
1.5.2.6	2C4ARP60026010	Area RP6, PH 4A, Lime Treat Subgrade	48	09-Aug-...	16-Oct-13	95
1.5.2.6	2C4AWG60010...	Area WG6, PH 4A, Rem Concrete Barrier	3	13-Aug-...	16-Aug-13	131
1.5.2.6	2C4AEG60010430	Area EG6, PH 4A, Rem Concrete Barrier	4	15-Aug-...	21-Aug-13	111
1.5.3.6	2C4AXU60046510	Area XU6, PH 4A, Install MHs and Inlets	4	15-Aug-...	21-Aug-13	235
1.5.2.6	2C4ASG60054210	Area SG6, PH 4A, Rem MBGF	2	16-Aug-...	20-Aug-13	125
1.5.2.6	2C4ASG60060010	Area SG6, PH 4A, Rem Light Poles	2	16-Aug-...	20-Aug-13	125
1.5.2.6	2C4AWG60010...	Area WG6, PH 4A, Rem Conc Pavement	3	16-Aug-...	21-Aug-13	131
1.5.2.6	2C4ASG60063010	Area SG6, PH 4A, Rem Overhead Sign Supp...	5	16-Aug-...	23-Aug-13	122
1.5.2.6	2C4AEG60010410	Area EG6, PH 4A, Rem Conc Pavement	3	21-Aug-...	26-Aug-13	111
1.5.3.6	2C4AWG60046...	Area WG6, PH 4A, Install Large CBC	8	21-Aug-...	02-Sep-13	188
1.5.2.6	2C4AWG60013...	Area WG6, PH 4A, Place Embankment	14	21-Aug-...	10-Sep-13	136
1.5.9.6	2C4AWG60040...	Area WG6, PH 4A, Construct Temp Walls/Sh...	17	21-Aug-...	13-Sep-13	133
1.5.2.6	2C4AWG60011...	Area WG6, PH 4A, Excavate Cut Areas	19	21-Aug-...	17-Sep-13	131
1.5.3.6	2C4AML60046210	Area ML6, PH 4A, Install Small CBC	11	22-Aug-...	06-Sep-13	71
1.5.2.6	2C4ASG60010430	Area SG6, PH 4A, Rem Concrete Barrier	5	23-Aug-...	30-Aug-13	122
1.5.3.6	2C4AEG60046230	Area EG6, PH 4A, Install Large CBC	8	26-Aug-...	05-Sep-13	175
1.5.2.6	2C4AEG60013210	Area EG6, PH 4A, Place Embankment	15	26-Aug-...	16-Sep-13	117
1.5.2.6	2C4AEG60011010	Area EG6, PH 4A, Excavate Cut Areas	21	26-Aug-...	24-Sep-13	111
1.5.2.6	2C4AXU60024710	Area XU6, PH 4A, Place Flexible Base	6	27-Aug-...	04-Sep-13	231
1.5.2.6	2C4ASG60010410	Area SG6, PH 4A, Rem Conc Pavement	4	30-Aug-...	05-Sep-13	122
1.5.3.6	2C4AWG60046...	Area WG6, PH 4A, Install Medium CBC	4	02-Sep-...	06-Sep-13	188
1.5.2.6	2C4AXU60052910	Area XU6, PH 4A, Place Curb & Gutter	2	04-Sep-...	06-Sep-13	231
1.5.3.6	2C4AEG60046220	Area EG6, PH 4A, Install Medium CBC	5	05-Sep-...	12-Sep-13	175
1.5.6.6	2C4ALA60016410	Area LA6, PH 4A, Place Seeding and Sodding	13	05-Sep-...	24-Sep-13	259
1.5.3.6	2C4ASG60046230	Area SG6, PH 4A, Install Large CBC	13	05-Sep-...	24-Sep-13	158
1.5.2.6	2C4ASG60013210	Area SG6, PH 4A, Place Embankment	23	05-Sep-...	08-Oct-13	132
1.5.2.6	2C4ASG60011010	Area SG6, PH 4A, Excavate Cut Areas	33	05-Sep-...	22-Oct-13	122
1.5.3.6	2C4AWG60046...	Area WG6, PH 4A, Install Small CBC	4	06-Sep-...	12-Sep-13	188
1.5.2.6	2C4AXU60034011	Area XU6, PH 4A, Place HMA Base	9	06-Sep-...	19-Sep-13	231
1.5.3.6	2C4AWG60046...	Area WG6, PH 4A, Install Medium RCP	1	12-Sep-...	13-Sep-13	188
1.5.3.6	2C4AEG60046210	Area EG6, PH 4A, Install Small CBC	4	12-Sep-...	18-Sep-13	175
1.5.3.6	2C4AML60046510	Area ML6, PH 4A, Install MHs and Inlets (2 C...	30	12-Sep-...	24-Oct-13	67
1.5.3.6	2C4AML60046410	Area ML6, PH 4A, Install Small RCP (2 Crews)	33	12-Sep-...	29-Oct-13	67
1.5.3.6	2C4ARP60046410	Area RP6, PH 4A, Install Small RCP	6	13-Sep-...	23-Sep-13	102
1.5.8.6	2C4AWG60061...	Area WG6, PH 4A, Install ITS Duct Bank	2	17-Sep-...	19-Sep-13	220
1.5.3.6	2C4AWG60046...	Area WG6, PH 4A, Install Small RCP	2	17-Sep-...	19-Sep-13	186
1.5.2.6	2C4AWG60026...	Area WG6, PH 4A, Lime Treat Subgrade	60	17-Sep-...	10-Dec-13	131
1.5.3.6	2C4AEG60046420	Area EG6, PH 4A, Install Medium RCP	2	18-Sep-...	20-Sep-13	175
1.5.9.6	2C4AXU60066200	Area XU6, PH 4A, Place Temp Marking & Si...	1	19-Sep-...	20-Sep-13	261
1.5.3.6	2C4AWG60046...	Area WG6, PH 4A, Install MHs and Inlets	3	19-Sep-...	24-Sep-13	186
1.5.7.6	2C4AXU60061020	Area XU6, PH 4A, Install Rdwy Illumination	7	19-Sep-...	30-Sep-13	245
1.5.8.6	2C4AWG60041...	Area WG6, PH 4A, Install ITS Structures & E...	11	19-Sep-...	04-Oct-13	220
1.5.2.6	2C4AXC60016010	Area XC6, PH 4A, Place Topsoil	31	19-Sep-...	01-Nov-13	218
1.5.7.6	2C4AXU60068010	Area XU6, PH 4A, Install Traffic Signal Syste...	31	19-Sep-...	01-Nov-13	231
1.5.2.6	2C4AML60024710	Area ML6, PH 4A, Place Flexible Base	50	19-Sep-...	28-Nov-13	67
1.5.3.6	2C4ARP60046510	Area RP6, PH 4A, Install MHs and Inlets	10	23-Sep-...	07-Oct-13	102
1.5	2C4ALA60099999	Area LA6, PH 4A, Finish	0		24-Sep-13	259
1.5.3.6	2C4AEG60046410	Area EG6, PH 4A, Install Small RCP	2	24-Sep-...	26-Sep-13	173
1.5.8.6	2C4AEG60061899	Area EG6, PH 4A, Install ITS Duct Bank	3	24-Sep-...	27-Sep-13	201
1.5.3.6	2C4ASG60046220	Area SG6, PH 4A, Install Medium CBC	7	24-Sep-...	03-Oct-13	158
1.5.2.6	2C4AEG60026010	Area EG6, PH 4A, Lime Treat Subgrade	67	24-Sep-...	26-Dec-13	111
1.5.3.6	2C4AEG60046510	Area EG6, PH 4A, Install MHs and Inlets	3	26-Sep-...	01-Oct-13	173
1.5.2.6	2C4AML60034010	Area ML6, PH 4A, Place HMA Base	66	26-Sep-...	27-Dec-13	67
1.5.7.6	2C4AML60065010	Area ML6, PH 4A, Install OH Sign Structures	102	26-Sep-...	17-Feb-14	70
1.5.8.6	2C4AEG60041699	Area EG6, PH 4A, Install ITS Structures & Eq...	21	27-Sep-...	28-Oct-13	201
1.5.2.6	2C4AXU60034610	Area XU6, PH 4A, Place SMA Surface	9	30-Sep-...	11-Oct-13	245
1.5.3.6	2C4ASG60046210	Area SG6, PH 4A, Install Small CBC	6	03-Oct-13	11-Oct-13	158
1.5.2.6	2C4ARP60024710	Area RP6, PH 4A, Place Flexible Base	10	09-Oct-13	23-Oct-13	95
1.5.2.6	2C4AML60051410	Area ML6, PH 4A, Place Median Barrier	145	10-Oct-13	01-May-14	78

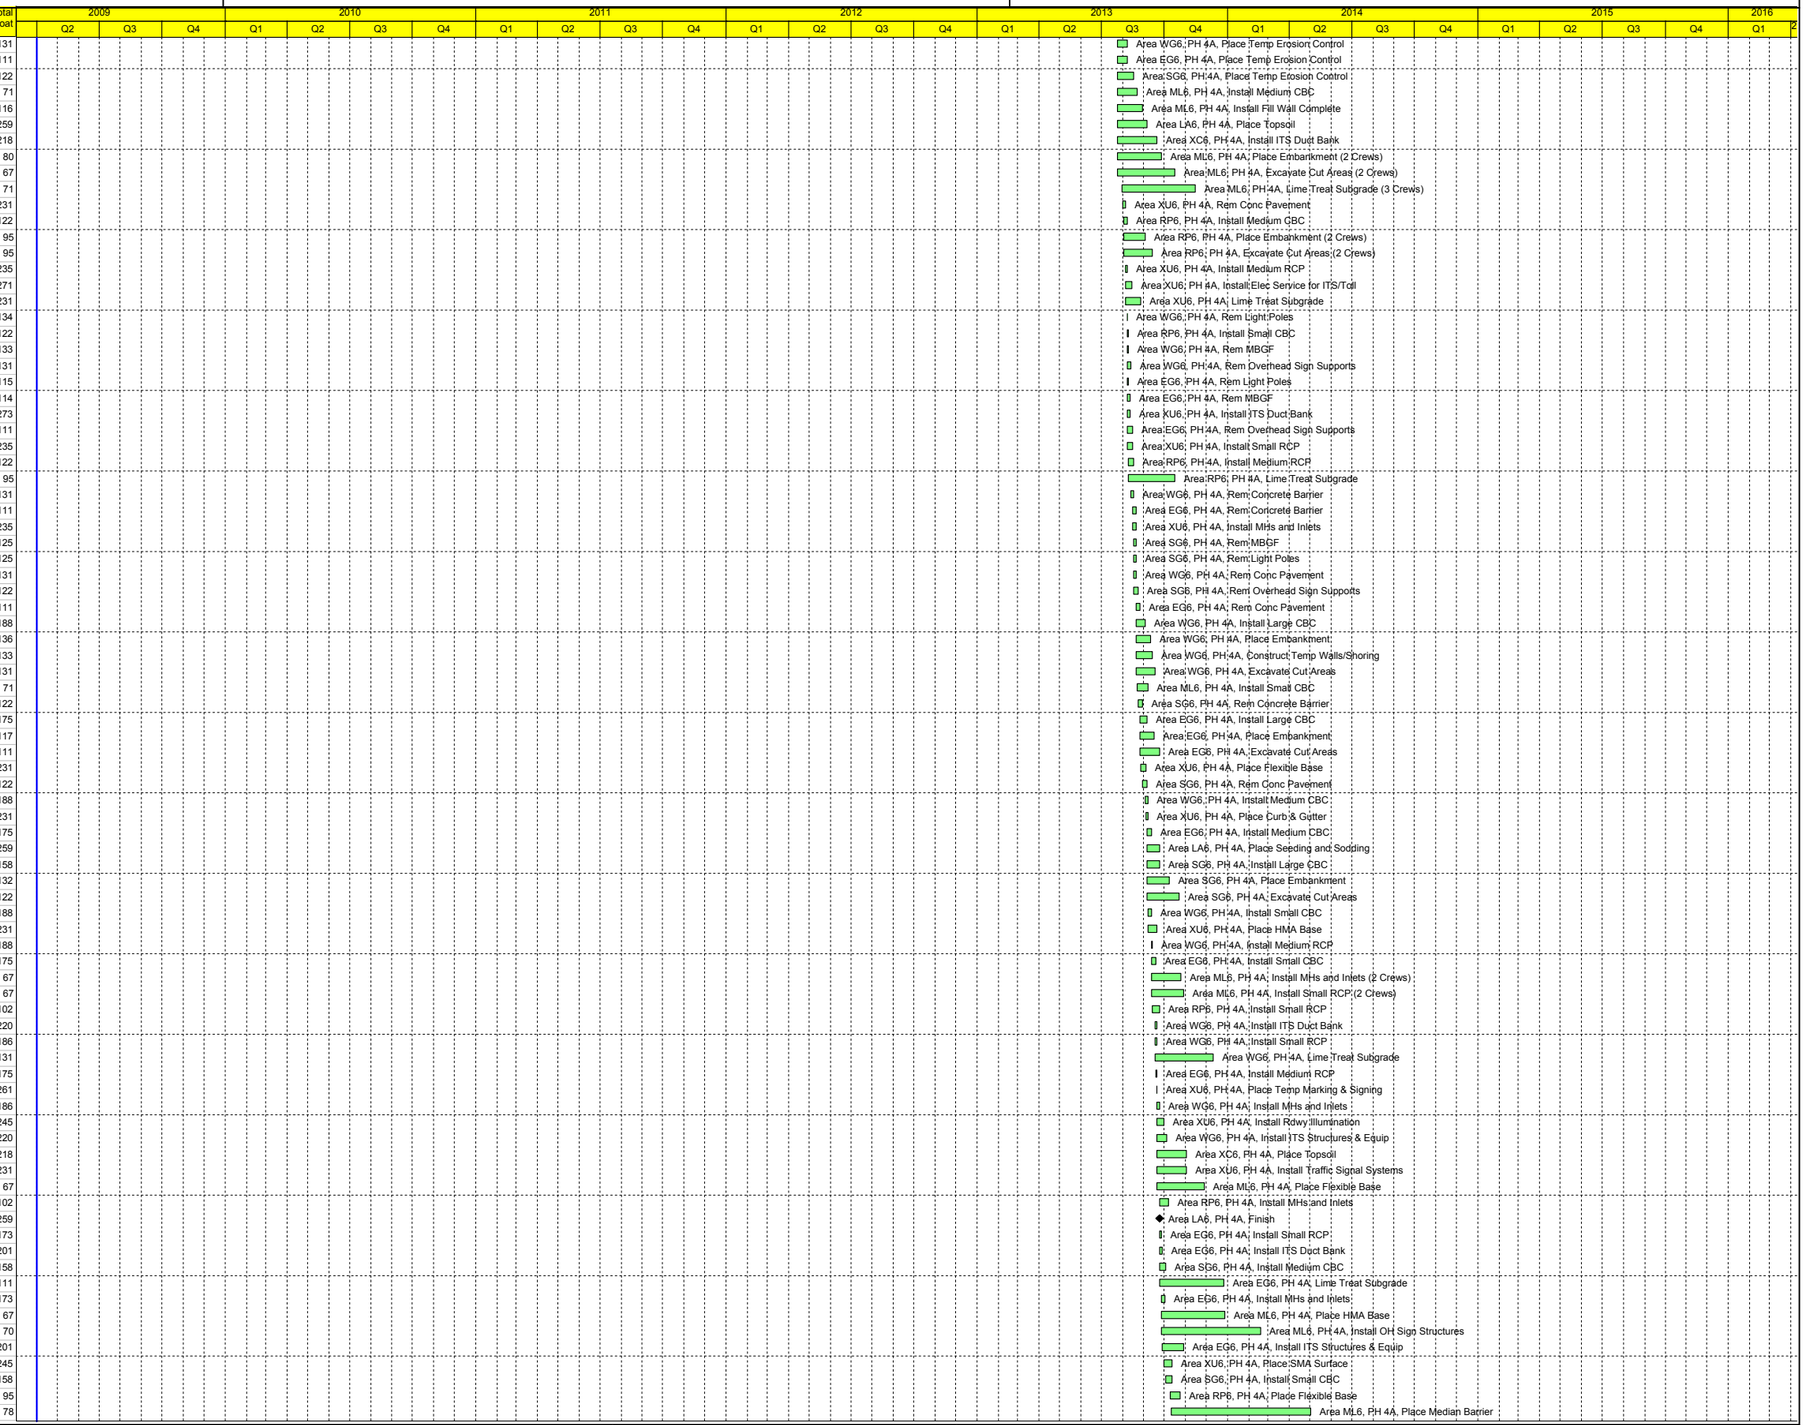

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.5.7.6	2C4AXU60066610	Area XU6, PH 4A, Install Perm Markings	1	11-Oct-13	14-Oct-13	245
1.5.3.6	2C4ASG60046420	Area SG6, PH 4A, Install Medium RCP	2	11-Oct-13	15-Oct-13	158
1.5.8.6	2C4AML60061899	Area ML6, PH 4A, Install ITS Duct Bank	9	15-Oct-13	28-Oct-13	184
1.5.8.6	2C4ASG60061899	Area SG6, PH 4A, Install ITS Duct Bank	1	22-Oct-13	23-Oct-13	215
1.5.3.6	2C4ASG60046410	Area SG6, PH 4A, Install Small RCP	3	22-Oct-13	25-Oct-13	153
1.5.7.6	2C4ASG60061320	Area SG6, PH 4A, Install High Mast Illuminati...	8	22-Oct-13	01-Nov-13	230
1.5.2.6	2C4ASG60026010	Area SG6, PH 4A, Lime Treat Subgrade (2 C...	38	22-Oct-13	13-Dec-13	122
1.5.8.6	2C4ASG60041699	Area SG6, PH 4A, Install ITS Structures & Eq...	2	23-Oct-13	25-Oct-13	215
1.5.2.6	2C4ARP60052910	Area RP6, PH 4A, Place Curb & Gutter	9	23-Oct-13	05-Nov-13	95
1.5.3.6	2C4ASG60046510	Area SG6, PH 4A, Install MHs and Inlets	4	25-Oct-13	31-Oct-13	153
1.5.8.6	2C4AML60041699	Area ML6, PH 4A, Install ITS Structures & Eq...	51	28-Oct-13	07-Jan-14	184
1.5	2C4AXU60099999	Area XU6, PH 4A, Finish	0		01-Nov-13	231
1.5.6.6	2C4AXC60016410	Area XC6, PH 4A, Place Seeding and Sodding	13	01-Nov-...	20-Nov-13	218
1.5.10.6	2C4ARP60041698	Area RP6, PH 4A, Install Tolling Systems	9	05-Nov-...	18-Nov-13	220
1.5.2.6	2C4ARP60034012	Area RP6, PH 4A, Place HMA Base	15	05-Nov-...	26-Nov-13	95
1.5.4.6	2C4AML60042315	Area ML6, PH 4A, Install Moment Slabs	13	15-Nov-...	04-Dec-13	79
1.5	2C4AXC60099999	Area XC6, PH 4A, Finish	0		20-Nov-13	218
1.5.2.6	2C4ASG60024710	Area SG6, PH 4A, Place Flexible Base	19	25-Nov-...	20-Dec-13	122
1.5.2.6	2C4ARP60045010	Area RP6, PH 4A, Place Conc Rail (Ret Wall)	18	26-Nov-...	20-Dec-13	194
1.5.7.6	2C4ARP60065010	Area RP6, PH 4A, Install OH Sign Structures	44	26-Nov-...	27-Jan-14	95
1.5.2.6	2C4AWG60024...	Area WG6, PH 4A, Place Flexible Base	11	10-Dec-...	25-Dec-13	131
1.5.2.6	2C4ASG60053110	Area SG6, PH 4A, Place Sidewalks & Drivew...	18	20-Dec-...	15-Jan-14	177
1.5.2.6	2C4ASG60034012	Area SG6, PH 4A, Place HMA Base	28	20-Dec-...	29-Jan-14	122
1.5.2.6	2C4AWG60053...	Area WG6, PH 4A, Place Sidewalks & Drive...	10	25-Dec-...	08-Jan-14	164
1.5.2.6	2C4AWG60034...	Area WG6, PH 4A, Place HMA Base	16	25-Dec-...	16-Jan-14	131
1.5.2.6	2C4ASG60034610	Area SG6, PH 4A, Place SMA Surface	30	25-Dec-...	05-Feb-14	160
1.5.2.6	2C4AEG60024710	Area EG6, PH 4A, Place Flexible Base	12	26-Dec-...	13-Jan-14	111
1.5.2.6	2C4AML60045010	Area ML6, PH 4A, Place Conc Rail (Ret Wall)	39	27-Dec-...	20-Feb-14	67
1.5.10.6	2C4AML60041698	Area ML6, PH 4A, Install Tolling Systems	41	27-Dec-...	24-Feb-14	150
1.5.2.6	2C4AEG60053110	Area EG6, PH 4A, Place Sidewalks & Drivew...	12	13-Jan-14	29-Jan-14	147
1.5.2.6	2C4AEG60034012	Area EG6, PH 4A, Place HMA Base	18	13-Jan-14	06-Feb-14	111
1.5.9.6	2C4AWG60050...	Area WG6, PH 4A, Const Temp Detour	5	16-Jan-14	23-Jan-14	159
1.5.2.6	2C4AWG60045...	Area WG6, PH 4A, Place Conc Rail (Ret Wall)	6	16-Jan-14	24-Jan-14	155
1.5.7.6	2C4AWG60065...	Area WG6, PH 4A, Install OH Sign Structures	15	16-Jan-14	06-Feb-14	131
1.5.7.6	2C4AML60061020	Area ML6, PH 4A, Install Rdwy Illumination	81	22-Jan-14	15-May-14	78
1.5.9.6	2C4AWG60051...	Area WG6, PH 4A, Place Temp Conc Barrier	11	23-Jan-14	07-Feb-14	159
1.5.2.6	2C4AWG60054...	Area WG6, PH 4A, Install MBGF	13	24-Jan-14	12-Feb-14	155
1.5.7.6	2C4ARP60061020	Area RP6, PH 4A, Install Rdwy Illumination	36	27-Jan-14	18-Mar-14	95
1.5.9.6	2C4ASG60066200	Area SG6, PH 4A, Place Temp Marking & Si...	4	29-Jan-14	04-Feb-14	164
1.5.2.6	2C4ASG60045010	Area SG6, PH 4A, Place Conc Rail (Ret Wall)	10	29-Jan-14	12-Feb-14	131
1.5.7.6	2C4ASG60065010	Area SG6, PH 4A, Install OH Sign Structures	25	29-Jan-14	05-Mar-14	122
1.5.9.6	2C4AEG60066200	Area EG6, PH 4A, Place Temp Marking & Si...	2	06-Feb-14	10-Feb-14	160
1.5.2.6	2C4AEG60045010	Area EG6, PH 4A, Place Conc Rail (Ret Wall)	7	06-Feb-14	17-Feb-14	138
1.5.7.6	2C4AWG60061...	Area WG6, PH 4A, Install Rdwy Illumination	12	06-Feb-14	24-Feb-14	131
1.5.7.6	2C4AEG60065010	Area EG6, PH 4A, Install OH Sign Structures	17	06-Feb-14	03-Mar-14	111
1.5.9.6	2C4AWG60066...	Area WG6, PH 4A, Place Temp Marking & Si...	2	07-Feb-14	11-Feb-14	159
1.5.2.6	2C4AWG60054...	Area WG6, PH 4A, Install Attenuators	1	12-Feb-14	13-Feb-14	155
1.5.2.6	2C4ASG60054010	Area SG6, PH 4A, Install MBGF	22	12-Feb-14	14-Mar-14	131
1.5.2.6	2C4AEG60054010	Area EG6, PH 4A, Install MBGF	14	17-Feb-14	07-Mar-14	138
1.5.2.6	2C4AML60034610	Area ML6, PH 4A, Place SMA Surface	79	20-Feb-14	11-Jun-14	67
1.5.7.6	2C4AWG60064...	Area WG6, PH 4A, Install Small Signs	1	24-Feb-14	25-Feb-14	149
1.5.2.6	2C4AWG60034...	Area WG6, PH 4A, Place SMA Surface	17	24-Feb-14	19-Mar-14	131
1.5.7.6	2C4AEG60061020	Area EG6, PH 4A, Install Rdwy Illumination	13	03-Mar-14	20-Mar-14	111
1.5.7.6	2C4ASG60061020	Area SG6, PH 4A, Install Rdwy Illumination	20	05-Mar-14	02-Apr-14	122
1.5.2.6	2C4AEG60054510	Area EG6, PH 4A, Install Attenuators	1	07-Mar-14	10-Mar-14	138
1.5.2.6	2C4ASG60054510	Area SG6, PH 4A, Install Attenuators	2	14-Mar-14	18-Mar-14	131
1.5.7.6	2C4ASG60066610	Area SG6, PH 4A, Install Perm Markings	3	18-Mar-14	21-Mar-14	131
1.5.2.6	2C4ARP60043210	Area RP6, PH 4A, Place Conc RipRap	21	18-Mar-14	16-Apr-14	95
1.5.7.6	2C4AWG60066...	Area WG6, PH 4A, Install Perm Markings	2	19-Mar-14	21-Mar-14	131
1.5.7.6	2C4AEG60064410	Area EG6, PH 4A, Install Small Signs	1	20-Mar-14	21-Mar-14	131
1.5.2.6	2C4AEG60034610	Area EG6, PH 4A, Place SMA Surface	19	20-Mar-14	16-Apr-14	111
1.5	2C4AWG60099...	Area WG6, PH 4A, Finish	0		21-Mar-14	131
1.5.7.6	2C4ASG60064410	Area SG6, PH 4A, Install Small Signs	1	02-Apr-14	03-Apr-14	122
1.5	2C4ASG60099999	Area SG6, PH 4A, Finish	0		03-Apr-14	122
1.5.7.6	2C4AEG60066610	Area EG6, PH 4A, Install Perm Markings	2	16-Apr-14	18-Apr-14	111
1.5.2.6	2C4ARP60034610	Area RP6, PH 4A, Place SMA Surface	16	16-Apr-14	08-May-14	95
1.5	2C4AEG60099999	Area EG6, PH 4A, Finish	0		18-Apr-14	111
1.5.7.6	2C4ARP60066610	Area RP6, PH 4A, Install Perm Markings	2	08-May...	12-May-14	95
1.5	2C4ARP60099999	Area RP6, PH 4A, Finish	0		12-May-14	95
1.5.7.6	2C4AML60066610	Area ML6, PH 4A, Install Perm Markings	6	11-Jun-14	19-Jun-14	67
1.5	2C4AML60099999	Area ML6, PH 4A, Finish	0		19-Jun-14	67
1.5.4.6.1.101	2C4AB101000001	BR 101, PH 4A, Start	0	19-Dec-...		49
1.5.4.6.1.101	2C4AB101049610	BR 101, PH 4A, Demo Extg Bridge	7	19-Dec-...	28-Dec-12	257
1.5.4.6.1.101	2C4AB101041600	BR 101, PH 4A, Install Drill Shafts	220	19-Dec-...	23-Oct-13	49
1.5.4.6.1.101	2C4AB101042010	BR 101, PH 4A, Install Footings	262	26-Dec-...	27-Dec-13	49
1.5.4.6.1.101	2C4AB101042040	BR 101, PH 4A, Install Abutments	5	02-Jan-13	09-Jan-13	350
1.5.4.6.1.101	2C4AB101042020	BR 101, PH 4A, Install Columns	355	09-Jan-13	21-May-14	49
1.5.4.6.1.101	2C4AB101042030	BR 101, PH 4A, Install Bent Caps	491	23-Jan-13	11-Dec-14	49
1.5.4.6.1.101	2C4AB101042510	BR 101, PH 4A, Install Conc Beams	63	06-Feb-13	06-May-13	277
1.5.4.6.1.101	2C4AB101042210	BR 101, PH 4A, Install Deck Slab	278	30-Dec-...	22-Jan-15	49
1.5.4.6.1.101	2C4AB101044210	BR 101, PH 4A, Install Plate Girders	44	31-Oct-14	01-Jan-15	49
1.5.4.6.1.101	2C4AB101042050	BR 101, PH 4A, Install Apprch Slabs	11	22-Jan-15	06-Feb-15	49
1.5.4.6.1.101	2C4AB101045020	BR 101, PH 4A, Install Conc Rail	38	06-Feb-15	01-Apr-15	49
1.5.4.6.1.101	2C4AB101045500	BR 101, PH 4A, Install Conc Median Barrier	11	01-Apr-15	16-Apr-15	49
1.5.4.6.1.101	2C4AB101099999	BR 101, PH 4A, Finish	0		16-Apr-15	49
1.5.4.6.1.102	2C4AB102000001	BR 102, PH 4A, Start	0	24-Jul-13		70

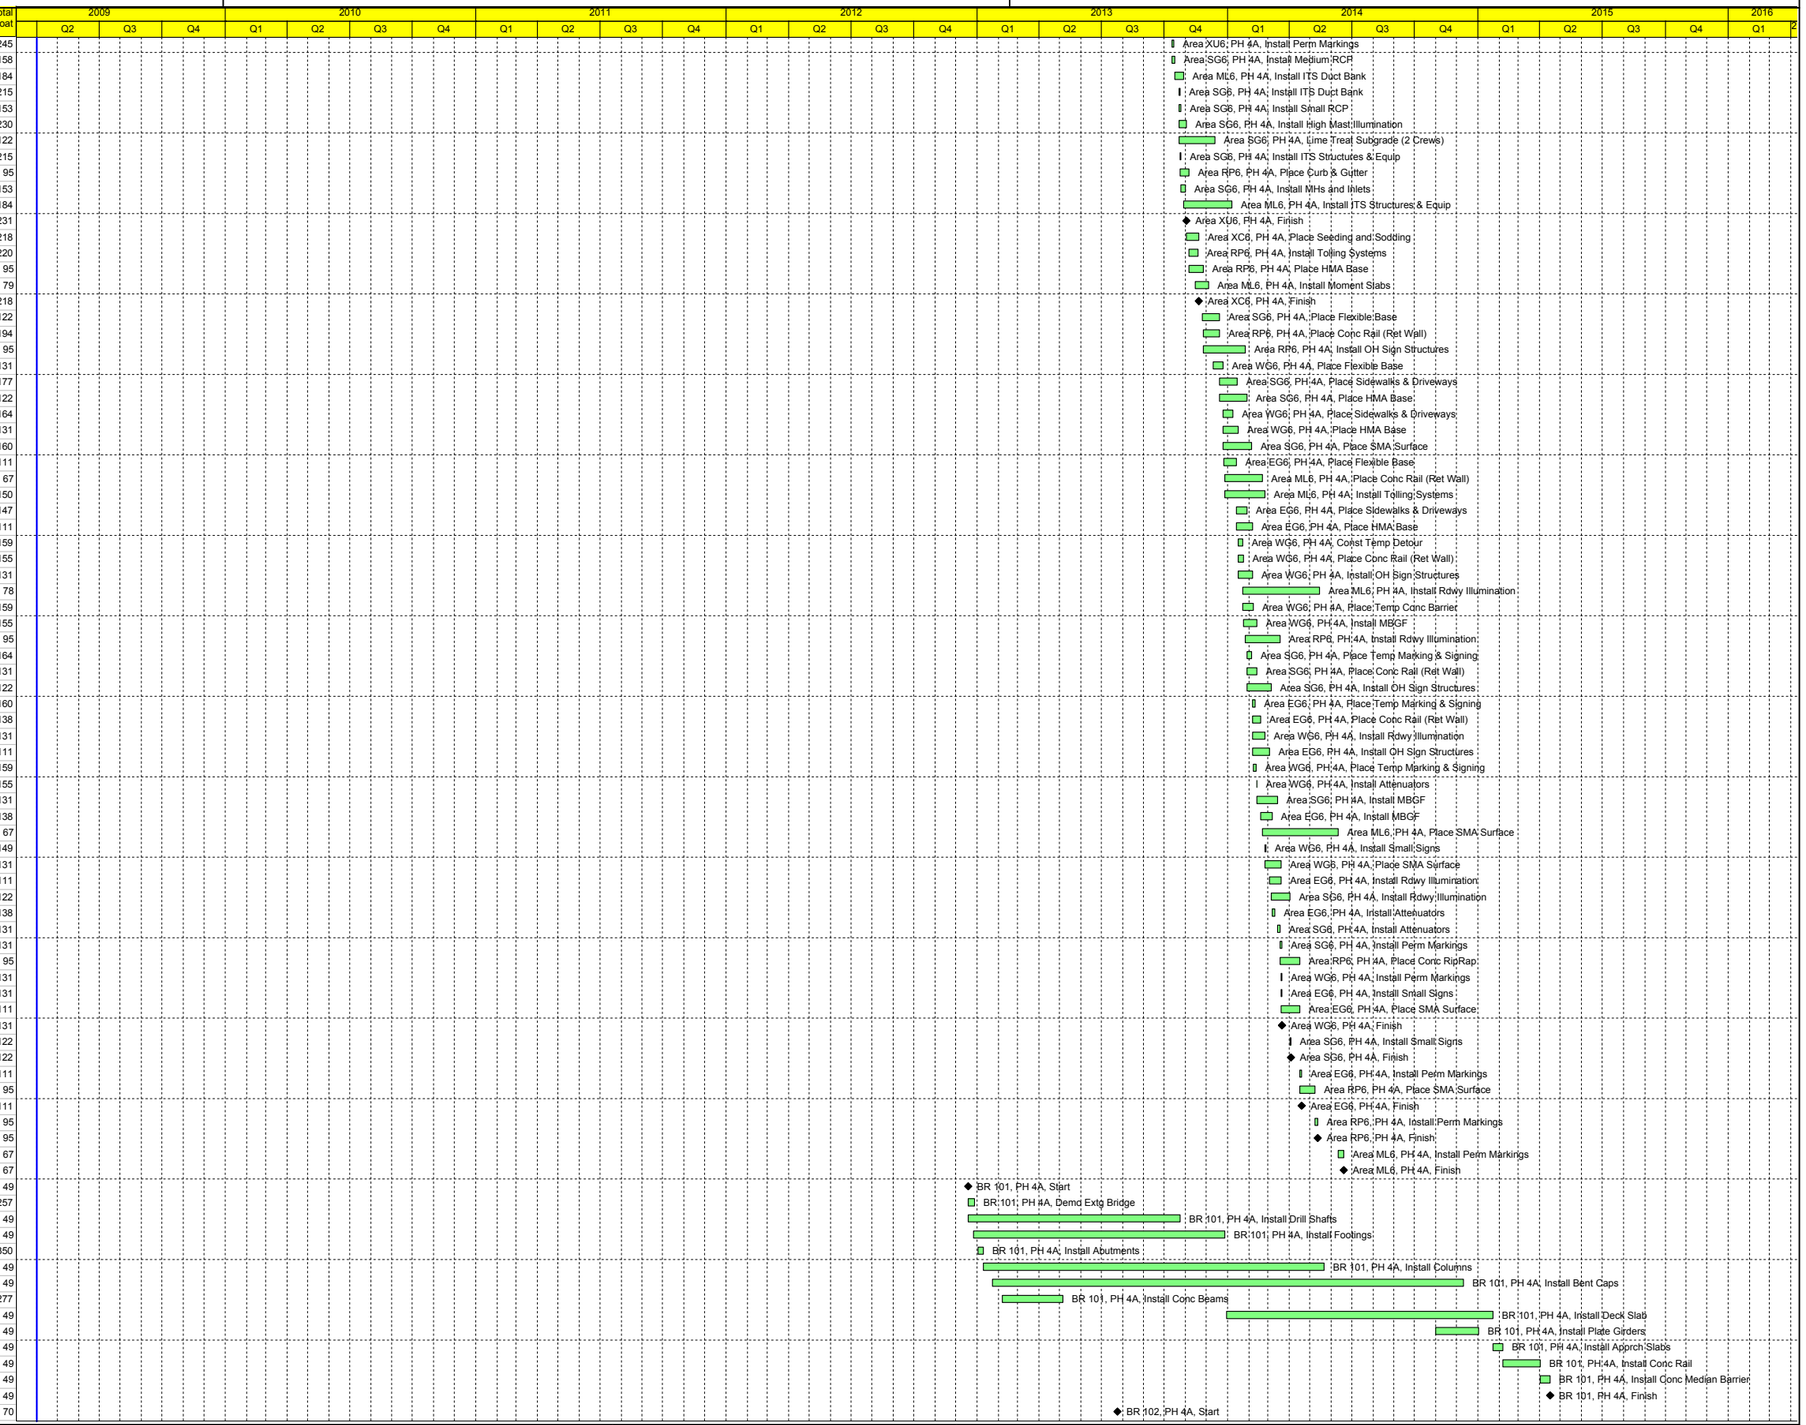

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.5.4.6.1.102	2C4AB102041600	BR 102, PH 4A, Install Drill Shafts (2 Crews)	76	24-Jul-13	07-Nov-13	70
1.5.4.6.1.102	2C4AB102042040	BR 102, PH 4A, Install Abutments	7	31-Jul-13	09-Aug-13	172
1.5.4.6.1.102	2C4AB102042010	BR 102, PH 4A, Install Footings (3 Crews)	93	31-Jul-13	09-Dec-13	70
1.5.4.6.1.102	2C4AB102042020	BR 102, PH 4A, Install Columns (3 Crews)	67	26-Sep-...	30-Dec-13	70
1.5.4.6.1.102	2C4AB102042030	BR 102, PH 4A, Install Bent Caps (5 crews)	96	10-Oct-13	21-Feb-14	70
1.5.4.6.1.102	2C4AB102042510	BR 102, PH 4A, Install Conc Beams	48	07-Nov-...	14-Jan-14	70
1.5.4.6.1.102	2C4AB102042210	BR 102, PH 4A, Install Deck Slab	103	14-Nov-...	08-Apr-14	70
1.5.4.6.1.102	2C4AB102045020	BR 102, PH 4A, Install Conc Rail	29	12-Mar-14	22-Apr-14	70
1.5.4.6.1.102	2C4AB102042050	BR 102, PH 4A, Install Apprch Slabs	16	24-Mar-14	15-Apr-14	70
1.5.4.6.1.102	2C4AB102045500	BR 102, PH 4A, Install Conc Median Barrier	39	22-Apr-14	16-Jun-14	70
1.5.4.6.1.102	2C4AB102099999	BR 102, PH 4A, Finish	0		16-Jun-14	70
1.5.4.6.1.104	2C4AB104000001	BR 104, PH 4A, Start	0	24-Jul-13		114
1.5.4.6.1.104	2C4AB104041600	BR 104, PH 4A, Install Drill Shafts	33	24-Jul-13	09-Sep-13	114
1.5.4.6.1.104	2C4AB104042040	BR 104, PH 4A, Install Abutments	2	09-Sep-...	11-Sep-13	343
1.5.4.6.1.104	2C4AB104042010	BR 104, PH 4A, Install Footings	63	09-Sep-...	05-Dec-13	114
1.5.4.6.1.104	2C4AB104042020	BR 104, PH 4A, Install Columns	100	05-Dec-...	24-Apr-14	114
1.5.4.6.1.104	2C4AB104042030	BR 104, PH 4A, Install Bent Caps	68	24-Apr-14	29-Jul-14	114
1.5.4.6.1.104	2C4AB104042510	BR 104, PH 4A, Install Conc Beams	10	29-Jul-14	12-Aug-14	117
1.5.4.6.1.104	2C4AB104044210	BR 104, PH 4A, Install Plate Girders	13	29-Jul-14	15-Aug-14	114
1.5.4.6.1.104	2C4AB104045410	BR 104, PH 4A, Install Exp Joints	4	15-Aug-...	21-Aug-14	114
1.5.4.6.1.104	2C4AB104042210	BR 104, PH 4A, Install Deck Slab	78	21-Aug-...	09-Dec-14	114
1.5.4.6.1.104	2C4AB104042050	BR 104, PH 4A, Install Apprch Slabs	4	09-Dec-...	15-Dec-14	120
1.5.4.6.1.104	2C4AB104045020	BR 104, PH 4A, Install Conc Rail	17	23-Dec-...	15-Jan-15	114
1.5.4.6.1.104	2C4AB104099999	BR 104, PH 4A, Finish	0		15-Jan-15	114
1.5.4.6.1.105	2C4AB105000001	BR 105, PH 4A, Start	0	24-Jul-13		260
1.5.4.6.1.105	2C4AB105049610	BR 105, PH 4A, Demo Extg Bridge	6	24-Jul-13	01-Aug-13	260
1.5.4.6.1.105	2C4AB105041600	BR 105, PH 4A, Install Drill Shafts	57	01-Aug-...	21-Oct-13	260
1.5.4.6.1.105	2C4AB105042010	BR 105, PH 4A, Install Footings	92	08-Aug-...	16-Dec-13	260
1.5.4.6.1.105	2C4AB105042020	BR 105, PH 4A, Install Columns	144	15-Aug-...	05-Mar-14	260
1.5.4.6.1.105	2C4AB105042040	BR 105, PH 4A, Install Abutments	2	21-Oct-13	23-Oct-13	313
1.5.4.6.1.105	2C4AB105042030	BR 105, PH 4A, Install Bent Caps	67	16-Dec-...	19-Mar-14	260
1.5.4.6.1.105	2C4AB105042510	BR 105, PH 4A, Install Conc Beams	14	06-Jan-14	24-Jan-14	260
1.5.4.6.1.105	2C4AB105042210	BR 105, PH 4A, Install Deck Slab	85	13-Jan-14	12-May-14	260
1.5.4.6.1.105	2C4AB105044210	BR 105, PH 4A, Install Plate Girders	4	20-Mar-14	26-Mar-14	283
1.5.4.6.1.105	2C4AB105042050	BR 105, PH 4A, Install Apprch Slabs	4	12-May...	16-May-14	266
1.5.4.6.1.105	2C4AB105045020	BR 105, PH 4A, Install Conc Rail	22	26-May...	25-Jun-14	260
1.5.4.6.1.105	2C4AB105099999	BR 105, PH 4A, Finish	0		25-Jun-14	260
1.5.4.6.1.114	2C4AB114000001	BR 114, PH 4A, Start	0	24-Jul-13		254
1.5.4.6.1.114	2C4AB114041600	BR 114, PH 4A, Install Drill Shafts	5	24-Jul-13	31-Jul-13	254
1.5.4.6.1.114	2C4AB114042020	BR 114, PH 4A, Install Columns	2	31-Jul-13	02-Aug-13	256
1.5.4.6.1.114	2C4AB114042040	BR 114, PH 4A, Install Abutments	7	31-Jul-13	09-Aug-13	254
1.5.4.6.1.114	2C4AB114042030	BR 114, PH 4A, Install Bent Caps	3	02-Aug-...	07-Aug-13	256
1.5.4.6.1.114	2C4AB114042510	BR 114, PH 4A, Install Conc Beams	2	09-Aug-...	13-Aug-13	254
1.5.4.6.1.114	2C4AB114045410	BR 114, PH 4A, Install Exp Joints	2	13-Aug-...	15-Aug-13	254
1.5.4.6.1.114	2C4AB114042210	BR 114, PH 4A, Install Deck Slab	15	15-Aug-...	05-Sep-13	254
1.5.4.6.1.114	2C4AB114042050	BR 114, PH 4A, Install Apprch Slabs	16	05-Sep-...	27-Sep-13	254
1.5.4.6.1.114	2C4AB114045020	BR 114, PH 4A, Install Conc Rail	2	27-Sep-...	01-Oct-13	254
1.5.4.6.1.114	2C4AB114099999	BR 114, PH 4A, Finish	0		01-Oct-13	254
1.5.4.6.1.115	2C4AB115000001	BR 115, PH 4A, Start	0	24-Jul-13		68
1.5.4.6.1.115	2C4AB115041600	BR 115, PH 4A, Install Drill Shafts (2 Crews)	75	24-Jul-13	06-Nov-13	68
1.5.4.6.1.115	2C4AB115042040	BR 115, PH 4A, Install Abutments	15	31-Jul-13	21-Aug-13	93
1.5.4.6.1.115	2C4AB115042010	BR 115, PH 4A, Install Footings (3 crews)	126	31-Jul-13	23-Jan-14	68
1.5.4.6.1.115	2C4AB115042020	BR 115, PH 4A, Install Columns (3 crews)	135	14-Aug-...	19-Feb-14	68
1.5.4.6.1.115	2C4AB115042030	BR 115, PH 4A, Install Bent Caps (4 crews)	155	28-Aug-...	02-Apr-14	68
1.5.4.6.1.115	2C4AB115042510	BR 115, PH 4A, Install Conc Beams	65	09-Oct-13	08-Jan-14	68
1.5.4.6.1.115	2C4AB115042210	BR 115, PH 4A, Install Deck Slab	160	16-Oct-13	28-May-14	68
1.5.4.6.1.115	2C4AB115044210	BR 115, PH 4A, Install Plate Girders	33	28-Feb-14	16-Apr-14	88
1.5.4.6.1.115	2C4AB115045020	BR 115, PH 4A, Install Conc Rail	35	30-Apr-14	18-Jun-14	68
1.5.4.6.1.115	2C4AB115042050	BR 115, PH 4A, Install Apprch Slabs	6	28-May...	05-Jun-14	77
1.5.4.6.1.115	2C4AB115099999	BR 115, PH 4A, Finish	0		18-Jun-14	68
1.5.4.6.1.125	2C4AB125000001	BR 125, PH 4A, Start	0	24-Jul-13		242
1.5.4.6.1.125	2C4AB125041600	BR 125, PH 4A, Install Drill Shafts	4	24-Jul-13	30-Jul-13	242
1.5.4.6.1.125	2C4AB125042020	BR 125, PH 4A, Install Columns	3	30-Jul-13	02-Aug-13	243
1.5.4.6.1.125	2C4AB125042040	BR 125, PH 4A, Install Abutments	7	30-Jul-13	08-Aug-13	242
1.5.4.6.1.125	2C4AB125042030	BR 125, PH 4A, Install Bent Caps	3	02-Aug-...	07-Aug-13	243
1.5.4.6.1.125	2C4AB125042510	BR 125, PH 4A, Install Conc Beams	3	08-Aug-...	13-Aug-13	242
1.5.4.6.1.125	2C4AB125045410	BR 125, PH 4A, Install Exp Joints	2	13-Aug-...	15-Aug-13	242
1.5.4.6.1.125	2C4AB125042210	BR 125, PH 4A, Install Deck Slab	18	15-Aug-...	10-Sep-13	242
1.5.4.6.1.125	2C4AB125042050	BR 125, PH 4A, Install Apprch Slabs	25	10-Sep-...	15-Oct-13	242
1.5.4.6.1.125	2C4AB125045020	BR 125, PH 4A, Install Conc Rail	2	15-Oct-13	17-Oct-13	242
1.5.4.6.1.125	2C4AB125099999	BR 125, PH 4A, Finish	0		17-Oct-13	242
1.5.4.6.1.128	2C4AB128000001	BR 128, PH 4A, Start	0	24-Jul-13		244
1.5.4.6.1.128	2C4AB128041600	BR 128, PH 4A, Install Drill Shafts	6	24-Jul-13	01-Aug-13	244
1.5.4.6.1.128	2C4AB128042020	BR 128, PH 4A, Install Columns	2	01-Aug-...	05-Aug-13	246
1.5.4.6.1.128	2C4AB128042040	BR 128, PH 4A, Install Abutments	7	01-Aug-...	12-Aug-13	244
1.5.4.6.1.128	2C4AB128042030	BR 128, PH 4A, Install Bent Caps	3	05-Aug-...	08-Aug-13	246
1.5.4.6.1.128	2C4AB128042510	BR 128, PH 4A, Install Conc Beams	3	12-Aug-...	15-Aug-13	244
1.5.4.6.1.128	2C4AB128045410	BR 128, PH 4A, Install Exp Joints	2	15-Aug-...	19-Aug-13	244
1.5.4.6.1.128	2C4AB128042210	BR 128, PH 4A, Install Deck Slab	21	19-Aug-...	17-Sep-13	244
1.5.4.6.1.128	2C4AB128042050	BR 128, PH 4A, Install Apprch Slabs	18	17-Sep-...	11-Oct-13	244
1.5.4.6.1.128	2C4AB128045020	BR 128, PH 4A, Install Conc Rail	2	11-Oct-13	15-Oct-13	244
1.5.4.6.1.128	2C4AB128099999	BR 128, PH 4A, Finish	0		15-Oct-13	244
1.5.4.6.1.131	2C4AB131000001	BR 131, PH 4A, Start	0	24-Jul-13		251
1.5.4.6.1.131	2C4AB131041600	BR 131, PH 4A, Install Drill Shafts	5	24-Jul-13	31-Jul-13	251
1.5.4.6.1.131	2C4AB131042020	BR 131, PH 4A, Install Columns	3	31-Jul-13	05-Aug-13	252
1.5.4.6.1.131	2C4AB131042040	BR 131, PH 4A, Install Abutments	7	31-Jul-13	09-Aug-13	251

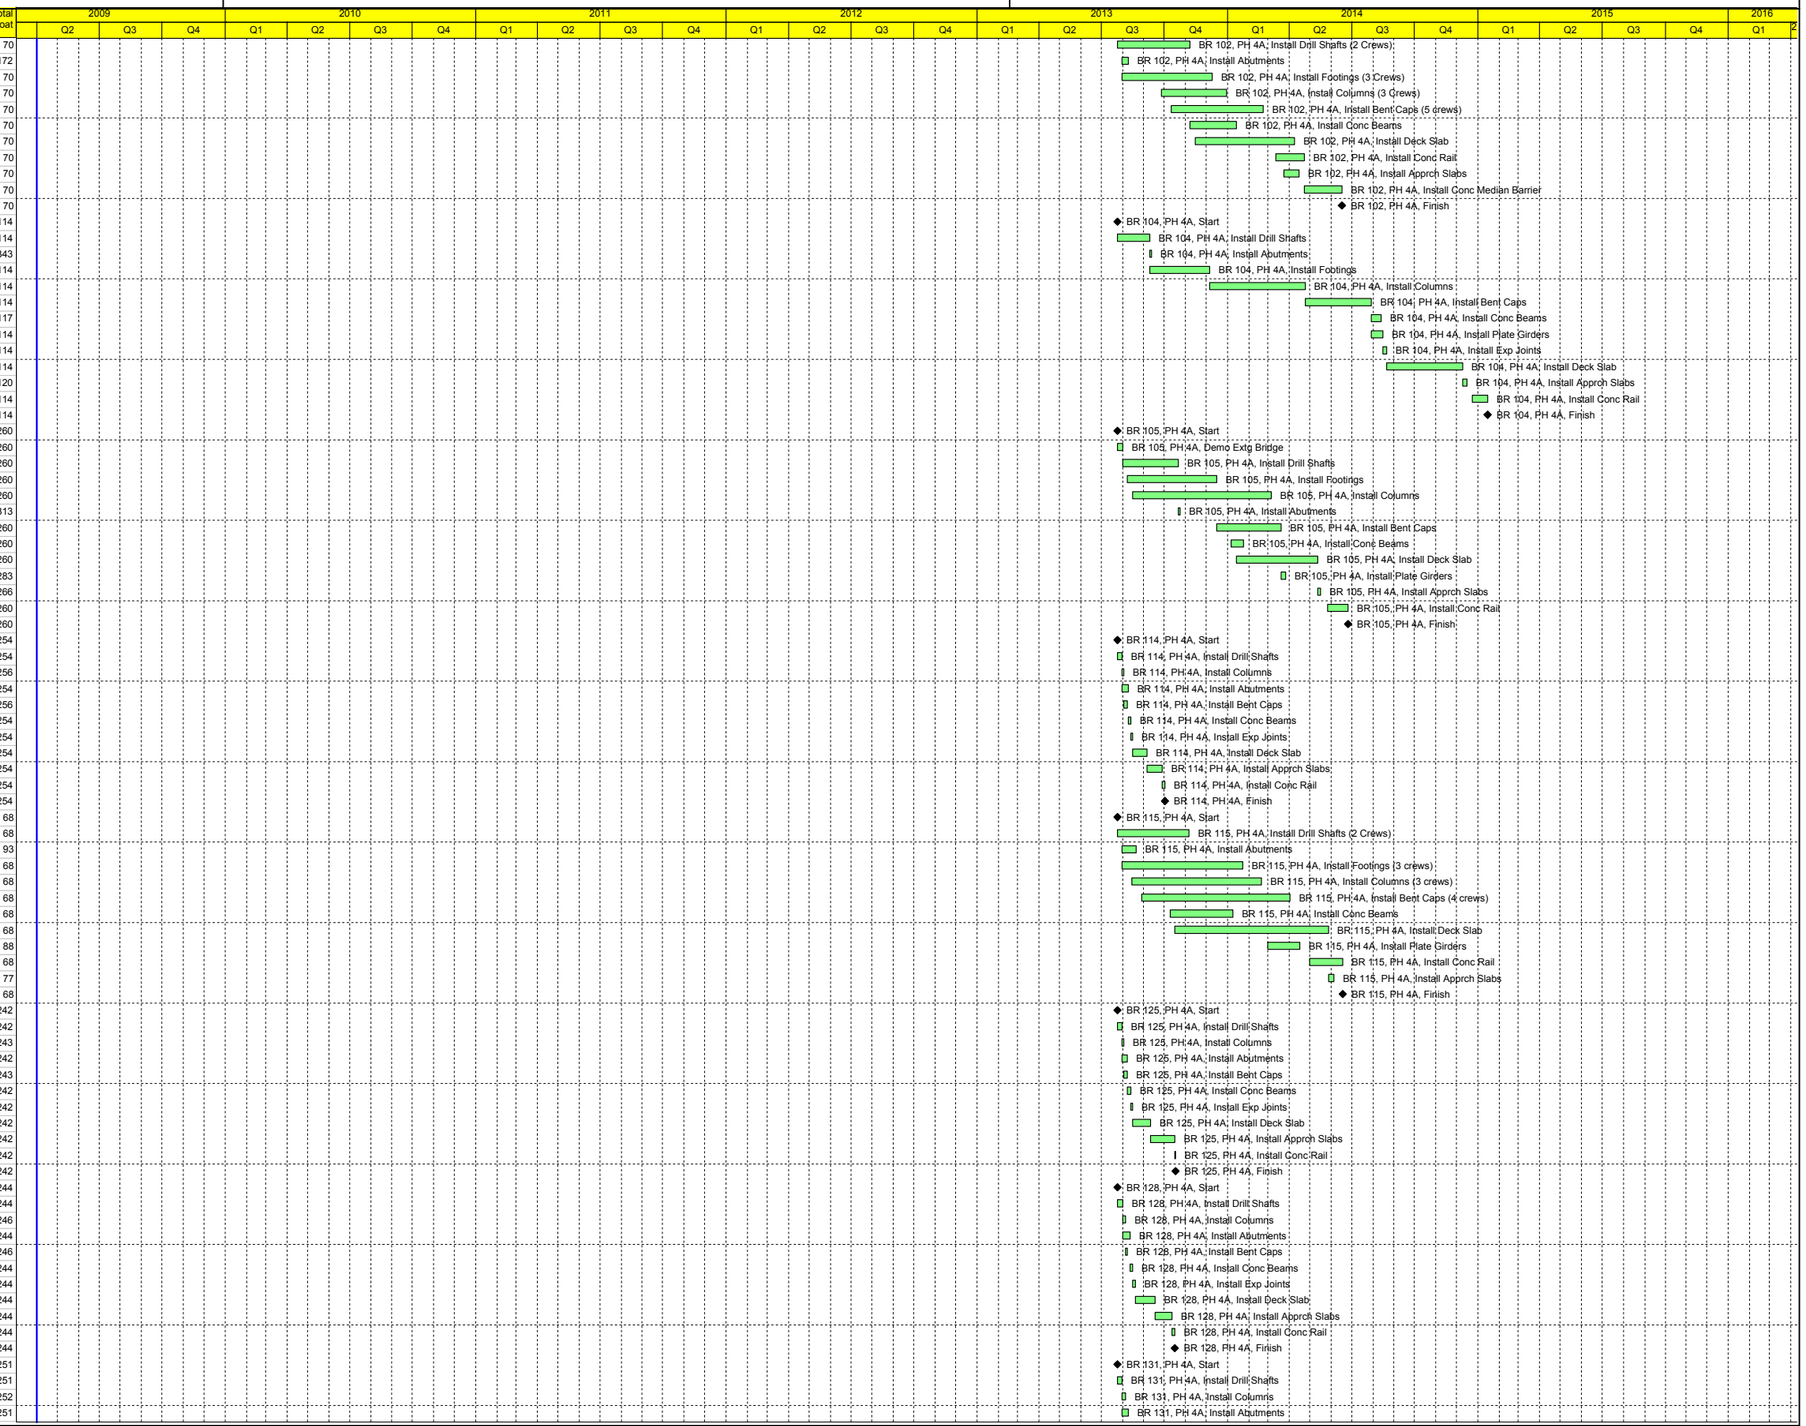

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.5.4.6.1.131	2C4AB131042030	BR 131, PH 4A, Install Bent Caps	3	05-Aug-...	08-Aug-13	252
1.5.4.6.1.131	2C4AB131042510	BR 131, PH 4A, Install Conc Beams	3	09-Aug-...	14-Aug-13	251
1.5.4.6.1.131	2C4AB131045410	BR 131, PH 4A, Install Exp Joints	2	14-Aug-...	16-Aug-13	251
1.5.4.6.1.131	2C4AB131042210	BR 131, PH 4A, Install Deck Slab	17	16-Aug-...	10-Sep-13	251
1.5.4.6.1.131	2C4AB131042050	BR 131, PH 4A, Install Apprch Slabs	16	10-Sep-...	02-Oct-13	251
1.5.4.6.1.131	2C4AB131045020	BR 131, PH 4A, Install Conc Rail	2	02-Oct-13	04-Oct-13	251
1.5.4.6.1.131	2C4AB131099999	BR 131, PH 4A, Finish	0		04-Oct-13	251
1.5.4.6.1.134	2C4AB134000001	BR 134, PH 4A, Start	0	24-Jul-13		224
1.5.4.6.1.134	2C4AB134041600	BR 134, PH 4A, Install Drill Shafts	4	24-Jul-13	30-Jul-13	224
1.5.4.6.1.134	2C4AB134042040	BR 134, PH 4A, Install Abutments	2	30-Jul-13	01-Aug-13	263
1.5.4.6.1.134	2C4AB134042010	BR 134, PH 4A, Install Footings	17	30-Jul-13	22-Aug-13	224
1.5.4.6.1.134	2C4AB134042020	BR 134, PH 4A, Install Columns	10	22-Aug-...	05-Sep-13	224
1.5.4.6.1.134	2C4AB134042030	BR 134, PH 4A, Install Bent Caps	14	05-Sep-...	25-Sep-13	224
1.5.4.6.1.134	2C4AB134042510	BR 134, PH 4A, Install Conc Beams	3	25-Sep-...	30-Sep-13	224
1.5.4.6.1.134	2C4AB134045410	BR 134, PH 4A, Install Exp Joints	1	30-Sep-...	01-Oct-13	224
1.5.4.6.1.134	2C4AB134042210	BR 134, PH 4A, Install Deck Slab	16	01-Oct-13	23-Oct-13	224
1.5.4.6.1.134	2C4AB134042050	BR 134, PH 4A, Install Apprch Slabs	4	23-Oct-13	29-Oct-13	230
1.5.4.6.1.134	2C4AB134045020	BR 134, PH 4A, Install Conc Rail	4	06-Nov-...	12-Nov-13	224
1.5.4.6.1.134	2C4AB134099999	BR 134, PH 4A, Finish	0		12-Nov-13	224
1.5.4.6.1.135	2C4AB135000001	BR 135, PH 4A, Start	0	24-Jul-13		235
1.5.4.6.1.135	2C4AB135041600	BR 135, PH 4A, Install Drill Shafts	1	24-Jul-13	25-Jul-13	235
1.5.4.6.1.135	2C4AB135042040	BR 135, PH 4A, Install Abutments	2	25-Jul-13	29-Jul-13	257
1.5.4.6.1.135	2C4AB135042010	BR 135, PH 4A, Install Footings	5	25-Jul-13	01-Aug-13	235
1.5.4.6.1.135	2C4AB135042020	BR 135, PH 4A, Install Columns	6	01-Aug-...	09-Aug-13	235
1.5.4.6.1.135	2C4AB135042030	BR 135, PH 4A, Install Bent Caps	13	09-Aug-...	28-Aug-13	235
1.5.4.6.1.135	2C4AB135042510	BR 135, PH 4A, Install Conc Beams	3	28-Aug-...	02-Sep-13	237
1.5.4.6.1.135	2C4AB135044210	BR 135, PH 4A, Install Plate Girders	5	28-Aug-...	04-Sep-13	235
1.5.4.6.1.135	2C4AB135045410	BR 135, PH 4A, Install Exp Joints	1	04-Sep-...	05-Sep-13	235
1.5.4.6.1.135	2C4AB135042210	BR 135, PH 4A, Install Deck Slab	22	05-Sep-...	07-Oct-13	235
1.5.4.6.1.135	2C4AB135042050	BR 135, PH 4A, Install Apprch Slabs	4	07-Oct-13	11-Oct-13	241
1.5.4.6.1.135	2C4AB135045020	BR 135, PH 4A, Install Conc Rail	5	21-Oct-13	28-Oct-13	235
1.5.4.6.1.135	2C4AB135099999	BR 135, PH 4A, Finish	0		28-Oct-13	235
1.5.4.6.1.140	2C4AB140000001	BR 140, PH 4A, Start	0	24-Jul-13		246
1.5.4.6.1.140	2C4AB140041600	BR 140, PH 4A, Install Drill Shafts	3	24-Jul-13	29-Jul-13	246
1.5.4.6.1.140	2C4AB140042040	BR 140, PH 4A, Install Abutments	2	29-Jul-13	31-Jul-13	275
1.5.4.6.1.140	2C4AB140042010	BR 140, PH 4A, Install Footings	11	29-Jul-13	13-Aug-13	246
1.5.4.6.1.140	2C4AB140042020	BR 140, PH 4A, Install Columns	7	13-Aug-...	22-Aug-13	246
1.5.4.6.1.140	2C4AB140042030	BR 140, PH 4A, Install Bent Caps	13	22-Aug-...	10-Sep-13	246
1.5.4.6.1.140	2C4AB140042510	BR 140, PH 4A, Install Conc Beams	2	10-Sep-...	12-Sep-13	246
1.5.4.6.1.140	2C4AB140045410	BR 140, PH 4A, Install Exp Joints	1	12-Sep-...	13-Sep-13	246
1.5.4.6.1.140	2C4AB140042210	BR 140, PH 4A, Install Deck Slab	8	13-Sep-...	25-Sep-13	246
1.5.4.6.1.140	2C4AB140042050	BR 140, PH 4A, Install Apprch Slabs	4	25-Sep-...	01-Oct-13	252
1.5.4.6.1.140	2C4AB140045020	BR 140, PH 4A, Install Conc Rail	2	09-Oct-13	11-Oct-13	246
1.5.4.6.1.140	2C4AB140099999	BR 140, PH 4A, Finish	0		11-Oct-13	246
1.5.4.6.1.143	2C4AB143000001	BR 143, PH 4A, Start	0	24-Jul-13		221
1.5.4.6.1.143	2C4AB143041600	BR 143, PH 4A, Install Drill Shafts	5	24-Jul-13	31-Jul-13	221
1.5.4.6.1.143	2C4AB143042040	BR 143, PH 4A, Install Abutments	7	31-Jul-13	09-Aug-13	237
1.5.4.6.1.143	2C4AB143042010	BR 143, PH 4A, Install Footings	9	31-Jul-13	13-Aug-13	221
1.5.4.6.1.143	2C4AB143042020	BR 143, PH 4A, Install Columns	3	13-Aug-...	16-Aug-13	221
1.5.4.6.1.143	2C4AB143042030	BR 143, PH 4A, Install Bent Caps	11	16-Aug-...	02-Sep-13	221
1.5.4.6.1.143	2C4AB143042510	BR 143, PH 4A, Install Conc Beams	2	02-Sep-...	04-Sep-13	221
1.5.4.6.1.143	2C4AB143045410	BR 143, PH 4A, Install Exp Joints	2	04-Sep-...	06-Sep-13	221
1.5.4.6.1.143	2C4AB143042210	BR 143, PH 4A, Install Deck Slab	15	06-Sep-...	27-Sep-13	221
1.5.4.6.1.143	2C4AB143042050	BR 143, PH 4A, Install Apprch Slabs	33	27-Sep-...	13-Nov-13	221
1.5.4.6.1.143	2C4AB143045020	BR 143, PH 4A, Install Conc Rail	2	13-Nov-...	15-Nov-13	221
1.5.4.6.1.143	2C4AB143099999	BR 143, PH 4A, Finish	0		15-Nov-13	221
1.5	2C4A0000000001	START PHASE 4A, SUBSEGMENT 2C	0	24-Jul-13		67
1.5	2C4A0000099999	FINISH PHASE 4A, SUBSEGMENT 2C	0		19-Jun-14	67
CONSTRUCTION PHASE 4B			84	19-Jun-14	15-Oct-14	180
1.5	2C4BEG60000001	Area EG6, PH 4B, Start	0	19-Jun-14		118
1.5	2C4BRP60000001	Area RP6, PH 4B, Start	0	19-Jun-14		94
1.5	2C4BWG60000...	Area WG6, PH 4B, Start	0	19-Jun-14		67
1.5	2C4BXU60000001	Area XU6, PH 4B, Start	0	19-Jun-14		125
1.5.2.6	2C4BRP60010410	Area RP6, PH 4B, Rem Conc Pavement	1	19-Jun-14	20-Jun-14	114
1.5.2.6	2C4BEG60050600	Area EG6, PH 4B, Place Temp Erosion Control	2	19-Jun-14	23-Jun-14	118
1.5.2.6	2C4BWG60010...	Area WG6, PH 4B, Rem Conc Pavement	2	19-Jun-14	23-Jun-14	70
1.5.2.6	2C4BXU60050600	Area XU6, PH 4B, Place Temp Erosion Control	2	19-Jun-14	23-Jun-14	125
1.5.2.6	2C4BWG60010...	Area WG6, PH 4B, Rem Concrete Barrier	3	19-Jun-14	24-Jun-14	261
1.5.2.6	2C4BWG60063...	Area WG6, PH 4B, Rem Overhead Sign Sup...	3	19-Jun-14	24-Jun-14	261
1.5.2.6	2C4BWG60050...	Area WG6, PH 4B, Place Temp Erosion Cont...	5	19-Jun-14	26-Jun-14	67
1.5.3.6	2C4BRP60046220	Area RP6, PH 4B, Install Medium CBC	1	20-Jun-14	23-Jun-14	122
1.5.2.6	2C4BRP60013210	Area RP6, PH 4B, Place Embankment	5	20-Jun-14	27-Jun-14	116
1.5.2.6	2C4BRP60011010	Area RP6, PH 4B, Excavate Cut Areas	7	20-Jun-14	01-Jul-14	114
1.5.2.6	2C4BEG60054210	Area EG6, PH 4B, Rem MBGF	1	23-Jun-14	24-Jun-14	118
1.5.2.6	2C4BEG60060010	Area EG6, PH 4B, Rem Light Poles	1	23-Jun-14	24-Jun-14	118
1.5.2.6	2C4BEG60063010	Area EG6, PH 4B, Rem Overhead Sign Supp...	1	23-Jun-14	24-Jun-14	118
1.5.3.6	2C4BRP60046210	Area RP6, PH 4B, Install Small CBC	1	23-Jun-14	24-Jun-14	122
1.5.2.6	2C4BXU60010410	Area XU6, PH 4B, Rem Conc Pavement	1	23-Jun-14	24-Jun-14	125
1.5.2.6	2C4BEG60010430	Area EG6, PH 4B, Rem Concrete Barrier	1	24-Jun-14	25-Jun-14	118
1.5.3.6	2C4BRP60046420	Area RP6, PH 4B, Install Medium RCP	1	24-Jun-14	25-Jun-14	122
1.5.3.6	2C4BXU60046420	Area XU6, PH 4B, Install Medium RCP	1	24-Jun-14	25-Jun-14	127
1.5.8.6	2C4BXU60062899	Area XU6, PH 4B, Install Elec Service for ITS...	3	24-Jun-14	27-Jun-14	137
1.5.2.6	2C4BXU60026010	Area XU6, PH 4B, Lime Treat Subgrade	6	24-Jun-14	02-Jul-14	125
1.5.2.6	2C4BEG60010410	Area EG6, PH 4B, Rem Conc Pavement	1	25-Jun-14	26-Jun-14	118
1.5.8.6	2C4BXU60061899	Area XU6, PH 4B, Install ITS Duct Bank	1	25-Jun-14	26-Jun-14	138
1.5.3.6	2C4BXU60046410	Area XU6, PH 4B, Install Small RCP	2	25-Jun-14	27-Jun-14	127

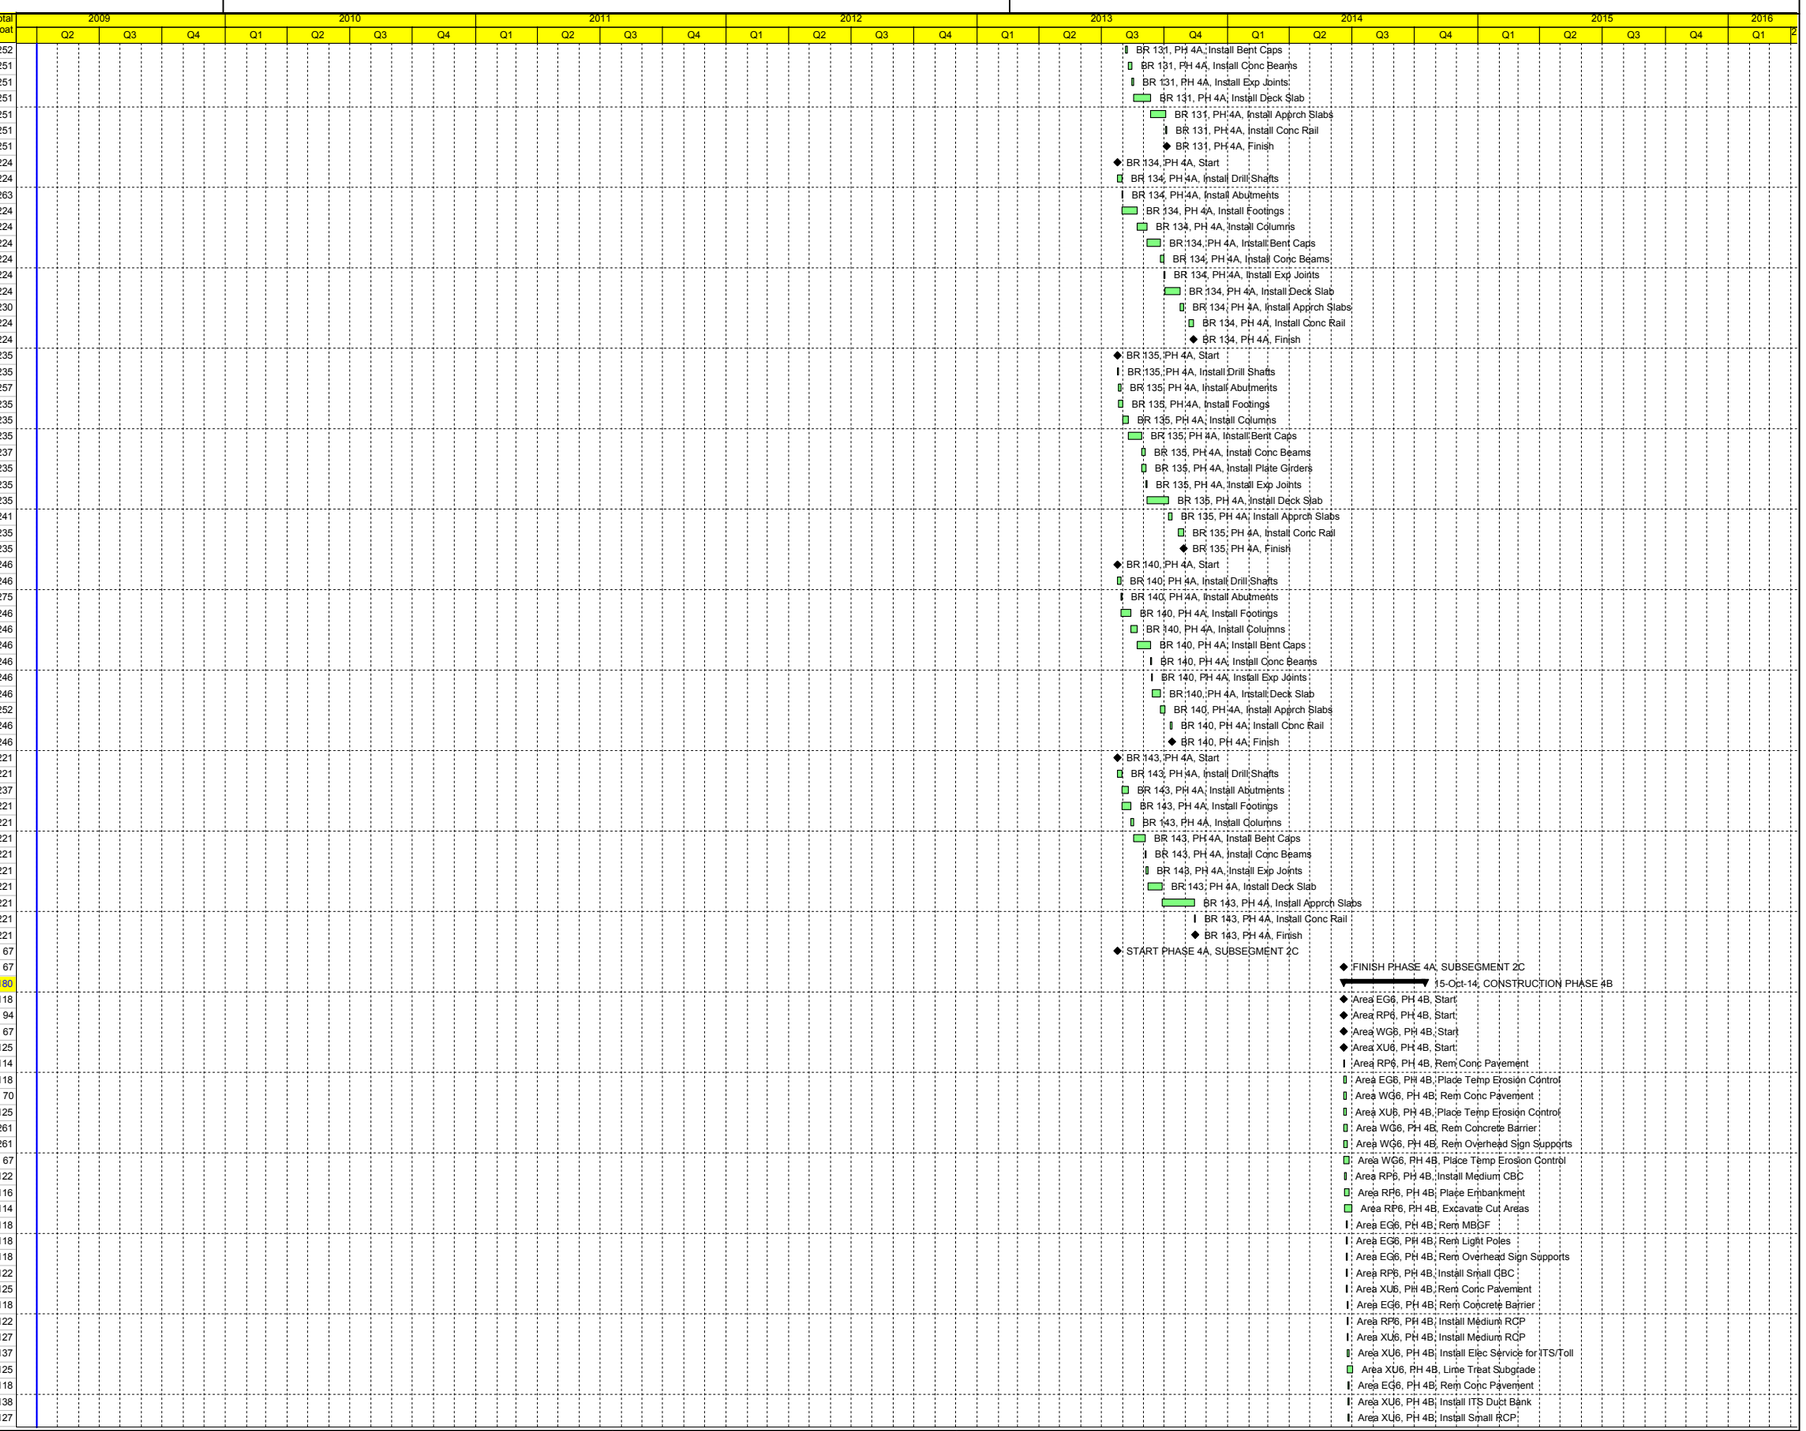

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.5.3.6	2C4BEG60046230	Area EG6, PH 4B, Install Large CBC	2	26-Jun-14	30-Jun-14	125
1.5.2.6	2C4BEG60013210	Area EG6, PH 4B, Place Embankment	3	26-Jun-14	01-Jul-14	119
1.5.2.6	2C4BEG60011010	Area EG6, PH 4B, Excavate Cut Areas	4	26-Jun-14	02-Jul-14	118
1.5.3.6	2C4BWG60046...	Area WG6, PH 4B, Install Large CBC	6	26-Jun-14	04-Jul-14	88
1.5.2.6	2C4BWG60013...	Area WG6, PH 4B, Place Embankment	10	26-Jun-14	10-Jul-14	67
1.5.2.6	2C4BWG60011...	Area WG6, PH 4B, Excavate Cut Areas	15	26-Jun-14	17-Jul-14	67
1.5.3.6	2C4BXU60046510	Area XU6, PH 4B, Install MHs and Inlets	1	27-Jun-14	30-Jun-14	127
1.5.3.6	2C4BEG60046220	Area EG6, PH 4B, Install Medium CBC	1	30-Jun-14	01-Jul-14	125
1.5.3.6	2C4BEG60046210	Area EG6, PH 4B, Install Small CBC	1	01-Jul-14	02-Jul-14	125
1.5.3.6	2C4BRP60046410	Area RP6, PH 4B, Install Small RCP	1	01-Jul-14	02-Jul-14	118
1.5.2.6	2C4BRP60026010	Area RP6, PH 4B, Lime Treat Subgrade	7	01-Jul-14	10-Jul-14	114
1.5.3.6	2C4BEG60046420	Area EG6, PH 4B, Install Medium RCP	1	02-Jul-14	03-Jul-14	125
1.5.3.6	2C4BRP60046510	Area RP6, PH 4B, Install MHs and Inlets	2	02-Jul-14	04-Jul-14	118
1.5.2.6	2C4BXU60024710	Area XU6, PH 4B, Place Flexible Base	2	02-Jul-14	04-Jul-14	125
1.5.2.6	2C4BEG60026010	Area EG6, PH 4B, Lime Treat Subgrade	10	02-Jul-14	16-Jul-14	118
1.5.8.6	2C4BEG60061899	Area EG6, PH 4B, Install ITS Duct Bank	1	03-Jul-14	04-Jul-14	132
1.5.3.6	2C4BEG60046410	Area EG6, PH 4B, Install Small RCP	1	03-Jul-14	04-Jul-14	125
1.5.2.6	2C4BWG60026...	Area WG6, PH 4B, Lime Treat Subgrade	35	03-Jul-14	21-Aug-14	67
1.5.3.6	2C4BEG60046510	Area EG6, PH 4B, Install MHs and Inlets	1	04-Jul-14	07-Jul-14	125
1.5.2.6	2C4BXU60052910	Area XU6, PH 4B, Place Curb & Gutter	1	04-Jul-14	07-Jul-14	125
1.5.8.6	2C4BEG60041699	Area EG6, PH 4B, Install ITS Structures & Eq...	2	04-Jul-14	08-Jul-14	132
1.5.3.6	2C4BWG60046...	Area WG6, PH 4B, Install Medium CBC	3	04-Jul-14	09-Jul-14	88
1.5.2.6	2C4BXU60034011	Area XU6, PH 4B, Place HMA Base	3	07-Jul-14	10-Jul-14	125
1.5.3.6	2C4BWG60046...	Area WG6, PH 4B, Install Small CBC	3	09-Jul-14	14-Jul-14	88
1.5.9.6	2C4BXU60066200	Area XU6, PH 4B, Place Temp Marking & Si...	1	10-Jul-14	11-Jul-14	135
1.5.2.6	2C4BRP60024710	Area RP6, PH 4B, Place Flexible Base	2	10-Jul-14	14-Jul-14	114
1.5.7.6	2C4BXU60061020	Area XU6, PH 4B, Install Rdwy Illumination	3	10-Jul-14	15-Jul-14	128
1.5.7.6	2C4BXU60068010	Area XU6, PH 4B, Install Traffic Signal Syste...	11	10-Jul-14	25-Jul-14	125
1.5.2.6	2C4BRP60052910	Area RP6, PH 4B, Place Curb & Gutter	1	14-Jul-14	15-Jul-14	114
1.5.2.6	2C4BRP60034012	Area RP6, PH 4B, Place HMA Base	2	15-Jul-14	17-Jul-14	114
1.5.10.6	2C4BRP60041698	Area RP6, PH 4B, Install Tolling Systems	2	15-Jul-14	17-Jul-14	131
1.5.2.6	2C4BXU60034610	Area XU6, PH 4B, Place SMA Surface	4	15-Jul-14	21-Jul-14	128
1.5.2.6	2C4BEG60024710	Area EG6, PH 4B, Place Flexible Base	2	16-Jul-14	18-Jul-14	118
1.5.3.6	2C4BWG60046...	Area WG6, PH 4B, Install Small RCP	2	17-Jul-14	21-Jul-14	85
1.5.3.6	2C4BWG60046...	Area WG6, PH 4B, Install MHs and Inlets	2	17-Jul-14	21-Jul-14	85
1.5.2.6	2C4BRP60045010	Area RP6, PH 4B, Place Conc Rail (Ret Wall)	3	17-Jul-14	22-Jul-14	127
1.5.7.6	2C4BRP60065010	Area RP6, PH 4B, Install OH Sign Structures	6	17-Jul-14	25-Jul-14	114
1.5.8.6	2C4BWG60041...	Area WG6, PH 4B, Install ITS Structures & E...	9	17-Jul-14	30-Jul-14	112
1.5.2.6	2C4BEG60053110	Area EG6, PH 4B, Place Sidewalks & Drivew...	2	18-Jul-14	22-Jul-14	124
1.5.2.6	2C4BEG60034012	Area EG6, PH 4B, Place HMA Base	3	18-Jul-14	23-Jul-14	118
1.5.7.6	2C4BXU60066610	Area XU6, PH 4B, Install Perm Markings	1	21-Jul-14	22-Jul-14	128
1.5.2.6	2C4BEG60045010	Area EG6, PH 4B, Place Conc Rail (Ret Wall)	1	23-Jul-14	24-Jul-14	121
1.5.9.6	2C4BEG60066200	Area EG6, PH 4B, Place Temp Marking & Si...	1	23-Jul-14	24-Jul-14	126
1.5.7.6	2C4BEG60065010	Area EG6, PH 4B, Install OH Sign Structures	3	23-Jul-14	28-Jul-14	118
1.5.2.6	2C4BEG60054010	Area EG6, PH 4B, Install MBGF	3	24-Jul-14	29-Jul-14	121
1.5	2C4BXU60099999	Area XU6, PH 4B, Finish	0		25-Jul-14	125
1.5.7.6	2C4BRP60061020	Area RP6, PH 4B, Install Rdwy Illumination	5	25-Jul-14	01-Aug-14	114
1.5.7.6	2C4BEG60061020	Area EG6, PH 4B, Install Rdwy Illumination	2	28-Jul-14	30-Jul-14	118
1.5.2.6	2C4BEG60054510	Area EG6, PH 4B, Install Attenuators	1	29-Jul-14	30-Jul-14	121
1.5.7.6	2C4BEG60064410	Area EG6, PH 4B, Install Small Signs	1	30-Jul-14	31-Jul-14	121
1.5.2.6	2C4BEG60034610	Area EG6, PH 4B, Place SMA Surface	3	30-Jul-14	04-Aug-14	118
1.5.2.6	2C4BRP60043210	Area RP6, PH 4B, Place Conc RipRap	3	01-Aug-...	06-Aug-14	114
1.5.7.6	2C4BEG60066610	Area EG6, PH 4B, Install Perm Markings	1	04-Aug-...	05-Aug-14	118
1.5	2C4BEG60099999	Area EG6, PH 4B, Finish	0		05-Aug-14	118
1.5.2.6	2C4BRP60034610	Area RP6, PH 4B, Place SMA Surface	2	06-Aug-...	08-Aug-14	114
1.5.7.6	2C4BRP60066610	Area RP6, PH 4B, Install Perm Markings	1	08-Aug-...	11-Aug-14	114
1.5.2.6	2C4BWG60024...	Area WG6, PH 4B, Place Flexible Base	9	14-Aug-...	27-Aug-14	67
1.5.2.6	2C4BWG60053...	Area WG6, PH 4B, Place Sidewalks & Drive...	8	27-Aug-...	08-Sep-14	93
1.5.2.6	2C4BWG60034...	Area WG6, PH 4B, Place HMA Base	13	27-Aug-...	15-Sep-14	67
1.5	2C4BRP60099999	Area RP6, PH 4B, Finish	0		08-Sep-14	94
1.5.2.6	2C4BWG60034...	Area WG6, PH 4B, Place SMA Surface	10	08-Sep-...	22-Sep-14	83
1.5.2.6	2C4BWG60045...	Area WG6, PH 4B, Place Conc Rail (Ret Wall)	5	15-Sep-...	22-Sep-14	73
1.5.9.6	2C4BWG60051...	Area WG6, PH 4B, Place Temp Conc Barrier	11	15-Sep-...	30-Sep-14	76
1.5.7.6	2C4BWG60065...	Area WG6, PH 4B, Install OH Sign Structures	12	15-Sep-...	01-Oct-14	67
1.5.2.6	2C4BWG60054...	Area WG6, PH 4B, Install MBGF	10	22-Sep-...	06-Oct-14	73
1.5.9.6	2C4BWG60066...	Area WG6, PH 4B, Place Temp Marking & Si...	2	30-Sep-...	02-Oct-14	76
1.5.7.6	2C4BWG60061...	Area WG6, PH 4B, Install Rdwy Illumination	9	01-Oct-14	14-Oct-14	67
1.5.7.6	2C4BWG60066...	Area WG6, PH 4B, Install Perm Markings	1	06-Oct-14	07-Oct-14	73
1.5.7.6	2C4BWG60064...	Area WG6, PH 4B, Install Small Signs	1	14-Oct-14	15-Oct-14	67
1.5	2C4BWG60099...	Area WG6, PH 4B, Finish	0		15-Oct-14	67
1.5.4.6.1.137	2C4BB137000001	BR 137, PH 4B, Start	0	19-Jun-14		94
1.5.4.6.1.137	2C4BB137041600	BR 137, PH 4B, Install Drill Shafts	2	19-Jun-14	23-Jun-14	94
1.5.4.6.1.137	2C4BB137042040	BR 137, PH 4B, Install Abutments	4	23-Jun-14	27-Jun-14	118
1.5.4.6.1.137	2C4BB137042010	BR 137, PH 4B, Install Footings	12	23-Jun-14	09-Jul-14	94
1.5.4.6.1.137	2C4BB137042020	BR 137, PH 4B, Install Columns	6	09-Jul-14	17-Jul-14	94
1.5.4.6.1.137	2C4BB137042030	BR 137, PH 4B, Install Bent Caps	10	17-Jul-14	31-Jul-14	94
1.5.4.6.1.137	2C4BB137042510	BR 137, PH 4B, Install Conc Beams	2	31-Jul-14	04-Aug-14	94
1.5.4.6.1.137	2C4BB137045410	BR 137, PH 4B, Install Exp Joints	1	04-Aug-...	05-Aug-14	94
1.5.4.6.1.137	2C4BB137042210	BR 137, PH 4B, Install Deck Slab	11	05-Aug-...	20-Aug-14	94
1.5.4.6.1.137	2C4BB137042050	BR 137, PH 4B, Install Apprch Slabs	8	20-Aug-...	01-Sep-14	96
1.5.4.6.1.137	2C4BB137045020	BR 137, PH 4B, Install Conc Rail	3	03-Sep-...	08-Sep-14	94
1.5.4.6.1.137	2C4BB137099999	BR 137, PH 4B, Finish	0		08-Sep-14	94
1.5	2C4B0000000001	START PHASE 4B, SUBSEGMENT 2C	0	19-Jun-14		67
1.5	2C4B0000099999	FINISH PHASE 4B, SUBSEGMENT 2C	0		15-Oct-14	67
CONSTRUCTION PHASE 4C			131	15-Oct-14	16-Apr-15	49
1.5	2C4CML600000...	Area ML6, PH 4C, Start	0	15-Oct-14		67

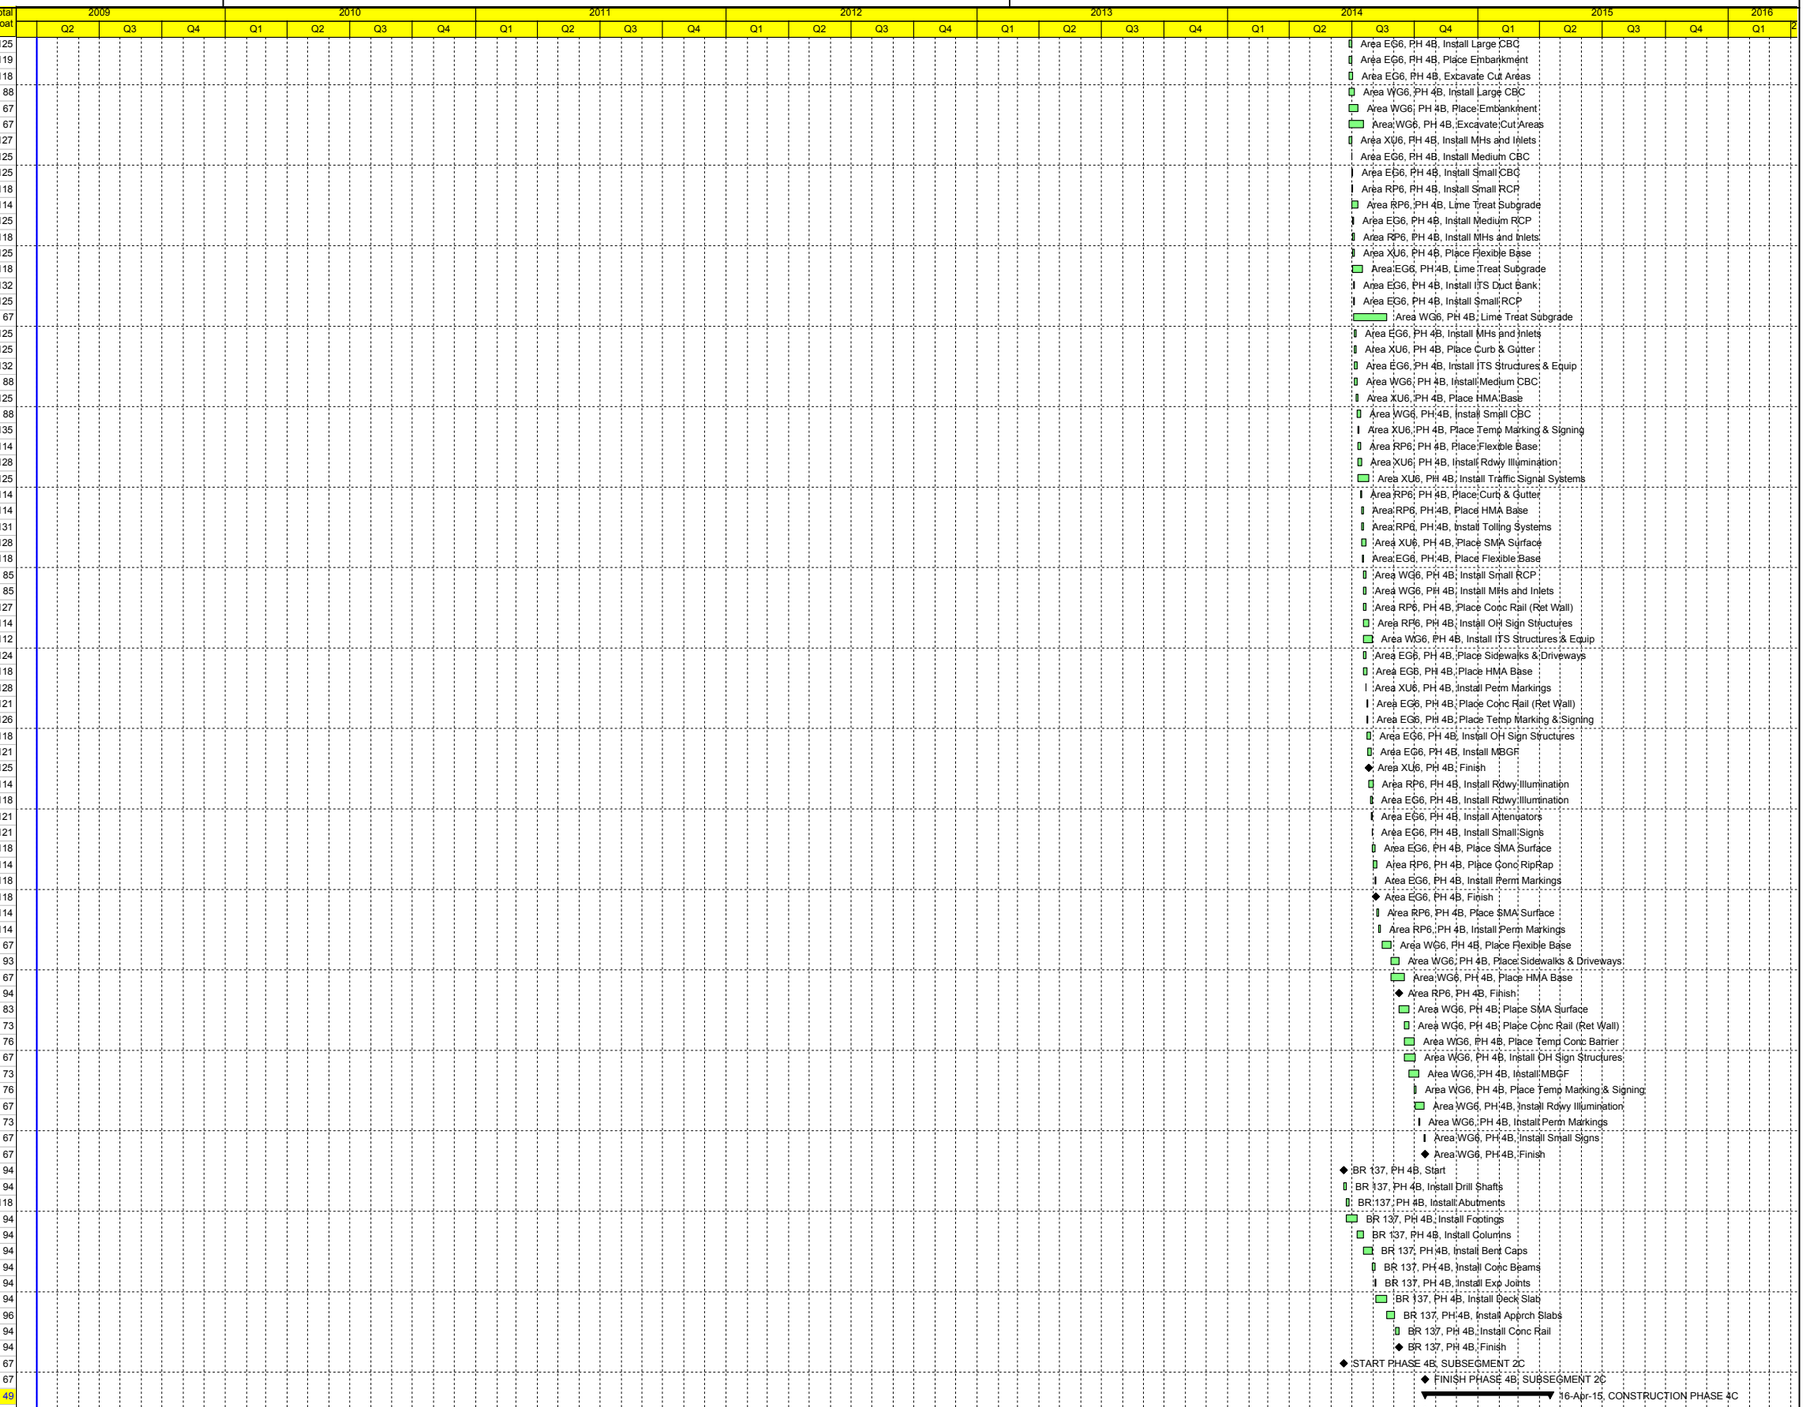

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.

WBS	Activity ID	Activity Name	Original Duration	Start	Finish	Total Float
1.5	2C4CWG60000...	Area WG6, PH 4C, Start	0	15-Oct-14		80
1.5	2C4CXU60000001	Area XU6, PH 4C, Start	0	15-Oct-14		138
1.5.2.6	2C4CXU60050600	Area XU6, PH 4C, Place Temp Erosion Control	2	15-Oct-14	17-Oct-14	138
1.5.3.6	2C4CML600462...	Area ML6, PH 4C, Install Medium CBC	6	15-Oct-14	23-Oct-14	83
1.5.2.6	2C4CWG60050...	Area WG6, PH 4C, Place Temp Erosion Cont...	6	15-Oct-14	23-Oct-14	80
1.5.2.6	2C4CML600132...	Area ML6, PH 4C, Place Embankment	22	15-Oct-14	14-Nov-14	67
1.5.2.6	2C4CML600110...	Area ML6, PH 4C, Excavate Cut Areas	32	15-Oct-14	28-Nov-14	67
1.5.2.6	2C4CXU60010410	Area XU6, PH 4C, Rem Conc Pavement	2	17-Oct-14	21-Oct-14	138
1.5.3.6	2C4CXU60046420	Area XU6, PH 4C, Install Medium RCP	2	21-Oct-14	23-Oct-14	139
1.5.8.6	2C4CXU60062899	Area XU6, PH 4C, Install Elec Service for ITS...	3	21-Oct-14	24-Oct-14	162
1.5.2.6	2C4CXU60026010	Area XU6, PH 4C, Lime Treat Subgrade	8	21-Oct-14	31-Oct-14	138
1.5.2.6	2C4CWG60010...	Area WG6, PH 4C, Rem Concrete Barrier	2	23-Oct-14	27-Oct-14	80
1.5.8.6	2C4CXU60061899	Area XU6, PH 4C, Install ITS Duct Bank	2	23-Oct-14	27-Oct-14	161
1.5.3.6	2C4CML600462...	Area ML6, PH 4C, Install Small CBC	3	23-Oct-14	28-Oct-14	83
1.5.3.6	2C4CXU60046410	Area XU6, PH 4C, Install Small RCP	3	23-Oct-14	28-Oct-14	139
1.5.2.6	2C4CML600260...	Area ML6, PH 4C, Lime Treat Subgrade	30	24-Oct-14	05-Dec-14	76
1.5.2.6	2C4CWG60010...	Area WG6, PH 4C, Rem Conc Pavement	2	27-Oct-14	29-Oct-14	80
1.5.3.6	2C4CXU60046510	Area XU6, PH 4C, Install MHs and Inlets	2	28-Oct-14	30-Oct-14	139
1.5.3.6	2C4CWG60046...	Area WG6, PH 4C, Install Large CBC	4	29-Oct-14	04-Nov-14	119
1.5.4.6	2C4CWG60042...	Area WG6, PH 4C, Install Cut Wall, Stage 1	6	29-Oct-14	06-Nov-14	80
1.5.2.6	2C4CXU60024710	Area XU6, PH 4C, Place Flexible Base	5	31-Oct-14	07-Nov-14	138
1.5.3.6	2C4CWG60046...	Area WG6, PH 4C, Install Medium CBC	2	04-Nov-...	06-Nov-14	119
1.5.3.6	2C4CWG60046...	Area WG6, PH 4C, Install Small CBC	2	06-Nov-...	10-Nov-14	119
1.5.2.6	2C4CWG60013...	Area WG6, PH 4C, Place Embankment	7	06-Nov-...	17-Nov-14	83
1.5.2.6	2C4CWG60011...	Area WG6, PH 4C, Excavate Cut Areas	10	06-Nov-...	20-Nov-14	80
1.5.2.6	2C4CXU60052910	Area XU6, PH 4C, Place Curb & Gutter	5	07-Nov-...	14-Nov-14	138
1.5.2.6	2C4CXU60034011	Area XU6, PH 4C, Place HMA Base	5	14-Nov-...	21-Nov-14	138
1.5.3.6	2C4CML600465...	Area ML6, PH 4C, Install MHs and Inlets	15	14-Nov-...	05-Dec-14	67
1.5.3.6	2C4CML600464...	Area ML6, PH 4C, Install Small RCP	18	14-Nov-...	10-Dec-14	67
1.5.3.6	2C4CWG60046...	Area WG6, PH 4C, Install MHs and Inlets	2	20-Nov-...	24-Nov-14	111
1.5.4.6	2C4CWG60042...	Area WG6, PH 4C, Install Cut Wall, Stage 2	9	20-Nov-...	03-Dec-14	110
1.5.2.6	2C4CWG60026...	Area WG6, PH 4C, Lime Treat Subgrade	33	20-Nov-...	06-Jan-15	80
1.5.9.6	2C4CXU60066200	Area XU6, PH 4C, Place Temp Marking & Si...	1	21-Nov-...	24-Nov-14	152
1.5.7.6	2C4CXU60061020	Area XU6, PH 4C, Install Rdwy Illumination	6	21-Nov-...	01-Dec-14	142
1.5.7.6	2C4CXU60068010	Area XU6, PH 4C, Install Traffic Signal Syste...	15	21-Nov-...	12-Dec-14	138
1.5.2.6	2C4CXU60034610	Area XU6, PH 4C, Place SMA Surface	4	01-Dec-...	05-Dec-14	142
1.5.7.6	2C4CXU60066610	Area XU6, PH 4C, Install Perm Markings	1	05-Dec-...	08-Dec-14	142
1.5.2.6	2C4CML600247...	Area ML6, PH 4C, Place Flexible Base	14	05-Dec-...	25-Dec-14	67
1.5	2C4CXU60099999	Area XU6, PH 4C, Finish	0		12-Dec-14	138
1.5.2.6	2C4CML600340...	Area ML6, PH 4C, Place HMA Base	17	12-Dec-...	06-Jan-15	67
1.5.2.6	2C4CML600514...	Area ML6, PH 4C, Place Median Barrier	34	19-Dec-...	05-Feb-15	67
1.5.2.6	2C4CWG60024...	Area WG6, PH 4C, Place Flexible Base	6	06-Jan-15	14-Jan-15	80
1.5.7.6	2C4CML600650...	Area ML6, PH 4C, Install OH Sign Structures	29	09-Jan-15	19-Feb-15	67
1.5.2.6	2C4CWG60053...	Area WG6, PH 4C, Place Sidewalks & Drive...	6	14-Jan-15	22-Jan-15	98
1.5.2.6	2C4CWG60034...	Area WG6, PH 4C, Place HMA Base	9	14-Jan-15	27-Jan-15	80
1.5.7.6	2C4CML600610...	Area ML6, PH 4C, Install Rdwy Illumination	23	19-Jan-15	19-Feb-15	89
1.5.9.6	2C4CWG60066...	Area WG6, PH 4C, Place Temp Marking & Si...	1	27-Jan-15	28-Jan-15	105
1.5.2.6	2C4CWG60045...	Area WG6, PH 4C, Place Conc Rail (Ret Wall)	4	27-Jan-15	02-Feb-15	93
1.5.7.6	2C4CWG60065...	Area WG6, PH 4C, Install OH Sign Structures	8	27-Jan-15	06-Feb-15	80
1.5.2.6	2C4CWG60054...	Area WG6, PH 4C, Install MBGF	7	02-Feb-15	11-Feb-15	93
1.5.7.6	2C4CWG60061...	Area WG6, PH 4C, Install Rdwy Illumination	7	06-Feb-15	17-Feb-15	80
1.5.2.6	2C4CWG60054...	Area WG6, PH 4C, Install Attenuators	1	11-Feb-15	12-Feb-15	93
1.5.7.6	2C4CWG60064...	Area WG6, PH 4C, Install Small Signs	1	17-Feb-15	18-Feb-15	90
1.5.2.6	2C4CWG60034...	Area WG6, PH 4C, Place SMA Surface	10	17-Feb-15	03-Mar-15	80
1.5.2.6	2C4CML600346...	Area ML6, PH 4C, Place SMA Surface	20	19-Feb-15	19-Mar-15	67
1.5.7.6	2C4CWG60066...	Area WG6, PH 4C, Install Perm Markings	1	03-Mar-15	04-Mar-15	80
1.5	2C4CWG60099...	Area WG6, PH 4C, Finish	0		04-Mar-15	80
1.5.7.6	2C4CML600666...	Area ML6, PH 4C, Install Perm Markings	2	19-Mar-15	23-Mar-15	67
1.5	2C4CML600999...	Area ML6, PH 4C, Finish	0		16-Apr-15	49
1.5.4.6.1.115	2C4CB115000001	BR 115, PH 4C, Start	0	15-Oct-14		77
1.5.4.6.1.115	2C4CB115041600	BR 115, PH 4C, Install Drill Shafts (2 Crews)	41	15-Oct-14	11-Dec-14	77
1.5.4.6.1.115	2C4CB115042040	BR 115, PH 4C, Install Abutments	10	22-Oct-14	05-Nov-14	127
1.5.4.6.1.115	2C4CB115042010	BR 115, PH 4C, Install Footings (3 crews)	48	22-Oct-14	29-Dec-14	77
1.5.4.6.1.115	2C4CB115042020	BR 115, PH 4C, Install Columns (3 crews)	51	31-Oct-14	12-Jan-15	77
1.5.4.6.1.115	2C4CB115042050	BR 115, PH 4C, Install Apprch Slabs	3	05-Nov-...	10-Nov-14	157
1.5.4.6.1.115	2C4CB115042030	BR 115, PH 4C, Install Bent Caps (4 crews)	58	07-Nov-...	28-Jan-15	77
1.5.4.6.1.115	2C4CB115042510	BR 115, PH 4C, Install Conc Beams	35	28-Nov-...	16-Jan-15	77
1.5.4.6.1.115	2C4CB115042210	BR 115, PH 4C, Install Deck Slab	61	05-Dec-...	02-Mar-15	77
1.5.4.6.1.115	2C4CB115044210	BR 115, PH 4C, Install Plate Girders	16	20-Jan-15	11-Feb-15	85
1.5.4.6.1.115	2C4CB115045020	BR 115, PH 4C, Install Conc Rail	28	28-Jan-15	09-Mar-15	77
1.5.4.6.1.115	2C4CB115099999	BR 115, PH 4C, Finish	0		09-Mar-15	77
1.5	2C4C0000000001	START PHASE 4C, SUBSEGMENT 2C	0	15-Oct-14		67
1.5	2C4C0000099999	FINISH PHASE 4C, SUBSEGMENT 2C	0		16-Apr-15	49

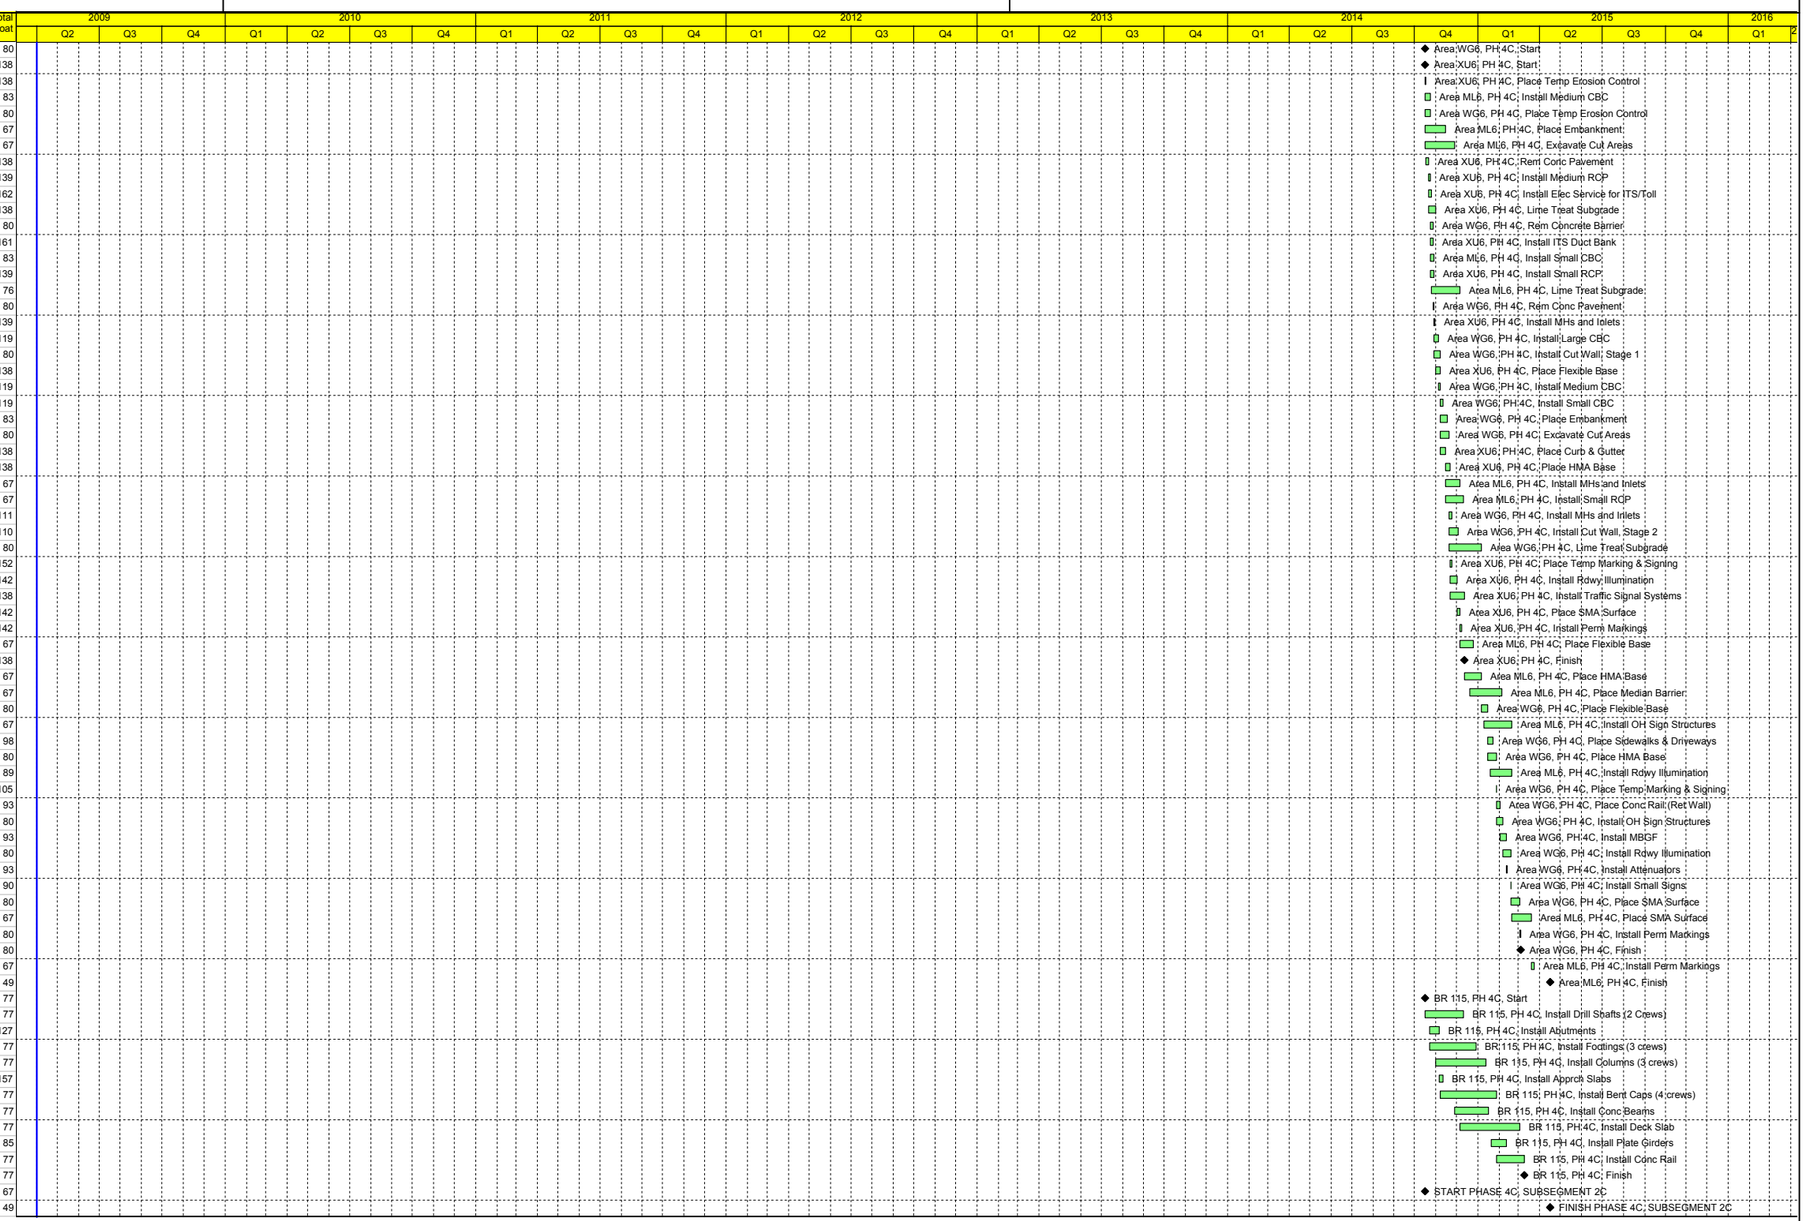

Remaining Level of Effort | Remaining Work | ◆ Milestone
Actual Work | Critical Remaining Work | Summary

TASK filter: All Activities

© Primavera Systems, Inc.
